



JOB No.: TCS00864/16

**CEDD SERVICE CONTRACT NO. NTE/07/2016
ENVIRONMENTAL TEAM FOR DEVELOPMENT OF
ANDERSON ROAD QUARRY SITE – SITE FORMATION
AND ASSOCIATED INFRASTRUCTURE WORKS**

**MONTHLY ENVIRONMENTAL MONITORING AND AUDIT
REPORT (FEBRUARY 2018)**

**PREPARED FOR
CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT
(CEDD)**

Date	Reference No.	Prepared By	Certified By
14 March 2018	TCS00864/16/600/R0144v3	 Nicola Hon (Environmental Consultant)	 Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	8 March 2018	First Submission
2	13 March 2018	Amended according to the IEC's comments on 13 March 2018
3	14 March 2018	Amended according to the IEC's comments on 14 March 2018



Civil Engineering and Development Department
New Territories East Development Office
Suite 1213 Chinachem Golden Plaza
77 Mody Road
Tsim Sha Tsui East
Kowloon

Your reference:

Our reference: HKCEDD10/50/104883

Date: 14 March 2018

Attention: Mr Stephen T S Li

BY POST

Dear Sirs

Agreement No.: NTE 08/2016
Independent Environmental Checker for Development of Anderson Road Quarry Site
– Site Formation and Associated Infrastructure Works
Monthly Environmental Monitoring and Audit Report (February 2018)

We refer to the emails of 8, 13 and 14 March 2018 from Action-United Environmental Services and Consulting attaching a Monthly Environmental Monitoring and Audit Report (February 2018) for the captioned project.

We have no further comment and hereby verify the Monthly Environmental Monitoring and Audit Report (February 2018).

Should you have any queries, please do not hesitate to contact the undersigned or our Mr Nic Lam on 2618 2831.

Yours faithfully
ANewR CONSULTING LIMITED



Adri Lee

Independent Environmental Checker

LYMA/LHHN/WCKJ/lhnh

cc CEDD – Mr Eric Li (email: chikli@cedd.gov.hk)
CEDD – Mr Matthew Lai (email: matthewsylai@cedd.gov.hk)
AECOM – Mr Alex Wong (email: yc.wong@aecom.com)
AECOM – Mr Dennis Leung (email: sre1tpf@yahoo.com.hk)
AUES – Mr T W Tam (email: twtam@fordbusiness.com)

EXECUTIVE SUMMARY

- ES01 Action-United Environmental Services & Consulting (AUES) has been awarded the Civil Engineering and Development Department (CEDD) Service Contract No. NTE/07/2016 Environmental Team for Development of Anderson Road Quarry Site – Site Formation and Associated Infrastructure Works (hereinafter called “the Service Contract”) on 15 December 2016. The commencement date of the Service Contract is from December 2016 and the Contract Period is 70 months.
- ES02 The Services under the Service Contract is to provide environmental monitoring and audit (EM&A) services for the Works Contracts pursuant to the requirement of Environmental Team (ET) under the EM&A manual to ensure that the environmental performance of the Works Contracts comply with the requirement specified in the EM&A Manual and EIA Report of Development of Anderson Road Quarry and other relevant statutory requirements.
- ES03 To facilitate the project management and implementation, the Service Contract is divided to three CEDD contracts including Contract 1 (NE/2016/01), Contract 2 (NE/2016/05) and Contract 3. As advised by the RE, the date for commencement of Contract 1 was on 21 December 2016 and the major construction works has been commenced on 12 April 2017. The date for commencement of Contract 2 was 31 March 2017 and the major construction activities have been commenced on 2 May 2017. The EM&A programme under the Project was therefore commenced on 12 April 2017 pursuant to the requirement under the EM&A manual.
- ES04 This is the **11th** monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **1 to 28 February 2018** (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES05 Environmental monitoring activities under the EM&A programme in the Reporting Period are summarized in the following table.

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Reporting Period	
		Number of Active Monitoring Locations	Total Occasions
Air Quality	1-hour TSP	4	60
	24-hour TSP	4	20
Construction Noise	$L_{eq(30min)}$ Daytime	2	10

BREACH OF ACTION AND LIMIT (A/L) LEVELS

- ES06 No exceedance of air quality was recorded in the Reporting Period. However, for construction noise, three (3) noise complaints (which triggered Action Level) were recorded for Contract 1. The environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	0	0
	24-hour TSP	0	0	0	0	0
Construction Noise	$L_{eq(30min)}$ Daytime	3	0	0	Completed and details refer to Section 8.	Enhancement of noise mitigation measures to eliminate nuisance

ENVIRONMENTAL COMPLAINT

- ES07 In the Reporting Period, three (3) environmental complaints were received for Contract 1 in respect with the construction noise concerned by the nearby resident and investigations for the complaints have been conducted by ET. Investigation reports revealed that the Contractor had implemented noise mitigation measures to eliminate to noise nuisance to the public and the construction works were carried out within the non-restricted hours. It is considered that the works under the project did not breach the Noise Control Ordinance. Nevertheless, in view of the subject site of the project is close to the residential area, the Contractor was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

- ES08 No environmental summons or successful prosecutions for the Project were recorded in the Reporting Period.

REPORTING CHANGE

- ES09 No reporting changes were made in the Reporting Period.

SITE INSPECTION

- ES10 In this Reporting Period, joint site inspection to evaluate the site environmental performance for **Contract 1** was carried out by the RE, ET and Contractor on **9, 13, 21 and 27 February 2018** in which IEC joined the site inspection with SSEMC on **9 February 2018**. No non-compliance was noted during the site inspection.
- ES11 In this Reporting Period, joint site inspection to evaluate the site environmental performance for **Contract 2** was carried out by the RE, ET and Contractor on **7, 13, 23 and 26 February 2018** in which IEC joined the site inspection with SSEMC on **26 February 2018**. No non-compliance was noted during the site inspection.

FUTURE KEY ISSUES

- ES12 Special attention should be paid on the potential construction dust impact since most of the construction sites are adjacent to resident. The Contractor should fully implement the construction dust mitigation measures properly, particularly in coming dry season.
- ES13 Construction noise would be a key environmental issue during construction work of the Project. Noise mitigation measures such as using quiet plants should be implemented in accordance with the EM&A requirement.
- ES14 In addition, all effluent discharge shall be ensure to fulfill Technical Memorandum of Effluent Discharged into Drainage and Sewerage Systems, inland and Coastal Waters criteria or discharge permits stipulation.

Table of Contents

1. INTRODUCTION	1
1.1 PROJECT BACKGROUND	1
1.2 REPORT STRUCTURE	1
2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
2.1 CONSTRUCTION CONTRACT PACKAGING	2
2.2 PROJECT ORGANIZATION	3
2.3 CONSTRUCTION PROGRESS	3
3. SUMMARY OF IMPACT MONITORING REQUIREMENTS	6
3.1 GENERAL	6
3.2 MONITORING PARAMETERS	6
3.3 MONITORING LOCATIONS	6
3.4 MONITORING FREQUENCY AND PERIOD	8
3.5 MONITORING EQUIPMENT	8
3.6 MONITORING METHODOLOGY	9
3.7 DERIVATION OF ACTION/LIMIT (A/L) LEVELS	11
3.8 DATA MANAGEMENT AND DATA QA/QC CONTROL	12
4. AIR QUALITY MONITORING	13
4.1 GENERAL	13
4.2 RESULTS OF AIR QUALITY MONITORING	13
5. CONSTRUCTION NOISE MONITORING	15
5.1 GENERAL	15
5.2 NOISE MONITORING RESULTS IN REPORTING MONTH	15
6. WASTE MANAGEMENT	16
6.1 GENERAL WASTE MANAGEMENT	16
6.2 RECORDS OF WASTE QUANTITIES	16
7. SITE INSPECTION	17
7.1 REQUIREMENTS	17
7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	17
8. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	19
8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	19
9. IMPLEMENTATION STATUS OF MITIGATION MEASURES	21
9.1 GENERAL REQUIREMENTS	21
9.2 KEY ISSUES FOR THE COMING MONTH	23
10. CONCLUSIONS AND RECOMMENDATIONS	24
10.1 CONCLUSIONS	24
10.2 RECOMMENDATIONS	24

LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 1
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 2
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	IMPACT MONITORING STATIONS - AIR QUALITY
TABLE 3-3	IMPACT MONITORING STATIONS - CONSTRUCTION NOISE
TABLE 3-4	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-5	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-6	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-7	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 4-1	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-1)
TABLE 4-2	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-5)
TABLE 4-3	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-6)
TABLE 4-4	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-7)
TABLE 5-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 6-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 6-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 7-1	SITE OBSERVATIONS OF CONTRACT 1
TABLE 8-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 8-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 8-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 9-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	ORGANIZATION CHART
APPENDIX C	THREE-MONTHS ROLLING CONSTRUCTION PROGRAMME
APPENDIX D	MONITORING LOCATIONS FOR IMPACT MONITORING
APPENDIX E	CALIBRATION CERTIFICATE OF MONITORING EQUIPMENT AND HOKLAS-ACCREDITATION CERTIFICATE OF THE TESTING LABORATORY
APPENDIX F	EVENT AND ACTION PLAN
APPENDIX G	IMPACT MONITORING SCHEDULE
APPENDIX H	DATABASE OF MONITORING RESULT
APPENDIX I	GRAPHICAL PLOTS FOR MONITORING RESULT
APPENDIX J	METEOROLOGICAL DATA
APPENDIX K	WASTE FLOW TABLE
APPENDIX L	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES
APPENDIX M	COMPLAINT LOG AND INVESTIGATION REPORT FOR COMPLAINT

1. INTRODUCTION**1.1 PROJECT BACKGROUND**

- 1.1.1 Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) has been awarded the CEDD Service Contract No. NTE/07/2016 Environmental Team for Development of Anderson Road Quarry Site – Site Formation and Associated Infrastructure Works (hereinafter called “the Service Contract”) on 15 December 2016. The commencement date of the Service Contract is in December 2016 and the Contract Period is 70 months.
- 1.1.2 The Services under the Service Contract is to provide environmental monitoring and audit (EM&A) services for the Works Contracts pursuant to the requirement of Environmental Team (ET) under the EM&A manual to ensure that the environmental performance of the Works Contracts comply with the requirement specified in the EM&A Manual and EIA Report of Development of Anderson Road Quarry and other relevant statutory requirements.
- 1.1.3 Development of Anderson Road Quarry is to provide land and the associated infrastructures for the proposed land used at the existing Anderson Road Quarry Site at the North-eastern of East Kowloon according to the final Recommended Outline Development Plan (hereinafter named as the Project Works).
- 1.1.4 To facilitate the project management and implementation, the Service Contract is divided to three CEDD contracts including Contract 1 (NE/2016/01), Contract 2 (NE/2016/05) and Contract 3. As advised by the RE, the date for commencement of Contract 1 was on 21 December 2016 and the major construction works has been commenced on 12 April 2017. The date for commencement of Contract 2 was 31 March 2017 and the major construction activities have been commenced on 2 May 2017. The EM&A programme under the Project was therefore commenced on 12 April 2017 pursuant to the requirement under the EM&A manual.
- 1.1.5 According to the Approved EM&A Manual, air quality and noise monitoring are required to be monitored during the construction phase of the Project. As part of the EM&A program, baseline monitoring is required to determine the ambient environmental conditions. Baseline monitoring including air quality and noise were conducted on **17th January 2017 to 30th January 2017, 16th February 2017 to 2nd March 2017 and 26th March 2017 to 8th April 2017** at all designated monitoring locations before construction work commencement.
- 1.1.6 The Baseline Monitoring Report which verified by the Independent Environmental Checker (hereinafter referred as “the IEC”) has been submitted to Environmental Protection Department (EPD) on **9 May 2017** for endorsement.
- 1.1.7 This is the **11th** monthly EM&A report presenting the monitoring results and inspection findings for the reporting period from **1 to 28 February 2018**.

1.2 REPORT STRUCTURE

- 1.1.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

Section 1	<i>Introduction</i>
Section 2	<i>Project Organization and Construction Progress</i>
Section 3	<i>Summary of Impact Monitoring Requirements</i>
Section 4	<i>Air Quality Monitoring</i>
Section 5	<i>Construction Noise Monitoring</i>
Section 6	<i>Water Quality Monitoring</i>
Section 7	<i>Waste Management</i>
Section 8	<i>Site Inspections</i>
Section 9	<i>Environmental Complaints and Non-Compliance</i>
Section 10	<i>Implementation Status of Mitigation Measures</i>
Section 11	<i>Conclusions and Recommendations</i>

2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS**2.1 CONSTRUCTION CONTRACT PACKAGING**

- 2.1.1 To facilitate the project management and implementation, the Project would be divided by the 3 contracts as described in following. The details of each contracts is summarized below and the delineation of each contracts is shown in [Appendix A](#).

Contract 1 (Contract No. NE/2016/01)

- 2.1.2 Commencement date of Contract 1 was in late December 2016 and the major scope of work of Contract 1 is listed below:

- Formation of about 40 hectares (ha) of land platforms at the ARQ site and the associated geotechnical works;
- Road works including construction of approximately 3-kilometer long vehicular roads, footpaths, cycle tracks, an approximately 130-meter long underpass at the southern end and a public transport terminus at the northern end at the ARQ site;
- Provision of and improvement to water supply, drainage and sewerage systems as well as landscaping works; and
- Construction of proposed subway structures and lift tower structures of pedestrian connectivity facilities.

Contract 2 (Contract No. NE/2016/05)

- 2.1.3 Commencement date of Contract 2 was 31 March 2017 and the major Scope of Work of the Contract 2 is listed below:

- (i) Construction of the following pedestrian connectivity facilities with covered elevated walkways, covered at grade walkways, escalators, lift towers with associated staircase and lifts:-
 - (a) Linking Hiu Kwong street with Hiu Ming Street (E1)
 - (b) Linking the proposed “Footbridge Link at Sau Ming Road” with Hiu Ming Street (E2, C1 and E3)
 - (c) Linking the proposed bus-to-bus interchange at Tseung Kwan O Tunnel Toll Plaza with Lin Tak Road (E12)
- (ii) Construction of bus-to-bus interchange (BBI) at Tseung Kwan O Tunnel Toll Plaza; and
- (iii) Associated landscape works.
- (iv) Construction of green routes connecting to Jordan Valley Park and Choi Wing Road
- (v) Slope improvement works in the vicinity of Po Lam Road South and other associated works.

Contract 3 (Contract number to be assigned)

- 2.1.4 The commencement date of Contract 3 is to be confirmed.

- (i) Site formation and road works in the following sections:-
 - (a) at junction of Clear Water Bay Road (CWBR) and On Sau Road constructed under the Development at Anderson Road (DAR) project including the provision of U-turn facility and noise mitigation measures (RIW1);
 - (b) at New Clear Water Bay Road (NCWBR) near Shun Lee Tsuen Road including the road widening works at NCWBR, modification of existing subway structure and provision of noise mitigation measures (RIW2); and
 - (c) at the junction of Lin Tak Road and Sau Mau Ping Road, construction of flyover above Tseung Kwan O Road, provision of loading and unloading bays along Lin Tak Road and noise mitigation measures (RIW3).
- (ii) construction of the following pedestrian connectivity facilities with covered elevated walkways, escalators and lift towers with associated staircases and lifts:-
 - (a) linking Anderson Road Quarry site with the DAR Site (except the works covered under

- Contract 1) (System A and System B);
- (b) linking Hiu Ming Street with Hiu Yuk Path (E8); and
- (c) linking the proposed bus-bus interchange at Tseung Kwan O Tunnel Toll Plaza with Sau Mau Ping Road (E11).
- (iii) Associated landscape works.

2.2 PROJECT ORGANIZATION

- 2.2.1 The project organization for Contracts 1 and 2 is shown in [Appendix B](#).

2.3 CONSTRUCTION PROGRESS

- 2.3.1 The three-months rolling construction program for Contracts 1 and 2 are enclosed in [Appendix C](#). As provided by the Contractors of Contracts 1 and 2, the major construction activities conducted in the Reporting Period are summarized in below.

Contract 1 (NE/2016/01)

- i. Site Cleaning;
- ii. Land Contamination Ground Investigation (totally completed 18 out of 29 holes)
- iii. Site Formation in Portion A4:
- iv. Site Formation in Portion A3:
- v. Site Formation in Portion A6:
- vi. Site Formation in Portion B8 and KW Asphalt Plant:
- vii. Alliance Concrete Plant at Portion B7:
 - Debris removal and breaking of concrete slab
- viii. KWP Crushing Plant
 - Commenced demolition of structure.
- ix. West Portal Area;
 - Continued trimming slope at West Portal at top-down direction
 - The soil nailing works at Slope A3
 - Continued erection of scaffolds and platforms to proceed remaining soil nailing works at Slope A3
- x. East Portal Area;
 - Completed erection of scaffolds and platforms at Slope A1 East Portal
 - excavation for site formation at Slope A1
 - The soil nailing works at Slope A1
- xi. Underpass
 - Commenced tunnel face excavation from West Portal
- xii. Internal Road L4, RWA18, RWA12 and Pedestrian Connectivity System A:
 - construction of base slab of noise barrier bay #26
 - formworks for noise barrier bay #24
 - excavation of retaining wall RWA18 bay #5 to 3
 - excavation at retaining wall RWA12 bay #22
 - construction of the new haul road to retaining wall RWA12
- xiii. Underground Stormwater Retention Tank:
 - stripping soil to expose rock head level and excavation
 - rebar fixing of base slabs for bay #2, 3, 4 and 6
- xiv. Water Pumping Station and Retaining Wall RWA13 and RWA14:
 - excavation of slope A13 and the area of water pumping stations
 - construction of base slabs for retaining wall RWA13 and RWA14
- xv. Pedestrian Connectivity System B:
 - excavation at North lift tower and South lift tower
- xvi. Internal Road L1:
 - excavation for the internal road L1 adjacent to the Pedestrian Connectivity System B
 - assembly of formworks for the transition section CHA144 to CHA168.019 (Bay #13 and 14) of the box culvert BC1 and construction of base slab of the box culvert BC1
 - Excavation for DP750

Contract 2 (NE/2016/05)

1. Portion 1 : Continue piling works, Completed modification and relocation of the site entrance;
2. Portion 2: Completed piling works mobilization. Commence temporary rock fall fence works. Completed removal of temporary work access at Hiu Ming Street.
3. Portion 4 : Continue the Slip Road construction, Continue Tree transplant works
4. Portion 5 : Completed tree felling. Continue tree transplant works
5. Portion 6: Continue rock dowel installation works. Completed inspection pit to identify existing UU at TKOT Road
6. Portion 7 : Continue to construct Hiking trail extension work in Site A and Site B, Continue slope improvement works in Site B;
7. Portion 8 & 9: Completed rebar cutting for soil nail head. Placed purchase ordering materials of flexible barrier and stone pitching.

- 2.3.2 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project of contract 1 are presented in **Tables 2-1 and 2-2**.

Table 2-1 Status of Environmental Licenses and Permits of the Contract 1

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Form NA - Notification pursuant to Air pollution Control (Construction Dust) Regulation	EPD ref. no. 411762	NA	NA	valid
	Form NB - Notification pursuant to Air pollution Control (Construction Dust) Regulation	EPD ref. no. 412730	NA	NA	valid
2	Chemical Waste Producer Registration	Registration no. WPN 5213-292-C4115-01	15 Feb 2017	End of project	valid
3	Water Pollution Control Ordinance - Discharge License	WT00027252-2017	20 Mar 2017	31 Mar 2022	valid
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account no. 7026925	20 Jan 2017	End of project	valid
6	Construction Noise Permit	GW-RE1017-17	23 Dec 17	19 Jun 18	valid
		GW-RE0098-18	12 Feb 18	22 Aug 18	valid

Table 2-2 Status of Environmental Licenses and Permits of the Contract 2

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Notification pursuant to Air pollution Control (Construction Dust) Regulation	EPD ref. no. 312173	NA	NA	valid
2	Chemical Waste Producer Registration	Registration no. WPN 5213-294-K28 90-08	3 July 2017	End of Project	Valid
3	Water Pollution Control Ordinance - Discharge License	WT00028685-2017	02 Aug 2017	31 Aug 2022	Valid
		WT00028686-2017	02 Aug 2017	31 Aug 2022	Valid
		WT00028687-2017	02 Aug 2017	31 Aug 2022	Valid
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account no.7027548	12 Apr 2017	End of project	Valid
5	Construction Noise Permit	GW0RE0145-18	8 Mar 2018	4 Apr 2018	Valid

3. SUMMARY OF IMPACT MONITORING REQUIREMENTS

3.1 GENERAL

3.1.1 The Environmental Monitoring and Audit requirements are set out in the Approved EM&A manual. Environmental issues such as air quality, construction noise and water quality were identified as the key issues during the construction phase of the Project.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

3.2 MONITORING PARAMETERS

3.2.1 The EM&A program of construction phase monitoring shall cover the following environmental issues:

- Air quality; and
- Construction noise

3.2.2 A summary of the monitoring parameters is presented in *Table 3-1*.

Table 3-1 Summary of EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> • 1-hour TSP by Real-Time Portable Dust Meter; and • 24-hour TSP by High Volume Air Sampler
Noise	<ul style="list-style-type: none"> • Leq(30min) in normal working days (Monday to Saturday) 07:00-19:00 except public holiday • Supplementary information for data auditing, statistical results such as L₁₀ and L₉₀ shall also be obtained for reference.

3.3 MONITORING LOCATIONS

3.3.1 According to the EM&A Manual Section 4.6, seven (7) most representative and affected air sensitive receivers (ASR) were selected as air monitoring stations (AQM). The air quality monitoring locations are listed in *Table 3-2* and illustrated in *Appendix D*.

Table 3-2 Impact Monitoring Stations - Air Quality

ID	ASR ID in EIA	Location in the EM&A Manual	Identified Location during Site Visit
AMS-1	ACYC-01	Chi Yum Ching She	Ground of Chi Yum Ching facing the project site
AMS-2	DARB-13	Block 8, Site B ^{Note 1}	Ground of Block 8, Site B facing On Sau Road
AMS-3	DARC-16	Planned Clinic and Community Centre, Site C2 ^{Note 1}	Ground of Planned Clinic and Community Centre facing Anderson Road
AMS-4	DARC-26	Planned School, Site C2 ^{Note 2}	Ground of Planned School facing Anderson Road
AMS-5	DARE-06	Block 5, DAR Site E	Main roof of Oi Tat House of On Tat Estate facing the project site
AMS-6	DARE-17	Block 9, Site E	Main roof of Hau Tat House of On Tat Estate facing the project site
AMS-7	AMYT-04	Ma Yau Tong Village	Balcony at 2 nd floor of Village House Anderson Road No. 1 facing the project site

Note 1: The ASR is under construction and not yet in operation.

Note 2: The ASR is not yet constructed.

3.3.2 In our recent site visit at the subject site, it was noted that some planned ASRs identified in the

EM&A Manual are still under construction/ has not yet constructed and there were no suitable location to set up the high volume sampler to carry out the baseline 24-hour TSP monitoring. Therefore, a proposed changes for the baseline monitoring programme was submitted and agreed by EPD before the baseline monitoring.

3.3.3 In our baseline monitoring proposal, baseline 1-hour TSP monitoring will be conducted at all AQM location AMS-1 to AMS-7. However, baseline 24-hour TSP monitoring will be conducted at existing ASR AMS-1, AMS-5, AMS-6 and AMS-7 only with our justifications present below:

- (a) AQM Locations AMS-2, AMS-3 & AMS-4 are planned ASRs which are still under construction/ has not yet constructed. During recent site visit, there were no suitable locations for setting up the HVS and electricity supply at these AQM locations.
- (b) Alternative locations were considered in accordance with EM&A Manual Section 4.7.3. However, there were no suitable location found and our justifications are provided in below:
 - (i) Alternative locations Sau Mau Ping Estate and Shun Tin Estate were located at downhill of the subject site which separated by the active construction site (i.e., AMS-2, AMS-3 & AMS-4) and Sau Mau Ping Road. In view of the level deviation, the baseline data obtained in these alternative locations could not represent the baseline condition of the designated location AMS-2, AMS-3 & AMS-4. Moreover, when the planned ASR AMS-2, AMS-3 & AMS-4 activate sooner or later, impact monitoring should be carried out at these designated locations instead of the alternative locations.
 - (ii) Alternative location such as site boundary of the site subject was considered, however, there were no provisions of power supply to sustain the HVS continuously after consultation with the Contractor.
- (c) According to EM&A Manual Section 4.7.4, as an exceptional cases, it is proposed to adopt the Action Level established at AMS-5 to AMS-2, AMS-3 & AMS-4 for impact monitoring as AMS-5 with our justification below.
 - (i) AMS-5 is the closest ASR to AMS-2, AMS-3 & AMS-4 under same direction of prevailing wind.
 - (ii) In view of the baseline 1-hour TSP data, the measured results at AMS-5 were lower than those collected at AMS-2, AMS-3 & AMS-4. As a conservation approach, adopting Action Level at AMS-5 for Location AMS-2, AMS-3 & AMS-4 is more stringent for the project.
 - (iii) The Action level for AMS-2, AMS-3 & AMS-4 will be subject to review in accordance with EM&A Manual Section 4.7.5

Construction Noise

3.3.4 According to the EM&A Manual Section 5.5, three (3) most representative and affected noise sensitive receivers (NSR) were selected as monitoring stations. As recommended by the RE and agreed by IEC, one (1) additional noise monitoring location is proposed to add in Oi Tat House of On Tat Estate (hereafter “NMS-4”) to oversee the possible noise impact pose to the resident in On Tat Estate, which is an existing NSR close to the major works activities. Moreover, a review of impact monitoring location was proposed to IEC in view of the current site condition and it was agreed by all parties. The details of noise monitoring location are listed in **Table 2-3** and illustrated in **Appendix D**.

Table 3-3 Impact Monitoring Stations - Construction Noise

ID	NSR ID in EIA	Location
NMS-1	Site C2 – School 05 ^{Note 1}	Ground of planned school at DAR facing the project site
NMS-2	Site E – School ^{Note 1}	Ground area between the planned school and Him Tat House facing the project site

NMS-3	Site C2 – R102 ^{Note 1}	Ground of Ancillary Facilities Building facing the project site
NMS-4*	Oi Tat House	1m from the exterior of ground floor façade of Oi Tat House of On Tat Estate facing the project site
NMS-4a#	Oi Tat House	Rooftop of Oi Tat House where 1m from the exterior of Oi Tat House facing the project site
NMS-5#	Hau Tat House	22/F, refuge floor of Hau Tat House where 1m from the exterior of Hau Tat House facing the project site.

Note 1: The NSR is under construction and not yet in operation.

Remark: () Additional noise monitoring location is recommended by RE and agreed by IEC. It is temporary suspended and the monitoring location is relocated to NMS4a.*

(#) Review of noise monitoring locations which effective on 8 November 2017.

3.4 MONITORING FREQUENCY AND PERIOD

3.4.1 The requirements of impact monitoring in the approved *EM&A Manual* and presented as follows.

Air Quality Monitoring

3.4.2 Frequency of impact air quality monitoring is as follows:

- 1-hour TSP 3 times every six days during course of works throughout the construction period
- 24-hour TSP Once every 6 days during course of works throughout the construction period

Noise Monitoring

3.4.3 Noise monitoring will be to conduct at the all available designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:

- one set of Leq(30min) measurements between 07:00 and 19:00 hours on normal weekdays

3.5 MONITORING EQUIPMENT

Air Quality Monitoring

3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to prove that the instrument is capable of achieving a comparable results to the HVS. The instrument should be calibrated regularly, and the 1-hour sampling shall be determined on yearly basis by the HVS to check the validity and accuracy of the results measured by direct reading method. The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

3.5.2 All equipment to be used for air quality monitoring is listed in **Table 3-4**.

Table 3-4 Air Quality Monitoring Equipment

Equipment		Model
24-hour TSP	High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170
	Calibration Kit	TISCH Model TE-5025A
1- hour TSP	Portable Dust Meter	Sibata LD-3B Laser Dust Monitor

Noise Monitoring

- 3.5.3 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms^{-1} .
- 3.5.4 Noise equipment as perform for baseline monitoring is listed in *Table 3-5*.

Table 3-5 Construction Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	B&K Type 2238
Calibrator	Cesva CB - 5
Portable Wind Speed Indicator	Anemometer AZ Instrument 8908

3.6 MONITORING METHODOLOGY

1-hour TSP

- 3.6.1 The 1-hour TSP monitor was a brand named “Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter” which is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90° light scattering. The 1-hour TSP monitor consists of the following:
- (a.) A pump to draw sample aerosol through the optic chamber where TSP is measured;
 - (b.) A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
 - (c.) A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.
- 3.6.2 The 1-hour TSP meter to be used will be within the valid period, calibrated by the manufacturer prior to purchasing. Zero response of the instrument will be checked before and after each monitoring event.

24-hour TSP

- 3.6.3 The equipment used for 24-hour TSP measurement is Thermo Andersen Model GS2310 TSP high volume air sampling system, which complied with *EPA Code of Federal Regulation, Appendix B to Part 50*. The High Volume Air Sampler (HVS) consists of the following:
- (a.) An anodized aluminum shelter;
 - (b.) A 8"x10" stainless steel filter holder;
 - (c.) A blower motor assembly;
 - (d.) A continuous flow/pressure recorder;
 - (e.) A motor speed-voltage control/elapsed time indicator;
 - (f.) A 7-day mechanical timer, and
 - (g.) A power supply of 220v/50 Hz
- 3.6.4 For HVS for 24-hour TSP monitoring, the HVS is mounted in a metallic cage with a top for protection and also it is sat on the existing ground or the roof of building. The flow rate of the HVS between $0.6\text{m}^3/\text{min}$ and $1.7\text{m}^3/\text{min}$ will be properly set in accordance with the manufacturer's instruction to within the range recommended in *EPA Code of Federal Regulation, Appendix B to Part 50*. Glass Fiber Filter 8" x 10" of TE-653 will be used for 24-Hour TSP monitoring and would be supplied by laboratory. The general procedures of sampling are described as below:-
- A horizontal platform with appropriate support to secure the samples against gusty wind should be provided;
 - No two samplers should be placed less than 2 meters apart;
 - The distance between the sampler and an obstacle, such as building, must be at least twice the height that the obstacle protrudes above the sample;

- A minimum of 2 meters of separation from any supporting structure, measured horizontally is required;
- Before placing any filter media at the HVS, the power supply will be checked to ensure the sampler work properly;
- The filter paper will be set to align on the screen of HVS to ensure that the gasket formed an air tight seal on the outer edges of the filter. Then filter holder frame will be tightened to the filter hold with swing bolts. The holding pressure should be sufficient to avoid air leakage at the edge.
- The mechanical timer will be set for a sampling period of 24 hours (00:00 mid-night to 00:00 mid-night next day). Information will be recorded on the field data sheet, which would be included the sampling data, starting time, the weather condition at current and the filter paper ID with the initial weight;
- After sampling, the filter paper will be collected and transfer from the filter holder of the HVS to a sealed envelope and sent to a local HOKLAS accredited laboratory for quantifying.

3.6.5 All the sampled 24-hour TSP filters will be kept in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal.

3.6.6 The HVS used for 24-hour TSP monitoring will be calibrated before the commencement for sampling, and after in two months interval for 1 point checking of maintenance and six months interval for five points calibrate in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A) to establish a relationship between the follow recorder meter reading in cfm (cubic feet per minute) and the standard flow rate, Qstd, in m³/min. Motor brushes of HVS will be regularly replaced of about five hundred hours per time. The calibration certificates of all monitoring equipment used for the impact monitoring program in the Reporting Period and the HOKLAS accredited certificate of laboratory are attached in [Appendix E](#).

Noise Monitoring

3.6.7 As referred to in the Technical Memorandum (TM) issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804:1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.

3.6.8 All noise measurements will be performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq_(30 min) in six consecutive Leq_(5 min) measurements will be used as the monitoring parameter for the time period between 07:00-19:00 hours on weekdays throughout the construction period.

3.6.9 The sound level meter will be mounted on a tripod at a height of 1.2 m and placed at the assessment point and oriented such that the microphone is pointed to the site with the microphone facing perpendicular to the line of sight. The windshield will be fitted for all measurements. Where a measurement is to be carried out at a building, the assessment point would normally be at a position 1 m from the exterior of the building façade. Where a measurement is to be made for noise being received at a place other than a building, the assessment point would be at a position 1.2 m above the ground in a free-field situation, i.e. at least 3.5 m away from reflective surfaces such as adjacent buildings or walls.

3.6.10 Immediately prior to and following each noise measurement the accuracy of the sound level meter will be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.

- 3.6.11 Noise measurements will not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed will be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 3.6.12 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis. The calibration certificates of all monitoring equipment used for the impact monitoring program in the Reporting Period is attached in [Appendix E](#).

Meteorological Information

- 3.6.13 The meteorological information including wind direction, wind speed, humidity, rainfall, air pressure and temperature etc. during baseline monitoring is extracted from the closest Hong Kong Observatory Station. To obtain the most appropriate meteorological information where available, the data of temperature is extracted from the Kwun Tong Observatory Station; the data of wind speed and wind direction are extracted from Kai Tak Observatory Station and the data of humidity is extracted from King's Park Station.

3.7 DERIVATION OF ACTION/LIMIT (A/L) LEVELS

- 3.7.1 The baseline results form the basis for determining the environmental acceptance criteria for the impact monitoring. According to the approved Environmental Monitoring and Audit Manual, the air quality, construction noise were set up, namely Action and Limit levels are listed in **Tables 3-6 and 3-7**.

Table 3-6 Action and Limit Levels for Air Quality Monitoring

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AMS-1	313	154	500	260
AMS-2	319	165	500	260
AMS-3	319	165	500	260
AMS-4	315	165	500	260
AMS-5	299	166	500	260
AMS-6	303	168	500	260
AMS-7	307	156	500	260

Table 3-7 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
NMS-1	When one or more documented complaints are received	75 dB(A) ^{Note 1} /
NMS-2		70 dB(A) ^{Note 2} / 65 dB(A) ^{Note 2}
NMS-3		75 dB(A)
NMS-4a*		75 dB(A)
NMS-4*		75 dB(A)
NMS-5*		75 dB(A)

Note 1: Locations NMS-1 and NMS-2 are planned school as NSRs which are still under construction/ not yet constructed; hence the Limit Levels of 75dB(A) is adopted for NMS-1 and NMS-2 until the school is occupied and in operation.

Note 2: Noise Limit Levels for school is 70dB(A) and should be reduced to 65dB(A) during examination period.

Note: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

Remark: () Additional noise monitoring location is recommended by RE and agreed by IEC, NMS4 is temporary suspended and the monitoring location is relocated to NMS4a.*

- 3.7.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in [Appendix F](#).

3.8 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.8.1 All monitoring data will be handled by the ET's in-house data recording and management system. The monitoring data recorded in the equipment will be downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data will input into a computerized database properly maintained by the ET. The laboratory results will be input directly into the computerized database and checked by personnel other than those who input the data.
- 3.8.2 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.

4. AIR QUALITY MONITORING**4.1 GENERAL**

4.1.1 In the Reporting Period, air quality monitoring was performed at the active designated monitoring locations AMS-1, AMS-5, AMS-6 and AMS-7. No monitoring was conducted at AMS-2, AMS-3 and AMS-4 since they are planned ASR which are still under construction/ not yet constructed.

4.1.2 The air quality monitoring schedule is presented in *Appendix G* and the monitoring results are summarized in the following sub-sections.

4.2 RESULTS OF AIR QUALITY MONITORING

4.2.1 In the Reporting Period, a total of **60** events of 1-hour TSP and **20** events 24-hours TSP monitoring were carried out and the monitoring results are summarized in *Tables 4-1 to 4-4*. The detailed 24-hour TSP monitoring data are presented in *Appendix H* and the relevant graphical plots are shown in *Appendix I*.

Table 4-1 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-1)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Feb-18	45	2-Feb-18	9:26	53	52	58
12-Feb-18	44	8-Feb-18	9:13	57	55	56
15-Feb-18	44	14-Feb-18	13:21	47	46	48
20-Feb-18	32	20-Feb-18	9:21	52	49	55
27-Feb-18	56	26-Feb-18	13:55	78	80	79
Average (Range)	44 (32 – 56)	Average (Range)		58 (46 – 80)		

Table 4-2 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-5)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Feb-18	70	2-Feb-18	9:37	70	64	67
12-Feb-18	65	8-Feb-18	13:17	56	56	59
15-Feb-18	68	14-Feb-18	9:52	55	55	55
20-Feb-18	36	20-Feb-18	13:25	74	68	71
27-Feb-18	45	26-Feb-18	09::19	73	80	77
Average (Range)	57 (36 – 70)	Average (Range)		65 (55 – 80)		

Table 4-3 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-6)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Feb-18	46	2-Feb-18	13:00	61	61	63
12-Feb-18	69	8-Feb-18	13:33	52	51	50
15-Feb-18	83	14-Feb-18	9:26	61	55	54
20-Feb-18	42	20-Feb-18	13:08	72	69	74
27-Feb-18	35	26-Feb-18	9:36	80	77	78
Average (Range)	55 (35 – 83)	Average (Range)		64 (50 – 80)		

Table 4-4 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-7)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Feb-18	31	2-Feb-18	13:34	50	58	64
12-Feb-18	32	8-Feb-18	13:21	54	53	55
15-Feb-18	65	14-Feb-18	9:16	46	44	45
20-Feb-18	31	20-Feb-18	13:19	54	58	59
27-Feb-18	32	26-Feb-18	13:15	74	77	78
Average (Range)	38 (31 – 65)	Average (Range)		58 (44 – 78)		

4.2.2 As shown in *Tables 4-1 to 4-4*, all the 1-hour TSP and 24-hour TSP monitoring results were below the Action/Limit Levels. No Notification of Exceedance (NOE) was issued in this Reporting Period.

4.2.3 The meteorological data during the impact monitoring days are summarized in *Appendix J*.

5. CONSTRUCTION NOISE MONITORING**5.1 GENERAL**

5.1.1 In the Reporting Period, noise monitoring was performed at the additional monitoring locations NMS4a and NMS5. No monitoring was conducted at NMS1, NMS2 and NMS3 since they are planned NSR which are still under construction/ not yet constructed.

5.1.2 The noise monitoring schedule is presented in *Appendix G* and the monitoring results are summarized in the following sub-sections.

5.2 NOISE MONITORING RESULTS IN REPORTING MONTH

5.2.1 In the Reporting Period, a total of **10** events noise measurements were carried out at the designated locations. The noise monitoring results at the designated locations are summarized in *Tables 5-1*. The detailed noise monitoring data are presented in *Appendix H* and the relevant graphical plots are shown in *Appendix I*.

Table 5-1 Summary of Construction Noise Monitoring Results

Construction Noise Level ($L_{eq30min}$), dB(A)		
Date	NMS4a	NMS5
2-Feb-18	64	63
8-Feb-18	70	64
14-Feb-18	68	63
20-Feb-18	70	64
26-Feb-18	73	57
Limit Level	75 dB(A)	

5.2.2 As shown in *Tables 5-1*, no construction noise measurement results that exceeded the Limit Level were recorded.

5.2.3 In the Reporting Period, three (3) environmental complaints (which triggered Action Level exceedance) were received in respect with the construction noise concerned by the nearby resident. Investigation for the complaint was conducted by the ET and the detailed investigation result is presented in *Section 8*.

6. WASTE MANAGEMENT**6.1 GENERAL WASTE MANAGEMENT**

- 6.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

6.2 RECORDS OF WASTE QUANTITIES

- 6.2.1 All types of waste arising from the construction work are classified into the following:
- Construction & Demolition (C&D) Material;
 - Chemical Waste;
 - General Refuse; and
 - Excavated Soil.
- 6.2.2 The quantities of waste for disposal in this Reporting Period are summarized in **Tables 6-1** and **6-2** and the Monthly Summary Waste Flow Table is shown in **Appendix K**. Whenever possible, materials were reused on-site as far as practicable.

Table 6-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
Total generated Inert C&D Materials ('000m ³)	22.756	-	0.089	-
Hard Road and Large Broken Concrete	11.762	-	0	-
Reused in this Contract (Inert) ('000m ³)	10.887	-	0.001	-
Reused in other Projects (Inert) ('000m ³)	0	-	0	-
Disposal as Public Fill (Inert) ('000m ³)	0.107	TKO 137	0.088	TKO 137

Table 6-2 Summary of Quantities of C&D Wastes

Type of Waste	Contract 1		Contract 2	
	Quantity	Disposal Location	Quantity	Disposal Location
Recycled Metal ('000kg)	0	License collector	0	-
Recycled Paper / Cardboard Packing ('000kg)	0	-	0	-
Recycled Plastic ('000kg)	0	-	0	-
Chemical Wastes ('000kg)	0	-	0	-
General Refuses ('000m ³)	0.008	SENT	0.0028	SENT

7. SITE INSPECTION**7.1 REQUIREMENTS**

- 7.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should be carried out to confirm the environmental performance.

7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH**Contract 1**

- 7.2.1 In the Reporting Period, joint site inspection for Contract 1 to evaluate site environmental performance was carried out by the RE, ET and the Contractor on **9, 13, 21 and 27 February 2018** in which IEC joined the site inspection with SSEMC on **9 February 2018**. No non-compliance was noted.
- 7.2.2 The findings / deficiencies of **Contract 1** that observed during the weekly site inspection are listed in **Table 7-1**.

Table 7-1 Site Observations of Contract 1

Date	Findings / Deficiencies	Follow-Up Status
30 January 2018 (last reporting period)	<ul style="list-style-type: none"> General refuse cumulated on site should be cleaned more frequently and housekeeping should be improved. (Reinforcement Area) Diesel cumulated inside the drip tray should be cleared to prevent contamination. (Reinforcement Area) Drip tray should be provided for chemical storage on-site. (West Portal) 	<ul style="list-style-type: none"> General refuse cumulated on site was removed. Diesel cumulated inside the drip tray was removed. Drip tray was provided for chemical storage on-site.
9 February 2018	<ul style="list-style-type: none"> The Contractor was reminded that water spraying should be provided for all breaking works on site to reduce dust generation. 	<ul style="list-style-type: none"> Not required for reminder.
13 February 2018	<ul style="list-style-type: none"> C&D waste and general refuse scattered on site was observed. Housekeeping should be improved and waste generated on site should be disposed properly. (East Portal) 	<ul style="list-style-type: none"> C&D waste and general refuse scattered on site was cleared.
21 February 2018	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection. 	<ul style="list-style-type: none"> NA.
27 February 2018	<ul style="list-style-type: none"> Earth bund for the temporary drainage was damaged. Maintenance for the earth bund should be conducted and ensure all turbid water should be diverted to de-silting facilities for proper treatment prior discharge. (Q3) Drip tray should be provided for oil drums storage on-site. (West Portion) 	<ul style="list-style-type: none"> To be followed. To be followed.

Contract 2

- 7.2.3 In the Reporting Period, joint site inspection for Contract 2 to evaluate site environmental performance was carried out by the RE, ET and the Contractor on **7, 13, 23 and 26 February 2018** in which IEC joined the site inspection with SSEMC on **26 February 2018**. No non-compliance was noted.

- 7.2.4 The findings / deficiencies of **Contract 2** that observed during the weekly site inspection are listed in **Table 7-2**.

Table 7-2 Site Observations of Contract 2

Date	Findings / Deficiencies	Follow-Up Status
31 January 2018 (last reporting period)	<ul style="list-style-type: none"> Chemical container on bare ground was observed. The Contractor was advised to provide drip tray underneath or remove it. 	<ul style="list-style-type: none"> Chemical containers were removed from site area.
7 February 2018	<ul style="list-style-type: none"> The Contractor was reminded to cover stockpile properly after working hours at portion 4. 	<ul style="list-style-type: none"> Not required for reminder.
13 February 2018	<ul style="list-style-type: none"> Water bucket without cover was observed. The Contractor was advised to cover the bucket to prevent mosquito breeding. (portion 1) Felled tree was observed cumulated on site. The Contractor was advised to remove the felled tree properly. (portion 2) General refuse was observed inside the U-channel. The Contractor was advised to clean it properly. (portion 2) As a reminder, the Contractor should replace damaged sandbags regularly to avoid dust impact. 	<ul style="list-style-type: none"> Water bucket was removed. Felled tree was removed. General wastes were removed. Not required for reminder.
23 February 2018	<ul style="list-style-type: none"> As a reminder, the Contractor should remove stagnant water after rainstorm regularly. 	<ul style="list-style-type: none"> Not required for reminder.
26 February 2018	<ul style="list-style-type: none"> Generator without drip tray was observed at Portion 2. The Contractor should provide drip tray for the generator to contain any leaked chemical and avoid land contamination. 	<ul style="list-style-type: none"> The Contractor confirmed that generator was not in use.

Other Contracts

- 7.2.5 Since Contract 3 has not yet commenced, no site inspection was performed in the Reporting Period.

8. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE**8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION**

8.1.1 In the Reporting Period, three (3) environmental complaints were received for Contract 1 in respect with the construction noise concerned by the nearby resident and the complaint details are summarized below.

- (a) On 2 February 2018, a public complaint was received by SPRO regarding construction noise of heard at Chi Tat House of On Tai Estate on 1 February 2018. AECOM has liaised with the complainant immediately and ad-hoc noise measurement for Leq(30min) at the corridor of 22/F of Chi Tai House on 2 February 2018 facing the construction site. The ad-hoc measurement noise result was below the Limit Level under the EM&A programme. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. To eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate, such as maintain good site practices such as intermittent use of machine and plant and Sequencing operation of construction plant equipment. Investigation Report for the complaint has been submitted by the ET with no further comment by IEC.
- (b) On 2 February 2018, a public complaint was received by SPRO regarding disturbing noise heard at Shing Tat House on 1 February 2018. AECOM has liaised with the complainant immediately and it was reported that the noise was generated until 7:00pm on 1 February 2018. Investigation for the complaint was conducted by ET accordingly. It was advised that there was breaking works at Underground Stormwater Retention Tank (USRT) which opposite to Shing Tat House carried out from 8:00 to 18:00 and breaking works at System A was extended to 19:00 on 1 February 2018. As noise mitigation measures, noise barriers were erected for the works area. Further to the complaint case, CWSTVJV would seek for other quiet work method such as using drilling machine to reduce noise level and speed up the rock breaking process, so that to reduce the noise intensity level and the duration of exposure. Investigation Report for the complaint has been submitted by the ET with no further comment by IEC.
- (c) On 28 February 2018, a public complaint was received by EPD regarding construction noise of rock breaking heard at Shing Tat House. The investigation report is under reviewed by IEC.

8.1.2 The complaint log and Investigation Report for the above complaint is shown in [Appendix M](#).

8.1.3 In the Reporting Period, no summons and prosecution under the EM&A Programme was lodged for the project. The statistical summary table of environmental complaint is presented in **Tables 8-1, 8-2 and 8-3**.

Table 8-1 Statistical Summary of Environmental Complaints

Reporting Period	Contract no.	Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 April –31 Jan 2018	1	0	22	Dust, Noise and light nuisance
1 April –31 Jan 2018	2	0	0	NA
1 – 28 Feb 2018	1	3	25	Noise
1 – 28 Feb 2018	2	0	0	NA

Table 8-2 Statistical Summary of Environmental Summons

Reporting Period	Contract no.	Environmental Summons Statistics		
		Frequency	Cumulative	Summons Nature
1 April –31 Jan 2018	1	0	0	NA
1 April –31 Jan 2018	2	0	0	NA
1 – 28 Feb 2018	1	0	0	NA
1 – 28 Feb 2018	2	0	0	NA

Table 8-3 Statistical Summary of Environmental Prosecution

Reporting Period	Contract no.	Environmental Prosecution Statistics		
			Cumulative	Prosecution Nature
1 April –31 Jan 2018	1	0	0	NA
1 April –31 Jan 2018	2	0	0	NA
1 – 28 Feb 2018	1	0	0	NA
1 – 28 Feb 2018	2	0	0	NA

The Other Contracts

- 8.1.4 Since Contract 3 has not yet commenced, no environmental complaint, summons and prosecution are received in the Reporting Period.

9. IMPLEMENTATION STATUS OF MITIGATION MEASURES**9.1 GENERAL REQUIREMENTS**

- 9.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in [Appendix L](#).
- 9.1.2 All contracts under the Project shall be implementing the required environmental mitigation measures according to the approved EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented in this Reporting Period are summarized in **Table 9-1**.

Table 9-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> Wastewater to be treated by filtration system; such as, silt curtain or sedimentation tank before discharge. Replace silt curtain materials if necessary
Air Quality	<ul style="list-style-type: none"> Maintain damp / wet surface on access road Keep slow speed in the sites All vehicles must use wheel washing facility before off site All vehicles must use wheel washing facility before off site Sprayed water during breaking works
Noise	<ul style="list-style-type: none"> Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. Keep good maintenance of plants Place noisy plants away from residence or school Provide noise barriers or hoarding to enclose the noisy plants or works Shut down the plants when not in used.
Waste and Chemical Management	<ul style="list-style-type: none"> On-site sorting prior to disposal Follow requirements and procedures of the “Trip-ticket System” Predict required quantity of concrete accurately Collect the unused fresh concrete at designated locations in the sites for subsequent disposal
General	<ul style="list-style-type: none"> The site was generally kept tidy and clean.

9.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 9.2.1 Construction activities for Contract 1 in the coming month are listed below:
- Pedestrian Connectivity System B:
 - Commence piling works at the South Lift Tower
 - Internal Road L1 and Road L3:
 - Continue excavation of the internal road L1 adjacent to Pedestrian Connectivity System B
 - Continue construction of the box culvert BC1 CHA156.019 to CHA168.019 (Bay #14) after clarification of reinforcement according to RFI issued
 - Commence excavation of the box culvert BC2 CHB108 to CHB128 (Bay #10 to 11) along the internal road L3
 - Excavate for DP1350
 - West Portal, East Portal and Underpass Tunnel:
 - Continue slope cut at slope A3 and A4
 - Continue excavation of tunnel face from West Portal from CH.2392 heading to

- CH.2518
 - Continue diversion of CLP's 11kV cables at East Portal
- iv. Water Pumping Station including Retaining Wall RWA13 and RWA14:
 - Continue excavation at Water Pumping Station area
 - Continue construction of base slabs of retaining wall RWA13
 - Continue excavation works diversion of CLP's underground cables
 - Continue construction of blinding layers of retaining wall RWA14
- v. Portion A3:
 - Continue excavation for site formation
- vi. Portion A4:
 - Continue defect corrections according to the pre-inspection
- vii. Portion B8 and KW Asphalt Plant:
 - Continue backfilling and compacting
- viii. Portion B15:
 - Continue demolition of the KWP Crushing plant and Batching Plant
- ix. Underground Stormwater Retention Tank (USRT):
 - Continue open-cut excavation for the underground stormwater retention tank
 - Continue temporary soil nailing works
 - Continue construction of base slabs
- xvii. Internal Road L4 Pedestrian Connectivity System A, RWA12 and RWA18:
 - Continue rock backfilling alongside noise barrier bay #25 to 1
 - Continue excavation for retaining wall RWA12 bay #22
 - Continue excavation of retaining wall RWA18 bay #5 to 1
 - Continue construction of a temporary haul road to retaining wall RWA12 bay #17 to 22
 - Construct base slabs of retaining wall RWA12 and RWA18
 - Construct a new cascade
- x. PTT:
 - Commence the pile loading test after confirmation of raking piles
- xi. Rock Slope Survey and Slope Stabilization at Portion B1:
 - Commence drilling works for raking drainage and continue installation of protective mats at slope feature 11NE-D/C998
 - ◆ Continue grouting works at CH320 to CH370 of slope feature 11NE-D/C998
 - ◆ Continue drilling works for rock dowels at CH150 to CH225 slope feature 11NE-D/C998 and slope A16
 - ◆ Continue erection of inspection scaffold for slope feature 11NE-D/C999 for CH310 to CH320, CH335 to CH345 and CH347 to CH357 at 230mPD to 250mPD
 - ◆ Continue installation of protective mats at slope feature 11NE-D/C1004
- xii. Establishment Works of the Planting Medium on the Existing Slope Berms in Portion B1 and B5:
 - Continue establishment works at existing berms on slopes in Portion B1 for 9-month establishment works for landscape softworks under establishment schedule no.1
 - Continue establishment works at existing berms on slopes in Portion B1 for 17-month establishment works for landscape softworks under establishment schedule no.2
 - Continue establishment works on slopes in Portion B1 for 30-month establishment works for landscape softworks under establishment schedule no.3

- xiii. Mitigation Works for Natural Terrain Catchment B5:
 - Commence construction of drainage and slope works
- xiv. Road Improvement Works at Po Lam Road:
 - Commence excavation to expose underground utilities at Phase 1A and excavation of the trial pit at Phase 1B
- xv. Land Contamination – Ground Investigation:
 - Continue drilling works and installation of a monitoring well for ground investigation at BH05, BH10 and BH11

9.2.2 Construction activities for Contract 2 in the coming month are listed below:

1. Portion 1: Continue piling work. Complete tree pruning in order to facilitate the piling works at E1-RS1. Commence preparation for sheet piling installation at E1-PC2 and E1 –PC6.
2. Portion 2: Commence piling works; Complete to erect hoarding and rock fall temporary. Commence rock slope excavation.
3. Portion 4: Continue the slip road construction and commence temporary road diversion.
4. Portion 5: Complete sheet piling installation. Complete UU ground settlement markers. Complete tree transplant work, Commence covered walkway construction;
5. Portion 6: Continue Rock dowel installation work. Carry out removal of existing EPD fence. Carry out inspection pit to locate existing water mains;
6. Portion 7: Complete hiking trail extension in Site A. Commence slope improvement work in Site B;
7. Portion 8 & 9: Carry out soil nail head construction works. Carry out trial pits for baffle works

9.3 KEY ISSUES FOR THE COMING MONTH

9.3.1 Key issues to be considered in the coming month include:

- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Discharge of site effluent to the nearby wetland, stockpiling or disposal of materials, and any dredging or construction area at this area are prohibited;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures

10. CONCLUSIONS AND RECOMMENDATIONS

10.1 CONCLUSIONS



- 10.1.1 This is **11th** monthly EM&A report presenting the monitoring results and inspection findings for the Reporting Period from **1** to **28 February 2018**.
- 10.1.2 No 24-hour or 1-hour TSP monitoring results that triggered the Action or Limit Levels were recorded. No NOEs or the associated corrective actions were therefore issued.
- 10.1.3 In the Reporting Period, no construction noise measurement results that exceeded the Limit Level were recorded. However, three (3) noise complaints (which triggered Action Level) were recorded for Contract 1 and investigations for the complaints have been conducted by ET and the details could be referred to the complaint section.
- 10.1.4 No notification of summons or successful prosecution was received under the Project.
- 10.1.5 In the Reporting Period, three (3) environmental complaints were received for Contract 1 in respect with the construction noise concerned by the nearby resident and investigations for the complaints have been conducted by ET. Investigation reports revealed that the Contractor had implemented noise mitigation measures to eliminate to noise nuisance to the public and the construction works were carried out within the non-restricted hours. It is considered that the works under the project did not breach the Noise Control Ordinance. Nevertheless, in view of the subject site of the project is close to the residential area, the Contractor was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.
- 10.1.6 During the Reporting Period, weekly joint site inspection by the RE, ET with the relevant Main-contractor was carried out for Contracts 1 and 2 in accordance with the EM&A Manual stipulation whereas IEC performed monthly site inspection for both contracts. No non-compliance observed during the site inspection.

10.2 RECOMMENDATIONS

- 10.2.1 Special attention should be paid on the potential construction dust impact since most of the construction sites are adjacent to resident. The Contractor should fully implement the construction dust mitigation measures properly, particularly in coming dry season.
- 10.2.2 Moreover, muddy water and other water quality pollutants via site surface water runoff get into public areas should be avoided. Mitigation measures for water quality should be properly implemented.
- 10.2.3 Construction noise should be a key environmental impact during the works. The noise mitigation measures such as use of quiet plants or temporary noise barrier installation at the construction noise predominate area should be implemented as accordance with the EM&A requirement.
- 10.2.4 Mosquito control measures should be continued to prevent mosquito breeding on site.

Appendix A


Layout plan of the Project

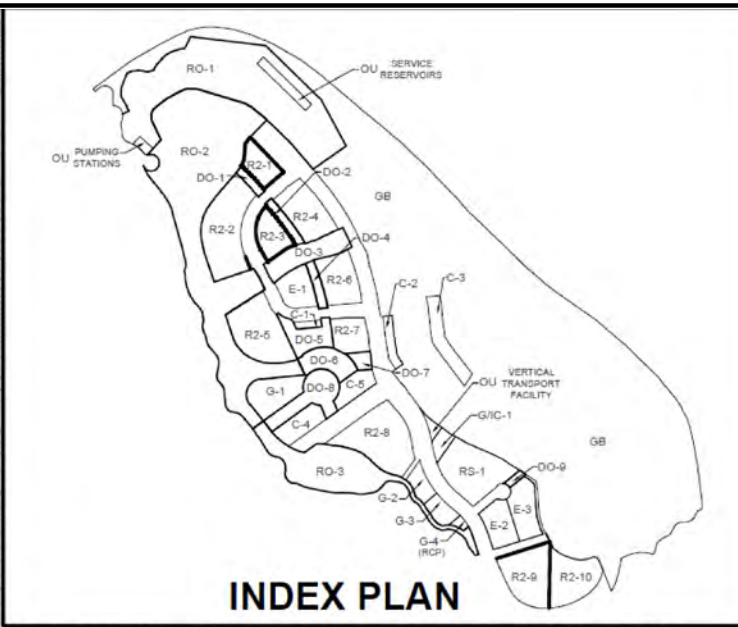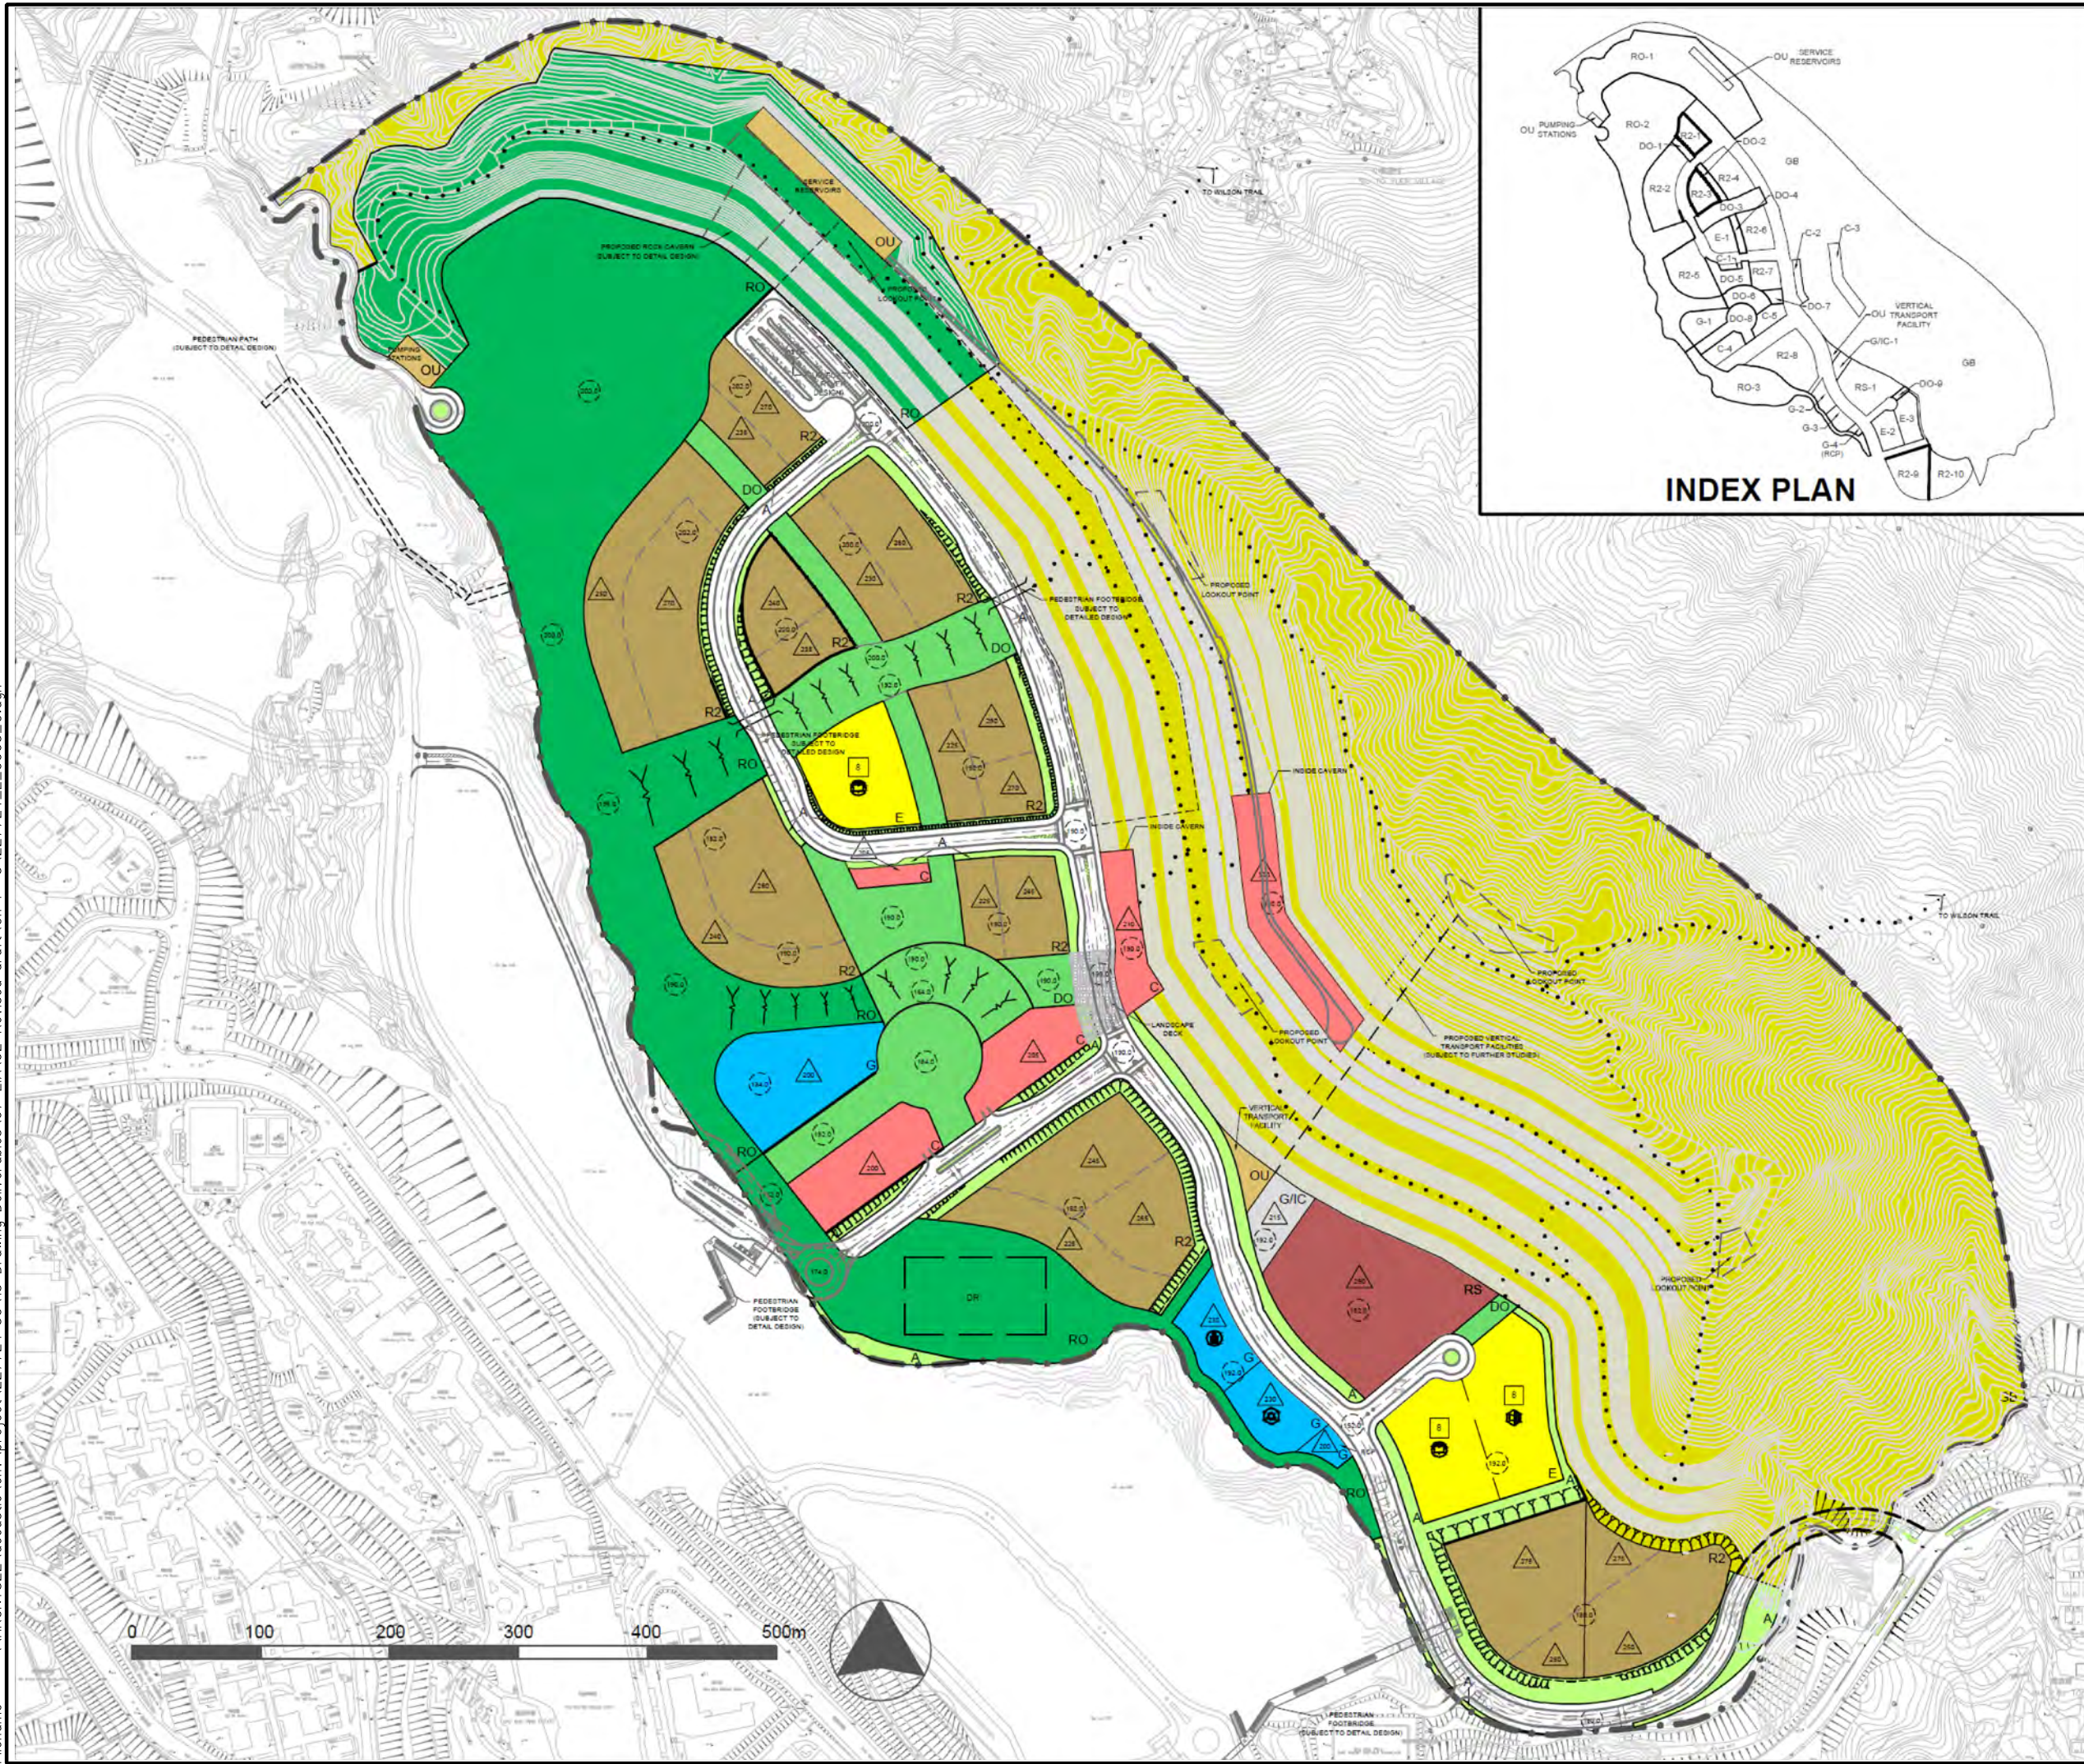


LEGEND

- POLICE STATION
- DIVISIONAL FIRE STATION
- SECONDARY SCHOOL
- PRIMARY SCHOOL
- PUBLIC TRANSPORT TERMINUS
- PLANNING BOUNDARY
- UNDERPASS
- PROPOSED PEDESTRIAN TRAIL
- PEDESTRIAN PRECINCT
- DRAINAGE RESERVE
- MAXIMUM BUILDING HEIGHT (in m above PD)
- MAXIMUM BUILDING HEIGHT (in storeys)
- PROPOSED LEVEL (in m above PD)
- PROPOSED SLOPE
- REFUSE COLLECTION POINT
- FOOTBRIDGE
- COMMERCIAL
- SPECIAL RESIDENTIAL
- RESIDENTIAL ZONE-2
- GOVERNMENT
- GOVERNMENT/ INSTITUTION OR COMMUNITY
- EDUCATION
- REGIONAL OPEN SPACE
- DISTRICT OPEN SPACE
- AMENITY
- OTHER SPECIFIED USES
- GREEN BELT
- ROADS, JUNCTIONS, ETC.
- AREA WITH POTENTIAL FOR ROCK CAVERN DEVELOPMENT


C	THIRD ISSUE	GL	03/14
B	SECOND ISSUE	GL	01/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Recommended Outline Development Plan			
Drawing no.		Rev.	
227724/E/0003		C	
Drawn	Date	Checked	Approved
GL	03/14	TC	ST
Scale	Status		
AS SHOWN	PRELIMINARY		
COPYRIGHT RESERVED			
土木工程拓展署 Civil Engineering and Development Department			

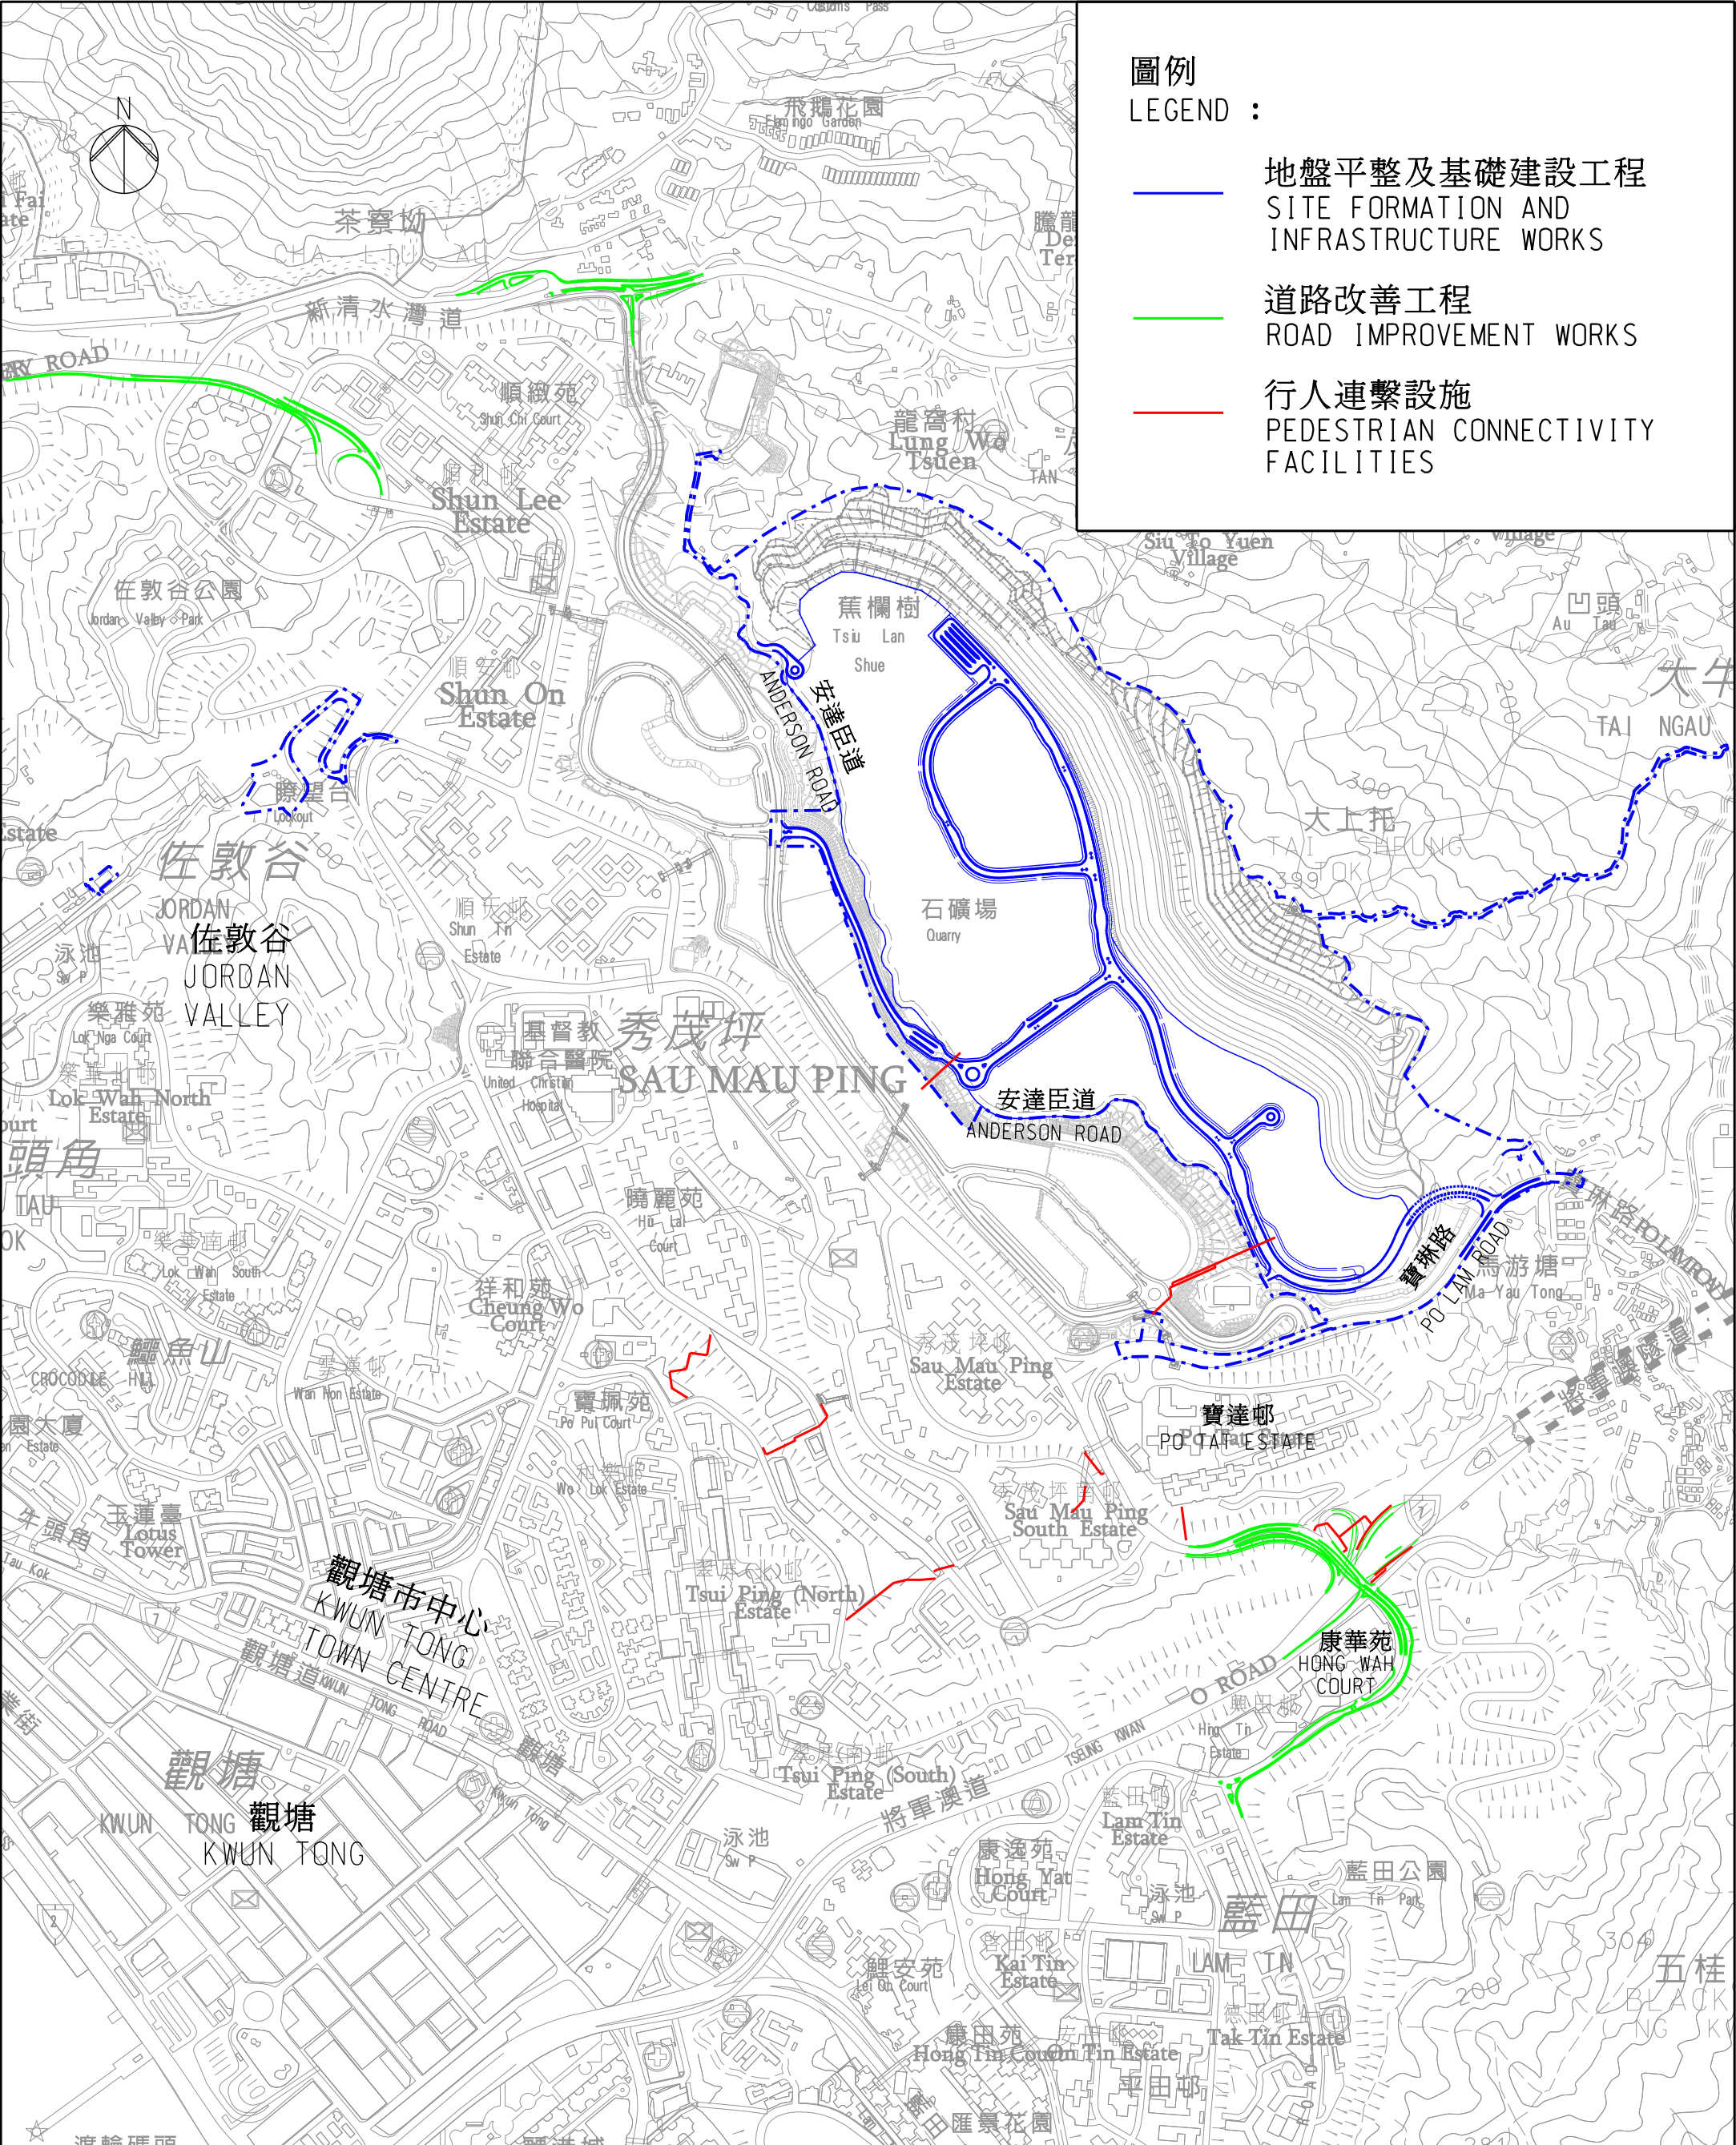

圖則名稱 drawing title 安達臣道石礦場發展工程位置圖 DEVELOPMENT OF ANDERSON ROAD QUARRY SITE PROJECT LOCATION PLAN	繪圖 drawn H K TSANG	簽署initial 日期date 23.3.16	項目編號 item no.	辦事處 office 新界東拓展處 NEW TERRITORIES EAST DEVELOPMENT OFFICE
	核對 checked L M CHAN	簽署initial 日期date 23.3.16	比例 scale 1:10 000 @ A3	
	核准 approved T S LI	簽署initial 日期date 23.3.16	圖則編號 drawing no. CDEARQZ0003	 土木工程拓展署 CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT

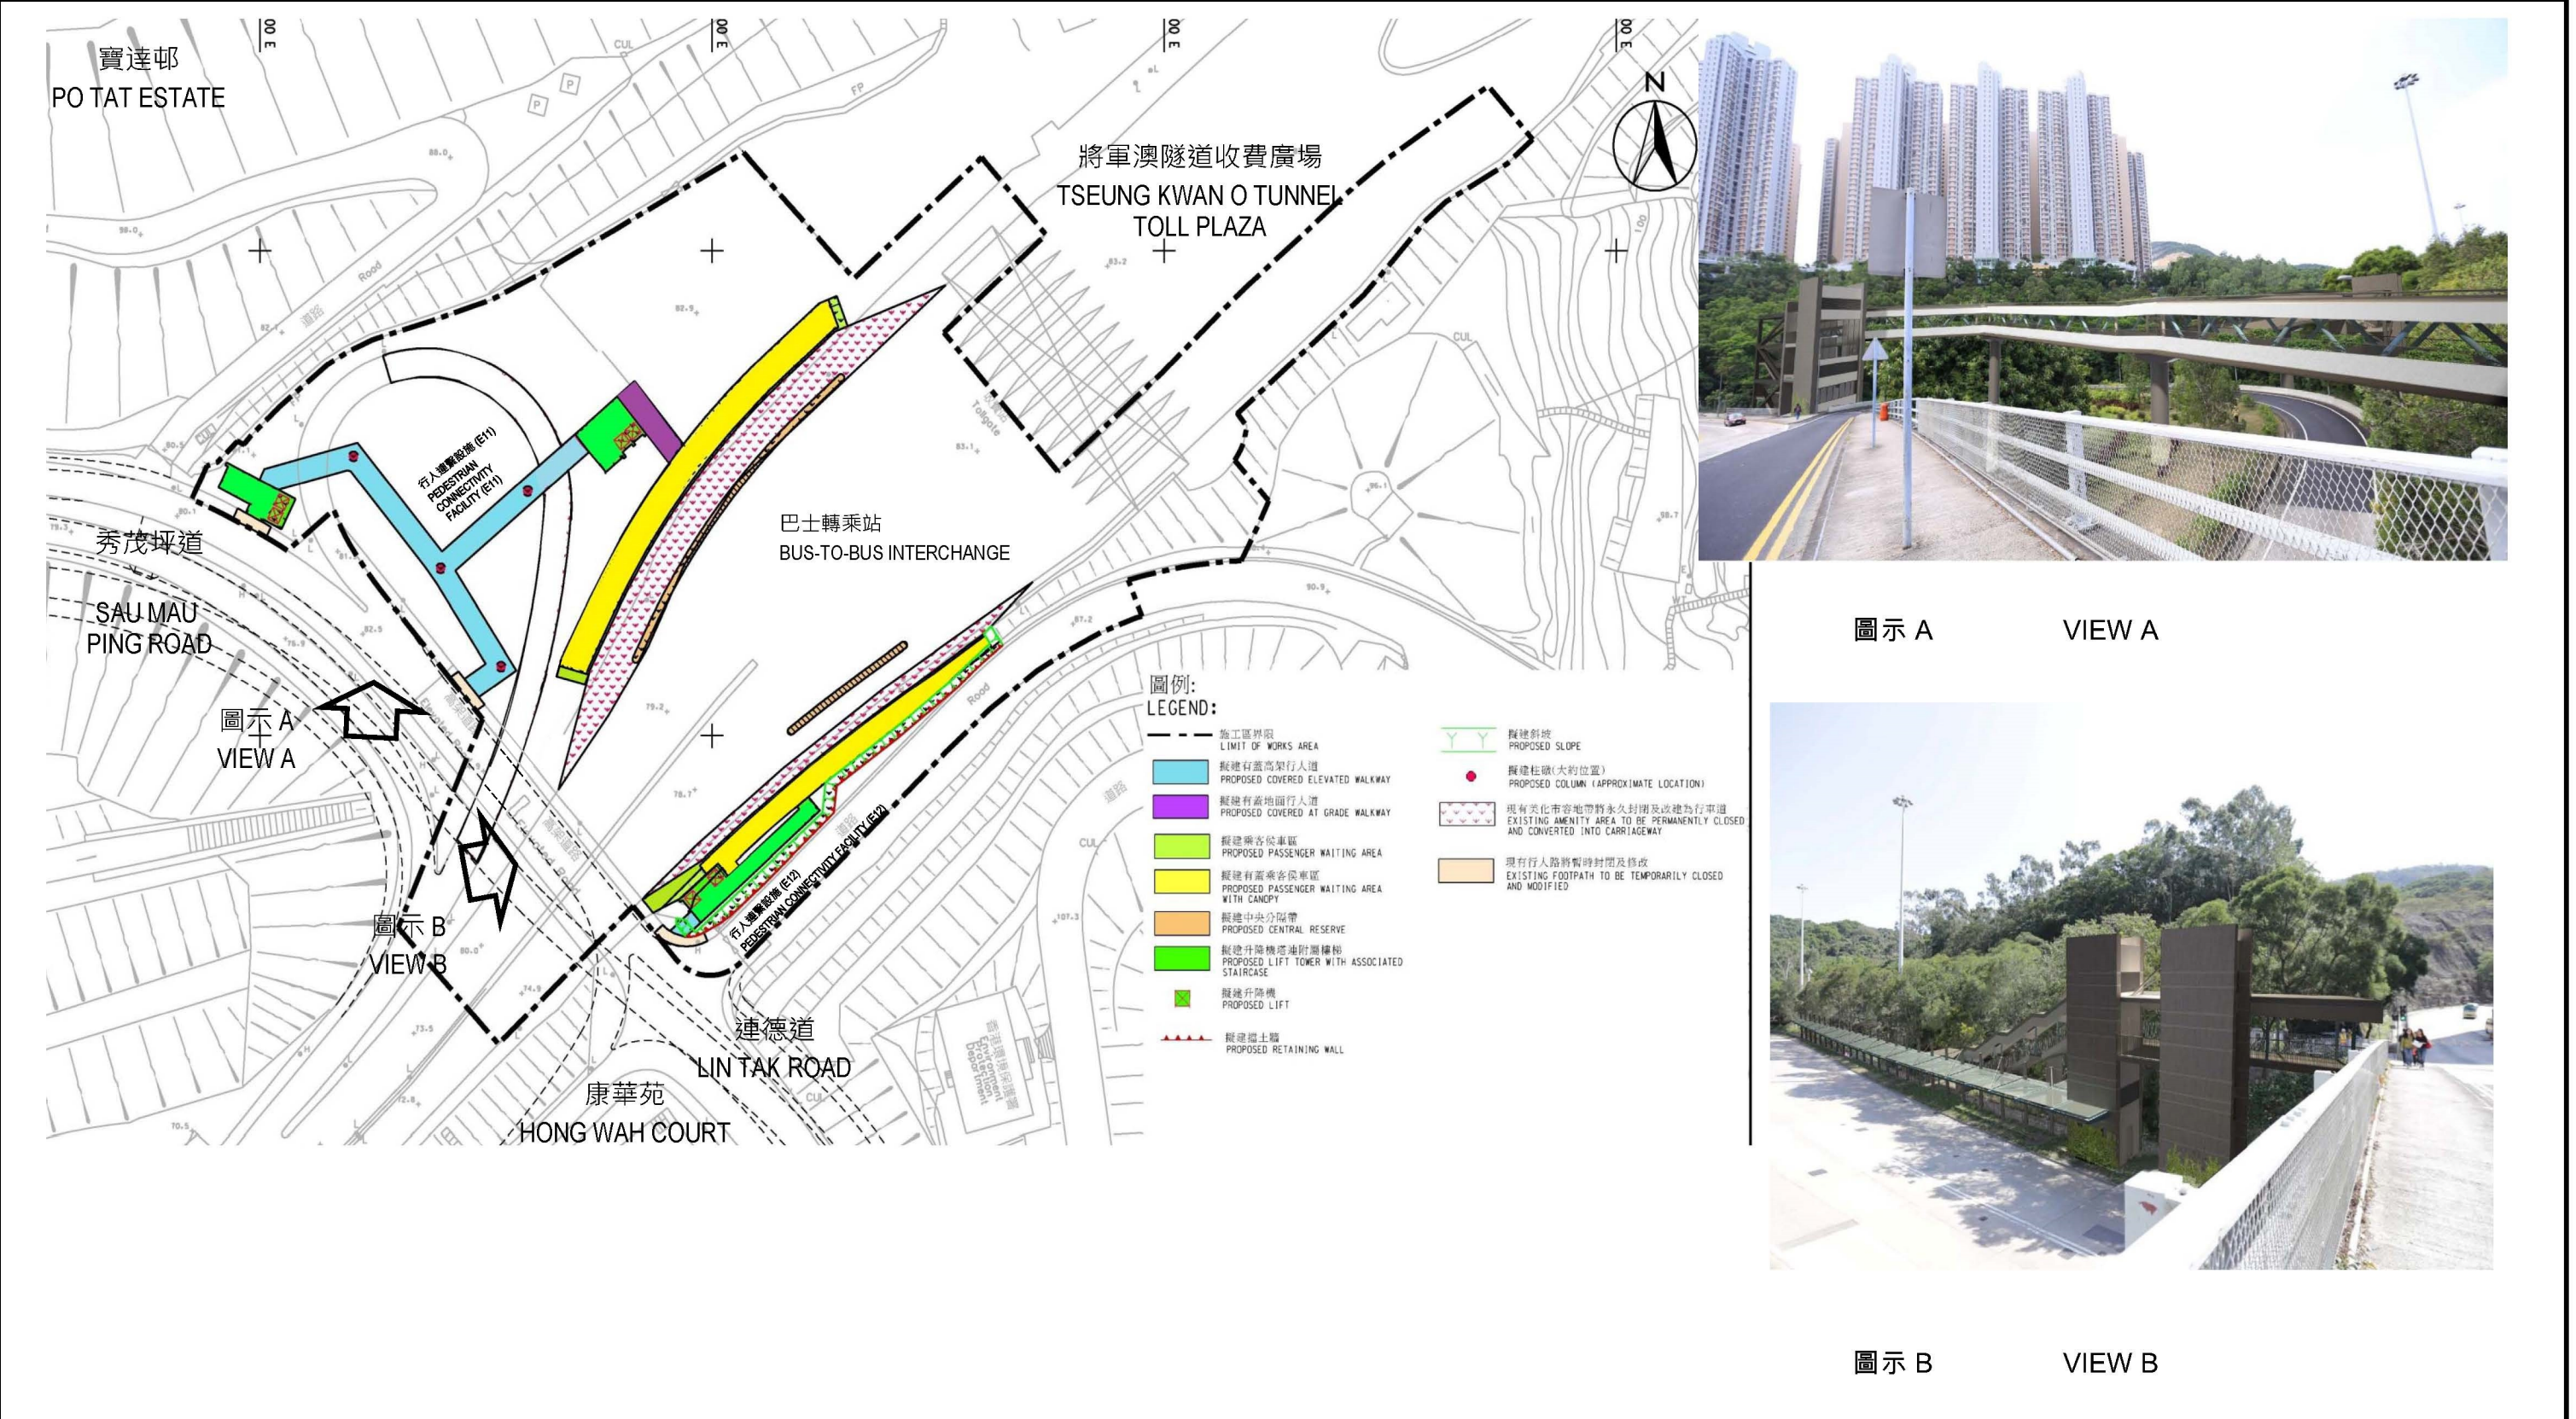

圖則名稱 Drawing Title	項目編號 Item No.	辦事處 Office 新界東拓展處 NEW TERRITORIES EAST DEVELOPMENT OFFICE
	765CL	
	比例 Scale	
行人連繫設施(巴士轉乘站、E11及E12) - 平面圖及構思圖 Pedestrian Connectivity Facilities (Bus-to-Bus Interchange, E11 and E12) - Layout Plan and Artist's Impression	圖則編號 Drawing No.	 土木工程拓展署 CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT
	附件五 Appendix 5	

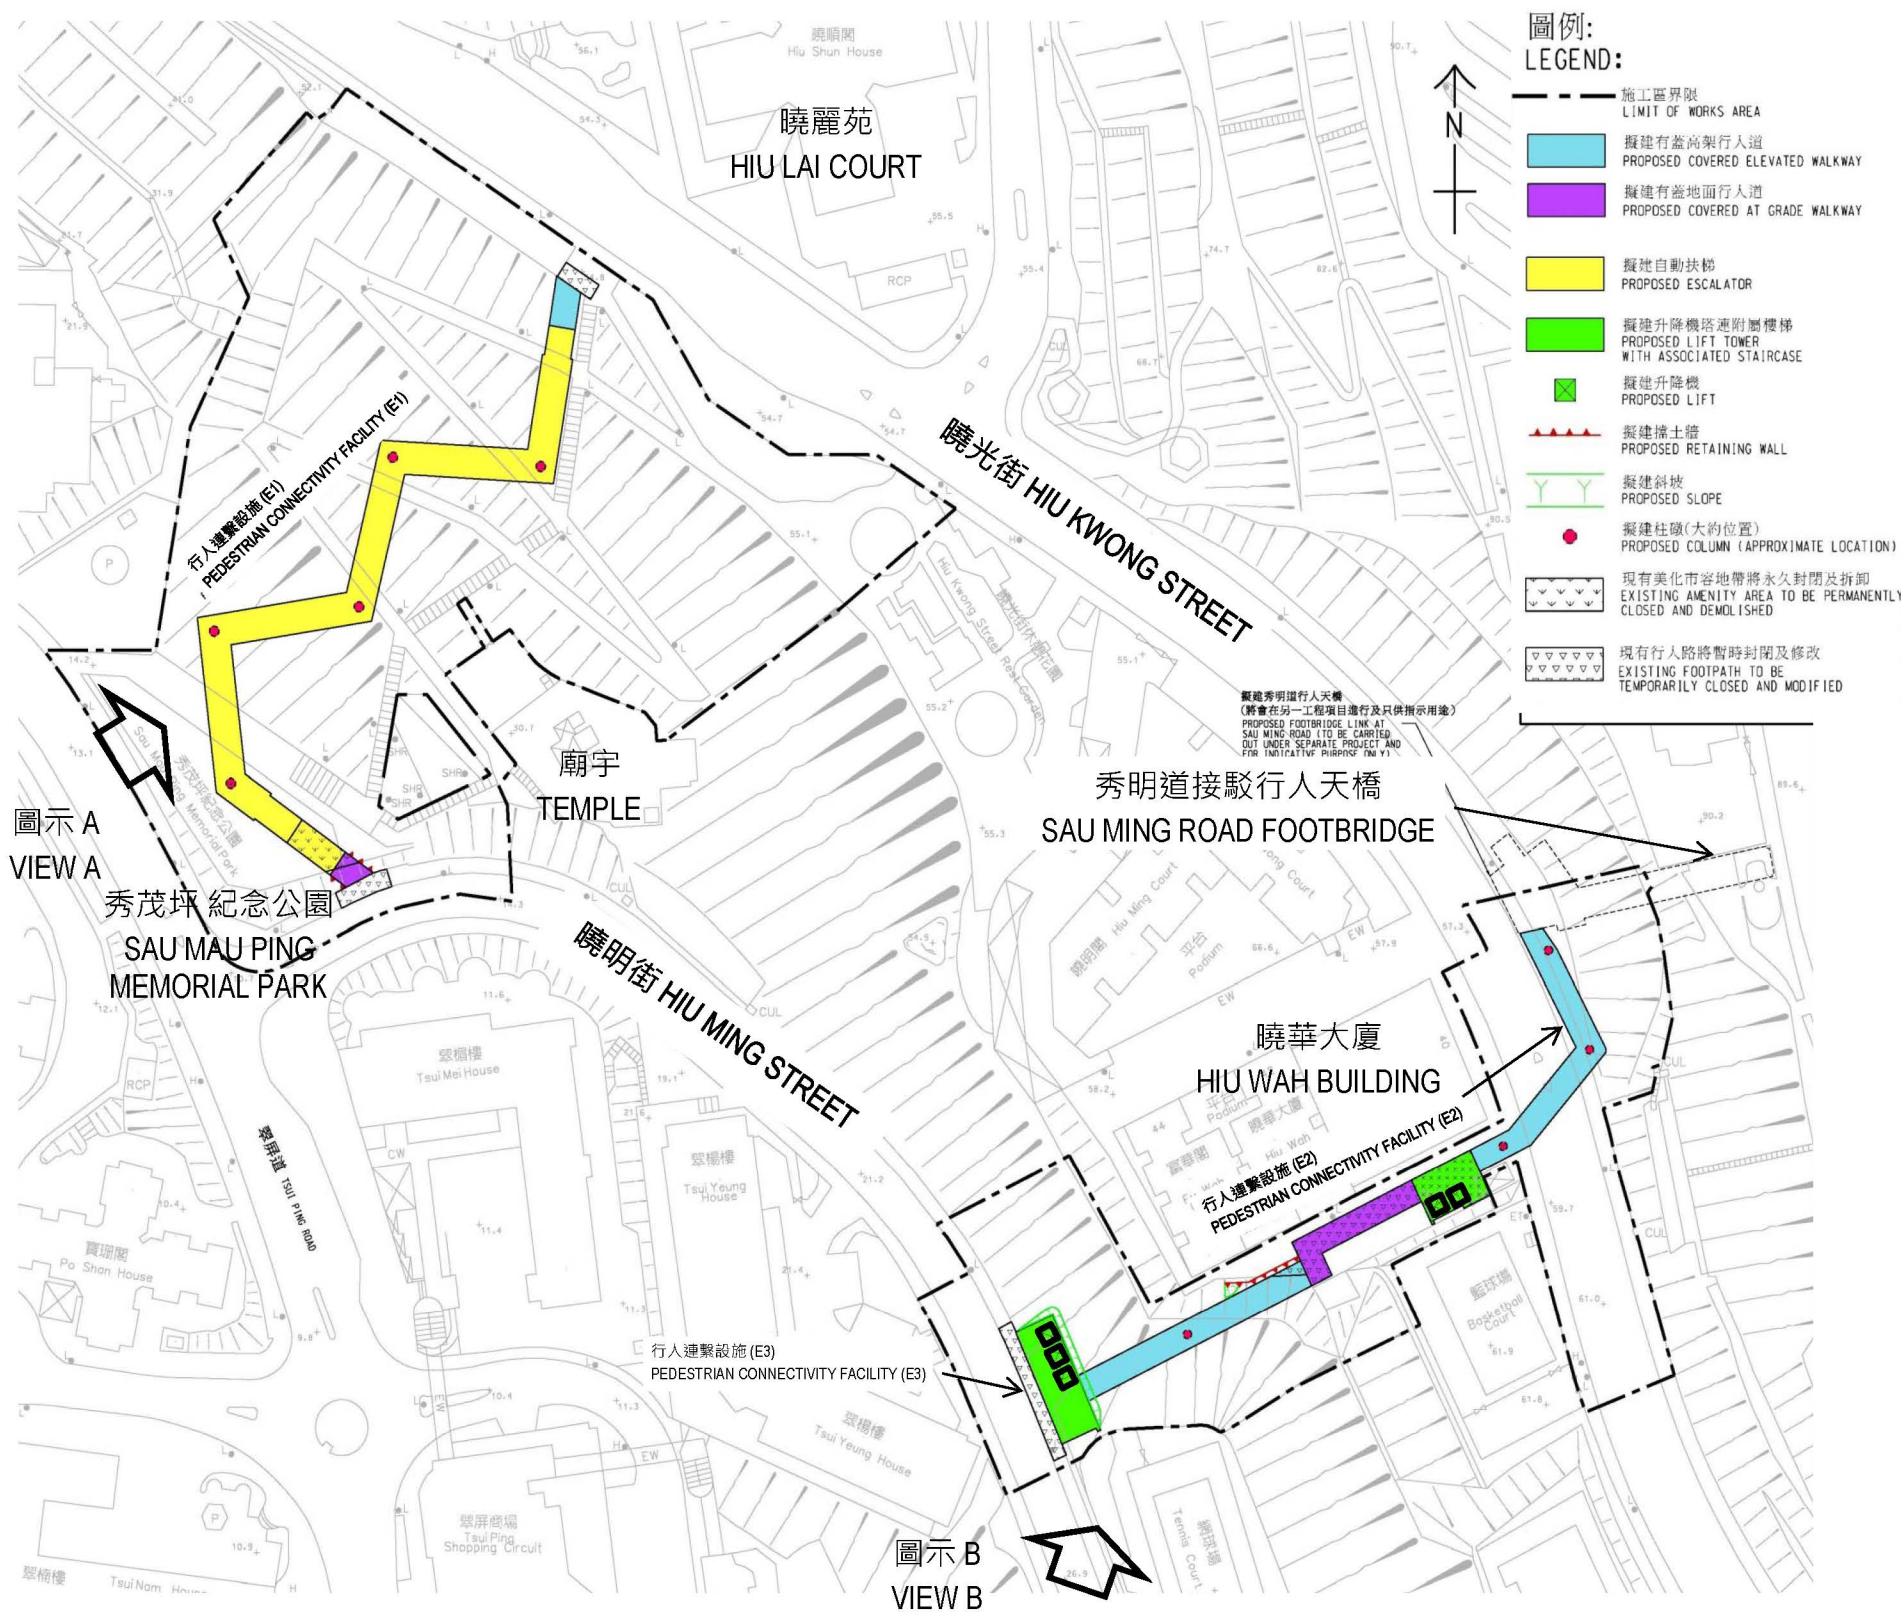


圖則名稱 Drawing Title 行人連繫設施(E1、E2及E3) - 平面圖及構思圖 Pedestrian Connectivity Facilities (E1, E2 and E3) - Layout Plan and Artist's Impression	項目編號 Item No. 765CL	辦事處 Office 新界東拓展處 NEW TERRITORIES EAST DEVELOPMENT OFFICE 土木工程拓展署 CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT
	比例 Scale	
	圖則編號 Drawing No. 附件二 Appendix 2	

Appendix B

Organization Chart

Project Organization Structure for

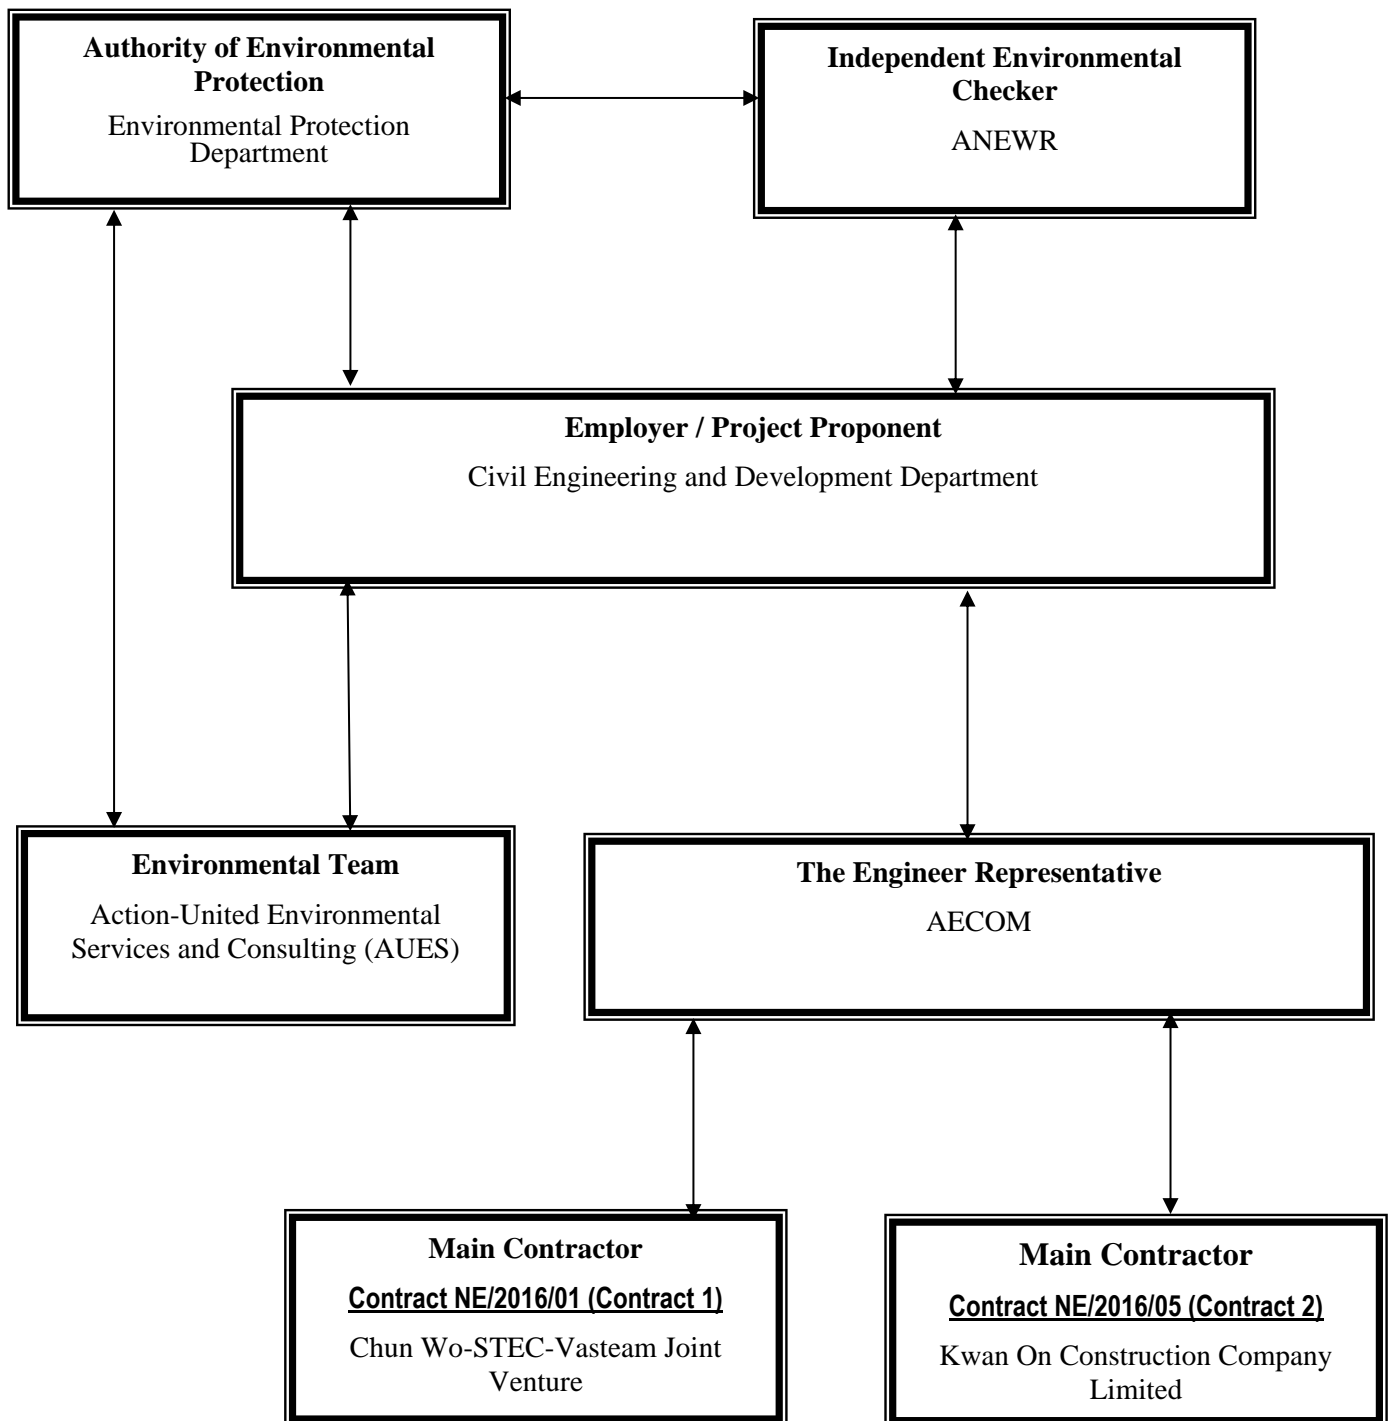

Contact Details of Key Personnel for Contract 1 – NE/2016/01

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Stephen Li	2301 1383	2739 0076
AECOM	Chief Resident Engineer	Dennis Leung	2967 6608	2473 3221
AECOM	Senior Resident Engineer	Simon Leung	2967 6608	2473 3221
ANEWR	Independent Environmental Checker	Adi Lee	2618 2836	3007 8648
CSVJV	Project Manager	William Leung	2638 7181	2744 6937
CSVJV	Site Agent	TY Leung	2638 7181	2744 6937
CSVJV	Project Environmental Manager	Shelton Chan	2638 7181	2744 6937
CSVJV	Environmental Officer	Kiwi Chan	2638 7181	2744 6937
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:

CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

CSVJV (Main Contractor) – Chun Wo-STECC-Vasteam Joint Venture

ANEWR (IEC) – ANewR Consulting Limited

AUES (ET) – Action-United Environmental Services & Consulting

Contact Details of Key Personnel for Contract 2 – NE/2016/05

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Stephen Li	2301 1383	2739 0076
AECOM	Chief Resident Engineer	Dennis Leung	2967 6608	2473 3221
AECOM	Senior Resident Engineer	Simon Leung	2967 6608	2473 3221
ANEWR	Independent Environmental Checker	Adi Lee	2618 2836	3007 8648
KOCCL	Project Director	Ambrose Kwong	2889 2675	2558 6900
KOCCL	Site Agent	Antony Kwok	2898 8510	2558 6900
KOCCL	Safety and Environmental Manager	Joly C K Kwong	6111 5711	2558 6900
KOCCL	Environmental Officer	Fung Hiu Lam, Purvi	6395 3685	2558 6900
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:

CEDD (Employer) – Civil Engineering and Development Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

KOCCL (Main Contractor) –Kwan On Construction Company Limited

ANEWR (IEC) –ANewR Consulting Limited

AUES (ET) – Action-United Environmental Services & Consulting

Appendix C

Construction Programme


- (a) Contract 1 (NE/2016/01)**
- (b) Contract 2 (NE/2016/05)**

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>				CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME										Page 1 of 14 23 Feb 2018					
Activity ID		Activity Name		BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018			Qtr 2, 2018					
											Jan	Feb		Mar		Apr		May	
ARQ - Works Programme Rev.1 - 3MRP (15 Feb 2018)																			
Project Key Dates																			
Key Dates for Completion of Sections of the Works																			
AKC1010		KD1 - Completion of Section I of the Works - Portion A4		0	0		23-Feb-18		23-Feb-18*	0%				◆ KD1 - Completion of Section I of the Works - Portion A4, 23-Feb-18*					
Possession Periods																			
AKP1220		Date for Possession of the Portion C1c		0	0	24-Jan-18		16-Feb-18*		0%	16-Feb-18* ◆			◆ Date for Possession of the Portion C1c,					
AKP1270		Date for Possession of the Portion E1		0	0	25-Dec-16		16-Feb-18*		0%				◆ Date for Possession of the Portion E1,					
Preliminary																			
Design																			
Alternative Design (AD)																			
PTT (Changing from Bored Piles to Socket H Piles and Pile Cap/Tie Beam Thickness)																			
APD1040		Preparation and Submission of Detailed Design Drawings to ICE Certification		30	230	07-Jul-17	10-Aug-17	16-May-17 A	20-Feb-18	98%				▮ Preparation and Submission of Detailed Design Drawings to ICE Certification					
APD1050		ICE Certification to Detailed Design Drawings of PTT		0	0		10-Aug-17		20-Feb-18	0%				◆ ICE Certification to Detailed Design Drawings of PTT, 20-Feb-18					
Noise Barriers (Re-design of Footings) at Road L4																			
APD2040		Preparation and Submission of Detailed Design Drawings to ICE Certification		30	309	29-May-17	04-Jul-17	06-Feb-17 A	20-Feb-18	98%				▮ Preparation and Submission of Detailed Design Drawings to ICE Certification					
APD2050		ICE Certification to Detailed Design Drawings of Nosie Barriers		0	0		04-Jul-17		20-Feb-18	0%				◆ ICE Certification to Detailed Design Drawings of Nosie Barriers, 20-Feb-18					
Excavation Permit (XP)																			
On Sau Road (Junction between Road L4 and On Sau Road)																			
APF1020		HyD Review Application of XP for Road Improvement at Junction between Road L4 and On Sau Road in Portion C1a		180	284	26-May-17	21-Nov-17	26-May-17 A	05-Mar-18	90%			■ HyD Review Application of XP for Road Improvement at Junction between Road L4 and On Sau Road in Portion C1a						
APF1030		HyD Approval of Application of XP for Road Improvement at Junction between Road L4 and On Sau Road in Portion C1a		0	0		21-Nov-17		05-Mar-18	0%				◆ HyD Approval of Application of XP for Road Improvement at Junction between Road L4 and On Sau Road in Portion C1a, 05-Mar-18					
Portion C1c																			
APF1170		HyD Review Application of XP for Waterworks in Portion C1c		180	92	01-Aug-17	27-Jan-18	04-Dec-17 A	05-Mar-18	90%			■ HyD Review Application of XP for Waterworks in Portion C1c						
APF1180		HyD Approval of Application of XP for Waterworks in Portion C1c		0	0		27-Jan-18		05-Mar-18	0%				◆ HyD Approval of Application of XP for Waterworks in Portion C1c, 05-Mar-18					
Temporary Traffic Arrangement and Control																			
On Sau Road (Junction between Road L4 and On Sau Road)																			
APT2030		Commencement of Implementation of TTA at Junction between Road L4 and On Sau Road (Road Improvement Works)		0	0	22-Nov-17		06-Mar-18		0%				◆ Commencement of Implementation of TTA at Junction between Road L4 and On Sau Road (Road Improvement Works),					
Portion C1c																			
APT4010		Submission and Review of Temporary Traffic Arrangement (TTA) Scheme for Portion C1c		75	75	28-Jan-18	12-Apr-18	06-Mar-18	19-May-18	0%			■						
Land Contamination - Ground Investigation																			
Portion B7/B12/B15 (BH-01 to BH-11)																			
APL1020		Start Date of Land Contamination Ground Investigation in Portion B7,B12 and B15		0	0	23-Aug-17		17-Jan-18 A		100%	◆								
APL1030A001		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH06		0	3			17-Jan-18 A	19-Jan-18 A	100%	■								
APL1030A002		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH09		0	3			22-Jan-18 A	24-Jan-18 A	100%	■								
APL1030A003		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH05		0	6			26-Feb-18*	03-Mar-18	0%			■ Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH05						
APL1030A004		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH08		0	5			24-Jan-18 A	29-Jan-18 A	100%	■								
APL1030A005		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH04		0	4			12-Feb-18 A	15-Feb-18 A	100%	■								
APL1030A006		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH07		0	23			20-Jan-18 A	15-Feb-18 A	100%	■								
APL1030A007		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH10		0	5			05-Mar-18	09-Mar-18	0%			■ Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH10						
APL1030A008		Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH11		0	5			12-Mar-18*	16-Mar-18	0%			■ Drilling Work and Monitoring Well Instrumentation for Ground Investigation idf BH11						
APL1040		Land Contamination Assessment and Submission of Contamination Action Report (CAR) to AECOM/EPD		28	28	30-Sep-17	04-Nov-17	17-Mar-18	23-Apr-18	0%			■ Land Contamination Assessment and S						
Ground Investigation																			
APG1110		Subnmisison and Approval of Ground Investigation Report for Pedestrian Connectivity System B in Portion C1b		21	234	01-Jun-17	24-Jun-17	10-May-17 A	20-Feb-18	98%			▮ Subnmisison and Approval of Ground Investigation Report for Pedestrian Connectivity System B in Portion C1b						
APG1120		Subnmisison and Approval of Ground Investigation Report for Pedestrian Connectivity System A in Portion B5		21	270	22-Mar-17	19-Apr-17	22-Mar-17 A	20-Feb-18	98%			▮ Subnmisison and Approval of Ground Investigation Report for Pedestrian Connectivity System A in Portion B5						
<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>				<div><div>■ Planned Bar (WP)</div><div>■ Actual Bar</div><div>■ Forecast Bar</div><div>◆ ◆ Planned Milestone (WP)</div></div>						3-MONTH ROLLING PROGRAMME (In comparison with WP Rev.1 dated 25 Aug 2017)						ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017			
										Date		Revision		Checked		Approved			
										23-Feb-18		3MRP Rev.1 (Cut Off on 15 Feb 18)							

<div><div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN Wo - STEC - VASTEAM JOINT VENTURE</div></div></div></div>				CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME										Page 2 of 14 23 Feb 2018			
Activity ID		Activity Name		BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018		Qtr 2, 2018				
											Jan	Feb	Mar	Apr	May		
APG1130		Subnmision and Approval of Ground Investigation Report for Pedestrian Connectivity System A in Portion C1a		21	121	24-Aug-17	16-Sep-17	21-Sep-17 A	20-Feb-18	98%			Submission and Approval of Ground Investigation Report for Pedestrian Connectivity System A in Portion C1a				
APG1140		Subnmision and Approval of Ground Investigation Report for PTT		21	246	05-Aug-17	29-Aug-17	24-Apr-17 A	20-Feb-18	98%			Submission and Approval of Ground Investigation Report for PTT				
ARQ - MEP Submission (Updated 31 Jan 2018)																	
General Submission																	
A1000		Submission and Approval for E&M Statutory Submission		0	24			19-Dec-17 A	18-Jan-18 A	100%							
A1029		Submission and Approval for Professional Indemnity Insurance (PI) for Designer		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Professional Indemnity Insurance (PI) for Designer				
A1030		Submission and Approval for Professional Indemnity Insurance (PI) for Independent Checking Engineer-R0		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Professional Indemnity Insurance (PI) for Independent Checking Engineer-R0				
A1031		Submission and Approval for Professional Indemnity Insurance (PI) for Independent Checking Engineer-R1		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Professional Indemnity Insurance (PI) for Independent Checking Engineer-R1				
A1050		Submission and Approval for Nomination of E&M Engineer (Pumping Station)-R1		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Nomination of E&M Engineer (Pumping Station)-R1				
A1140		Submission and Approval for Nomination of Designer		0	74			20-Nov-17 A	20-Feb-18	95%			Submission and Approval for Nomination of Designer				
A1170		Submission and Approval for Independent Test Laboratory of PE Pipe-R1		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Independent Test Laboratory of PE Pipe-R1				
A1180		Submission and Approval for Gate Valve and Sluice Valve		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Gate Valve and Sluice Valve				
A1190		Submission and Approval for 300&100 uPVC for Gravity Sewerage and Storm Water Pipes at Natural Terrain		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for 300&100 uPVC for Gravity Sewerage and Storm Water Pipes at Natural Terrain				
A1200		Submission and Approval for E-Co Ductile Iron Pipe and Fittings		0	103			16-Oct-17 A	21-Feb-18	95%			Submission and Approval for E-Co Ductile Iron Pipe and Fittings				
A1210		Submission and Approval for Mild Steel Pipes and Fittings		0	21			20-Feb-18*	15-Mar-18	0%			Submission and Approval for Mild Steel Pipes and Fittings				
Fresh and Salt Water Pumping Station																	
Mechanical																	
A1320		Submission and Approval for Material of High Head Pump Set at Fresh Water Pumping Station		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Material of High Head Pump Set at Fresh Water Pumping Station				
A1330		Submission and Approval for Material of High Head Pump Set at Salt Water Pumping Station		0	14			09-Apr-18*	24-Apr-18	0%			Submission and Approval for Material of High Head Pump Set at Salt Water Pumping Station				
Underground Stormwater Retention Tank																	
MVAC																	
A2460		Submission and Approval for Design of MVAC at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of MVAC at USRT				
A2470		Submission and Approval for Material of MVAC at USRT		0	14			23-Apr-18*	09-May-18	0%			Submission and Approval for Material of MVAC at USRT				
Fire Services																	
A2600		Submission and Approval for Design of FSS at USRT		0	14			08-Mar-18*	23-Mar-18	0%			Submission and Approval for Design of FSS at USRT				
A2610		Submission and Approval for Material of FSS at USRT		0	14			08-Mar-18*	23-Mar-18	0%			Submission and Approval for Material of FSS at USRT				
Mechanical																	
A2620		Submission and Approval for Material of SS Cages, Flap Valves, Stoplogs, Guide Rails and Roller Shutter at USRT		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Material of SS Cages, Flap Valves, Stoplogs, Guide Rails and Roller Shutter at USRT				
Electrical																	
A2480		Submission and Approval for Design of Power Supply System at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of Power Supply System at USRT				
A2490		Submission and Approval for Design of Electrical Works at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of Electrical Works at USRT				
A2500		Submission and Approval for Design of Earthing and Lightning Protection System at USRT		0	14			17-Mar-18*	06-Apr-18	0%			Submission and Approval for Design of Earthing and Lightning Protection System at USRT				
A2510		Submission and Approval for Design of Motor Control Centre at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of Motor Control Centre at USRT				
A2520		Submission and Approval for Design of Capacitor and Panel at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of Capacitor and Panel at USRT				
A2540		Submission and Approval for Design of Photovoltaic System at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of Photovoltaic System at USRT				
A2550		Submission and Approval for Design of Small Power and ELV at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Design of Small Power and ELV at USRT				
A2560		Submission and Approval for Material of Motor Control Centre at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Material of Motor Control Centre at USRT				
A2570		Submission and Approval for Material of Capacitor and Panel at USRT		0	14			03-Apr-18*	19-Apr-18	0%			Submission and Approval for Material of Capacitor and Panel at USRT				
A2590		Submission and Approval for Material of Photovoltaic System at USRT		0	14			22-Feb-18*	09-Mar-18	0%			Submission and Approval for Material of Photovoltaic System at USRT				
Pedestrian Connectivity System A																	
Passenger Lift																	
A2690		Submission and Approval for Design of Lift Service System at SYS-A and SYS-B		0	14			20-Feb-18*	07-Mar-18	0%			Submission and Approval for Design of Lift Service System at SYS-A and SYS-B				
A2700		Submission and Approval for Contractor's Design Shop Drawings at SYS-A and SYS-B		0	15			31-Jan-18 A	21-Feb-18	90%			Submission and Approval for Contractor's Design Shop Drawings at SYS-A and SYS-B				

<div><div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN Wo - STEC - VASTEAM JOINT VENTURE</div></div></div></div>				<div><div>Planned Bar (WP)</div><div>Actual Bar</div><div>Forecast Bar</div><div>Planned Milestone (WP)</div><div>Milestone</div></div>				3-MONTH ROLLING PROGRAMME (In comparison with WP Rev.1 dated 25 Aug 2017)				ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017			
		Date		Revision		Checked		Approved							
		23-Feb-18		3MRP Rev.1 (Cut Off on 15 Feb 18)											

<div><div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 3 of 14 23 Feb 2018				
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018			Qtr 2, 2018		
									Jan	Feb	Mar	Apr	May	
A2710	Submission and Approval for Material/ Sample of Lift System at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Material/ Sample of Lift System at SYS-A and SYS-B			
A2720	Submission and Approval for Galvanized Steel Conduit at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Galvanized Steel Conduit at SYS-A and SYS-B			
A2730	Submission and Approval for Hall Position with 16x120 dot matrix at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Hall Position with 16x120 dot matrix at SYS-A and SYS-B			
A2740	Submission and Approval for Intercom System at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Intercom System at SYS-A and SYS-B			
A2750	Submission and Approval for Water Tight 2-way Switch 10A at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Water Tight 2-way Switch 10A at SYS-A and SYS-B			
A2760	Submission and Approval for Lift Shaft Lighting at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Lift Shaft Lighting at SYS-A and SYS-B			
A2770	Submission and Approval for LSOH Power Cable at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for LSOH Power Cable at SYS-A and SYS-B			
A2780	Submission and Approval for Water Tight 3-pin 13A at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Water Tight 3-pin 13A at SYS-A and SYS-B			
A2790	Submission and Approval for Metal Trunking and Cover (Screw Type) at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Metal Trunking and Cover (Screw Type) at SYS-A and SYS-B			
A2800	Submission and Approval for Emergency Stop Switch at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Emergency Stop Switch at SYS-A and SYS-B			
A2810	Submission and Approval for Adptor Box at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Adptor Box at SYS-A and SYS-B			
A2820	Submission and Approval for Flexible Conduit and Fittings at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Flexible Conduit and Fittings at SYS-A and SYS-B			
A2830	Submission and Approval for Alarm Sounder at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Alarm Sounder at SYS-A and SYS-B			
A2840	Submission and Approval for Car Position Indicator Dot Matrix at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Car Position Indicator Dot Matrix at SYS-A and SYS-B			
A2850	Submission and Approval for Anchor Bolt at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Anchor Bolt at SYS-A and SYS-B			
A2860	Submission and Approval for Floating Switch at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Floating Switch at SYS-A and SYS-B			
A2870	Submission and Approval for Signal Cable at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Signal Cable at SYS-A and SYS-B			
A2880	Submission and Approval for Battery Charger at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Battery Charger at SYS-A and SYS-B			
A2890	Submission and Approval for Push Button at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Push Button at SYS-A and SYS-B			
A2900	Submission and Approval for Ventilation Fan at SYS-A and SYS-B	0	14			20-Feb-18*	07-Mar-18	0%			<div></div> Submission and Approval for Ventilation Fan at SYS-A and SYS-B			
Common for All Areas														
MVAC														
A2970	Submission and Approval for Material of MVAC Thermal Insulation at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
Fire Services														
A3070	Submission and Approval for Material of Manual Fire Alarm System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3080	Submission and Approval for Material of Manual Fire Alarm Control at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3090	Submission and Approval for Material of Battery and Charger at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
Electrical														
A2990	Submission and Approval for Material of Main Power Supply and Distribution System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3000	Submission and Approval for Material of LV Power Cables and Associated Cabling Facilities at Common Areas	0	1			19-Feb-18 A	21-Feb-18	90%	<div></div>		<div></div> Submission and Approval for Material of LV Power Cables and Associated Cabling Facilities at Common Areas			
A3010	Submission and Approval for Material of Cables Containments at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3020	Submission and Approval for Material of Earthing and Lightning Protection System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3030	Submission and Approval for Material of Sub-main Power Distribution System at Common Areas	0	50			18-Dec-17 A	21-Feb-18	90%	<div></div>		<div></div> Submission and Approval for Material of Sub-main Power Distribution System at Common Areas			
A3040	Submission and Approval for Material of Lighting System at Common Areas	0	50			18-Dec-17 A	21-Feb-18	90%	<div></div>		<div></div> Submission and Approval for Material of Lighting System at Common Areas			
A3050	Submission and Approval for Material of Lighting Control Panel at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3051	Submission and Approval for Method Statement for measuring of Soil Resistivity	0	11			05-Feb-18 A	21-Feb-18	90%	<div></div>	<div></div>	<div></div> Submission and Approval for Method Statement for measuring of Soil Resistivity			
A3060	Submission and Approval for Material of Switches,Power Socket Outlets and Ass. Lighting and Power at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3210	Submission and Approval for Material of CCTV at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3220	Submission and Approval for Material of Intercom System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3230	Submission and Approval for Material of Telephone System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3240	Submission and Approval for Material of Security System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3250	Submission and Approval for Material of Radio System at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
A3260	Submission and Approval for Material of ELV Cable at Common Areas	0	14			09-Apr-18*	24-Apr-18	0%				<div></div> Submission and Approval for Material		
<div><div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div><div><div><div>Planned Bar (WP)</div><div>Actual Bar</div><div>Forecast Bar</div><div>Planned Milestone (WP)</div></div><div>◆ ◆ Milestone</div></div><div>3-MONTH ROLLING PROGRAMME (In comparison with WP Rev.1 dated 25 Aug 2017)</div></div>									ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017					
									Date	Revision		Checked	Approved	
									23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)				



俊和 - 上隧 - 浩隆聯營
CHUN WO - STec - VASTEAM JOINT VENTURE

Planned Bar (WP) ◆ ◆ Milestone

Actual Bar

Forecast Bar


◆ Planned Milestone (WP)

3-MONTH ROLLING PROGRAMME

(In comparison with WP Rev.1 dated 25 Aug 2017)

ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017

Date	Revision	Checked	Approved
23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)		



俊和 - 上隧 - 浩隆聯營

CHUN WO - STEC - VASTEAM JOINT VENTURE

Planned Bar (WP)

Actual Bar

Forecast Bar

◆ ◆ Milestone

◆ Planned Milestone (WP)

3-MONTH ROLLING PROGRAMME

(In comparison with WP Rev.1 dated 25 Aug 2017)

ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017

Date	Revision	Checked	Approved
23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)		

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 6 of 14 23 Feb 2018										
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018			Qtr 2, 2018								
									Jan	Feb	Mar	Apr	May							
ACU3010A04	10th Cycle (CH2412 to CH2414) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)	0	1			29-Mar-18	30-Mar-18	0%				<div>10th Cycle (CH2412 to CH2414) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)</div>								
	10th Cycle (CH2412 to CH2414) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support	0	1			30-Mar-18	31-Mar-18	0%				<div>10th Cycle (CH2412 to CH2414) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support</div>								
	11th Cycle (CH2414 to CH2416) - Survey Setting Out and Drilling for Cut Hole/ Non-Cut Hole (102mm Dia.)	0	4			31-Mar-18	04-Apr-18	0%				<div>11th Cycle (CH2414 to CH2416) - Survey Setting Out and Drilling for Cut Hole (102mm Dia.)</div>								
	11th Cycle (CH2414 to CH2416) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole	0	2			04-Apr-18	06-Apr-18	0%				<div>11th Cycle (CH2414 to CH2416) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole</div>								
	11th Cycle (CH2414 to CH2416) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking	0	2			06-Apr-18	08-Apr-18	0%				<div>11th Cycle (CH2414 to CH2416) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking</div>								
	11th Cycle (CH2414 to CH2416) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)	0	1			08-Apr-18	09-Apr-18	0%				<div>11th Cycle (CH2414 to CH2416) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)</div>								
	11th Cycle (CH2414 to CH2416) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support	0	1			09-Apr-18	10-Apr-18	0%				<div>11th Cycle (CH2414 to CH2416) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support</div>								
	12th Cycle (CH2416 to CH2418) - Survey Setting Out and Drilling for Cut Hole/ Non-Cut Hole (102mm Dia.)	0	4			10-Apr-18	14-Apr-18	0%				<div>12th Cycle (CH2416 to CH2418) - Survey Setting Out and Drilling for Cut Hole (102mm Dia.)</div>								
	12th Cycle (CH2416 to CH2418) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole	0	2			14-Apr-18	16-Apr-18	0%				<div>12th Cycle (CH2416 to CH2418) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole</div>								
	12th Cycle (CH2416 to CH2418) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking	0	2			16-Apr-18	18-Apr-18	0%				<div>12th Cycle (CH2416 to CH2418) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking</div>								
	12th Cycle (CH2416 to CH2418) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)	0	1			18-Apr-18	19-Apr-18	0%				<div>12th Cycle (CH2416 to CH2418) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)</div>								
	12th Cycle (CH2416 to CH2418) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support	0	1			19-Apr-18	20-Apr-18	0%				<div>12th Cycle (CH2416 to CH2418) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support</div>								
	13th Cycle (CH2418 to CH2420) - Survey Setting Out and Drilling for Cut Hole/ Non-Cut Hole (102mm Dia.)	0	4			20-Apr-18	24-Apr-18	0%				<div>13th Cycle (CH2418 to CH2420) - Survey Setting Out and Drilling for Cut Hole (102mm Dia.)</div>								
	13th Cycle (CH2418 to CH2420) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole	0	2			24-Apr-18	26-Apr-18	0%				<div>13th Cycle (CH2418 to CH2420) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole</div>								
	13th Cycle (CH2418 to CH2420) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking	0	2			26-Apr-18	28-Apr-18	0%				<div>13th Cycle (CH2418 to CH2420) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking</div>								
	13th Cycle (CH2418 to CH2420) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)	0	1			28-Apr-18	29-Apr-18	0%				<div>13th Cycle (CH2418 to CH2420) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)</div>								
	13th Cycle (CH2418 to CH2420) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support	0	1			29-Apr-18	30-Apr-18	0%				<div>13th Cycle (CH2418 to CH2420) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support</div>								
	14th Cycle (CH2420 to CH2422) - Survey Setting Out and Drilling for Cut Hole/ Non-Cut Hole (102mm Dia.)	0	4			30-Apr-18	04-May-18	0%				<div>14th Cycle (CH2420 to CH2422) - Survey Setting Out and Drilling for Cut Hole (102mm Dia.)</div>								
	14th Cycle (CH2420 to CH2422) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole	0	2			04-May-18	06-May-18	0%				<div>14th Cycle (CH2420 to CH2422) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole</div>								
	14th Cycle (CH2420 to CH2422) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking	0	2			06-May-18	08-May-18	0%				<div>14th Cycle (CH2420 to CH2422) - Drilling for Tunnel Crown (76mm Dia.) and Rock Breaking</div>								
	14th Cycle (CH2420 to CH2422) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)	0	1			08-May-18	09-May-18	0%				<div>14th Cycle (CH2420 to CH2422) - Rock Scaling for Underbreak Zone and Rock Mapping for Temporary Support (CATIII)</div>								
	14th Cycle (CH2420 to CH2422) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support	0	1			09-May-18	10-May-18	0%				<div>14th Cycle (CH2420 to CH2422) - Drill, Install and Gout Rock Dowels (46mm Dia.) incl. Shotcrete for Temporary Support</div>								
	15th Cycle (CH2422 to CH2424) - Survey Setting Out and Drilling for Cut Hole/ Non-Cut Hole (102mm Dia.)	0	4			10-May-18	14-May-18	0%				<div>15th Cycle (CH2422 to CH2424) - Survey Setting Out and Drilling for Cut Hole (102mm Dia.)</div>								
	15th Cycle (CH2422 to CH2424) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole	0	2			14-May-18	16-May-18	0%				<div>15th Cycle (CH2422 to CH2424) - Rock Breaking for Non-cut Hole (102mm Dia.) and Insert Wedge into Non-cut Hole</div>								
Pedestrian Connectivity System A																				
Lift Tower (North) and Subway within Portion B5																				
ACS1020	B5 - Construction of Pre-Bored H-Piles (66nos) of Lift Tower (4 days/pile/plant by 2 plants)	132	132	21-Nov-17	05-May-18	23-Apr-18	29-Sep-18	0%	<div></div>											
Lift Tower (South) and Subway within Portion C1a																				
ACS1090	C1a - Construction of Pre-Bored H-Piles (48nos) of Lift Tower (3 days/pile/plant, assume 2 rigs)	144	72	18-Sep-17	14-Mar-18	23-Apr-18	20-Jul-18	0%	<div></div>											
Pedestrian Connectivity System B																				
Lift Tower (South) and Subway within Portion C1b																				
ACS2110	C1b - Excavation for Pedestrian Connectivity System B (South)	90	78	07-Jul-17	21-Oct-17	20-Nov-17 A	24-Feb-18	95%	<div>C1b - Excavation for Pedestrian Connectivity System B (South)</div>											
ACS2120	C1b - Construction of Pre-bored H-Piles (55nos) of Lift Tower (2.5days/pile/plant) by 1 workfront	110	140	23-Oct-17	07-Mar-18	24-Feb-18*	16-Aug-18	0%	<div></div>											
Underground Stormwater Retention Tank (Portion A1)																				
ACN1010	A1 - Excavation (Open Cut) of Underground Stormwater Tank	201	254	02-May-17	30-Dec-17	10-May-17 A	14-Mar-18	90%	<div>A1 - Excavation (Open Cut) of Underground Stormwater Tank</div>											
ACN1010A006	A1 - Drilling and Grouting for Temporary soil Nails AF11 to AF22 (11 nails)	0	24			27-Dec-17 A	24-Jan-18 A	100%												
ACN1010A007	A1 - Drilling and Grouting for Temporary soil Nails AG12 to AG23 (12 nails)	0	16			27-Jan-18 A	14-Feb-18 A	100%												
ACN1010A008	A1 - Drilling and Grouting for Temporary soil Nails AH1 to AH15 (15 nails)	0	7			05-Mar-18*	12-Mar-18	0%	<div>A1 - Drilling and Grouting for Temporary soil Nails AH1 to AH15 (15 nails)</div>											
ACN1010A011	A1 - Blinding Layer for Underground Stormwater Tank - Bay 2 (Zone A)	0	3			27-Jan-18 A	30-Jan-18 A	100%												
ACN1010A015	A1 - Blinding Layer for Underground Stormwater Tank - Bay 6 (Zone A)	0	10			27-Jan-18 A	07-Feb-18 A	100%												
ACN1010A016	A1 - Blinding Layer for Underground Stormwater Tank - Bay 7 (Zone C)	0	19			20-Jan-18 A	10-Feb-18 A	100%												
ACN1010A018	A1 - Blinding Layer for Underground Stormwater Tank - Bay 9 (Zone C)	0	5			20-Jan-18 A	25-Jan-18 A	100%												
ACN1010A019	A1 - Blinding Layer for Underground Stormwater Tank - Bay 10 (Zone A)	0	4			09-Feb-18 A	13-Feb-18 A	100%												
<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>									<div><div><div>Planned Bar (WP)</div><div>Actual Bar</div><div>Forecast Bar</div><div>Planned Milestone (WP)</div><div>Milestone</div></div></div>				3-MONTH ROLLING PROGRAMME (In comparison with WP Rev.1 dated 25 Aug 2017)				ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017			
									Date	Revision	Checked	Approved								
									23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)										

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 7 of 14 23 Feb 2018			
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018		Qtr 2, 2018		
									Jan	Feb	Mar	Apr	May
ACN1010A020	A1 - Blinding Layer for Underground Stormwater Tank - Bay 11 (Zone C)	0	4			07-Mar-18	10-Mar-18	0%			A1 - Blinding Layer for Underground Stormwater tank - Bay 11 (Zone C)		
ACN1010A021	A1 - Blinding Layer for Underground Stormwater Tank - Bay 12 (Zone A)	0	4			09-Feb-18 A	13-Feb-18 A	100%					
ACN1010A022	A1 - Blinding Layer for Underground Stormwater Tank - Bay 13 (Zone C)	0	4			12-Mar-18	15-Mar-18	0%			A1 - Blinding Layer for Underground Stormwater Tank - Bay 13 (Zone C)		
ACN1010A023	A1 - Blinding Layer for Underground Stormwater Tank - Bay 14 (Zone B)	0	4			03-Apr-18	07-Apr-18	0%				A1 - Blinding Layer for Underground Stormwater Tank - Bay 14 (Zone B)	
ACN1010A024	A1 - Blinding Layer for Underground Stormwater Tank - Bay 15 (Zone C)	0	4			02-Mar-18	06-Mar-18	0%			A1 - Blinding Layer for Underground Stormwater Tank - Bay 15 (Zone C)		
ACN1010A025	A1 - Blinding Layer for Underground Stormwater Tank - Bay 16 (Zone B)	0	4			13-Apr-18	17-Apr-18	0%				A1 - Blinding Layer for Underground Stormwater Tank - Bay 16 (Zone B)	
ACN1010A027	A1 - Blinding Layer for Underground Stormwater Tank - Bay 18 (Zone C)	0	4			26-Feb-18*	01-Mar-18	0%			A1 - Blinding Layer for Underground Stormwater Tank - Bay 18 (Zone C)		
ACN1010A028	A1 - Blinding Layer for Underground Stormwater Tank - Bay 19 (Zone B)	0	4			09-Apr-18	12-Apr-18	0%				A1 - Blinding Layer for Underground Stormwater Tank - Bay 19 (Zone B)	
ACN1010A029	A1 - Blinding Layer for Underground Stormwater Tank - Bay 20 (Zone B)	0	4			26-Mar-18	29-Mar-18	0%				A1 - Blinding Layer for Underground Stormwater Tank - Bay 20 (Zone B)	
ACN1010A030	A1 - Blinding Layer for Underground Stormwater Tank - Bay 21 (Zone B)	0	14			06-Jan-18 A	22-Jan-18 A	100%					
ACN1010A031	A1 - Blinding Layer for Underground Stormwater Tank - Bay 22 (Zone B)	0	14			06-Jan-18 A	22-Jan-18 A	100%					
ACN1010A032	A1 - Blinding Layer for Underground Stormwater Tank - Bay 23 (Zone B)	0	4			21-Mar-18	24-Mar-18	0%			A1 - Blinding Layer for Underground Stormwater Tank - Bay 23 (Zone B)		
ACN1010A033	A1 - Blinding Layer for Underground Stormwater Tank - Bay 24 (Zone B)	0	11			10-Jan-18 A	22-Jan-18 A	100%					
ACN1010A034	A1 - Blinding Layer for Underground Stormwater Tank - Bay 25 (Zone B)	0	13			08-Jan-18 A	22-Jan-18 A	100%					
ACN1010A035	A1 - Blinding Layer for Underground Stormwater Tank - Bay 26 (Zone B)	0	4			16-Mar-18	20-Mar-18	0%			A1 - Blinding Layer for Underground Stormwater Tank - Bay 26 (Zone B)		
ACN1010A036	A1 - Blinding Layer for Underground Stormwater Tank - Bay 27 (Zone B)	0	8			13-Jan-18 A	22-Jan-18 A	100%					
ACN1020A001	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 1	0	19			24-Jan-18 A	14-Feb-18 A	100%					
ACN1020A002	A1 - Concrete Pouring of Base Slab for USRT - Bay 1	0	1			20-Feb-18	20-Feb-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 1		
ACN1020A003	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 2	0	7			14-Feb-18 A	24-Feb-18	50%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 2		
ACN1020A004	A1 - Concrete Pouring of Base Slab for USRT - Bay 2	0	1			26-Feb-18	26-Feb-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 2		
ACN1020A005	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 3	0	7			14-Feb-18 A	24-Feb-18	50%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 3		
ACN1020A006	A1 - Concrete Pouring of Base Slab for USRT - Bay 3	0	1			26-Feb-18	26-Feb-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 3		
ACN1020A007	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 4	0	23			26-Jan-18 A	24-Feb-18	50%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 4		
ACN1020A008	A1 - Concrete Pouring of Base Slab for USRT - Bay 4	0	1			26-Feb-18	26-Feb-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 4		
ACN1020A009	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 5	0	10			09-Mar-18	20-Mar-18	0%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 5		
ACN1020A010	A1 - Concrete Pouring of Base Slab for USRT - Bay 5	0	1			21-Mar-18	21-Mar-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 5		
ACN1020A011	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 6	0	7			14-Feb-18 A	24-Feb-18	50%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 6		
ACN1020A012	A1 - Concrete Pouring of Base Slab for USRT - Bay 6	0	1			26-Feb-18	26-Feb-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 6		
ACN1020A013	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 7	0	12			19-Mar-18	04-Apr-18	0%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 7		
ACN1020A014	A1 - Concrete Pouring of Base Slab for USRT - Bay 7	0	1			06-Apr-18	06-Apr-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 7		
ACN1020A015	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 8	0	10			26-Feb-18	08-Mar-18	0%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 8		
ACN1020A016	A1 - Concrete Pouring of Base Slab for USRT - Bay 8	0	1			09-Mar-18	09-Mar-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 8		
ACN1020A017	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 9	0	12			05-Mar-18*	17-Mar-18	0%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 9		
ACN1020A018	A1 - Concrete Pouring of Base Slab for USRT - Bay 9	0	1			19-Mar-18	19-Mar-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 9		
ACN1020A019	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 10	0	10			21-Mar-18	04-Apr-18	0%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 10		
ACN1020A020	A1 - Concrete Pouring of Base Slab for USRT - Bay 10	0	1			06-Apr-18	06-Apr-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 10		
ACN1020A021	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 11	0	10			30-Apr-18	11-May-18	0%				A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 11	
ACN1020A022	A1 - Concrete Pouring of Base Slab for USRT - Bay 11	0	1			12-May-18	12-May-18	0%				A1 - Concrete Pouring of Base Slab for USRT - Bay 11	
ACN1020A023	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 12	0	10			21-Mar-18	04-Apr-18	0%			A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 12		
ACN1020A024	A1 - Concrete Pouring of Base Slab for USRT - Bay 12	0	1			06-Apr-18	06-Apr-18	0%			A1 - Concrete Pouring of Base Slab for USRT - Bay 12		
ACN1020A025	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 13	0	10			12-May-18	24-May-18	0%				A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 13	
ACN1020A029	A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 15	0	10			18-Apr-18	28-Apr-18	0%				A1 - Formwork and Rebar Fixing of Base Slab for USRT - Bay 15	
ACN1020A030	A1 - Concrete Pouring of Base Slab for USRT - Bay 15	0	1			30-Apr-18	30-Apr-18	0%				A1 - Concrete Pouring of Base Slab for USRT - Bay 15	
									ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017				
									Date	Revision		Checked	Approved
									23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)			

TEC

隆道股份

俊和 - 上隧 - 浩隆聯營

CHUN WO - STEC - VASTEAM JOINT VENTURE

Planned Bar (WP)

Actual Bar


Forecast Bar

Planned Milestone (WP)

Milestone

3-MONTH ROLLING PROGRAMME
(In comparison with WP Rev.1 dated 25 Aug 2017)

ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017				
Date	Revision		Checked	Approved
23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)			



俊和 - 上隧 - 浩隆聯營

CHUN WO - STEC - VASTEAM JOINT VENTURE

◆
Planned Milestone (WP)

◆ Milestone


3-MONTH ROLLING PROGRAMME

(In comparison with WP Rev.1 dated 25 Aug 2017)

ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017

Date	Revision	Checked	Approved
23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)		

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 9 of 14 23 Feb 2018				
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018		Qtr 2, 2018			
									Jan	Feb	Mar	Apr	May	
ACW1090	B5 - Back Fill for RWA13	90	30	26-Oct-17	12-Feb-18	19-Mar-18	26-Apr-18	0%	<div></div>					B5 - Back Fill for RWA13
ACW1110	B5 - Cut Down Existing Anderson Road to RWA14 Footing Level (from +194mPD to +192mPD)	30	65	19-Apr-18	25-May-18	04-Jan-18 A	24-Mar-18	6%	<div></div>					
ACW1120	C2/D2 - Construct RWA14 - Bay #1 to 6 (by 2 teams; 3 bays/month/work front)	48	48	08-May-18	05-Jul-18	27-Apr-18	25-Jun-18	0%	<div></div>					
Public Transportation Terminus (Portion B5)														
ACP1030A200A0	B5 - Grouting of VB14 of PTT	0	1			15-Jan-18 A	15-Jan-18 A	100%	<div></div>					
ACP1030A200A0	B5 - Grouting of VB11 of PTT	0	1			16-Jan-18 A	16-Jan-18 A	100%	<div></div>					
ACP1030A200A0	B5 - Pile Load Tests	0	10			26-Feb-18*	08-Mar-18	0%	<div></div>					B5 - Pile Load Tests
ACP1040	B5 - Excavation and Construct Pile Caps with Erection of Steel Posts GLE/1-9 (PC3)	36	90	04-May-18	15-Jun-18	09-Mar-18*	29-Jun-18	0%	<div></div>					
Internal Road Construction														
Single Cell Box Culvert BC1 incl. Transition Section CH141.820 to CH168.019														
ACL10050A001	Laying Geotextile Filter and Rockfilling for Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)	0	2			16-Jan-18 A	17-Jan-18 A	100%	<div></div>					
ACL10050A003	Blinding Layer for Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)	0	1			29-Jan-18 A	29-Jan-18 A	100%	<div></div>					
ACL10050A004	Formwork,Rebar Fixing and Water Stop for Base Slab of Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)	0	8			03-Feb-18 A	12-Feb-18 A	100%	<div></div>					
ACL10050A006	Concrete Pouring for Base Slab of Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)	0	1			13-Feb-18 A	13-Feb-18 A	100%	<div></div>					
ACL10050A007	Formwork and Rebar Fixing for Wall and Top Slab of Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)	0	11			20-Feb-18	03-Mar-18	0%	<div></div>					Formwork and Rebar Fixing for Wall and Top Slab of Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)
ACL10050A009	Concrete Pouring for Wall andTop Slab of Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)	0	1			05-Mar-18	05-Mar-18	0%	<div></div>					Concrete Pouring for Wall andTop Slab of Box Culvert BC1 Bay 13 (CHA141.820 to CHA156.019)
ACL10050A011	Laying Geotextile Filter and Rockfilling for Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)	0	2			16-Jan-18 A	17-Jan-18 A	100%	<div></div>					
ACL10050A012	Blinding Layer for Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)	0	1			29-Jan-18 A	29-Jan-18 A	100%	<div></div>					
ACL10050A013	Formwork,Rebar Fixing and Water Stop for Base Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)	0	19			03-Feb-18 A	01-Mar-18	10%	<div></div>					Formwork,Rebar Fixing and Water Stop for Base Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)
ACL10050A014	Concrete Pouring for Base Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)	0	1			01-Mar-18	02-Mar-18	0%	<div></div>					Concrete Pouring for Base Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)
ACL10050A015	Formwork and Rebar Fixing for Wall and Top Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)	0	11			06-Mar-18	17-Mar-18	0%	<div></div>					Formwork and Rebar Fixing for Wall and Top Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)
ACL10050A017	Concrete Pouring for Wall andTop Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)	0	1			19-Mar-18	19-Mar-18	0%	<div></div>					Concrete Pouring for Wall andTop Slab of Box Culvert BC1 Bay 14 (CHA156.019 to CHA168.019)
ACL10050A018	B2 - Back Fill of Box Culvert BC1 Transition Bay 13/14 (CHA141.820 to CHA168.019)	0	24			20-Mar-18	20-Apr-18	0%	<div></div>					B2 - Back Fill of Box Culvert BC1 Transition E
ACL10050A019	B2 - Divert Open Drainage Channel to crossover BC1 Bay 14 (CHA156.019 to CHA168.019)	0	6			19-Apr-18	25-Apr-18	0%	<div></div>					B2 - Divert Open Drainage Channel
ACL10050A020	Excavation of Box Culvert BC1 Bay 15 (CHCHA168.019 to CHA178.392)	0	5			26-Apr-18	02-May-18	0%	<div></div>					Excavation of Box Cu
ACL10050A021	Laying Geotextile Filter and Rockfilling for Box Culvert BC1 Bay 15 (CHA168.019 to CHA178.392)	0	4			03-May-18*	07-May-18	0%	<div></div>					Laying Geot
ACL10050A022	Blinding Layer for Box Culvert BC1 Bay 15 (CHA168.019 to CHA178.392)	0	1			08-May-18	08-May-18	0%	<div></div>					Blinding La
ACL10050A023	Formwork,Rebar Fixing and Water Stop for Base Slab of Box Culvert BC1 Bay 15 (CHA168.019 to CHA178.392)	0	9			09-May-18	18-May-18	0%	<div></div>					
ACL10050A151	Excavation of Box Culvert BC1 Bay 12 (CHA144 to CHA132)	0	5			25-Apr-18	30-Apr-18	0%	<div></div>					Excavation of Box Culvert
ACL10050A152	Laying Geotextile Filter and Rockfilling for Box Culvert BC1 Bay 12 (CHA144 to CHA132)	0	4			02-May-18*	05-May-18	0%	<div></div>					Laying Geotextil
ACL10050A153	Blinding Layer for Box Culvert BC1 Bay 12 (CHA144 to CHA132)	0	1			07-May-18	07-May-18	0%	<div></div>					Blinding Layer
ACL10050A158	Excavation of Box Culvert BC1 Bay 11 (CHA132 to CHA120)	0	5			02-May-18	07-May-18	0%	<div></div>					Excavation of
ACL10050A159	Laying Geotextile Filter and Rockfilling for Box Culvert BC1 Bay 11 (CHA132 to CHA120)	0	4			08-May-18*	11-May-18	0%	<div></div>					Laying
ACL10050A160	Blinding Layer for Box Culvert BC1 Bay 11 (CHA132 to CHA120)	0	1			12-May-18	12-May-18	0%	<div></div>					Blinding
ACL10050A161	Formwork,Rebar Fixing and Water Stop for Base Slab of Box Culvert BC1 Bay 11 (CHA132 to CHA120)	0	9			14-May-18	24-May-18	0%	<div></div>					
ACL10050A165	Excavation of Box Culvert BC1 Bay 10 (CHA120 to CHA108)	0	5			08-May-18	12-May-18	0%	<div></div>					Excavation of
ACL10050A166	Laying Geotextile Filter and Rockfilling for Box Culvert BC1 Bay 10 (CHA120 to CHA108)	0	4			14-May-18*	17-May-18	0%	<div></div>					
ACL10050A172	Excavation of Box Culvert BC1 Bay 9 (CHA108 to CHA96)	0	5			14-May-18	18-May-18	0%	<div></div>					
Twin Cell Box Culvert BC2														
ACL10050A030	Excavation of Box Culvert BC2 Bay 1 (CHB0 to CHB12)	0	5			03-May-18	08-May-18	0%	<div></div>					Excavation of
ACL10050A031	Laying Geotextile Filter and Rockfilling for BC2 Bay 1 (CHB0 to CHB12)	0	4			09-May-18*	12-May-18	0%	<div></div>					Laying
ACL10050A032	Blinding Layer for Box Culvert BC2 Bay 1 (CHB0 to CHB12)	0	1			14-May-18	14-May-18	0%	<div></div>					Blinding
ACL10050A037	Excavation of Box Culvert BC2 Bay 2 (CHB12 to CHB24)	0	5			09-May-18	14-May-18	0%	<div></div>					
									ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017					
									Date	Revision		Checked	Approved	
									23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)				



俊和 - 上隴 - 浩隆聯營
CHUN WO - STec - VASTEAM JOINT VENTURE

Planned Bar (WP) ◆ ◆ Milestone

Actual Bar

Forecast Bar

◆ ◆ Planned Milestone (WP)

3-MONTH ROLLING PROGRAMME

(In comparison with WP Rev.1 dated 25 Aug 2017)

ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017

Date	Revision	Checked	Approved
23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)		

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 11 of 14 23 Feb 2018			
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Jan	Qtr 1, 2018 Feb	Mar	Qtr 2, 2018 Apr	May
ACL10050A145	Formwork,Rebar Fixing and Water Stop for Base Slab of Box Culvert BC2 Bay 17 (CHB192 to CHB201.096)	0	9			02-May-18	11-May-18	0%					Formwork
ACL10050A146	Concrete Pouring for Base Slab of Box Culvert BBC2 Bay 17 (CHB192 to CHB201.096)	0	1			12-May-18	12-May-18	0%					Concrete
At-grade Internal Road L1													
Road L1 and L5 (Portion A1)													
ACL10100A001	A1 - Excavation and Rock Breaking along Road L1 from Pedestrian Connectivity System B to West Portal	0	160			04-Sep-17 A	19-Mar-18	80%					A1 - Excavation and Rock Breaking along Road L1 from Pedestrian Connectivity System B to West Portal
ACL10110	A1 - Install Road Drainage, Water Mains, Ducts and Utilities along Road L1 from System B to West Portal	80	80	04-Apr-18	11-Jul-18	20-Mar-18	28-Jun-18	0%					
Road L1 (Portion B2)													
ACL10039A002	Form Platform for Slope Works at Slope A15	0	21			20-Feb-18*	15-Mar-18	0%					Form Platform for Slope Works at Slope A15
ACL10039A003	Rock Slope Cut at Slope A15	0	30			16-Mar-18	24-Apr-18	0%					Rock Slope Cut at Slope A15
At-grade Internal Road L4 (Portion C1a)													
ACL41250	C1a - Erect Scaffold for RockSlope Inspection along Road L4	180	30	13-Oct-17	25-May-18	02-May-18*	06-Jun-18	0%					
Noise Barrier													
ACL40590	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #16	12	12	26-Jul-17	08-Aug-17	19-Apr-18	04-May-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #16
ACL40605A57	C1a - Mass Concrete Pouring for Bay #1	0	1			17-Jan-18 A	17-Jan-18 A	100%					
ACL40605A72	C1a - Grade 200 Rockfilling alongside Noise Barrier Bay 22 to 17 (5 layers)	0	35			11-Jan-18 A	23-Feb-18	40%					C1a - Grade 200 Rockfilling alongside Noise Barrier Bay 22 to 17 (5 layers)
ACL40605A73	C1a - Grade 200 Rockfilling alongside Noise Barrier Bay 16 to 1 (5 layers)	0	6			23-Feb-18	02-Mar-18	0%					C1a - Grade 200 Rockfilling alongside Noise Barrier Bay 16 to 1 (5 layers)
ACL40630	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #18	12	12	19-Jul-17	01-Aug-17	04-May-18	18-May-18	0%					
ACL40650	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #19	12	12	05-Jul-17	18-Jul-17	04-Apr-18	19-Apr-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #19
ACL40660	C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #19	18	18	02-Aug-17	22-Aug-17	04-May-18	26-May-18	0%					
ACL40670	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #20	12	12	19-Jul-17	01-Aug-17	19-Apr-18	04-May-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #20
ACL40690	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #21	12	12	02-Aug-17	15-Aug-17	04-Apr-18	19-Apr-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #21
ACL40710	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #22	12	12	16-Aug-17	29-Aug-17	04-May-18	18-May-18	0%					
ACL40730	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #23	12	12	02-Aug-17	15-Aug-17	19-Apr-18	04-May-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #23
ACL40740	C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #23	18	18	30-Aug-17	19-Sep-17	04-May-18	26-May-18	0%					
ACL40750	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #24	12	24	16-Aug-17	29-Aug-17	01-Feb-18 A	03-Mar-18	50%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #24
ACL40770	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #25	12	12	30-Aug-17	12-Sep-17	17-Mar-18	04-Apr-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #25
ACL40780	C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #25	18	18	27-Sep-17	19-Oct-17	04-Apr-18	26-Apr-18	0%					C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #25
ACL40790	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #26	12	28	13-Sep-17	26-Sep-17	20-Jan-18 A	24-Feb-18	90%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #26
ACL40800	C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #26	18	18	20-Oct-17	10-Nov-17	26-Apr-18	18-May-18	0%					
ACL40810	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #27	12	12	30-Aug-17	12-Sep-17	17-Mar-18	04-Apr-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #27
ACL40820	C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #27	18	18	27-Sep-17	19-Oct-17	04-Apr-18	26-Apr-18	0%					C1a - Construction of Wall of Noise Barrier at Road L4 - Bay #27
ACL40830	C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #28	12	12	13-Sep-17	26-Sep-17	03-Mar-18	17-Mar-18	0%					C1a - Construction of Footing of Noise Barrier at Road L4 - Bay #28
Twin 1950 Dia. Downpipe and Cascade													
ACL40020A001	C1a - Submit Temporary Haul Road at Road L4 to retaining Wall RWA12	0	1			16-Jan-18 A	16-Jan-18 A	100%					
ACL40020A001	C1a - Construct Temporary Haul Road at Road L4 to retaining Wall RWA12	0	25			31-Jan-18 A	03-Mar-18	80%					C1a - Construct Temporary Haul Road at Road L4 to retaining Wall RWA12
ACL40050	C1a - Construction of New CP17-1 (IL +165mPD)	17	10	02-Jan-18	20-Jan-18	19-Mar-18	29-Mar-18	0%					C1a - Construction of New CP17-1 (IL +165mPD)
ACL40060	C1a - Construction of new 2x1950mm Dia Drainage Pipe (IL +165.6mPD)	17	10	20-Jan-18	08-Feb-18	21-Mar-18	04-Apr-18	0%					C1a - Construction of new 2x1950mm Dia Drainage Pipe (IL +165.6mPD)
ACL40070	C1a - Construction of new Manhole Q2 (IL +165.8mPD)	15	15	08-Feb-18	28-Feb-18	21-Mar-18	11-Apr-18	0%					C1a - Construction of new Manhole Q2 (IL +165.8mPD)
Retaining Wall RWA12													
ACL40020A002	C1a - Excavate RWA12 - Bay #20 to 17 (to +154mPD)	0	189			07-Aug-17 A	24-Mar-18	60%					C1a - Excavate RWA12 - Bay #20 to 17 (to +154mPD)
ACL40020A003	C1a - Construct RWA12 - Bay #20 Base Slab and Wall upward +165mPD as 1st Portion	0	12			26-Mar-18	12-Apr-18	0%					C1a - Construct RWA12 - Bay #20 Base Slab and Wall upward +165mPD as 1st Portion
ACL40020A004	C1a - Back Fill RWA12 - Bay #20 upward +163mPD	0	6			13-Apr-18	19-Apr-18	0%					C1a - Back Fill RWA12 - Bay #20 upward +163mPD
ACL40020A005	C1a - Construct RWA12 - Bay #19 to 17	0	6			20-Apr-18	26-Apr-18	0%					C1a - Construct RWA12 - Bay #19 to 17
									ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017				
									Date	Revision		Checked	Approved
									23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)			

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 12 of 14 23 Feb 2018			
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Jan	Qtr 1, 2018 Feb	Mar	Qtr 2, 2018 Apr	May
ACL40020A006	C1a - Construct RWA12 - Bay #20 Wall upward +175mPD as 2nd Portion	0	14			20-Apr-18	07-May-18	0%					C1a - Const
ACL40020A007	C1a - Back Fill RWA12 - Bay #19 to 17	0	6			27-Apr-18	04-May-18	0%					C1a - Back Fill RV
ACL40030	C1a - Excavate RWA12 - Bay #22 (to +154mPD)	12	39	04-Nov-17	17-Nov-17	08-Jan-18 A	26-Feb-18	55%			C1a - Excavate RWA12 - Bay #22 (to +154mPD)		
ACL40040A001	C1a - Construction of RWA12 - Bay #22 Base Slab and Wall upward +165mPD as 1st Portion	0	12			05-Mar-18	17-Mar-18	0%				C1a - Construction of RWA12 - Bay #22 Base Slab and Wall upward +165mPD as 1st Portion	
ACL40040A002	C1a - Construction of RWA12 - Bay #22 Wall upward +175mPD as 2nd Portion	0	14			06-Apr-18	21-Apr-18	0%				C1a - Construction of RWA12 - Bay #22 W	
ACL40110	C1a - Excavate RWA12 - Bay #21 (+156.6mPD) and Demolish Existing Soil Nails	5	18	28-Apr-18	04-May-18	26-Feb-18	19-Mar-18	0%					C1a - Excavate R
ACL40110A001	C1a - Back Fill SYS-A South Tower after Demolishing Existing Soil Nails to Form Platform	0	6			19-Mar-18	26-Mar-18	0%				C1a - Back Fill SYS-A South Tower after Demolishing Existing Soil Nails to Form Platform	
ACL40120A001	C1a - Construct RWA12 - Bay #21 Base Slab and Wall upward +165mPD as 1st Portion	0	14			26-Mar-18	16-Apr-18	0%				C1a - Construct RWA12 - Bay #21 Base Slab and Wa	
ACL40120A002	C1a - Back Fill RWA12 - Bay #21 and 22 upward +163mPD (15 layers @ 4 layers/day)	0	6			16-Apr-18	23-Apr-18	0%				C1a - Back Fill RWA12 - Bay #21 and 22	
ACL40955	C1a - Excavate RWA12 - Bay #1 to 8	78	60	26-Jul-17	26-Oct-17	23-Apr-18*	06-Jul-18	0%					
Retaining Wall RWA18													
ACL40170A001	C1a - Excavation at Slope A18 for Construction of RWA18 Bay #5	0	42			11-Jan-18 A	05-Mar-18	5%			C1a - Excavation at Slope A18 for Construction of RWA18 Bay #5		
ACL40170A002	C1a - Excavation at Slope A18 for Construction of RWA18 Bay #4	0	54			11-Jan-18 A	17-Mar-18	5%			C1a - Excavation at Slope A18 for Construction of RWA18 Bay #4		
ACL40170A003	C1a - Excavation at Slope A18 for Construction of RWA18 Bay #3	0	12			17-Mar-18	04-Apr-18	0%				C1a - Excavation at Slope A18 for Construction of RWA18 Bay #3	
ACL40170A004	C1a - Excavation at Slope A18 for Construction of RWA18 Bay #2	0	12			04-Apr-18	19-Apr-18	0%				C1a - Excavation at Slope A18 for Construction	
ACL40170A005	C1a - Excavation at Slope A18 for Construction of RWA18 Bay #1	0	12			19-Apr-18	04-May-18	0%				C1a - Excavation	
ACL40180	C1a - Construction of Footing of RWA18 - Bay #1	12	12	16-Dec-17	02-Jan-18	04-May-18	18-May-18	0%					
ACL40200	C1a - Construction of Footing of RWA18 - Bay #2	12	12	02-Dec-17	15-Dec-17	19-Apr-18	04-May-18	0%					C1a - Construction
ACL40210	C1a - Construction of Wall of RWA18 - Bay #2	12	12	14-Feb-18	02-Mar-18	04-May-18	18-May-18	0%					
ACL40220	C1a - Construction of Footing of RWA18 - Bay #3	12	12	18-Nov-17	01-Dec-17	04-Apr-18	19-Apr-18	0%					C1a - Construction of Footing of RWA18 - Bay
ACL40230	C1a - Construction of Wall of RWA18 - Bay #3	12	12	31-Jan-18	13-Feb-18	19-Apr-18	04-May-18	0%					C1a - Construction
ACL40240	C1a - Construction of Footing of RWA18 - Bay #4	12	12	02-Dec-17	15-Dec-17	17-Mar-18	04-Apr-18	0%					C1a - Construction of Footing of RWA18 - Bay #4
ACL40250	C1a - Construction of Wall of RWA18 - Bay #4	12	12	24-Feb-18	09-Mar-18	04-Apr-18	19-Apr-18	0%					C1a - Construction of Wall of RWA18 - Bay #4
ACL40260	C1a - Construction of Footing of RWA18 - Bay #5	12	12	18-Nov-17	01-Dec-17	20-Feb-18	05-Mar-18	0%					C1a - Construction of Footing of RWA18 - Bay #5
ACL40270	C1a - Construction of Wall of RWA18 - Bay #5	12	12	07-Feb-18	23-Feb-18	06-Mar-18	19-Mar-18	0%					C1a - Construction of Wall of RWA18 - Bay #5
WSD Access Road (Portion B5)													
ACL60010	B5 - Site Clearance and Tree Felling	46	46	19-Dec-17	13-Feb-18	27-Apr-18	22-Jun-18	0%					
Portion A3													
Site Formation													
ACA30020	A3 - Soil Excavation for Site Formation in Portion A3	306	142	07-Sep-17	18-Sep-18	13-Oct-17 A	09-Apr-18	46%					
ACA30030	A3 - Rock Breaking for Site Formation in Portion A3	56	98	19-Sep-18	26-Nov-18	25-Oct-17 A	24-Feb-18	80%					
ACA30035	A3 - Construct U-Channel with Cover (675UC) along Slope A16	14	14	27-Nov-18	12-Dec-18	09-Apr-18	25-Apr-18	0%					
ACA30040	A3 - Construction of U-Channel, Catchpits and 525mm dia. drainage pipe connecting to Manhole A1	45	35	27-Nov-18	21-Jan-19	25-Apr-18	07-Jun-18	0%					
Portion A4 (based on Sub Programme Ref.CWSTVJV/893/CSF/0208-2017)													
Site Formation													
ACA40131A001	A4 - Clean up Drainage Pipes and Conduct CCTV Inspection	0	1			20-Jan-18 A	20-Jan-18 A	100%					
ACA40131A002	A4 - Pre-Inspection Handover	0	1			13-Feb-18 A	13-Feb-18 A	100%					
ACA40131A2	A4 - Defect Correction according to the Pre-inspection	0	14			20-Feb-18	07-Mar-18	0%				A4 - Defect Correction according to the Pre-inspection	
Portion B1													
Site Formation													
ACB10010	B1 - 9 Months Establishment Works for Landscape Softworks (Dwg.No.60328348/SF&I/1051&1052)	270	402	24-Jan-17	20-Oct-17	15-Sep-17 A	22-Oct-18	8%					
ACB10020	B1 - 17 Months Establishment Works for Landscape Softworks (Dwg.No.60328348/SF&I/1051&1052)	510	623	24-Jan-17	17-Jun-18	15-Sep-17 A	31-May-19	8%					
ACB10030	B1 - 30 Months Establishment Works for Landscape Softworks (Dwg.No.60328348/SF&I/1051&1052)	900	884	24-Jan-17	12-Jul-19	19-Feb-17 A	22-Jul-19	42%					
												</	

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 13 of 14 23 Feb 2018				
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018			Qtr 2, 2018		
									Jan	Feb	Mar	Apr	May	
ACB10060	B1 - Rock Slope Mapping (Instructed by RE) for Slope A16	30	54	19-Jul-17	22-Aug-17	16-Jan-18 A	22-Mar-18	10%				B1 - Rock Slope Mapping (Instructed by RE) for Slope A16		
ACB10070	B1 - JV Prepare and Submit Detailed Design of RSSM for Slope A16 (Provisional Work)	18	18	23-Aug-17	12-Sep-17	23-Mar-18	17-Apr-18	0%				B1 - JV Prepare and Submit Detailed Design of RS		
ACB10080	B1 - RE Review and Approve Detailed Design of RSSM for Slope A16 (Provisional Work)	12	12	13-Sep-17	26-Sep-17	18-Apr-18	02-May-18	0%				B1 - RE Review and A		
ACB10090	B1 - Rock Slope Stabilization Measures of RSSM for Slope A16 (Provisional Work)	48	48	27-Sep-17	24-Nov-17	03-May-18	29-Jun-18	0%						
ACB10380	B1 - Erection of Scaffold for Slope 11NE-D/C1004 (2700 sqm) - 150sqm/d	20	20	27-Nov-17	19-Dec-17	27-Feb-18	22-Mar-18	0%				B1 - Erection of Scaffold for Slope 11NE-D/C1004 (2700 sqm) - 150sqm/d		
ACB10390	B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C1004 (2700 sqm) - 80sqm/d (Provisional Work)	38	38	20-Dec-17	05-Feb-18	22-Mar-18	11-May-18	0%					B1 -	
ACB10400	B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C1004 (2700 sqm) (Provisional Work)	6	6	06-Feb-18	12-Feb-18	11-May-18	18-May-18	0%						
ACB10650	B1 - Erection of Scaffold for Slope 11NE-D/C998 (980 sqm) - 150sqm/d	7	135	28-Jul-17	04-Aug-17	10-Jul-17 A	22-Feb-18	60%				B1 - Erection of Scaffold for Slope 11NE-D/C998 (980 sqm) - 150sqm/d		
ACB10660	B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C998 (980 sqm) - 80sqm/d (Provisional Work)	13	169	05-Aug-17	19-Aug-17	07-Aug-17 A	02-Mar-18	50%				B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C998 (980 sqm) - 80sqm/d (Provisional Work)		
ACB10670	B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C998 (980 sqm) (Provisional Work)	6	163	21-Aug-17	26-Aug-17	18-Aug-17 A	06-Mar-18	40%				B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C998 (980 sqm) (Provisional Work)		
ACB10680	B1 - RE Review and Approve Detailed Design of RSSM for Slope 11NE-D/C998 (980 sqm) (Provisional Work)	6	166	28-Aug-17	02-Sep-17	19-Aug-17 A	10-Mar-18	40%				B1 - RE Review and Approve Detailed Design of RSSM for Slope 11NE-D/C998 (980 sqm) (Provisional Work)		
ACB10690	B1 - Rock Slope Stabilization Measures for Slope 11NE-D/C998 (980 sqm)	48	143	04-Sep-17	01-Nov-17	08-Nov-17 A	05-May-18	10%					B1 - Rock Slope	
ACB10710	B1 - Erection of Scaffold for Slope 11NE-D/C999 (600 sqm) - 150sqm/d	4	31	13-Oct-17	17-Oct-17	16-Jan-18 A	23-Feb-18	5%				B1 - Erection of Scaffold for Slope 11NE-D/C999 (600 sqm) - 150sqm/d		
ACB10720	B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C999 (600 sqm) - 80sqm/d (Provisional Work)	8	8	18-Oct-17	26-Oct-17	23-Feb-18	05-Mar-18	0%				B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C999 (600 sqm) - 80sqm/d (Provisional Work)		
ACB10730	B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C999 (600 sqm) (Provisional Work)	6	6	27-Oct-17	03-Nov-17	05-Mar-18	12-Mar-18	0%				B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C999 (600 sqm) (Provisional Work)		
ACB10740	B1 - RE Review and Approve Detailed Design of RSSM for Slope 11NE-D/C999 (600 sqm) (Provisional Work)	6	6	04-Nov-17	10-Nov-17	12-Mar-18	19-Mar-18	0%				B1 - RE Review and Approve Detailed Design of RSSM for Slope 11NE-D/C999 (600 sqm) (Provisional Work)		
ACB10750	B1 - Rock Slope Stabilization Measures for Slope 11NE-D/C999 (600 sqm)	48	48	30-Dec-17	28-Feb-18	19-Mar-18	19-May-18	0%						
ACB10770	B1 - Erection of Scaffold for Slope 11NE-D/C1003 (400 sqm) - 150sqm/d	3	107	11-Sep-17	13-Sep-17	13-Oct-17 A	22-Feb-18	10%				B1 - Erection of Scaffold for Slope 11NE-D/C1003 (400 sqm) - 150sqm/d		
ACB10780	B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C1003 (400 sqm) - 80sqm/d (Provisional Work)	5	5	14-Sep-17	19-Sep-17	22-Feb-18*	28-Feb-18	0%				B1 - Rock Slope Mapping (Instructed by RE) for Slope 11NE-D/C1003 (400 sqm) - 80sqm/d (Provisional Work)		
ACB10790	B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C1003 (400 sqm) (Provisional Work)	6	6	20-Sep-17	26-Sep-17	28-Feb-18	07-Mar-18	0%				B1 - JV Prepare and Submit Detailed Design of RSSM for Slope 11NE-D/C1003 (400 sqm) (Provisional Work)		
ACB10800	B1 - RE Review and Approve Detailed Design of RSSM for Slope 11NE-D/C1003 (400 sqm) (Provisional Work)	6	6	27-Sep-17	04-Oct-17	07-Mar-18	14-Mar-18	0%				B1 - RE Review and Approve Detailed Design of RSSM for Slope 11NE-D/C1003 (400 sqm) (Provisional Work)		
ACB10810	B1 - Rock Slope Stabilization Measures for Slope 11NE-D/C1003 (400 sqm) (Provisional Work)	48	48	02-Nov-17	29-Dec-17	14-Mar-18	15-May-18	0%						
Portion B5														
Portion B5 North & East Side adjacent to Portion B2 and Pumping Station and Reservoirs														
Site Formation														
ACB50060	B5 - 9 Months Establishment Works for Landscape Softworks (Dwg.No.60328348/SF&I/1051&1052)	270	383	24-Jan-17	20-Dec-17	15-Sep-17 A	31-Dec-18	5%						
ACB50070	B5 - Erection of Scaffold and working Platform for Slope A15b	180	14	24-Jan-17	02-Sep-17	20-Feb-18*	07-Mar-18	0%				B5 - Erection of Scaffold and working Platform for Slope A15b		
Portion B8														
Site Formation														
ACB80020	B8 - Backfilling for Site Formation in Portion B8 (10 out of 48 layers completed)	60	181	09-Oct-17	18-Dec-17	01-Sep-17 A	14-Apr-18	29%				B8 - Backfilling for Site Formation in Portion B8 (10 out of		
ACB80030	B8 - Construct New U-Channel 300U (approx 80m) and Catchpit TC6c	30	30	14-Nov-17	18-Dec-17	14-Apr-18	21-May-18	0%						
ACB80040	B8 - Construct New U-Channel 375U (approx 66m) and Catchpit TC6d	26	26	19-Dec-17	20-Jan-18	19-Apr-18	21-May-18	0%						
ACB80050	B8 - Construct New U-Channel 450U (approx 73m) and Catchpit TC6a	30	30	22-Jan-18	28-Feb-18	19-Apr-18	26-May-18	0%						
ACB80060	B8 - Construct New U-Channel 525U (approx 80m) and Catchpit TC6c	36	36	01-Mar-18	16-Apr-18	19-Apr-18	02-Jun-18	0%						
Portion B10														
Site Formation														
ACB100020	B10 - Site Formation in Portion B10	45	170	31-Oct-17	21-Dec-17	01-Sep-17 A	28-Mar-18	29%				B10 - Site Formation in Portion B10		
ACB100030	B10 - Construct New U-Channel (450U,525U and 675U; approx 90m) and Catchpits (3nos)	40	40	22-Dec-17	09-Feb-18	28-Mar-18	19-May-18	0%						
Portion D1														
Road Improvement at Po Lam Road														
Phase 1A Road Improvement Works														
ACD10035A00	D1 - Phase 1A - Excavation to expose existing UU	0	24			05-Mar-18*	04-Apr-18	0%				D1 - Phase 1A - Excavation to expose existing UU		
ACD10035A00	D1 - Phase 1A - Confirm the new Location of Fire Hydrant	0	24			06-Apr-18	04-May-18	0%				D1 - Phase 1A - C		
<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN WO - STEC - VASTEAM JOINT VENTURE</div></div></div>									<div><div></div>Planned Bar (WP)</div> <div><div></div>Actual Bar</div> <div><div></div>Forecast Bar</div> <div><div></div>Planned Milestone (WP)</div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div> <div><div></div></div>					

<div><div><div><div></div><div>TEC</div><div>隆道股份</div></div><div>俊和 - 上隧 - 浩隆聯營</div><div>CHUN Wo - STEC - VASTEAM JOINT VENTURE</div></div></div>			CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME							Page 14 of 14 23 Feb 2018				
Activity ID	Activity Name	BL Project Duration	At Completion Duration	BL Project Start	BL Project Finish	Start	Finish	% Comp	Qtr 1, 2018			Qtr 2, 2018		
									Jan	Feb	Mar	Apr	May	
ACD10035A00	D1 - Phase 1A - Relocation of Fire Hydrant (By WSD)	0	24			05-May-18	02-Jun-18	0%						
Phase 1B Road Improvement Works														
ACD10130A00	D1 - Phase 1B - Trial Pit Excavation	0	12			05-Mar-18*	17-Mar-18	0%						
ACD10140A00	D1 - Phase 1B - Excavation to expose existing UU	0	12			19-Mar-18	04-Apr-18	0%						
ACD10150A00	D1 - Phase 1B - Confirm Proposed Location of Drawpits (Earth/E&M/ATC) and Light Signal Head	0	36			06-Apr-18	18-May-18	0%						
Shui Chuen O & Kau To (Portion E2) - Subject to Excision														
ACO10066	Handover Inspection for Slope 7NE-C/C499 (Landscape Softworks) - Awaiting Confirmation from HyD	7	4	13-Sep-17	20-Sep-17	20-Feb-18	23-Feb-18	0%						
ACO10241	Handover Inspection for Landscape Works for Slope 7NE-C/C207 (Kau To) - Awaiting Identification of Boundary	7	1	30-Oct-17	06-Nov-17	02-Feb-18 A	02-Feb-18 A	100%						
ACO10243	Handover Inspection for Landscape Works for Slope 7NE-C/C464 (Kau To) - Defect Rectification	7	46	30-Oct-17	06-Nov-17	21-Dec-17 A	20-Feb-18	90%						
ACO10251	Handover Inspection for Landscape Works for Slope 7NE-C/C471 (Kau To) - Defect Rectification	7	41	12-Dec-17	19-Dec-17	14-Dec-17 A	02-Feb-18 A	100%						
ACO10271	Handover Inspection for Landscape Works for Slope 7NE-C/CR78 (Kau To) - Awaiting Confirmation from HyD	7	3	15-Nov-17	22-Nov-17	20-Feb-18	22-Feb-18	0%						
ACO10281	Handover Inspection for Landscape Works for Slope 7SE-C/F238 (Shui Chuen O) - Awaiting Confirmation from HyD	7	4	19-Oct-17	26-Oct-17	20-Feb-18*	23-Feb-18	0%						
Mitigation Works for Natural Terrain Catchment B5 adjacent to Anderson Road - Subject to Excision														
ACO10140	Slope Trimming and Excavation for Gabion Barrier Construction (As directed by Engineer)	30	14	18-Jan-18	24-Feb-18	12-Apr-18	27-Apr-18	0%						
ACO10143	Large Disturbed Sample and Submission of Report	0	14			26-Feb-18*	13-Mar-18	0%						
ACO10144	Block and Submission of Report	0	14			14-Mar-18	29-Mar-18	0%						
ACO10145	Preliminary Logs Submission	0	7			03-Apr-18	11-Apr-18	0%						
ACO10150	Construct Gabion Barrier, 450UC and Catch Pits	50	50	26-Feb-18	28-Apr-18	28-Apr-18	28-Jun-18	0%						

TEC

隆道股份

俊和 - 上隧 - 浩隆聯營

CHUN Wo - STEC - VASTEAM JOINT VENTURE

Planned Bar (WP)

Actual Bar

Forecast Bar

Planned Milestone (WP)

◆

◆

Milestone

3-MONTH ROLLING PROGRAMME
(In comparison with WP Rev.1 dated 25 Aug 2017)

ARQ - Programme Logics based on WP Rev.1 dated 25 Aug 2017


Date	Revision	Checked	Approved
23-Feb-18	3MRP Rev.1 (Cut Off on 15 Feb 18)		

Revised programme for Section A-E1_Dec 17

ITEM	ID	Task Name	Duration	Remaining Duration	Start	Finish	2018												2019												2020			
							Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1	A.1.1	Section A, Portion 1 - Escalator (E1)	1096 days	986.55 days	Fri 31/3/17	Mon 30/3/20																												
2	A.1.1.1	Pre Construction Works	620 days	354.65 days	Fri 31/3/17	Mon 10/12/18	43%																											
3	A.1.1.1.1	Access Date for Portion 1	1 day	0 days	Fri 31/3/17	Fri 31/3/17	100%																											
4	A.1.1.1.2	Site Clearance	14 days	0 days	Fri 14/4/17	Thu 27/4/17	100%																											
5	A.1.1.1.3	Site Condition Survey	14 days	0 days	Fri 28/4/17	Thu 11/5/17	100%																											
6	A.1.1.1.4	Initial site survey and submission	58 days	17.4 days	Sun 17/9/17	Mon 13/11/17	70%																											
7	1.1.5	Carry out Tree Survey and Report Submission	14 days	0 days	Sat 13/5/17	Fri 26/5/17	100%																											
8	A.1.1.1.5	Application for Excavation Permit (XP)	180 days	0 days	Sat 1/4/17	Wed 27/9/17	100%																											
9	A.1.1.1.7	Implement TTA at Hiu Ming Street/Hiu Kwong Street	14 days	0 days	Wed 9/8/17	Tue 22/8/17	100%																											
10	A.1.1.1.8	Erection of Hoarding	33 days	0 days	Thu 13/7/17	Mon 14/8/17	100%																											
11	A.1.1.1.9	Tree Fell	84 days	67.2 days	Tue 5/9/17	Mon 27/11/17	20%																											
12	A.1.1.1.10	Design submission of Escalator	60 days	57 days	Sat 16/12/17	Tue 13/2/18	5%																											
13	A.1.1.1.11	Comment of design submission of Escalator	90 days	90 days	Wed 14/2/18	Mon 14/5/18	0%																											
14	1.1.12	Second design submission of Escalator	120 days	120 days	Tue 15/5/18	Tue 11/9/18	0%																											
15	1.1.13	Approval of design submission of Escalator	90 days	90 days	Wed 12/9/18	Mon 10/12/18	0%																											
16	A.1.1.2	Ground Investigation	132 days	0 days	Fri 31/3/17	Wed 9/8/17	100%																											
17	A.1.1.2.1	Proposal of ground investigation specialist	1 day	0 days	Fri 31/3/17	Fri 31/3/17	100%																											
18	A.1.1.2.2	Approval of ground investigation specialist	24 days	0 days	Sat 1/4/17	Mon 24/4/17	100%																											
19	A.1.1.2.3	Submission of Construction Impact Assessment	12 days	12 days	Mon 17/4/17	Fri 28/4/17	100%																											
20	A.1.1.2.4	Establishment of Drilling rigs	7 days	0 days	Fri 21/4/17	Fri 5/5/17	100%																											
21	A.1.1.2.5	Inspection Pits (10 nr)	14 days	0 days	Fri 21/4/17	Thu 4/5/17	100%																											
22	1.2.6	Additional Inspection Pit (PMI 1 & PMI 2)	2 days	0 days	Mon 5/6/17	Tue 6/6/17	100%																											
23	A.1.1.2.6	Predrilling (10 nr)	54 days	0 days	Fri 28/4/17	Tue 20/6/17	100%																											
24	1.2.8	Additional Pre-drilling (PMI 3)	2 days	0 days	Fri 7/7/17	Sat 8/7/17	100%																											
25	A.1.1.2.7	Demobilization of Drilling rigs	1 day	0 days	Wed 12/7/17	Wed 12/7/17	100%																											
26	A.1.1.2.8	In-situ testing and result submission	28 days	0 days	Thu 29/6/17	Wed 26/7/17	100%																											
27	A.1.1.2.9	Laboratory tests	14 days	0 days	Thu 27/7/17	Wed 9/8/17	100%																											
28	A.1.1.3	Piling Works (Pr-bored Socket H-Pile)	454.4 days	322.53 days	Sat 22/4/17	Fri 20/7/18	29%																											
29	A.1.1.3.1	Proposal of Piling Specialist	7 days	0 days	Sat 22/4/17	Fri 28/4/17	100%																											
30	A.1.1.3.2	Approval of Piling Specialist	24 days	0 days	Sat 29/4/17	Mon 22/5/17	100%																											
31	A.1.1.3.3	Establishment of Piling rigs (1 nr)	3 days	0 days	Thu 19/10/17	Sat 21/10/17	100%																											
32	A.1.1.3.4	Construction of Preliminary Pile (1 nr)	13 days	13 days	Sun 22/10/17	Fri 3/11/17	0%																											
33	A.1.1.3.5	Establishment of pile testing equipment	14 days	14 days	Sat 4/11/17	Fri 17/11/17	0%																											
34	A.1.1.3.6	Load Test Preliminary Pile (1 nr)	7 days	7 days	Sat 18/11/17	Fri 24/11/17	0%																											
35	A.1.1.3.7	Submission of Load Test Report (Preliminary Pile)	3 days	3 days	Sat 25/11/17	Mon 27/11/17	0%																											
36	A.1.1.3.8	Review of Load Test result	3 days	3 days	Tue 28/11/17	Thu 30/11/17	0%																											
37	A.1.1.3.9	Establishment of Piling rigs (1 nr)	3 days	0 days	Wed 25/10/17	Sat 4/11/17	100%																											
38	A.1.1.3.10	Submission of temporary working platform design	12 days	2.4 days	Fri 3/11/17	Tue 14/11/17	80%																											
39	A.1.1.3.11	Approval of temporary working platform design	28 days	5.6 days	Wed 15/11/17	Tue 12/12/17	80%																											
40	A.1.1.3.11a	CCTV on uncharted Manhole (PMI 12)	1 day	0 days	Tue 8/8/17	Tue 8/8/17	100%																											
41	A.1.1.3.11b	Demolition of Uncharted Manhole (PMI 15)	2 days	0 days	Mon 21/8/17	Tue 22/8/17	100%																											
42	A.1.1.2.11c	Revised Pile Loading Schedule (PMI 17)	1 day	0 days	Fri 8/9/17	Fri 8/9/17	100%																											
43	A.1.1.2.11d	Pile Sleeve Not Required For E1-RS1 & E1-PC1 (PMI 19)	1 day	0 days	Wed 4/10/17	Wed 4/10/17	100%																											
44	A.1.1.3.12	Construction of Main Pile for pile cap E1-RS1 and E1-PC1(34nrs)	60 days	30.4 days	Wed 15/11/17	Fri 26/1/18	49%																											
45	A.1.1.3.13	Construction of main pile for pile cap E1 PC6 and E1-PC5 (30 nrs)	53 days	53 days	Fri 26/1/18	Tue 20/3/18	0%																											
46	A.1.1.3.14	Construction of main pile for pile cap E1 PC2, E1 PC3 and E1 PC4 (44nrs)	77 days	77 days	Tue 20/3/18	Tue 5/6/18	0%																											
47	A.1.1.3.15	Establishment of Drilling rigs for proof drill (1 nr)	3 days	3 days	Tue 5/6/18	Fri 8/6/18	0%																											
48	A.1.1.3.16	Selection and Carry out Proof drill (2 nrs)	14 days	14 days	Fri 8/6/18	Fri 22/6/18	0%																											
49	A.1.1.3.17	Establishment of pile testing equipment	14 days	14 days	Fri 22/6/18	Fri 6/7/18	0%																											
50	A.1.1.3.18	Selection and Carry Out Load Test Main Pile (1 nr)	7 days	7 days	Fri 6/7/18	Fri 13/7/18	0%																											
51	A.1.1.3.19	Submission of Load Test Report (Main Pile)	7 days	7 days	Fri 13/7/18	Fri 20/7/18	0%																											
52	A.1.1.4	Pile Cap & Footing	184 days	184 days	Fri 20/7/18	Sun 20/1/19	0%																											
53	A.1.1.4.1	Submission of temporary works for ELS	14 days	14 days	Fri 20/7/18	Fri 3/8/18	0%																											
54	A.1.1.4.2	Approval of temporary works for ELS	28 days	28 days	Fri 3/8/18	Fri 31/8/18	0%																											
55	A.1.1.4.3	Installing ELS Works	90 days	90 days	Fri 31/8/18	Thu 29/11/18	0%																											
56	A.1.1.4.4	Pile cap (E1-PC1 and E1-PC2)	39 days	39 days	Fri 14/9/18	Tue 23/10/18	0%																											
57	A.1.1.4.5	Pile Cap (E1-PC3 ~ PC6)	79 days	79 days	Tue 23/10/18	Thu 10/1/19	0%																											
58	A.1.1.4.5a	Interface detail E1-RS1 (PMI 30)	3 days	3 days	Thu 29/11/18	Sun 2/12/18	0%																											
59	A.1.1.4.5b	Water Pipe Diversion (PMI 16)	3 days	3 days	Thu 29/11/18	Sun 2/12/18	0%																											
60	A.1.1.4.6	Retaining structure (E1-RS1)	21 days	21 days	Thu 29/11/18	Thu 20/12/18	0%																											

Critical	Task	Manual Task	Duration-only	Baseline Milestone	Summary	External Tasks	Inactive Milestone
Critical Split	Split	Start-only	Baseline	Milestone	Manual Summary	External Milestone	Inactive Summary
Critical Progress	Task Progress	Finish-only	Baseline Split	Summary Progress	Project Summary	Inactive Task	Deadline

ITEM	ID	Task Name	Duration	Remaining Duration	Start	Finish	2018												2019												2020			
							Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
61	A.1.1.4.7	Material submission of water proofing works	28 days	28 days	Thu 2/8/18	Wed 29/8/18																												
62	A.1.1.4.8	Approval of material of water proofing wroks	28 days	28 days	Thu 30/8/18	Wed 26/9/18																												
63	A.1.1.4.9	Procurement to delivery of water proofing material	30 days	30 days	Thu 27/9/18	Fri 26/10/18																												
64	A.1.1.4.10	Waterproofing Works	14 days	14 days	Thu 20/12/18	Thu 3/1/19																												
65	A.1.1.4.11	Backfilling	10 days	10 days	Thu 10/1/19	Sun 20/1/19																												
66	A.1.1.5	Superstructures	199 days	199 days	Sun 20/1/19	Wed 7/8/19																												
67	A.1.1.5.1	Submission of temporary work design and method for piers construction	10 days	10 days	Sun 20/1/19	Wed 30/1/19																												
68	A.1.1.5.2	Approval to temporary works design and method for piers construction	28 days	28 days	Wed 30/1/19	Wed 27/2/19																												
69	A.1.1.5.3	Construction of piers (E1-P1 ~ P5)	34 days	34 days	Wed 27/2/19	Tue 2/4/19																												
70	A.1.1.5.4	Conatruction of Ramp Structures	20 days	20 days	Tue 2/4/19	Mon 22/4/19																												
71	A.1.1.5.5	Construction of Abutment (E1-PC6)	27 days	27 days	Tue 2/4/19	Mon 29/4/19																												
72	A.1.1.5.6	Construction of deck slab with cast in items	100 days	100 days	Mon 29/4/19	Wed 7/8/19																												
73	A.1.1.6	Construction of Bearings and Movement Joints	333.4 days	333.4 days	Sat 6/10/18	Wed 4/9/19																												
74	A.1.1.6.1	Proposal of Bridge Bearing Specialist	45 days	45 days	Sat 6/10/18	Mon 19/11/18																												
75	A.1.1.6.2	Approval of Bridge Bearing Specialist	28 days	28 days	Tue 20/11/18	Mon 17/12/18																												
76	A.1.1.6.3	Design submission of Bridge Bearing	45 days	45 days	Sat 6/10/18	Mon 19/11/18																												
77	A.1.1.6.4	Approval of design submission of Bridge bearing	28 days	28 days	Tue 20/11/18	Mon 17/12/18																												
78	A.1.1.6.5	Material submission of Bridge Bearing	28 days	28 days	Tue 23/10/18	Mon 19/11/18																												
79	A.1.1.6.6	Approval of material submission to Bridge Bearing	28 days	28 days	Tue 20/11/18	Mon 17/12/18																												
80	A.1.1.6.7	Testing and submission of result of Bridge Bearing	14 days	14 days	Tue 18/12/18	Mon 31/12/18																												
81	A.1.1.6.8	Procurement and delivery of Bridge Bearing	90 days	90 days	Tue 1/1/19	Sun 31/3/19																												
82	A.1.1.6.9	Installation of Bearings (6 nr)	40 days	40 days	Tue 2/4/19	Sun 12/5/19																												
83	A.1.1.6.10	Material submission of movement joints	28 days	28 days	Sat 23/2/19	Fri 22/3/19																												
84	A.1.1.6.11	Approval of material submission of movement joints	28 days	28 days	Sat 23/3/19	Fri 19/4/19																												
85	A.1.1.6.12	Procurement to delivery of movement joints	60 days	60 days	Sat 20/4/19	Tue 18/6/19																												
86	A.1.1.6.13	Construction of MJ (3 nr)	28 days	28 days	Wed 7/8/19	Wed 4/9/19																												
87	A.1.1.7	Installation of Escalators (E1-ES01 to ES-12)	592 days	592 days	Thu 2/8/18	Sun 15/3/20																												
88	A.1.1.7.1	Proposal of Escalator Specialist	28 days	28 days	Thu 2/8/18	Wed 29/8/18																												
89	A.1.1.7.2	Approval of Escalator Specialist	28 days	28 days	Thu 30/8/18	Wed 26/9/18																												
90	A.1.1.7.3	Submission of Escalator E&M (SEM)	60 days	60 days	Thu 27/9/18	Sun 25/11/18																												
91	A.1.1.7.4	Approval of Escalator E&M (SEM)	28 days	28 days	Mon 26/11/18	Sun 23/12/18																												
92	A.1.1.7.5	Material submission of escalator	28 days	28 days	Sat 27/10/18	Fri 23/11/18																												
93	A.1.1.7.6	Approval of material submission of escalator	30 days	30 days	Sat 24/11/18	Sun 23/12/18																												
94	A.1.1.7.7	Procurement to delivery of escalator	260 days	260 days	Mon 24/12/18	Mon 9/9/19																												
95	A.1.1.7.8	Submission of method statement for installation of escalator	28 days	28 days	Mon 27/5/19	Sun 23/6/19																												
96	A.1.1.7.9	Approval of method statement for installation of escalator	28 days	28 days	Mon 24/6/19	Sun 21/7/19																												
97	A.1.1.7.10	Installation of escalators and associate works (E1-RS1 to E1-P2)	45 days	45 days	Tue 10/9/19	Thu 24/10/19																												
98	A.1.1.7.11	Installation of escalator and associate works (E1-P2 to E1 P4)	45 days	45 days	Fri 25/10/19	Sun 8/12/19																												
99	A.1.1.7.12	Escalator Installation and associate works (E1-P4 to E1-ABT)	45 days	45 days	Mon 9/12/19	Wed 22/1/20																												
100	A.1.1.7.13	Parapet and Roofing	259 days	259 days	Mon 1/7/19	Sun 15/3/20																												
101	A.1.1.7.14	Material submission of Plexiglass	28 days	28 days	Mon 1/7/19	Sun 28/7/19																												
102	A.1.1.7.15	Approval of material of Plexiglass	28 days	28 days	Mon 29/7/19	Sun 25/8/19																												
103	A.1.1.7.16	Procurement to delivery of Plexiglass	60 days	60 days	Mon 26/8/19	Thu 24/10/19																												
104	A.1.1.7.17	Construction of pedestrian Plexiglass parapet	70 days	70 days	Sat 9/11/19	Fri 17/1/20																												
105	A.1.1.7.18	Material submission of fall arrest system	28 days	28 days	Fri 30/8/19	Thu 26/9/19																												
106	A.1.1.7.19	Approval of material of fall arrest system	28 days	28 days	Fri 27/9/19	Thu 24/10/19																												
107	A.1.1.7.20	Procurement of fall arrest system	45 days	45 days	Fri 25/10/19	Sun 8/12/19																												
108	A.1.1.7.21	Material submission of corrugated steel roof	28 days	28 days	Sun 22/9/19	Sat 19/10/19																												
109	A.1.1.7.22	Approval of material for corrugated steel roof	28 days	28 days	Sun 20/10/19	Sat 16/11/19																												
110	A.1.1.7.23	Procurement of corrugated steel roof	30 days	30 days	Sun 17/11/19	Mon 16/12/19																												
111	A.1.1.7.24	Design submission of roof																																

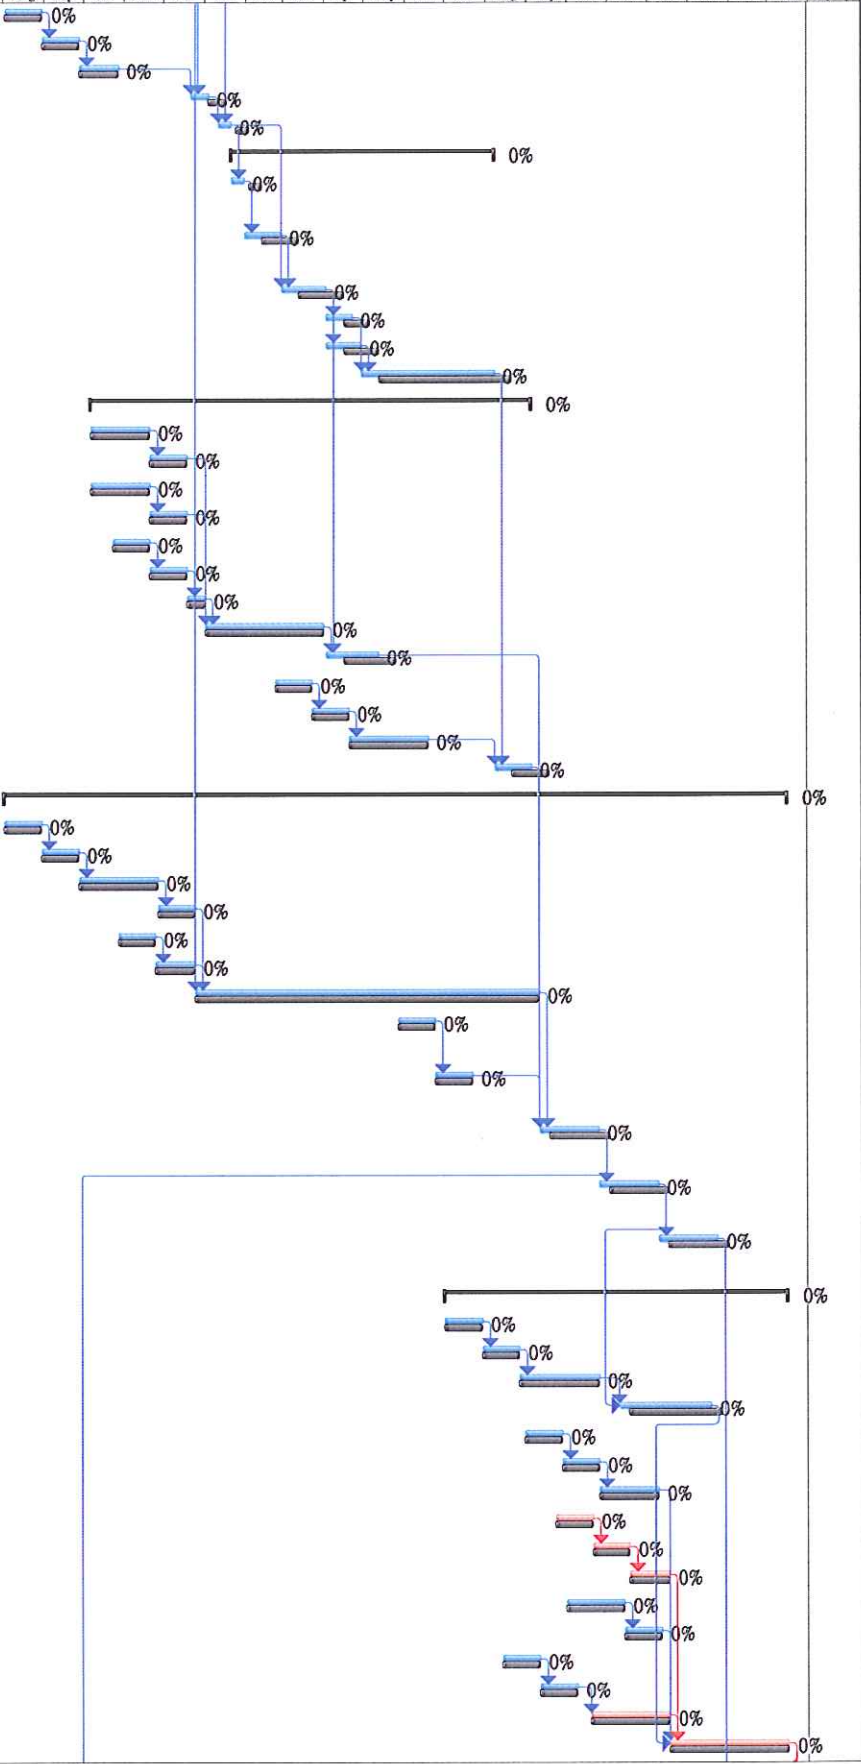

Critical

Critical Split

Critical Progress

Task

Split

Task Progress

Manual Task

Start-only

Finish-only

Duration-only

Baseline

Baseline Split

Baseline Milestone

Milestone

Summary Progress

Summary

Manual Summary

Project Summary

External Tasks

External Milestone


Inactive Task


Inactive Milestone

Inactive Summary

Deadline

[illegible]

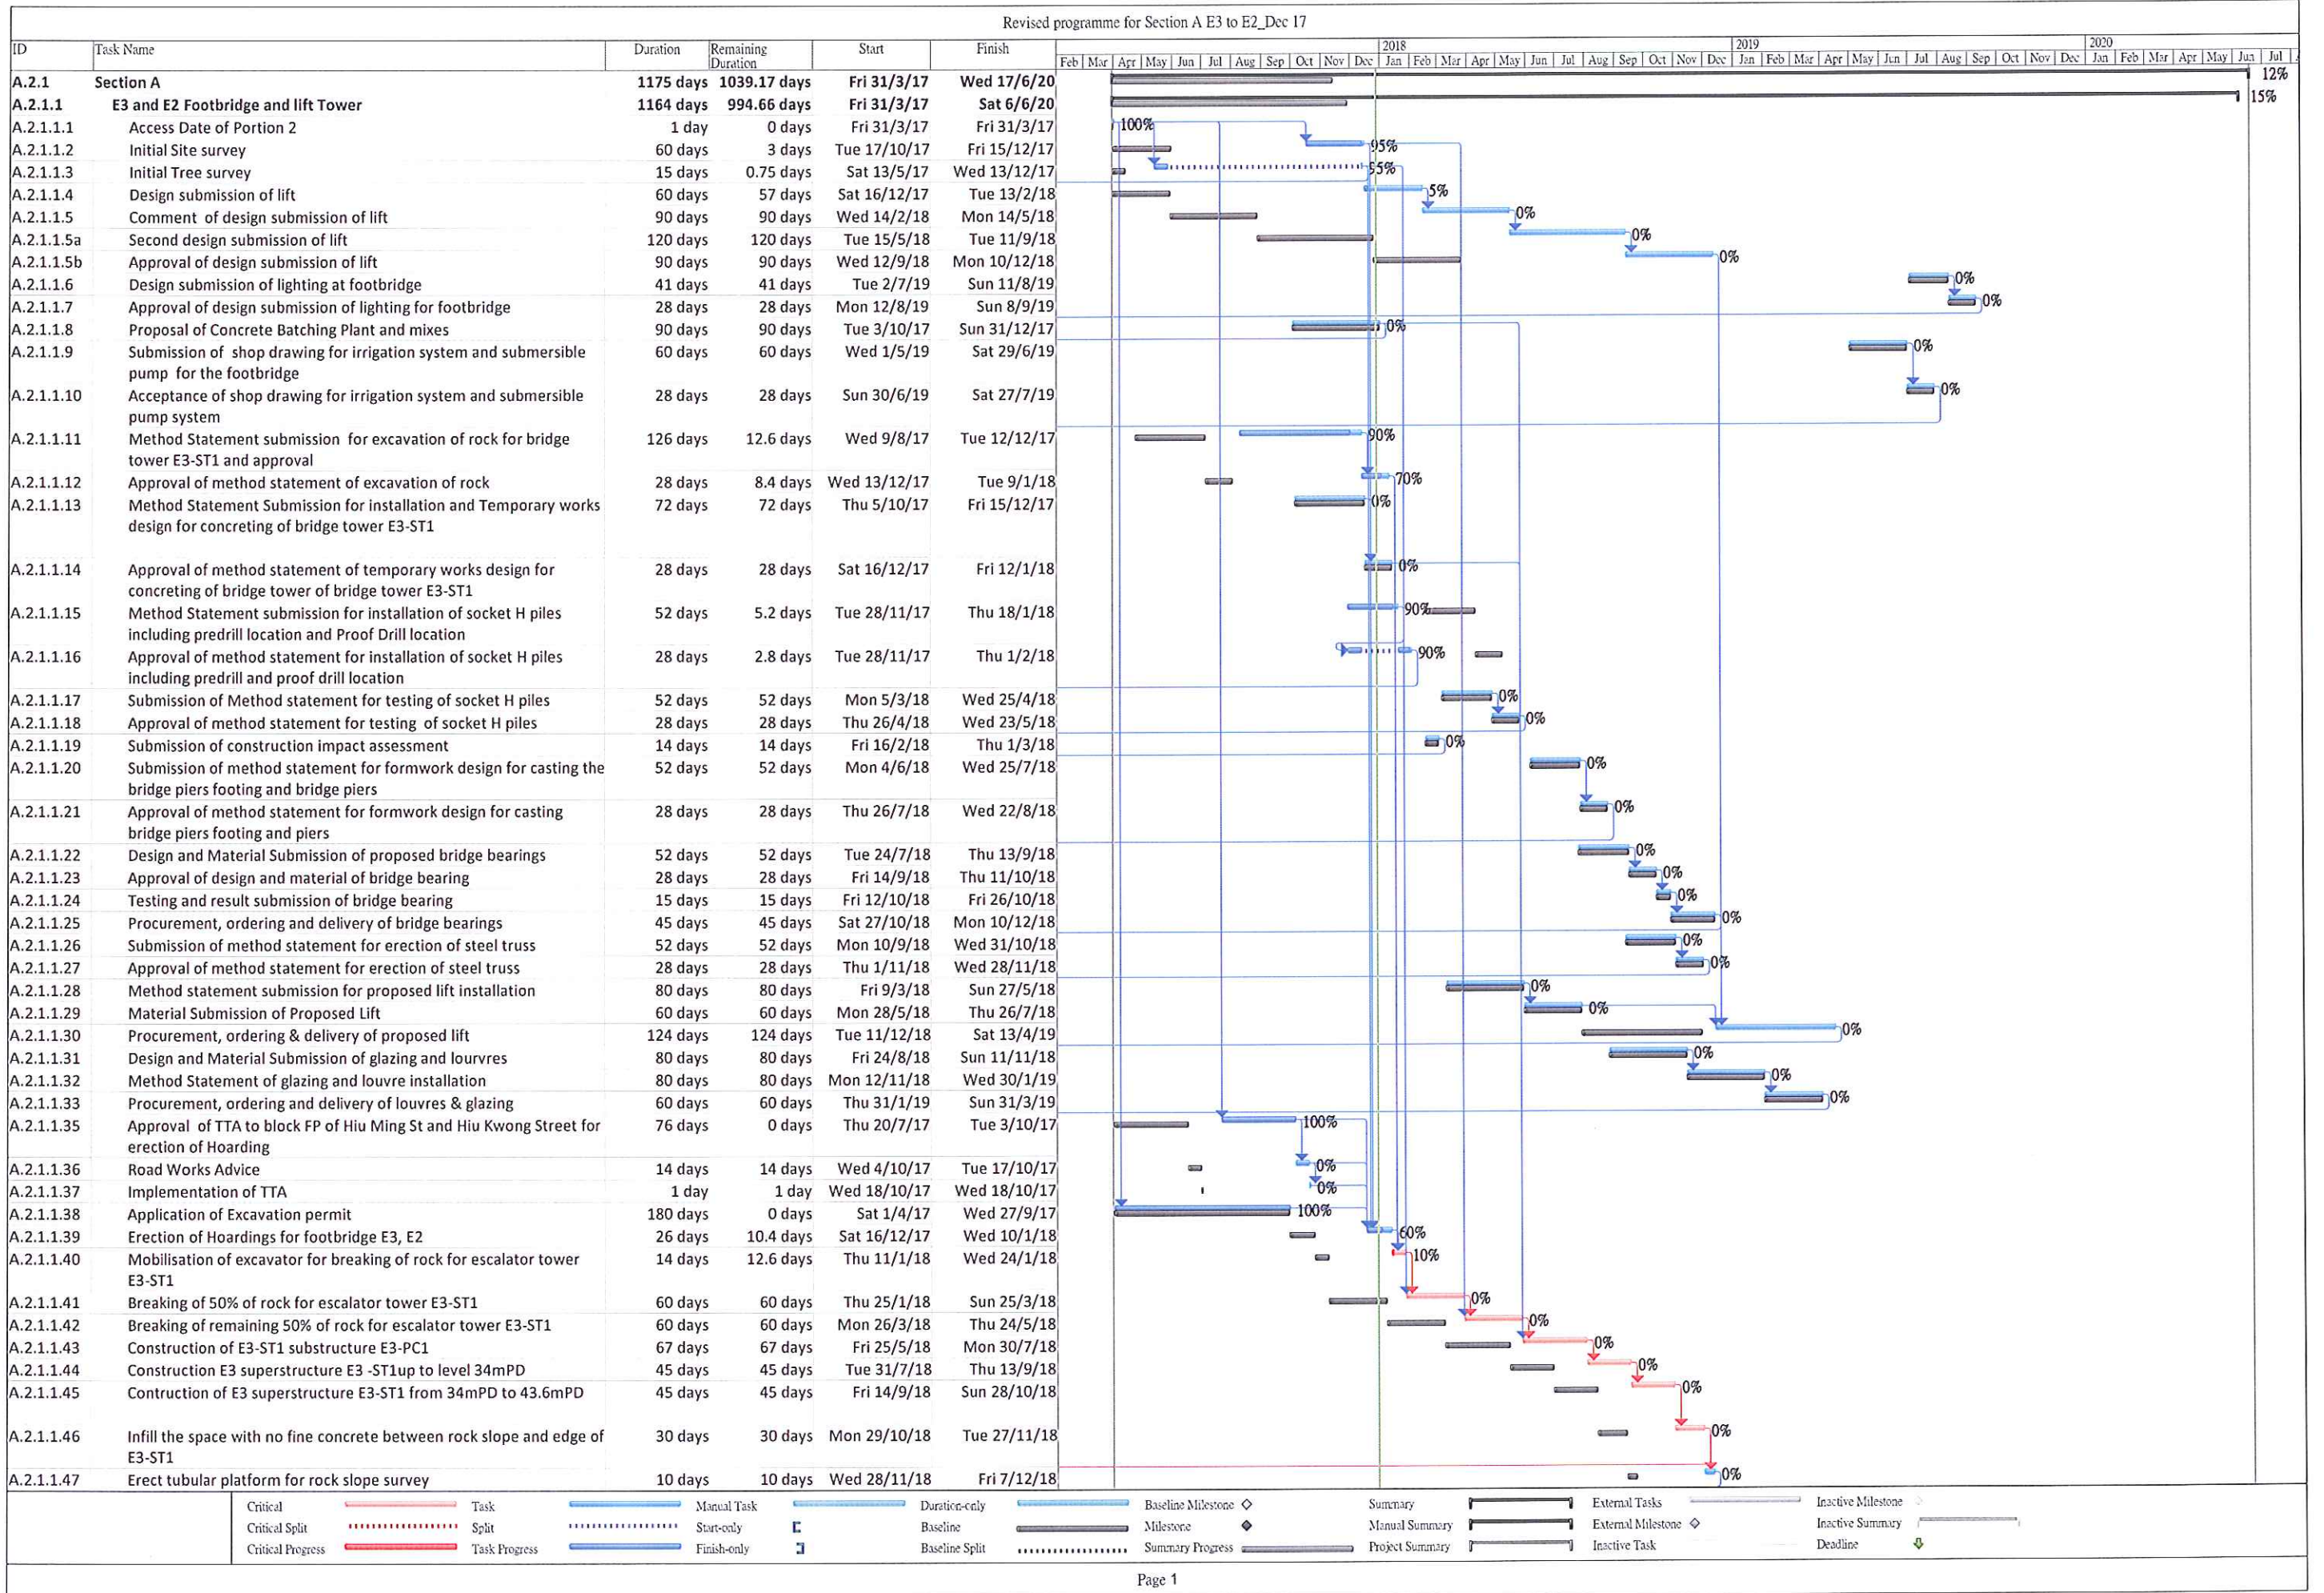


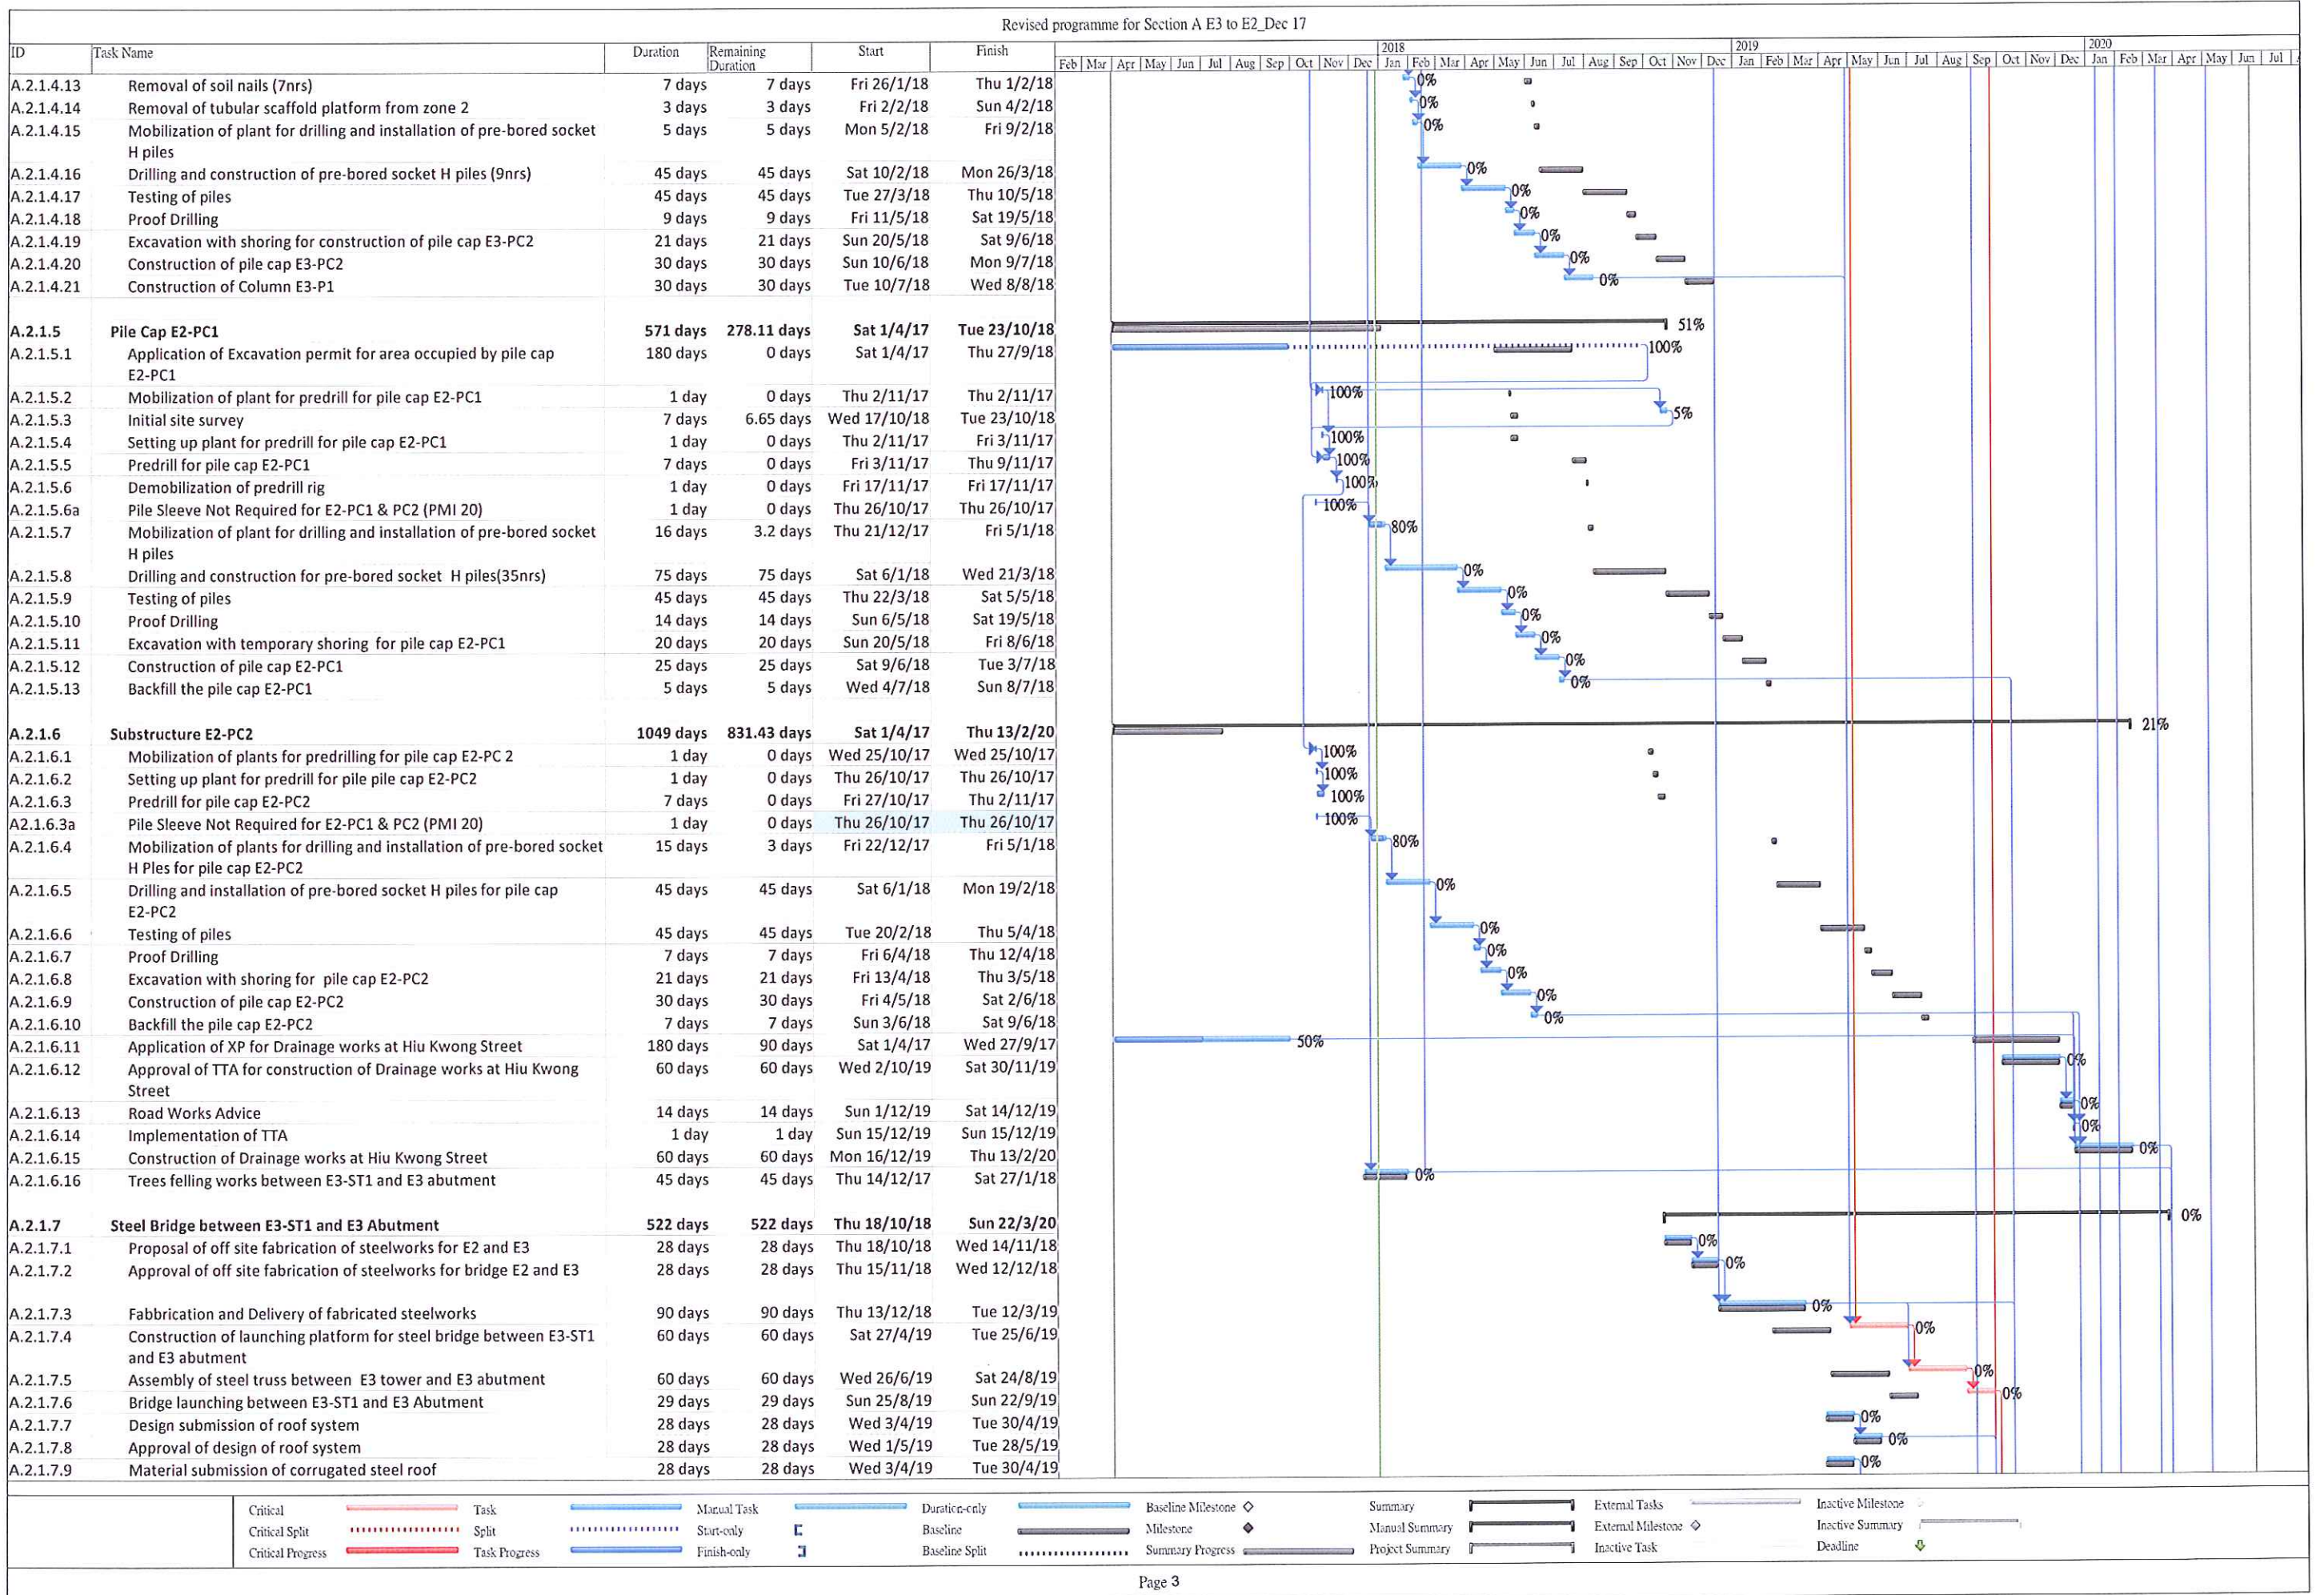


Revised programme for Section A E3 to E2_Dec 17


ID	Task Name	Duration	Remaining Duration	Start	Finish
A.2.1.7.10	Approval of corrugated steel roof	30 days	30 days	Wed 1/5/19	Thu 30/5/19
A.2.1.7.11	Procurement to delivery of corrugated steel roof	28 days	28 days	Fri 31/5/19	Thu 27/6/19
A.2.1.7.12	Material submission of fall arrest system	28 days	28 days	Wed 3/4/19	Tue 30/4/19
A.2.1.7.13	Approval of fall arrest system	28 days	28 days	Wed 1/5/19	Tue 28/5/19
A.2.1.7.14	Procurement to delivery of fall arrest system	30 days	30 days	Wed 29/5/19	Thu 27/6/19
A.2.1.7.15	Roof construction of the steel truss E3-ST1 to E3 abutment	50 days	50 days	Mon 23/9/19	Mon 11/11/19
A.2.1.7.16	Construction of screeding and paving blocks	40 days	40 days	Tue 12/11/19	Sat 21/12/19
A.2.1.7.17	Installation of parapets and planters	40 days	40 days	Sun 22/12/19	Thu 30/1/20
A.2.1.7.18	Installation of lightings to steel truss between E3 tower and E3 abutment	45 days	45 days	Fri 31/1/20	Sun 15/3/20
A.2.1.7.19	Installation of irrigation pipe and water point	7 days	7 days	Mon 16/3/20	Sun 22/3/20
A.2.1.8	Superstructure of Covered Walkway	162 days	162 days	Mon 23/9/19	Mon 2/3/20
A.2.1.8.1	Expose the substructure of the Covered Walkway	20 days	20 days	Mon 23/9/19	Sat 12/10/19
A.2.1.8.2	Construction of columns and beams for covered walkway	60 days	60 days	Sun 13/10/19	Wed 11/12/19
A.2.1.8.3	Installation of steel sheet roof for the covered walkway	30 days	30 days	Thu 12/12/19	Fri 10/1/20
A.2.1.8.4	Installation of Lighting to covered walkway	45 days	45 days	Sat 11/1/20	Mon 24/2/20
A.2.1.8.5	Installation of irrigation pipe	7 days	7 days	Tue 25/2/20	Mon 2/3/20
A.2.1.9	Superstructure of E2-LT1 and Lift	287 days	287 days	Wed 4/9/19	Tue 16/6/20
A.2.1.9.1	Excavation to expose footing E2-PC1	7 days	7 days	Sun 13/10/19	Sat 19/10/19
A.2.1.9.2	Construction of superstructure of lift tower E2-LT1	62 days	62 days	Sun 20/10/19	Fri 20/12/19
A.2.1.9.3	Installation of lift (2nrs)	60 days	60 days	Sat 21/12/19	Tue 18/2/20
A.2.1.9.4	Installation of E&M for the lift towers and Pillar Box	50 days	50 days	Wed 19/2/20	Wed 8/4/20
A.2.1.9.5	Testing and commissioning of lifts and submission of form LE5 to EMSD	60 days	60 days	Thu 9/4/20	Sun 7/6/20
A.2.1.9.6	Installation of louver and finishing works	20 days	20 days	Thu 28/5/20	Tue 16/6/20
A.2.1.9.7	Application for connection to existing water mains	90 days	90 days	Wed 4/9/19	Mon 2/12/19
A.2.1.9.8	Trenching works for connection of existing water connection point	28 days	28 days	Tue 3/12/19	Mon 30/12/19
A.2.1.9.9	Installation of water meter box	7 days	7 days	Thu 9/4/20	Wed 15/4/20
A.2.1.9.10	Planting works on bridge	7 days	7 days	Thu 16/4/20	Wed 22/4/20
A.2.1.10	Superstructure of E2-P1	48 days	48 days	Sat 21/12/19	Thu 6/2/20
A.2.1.10.1	Excavation to expose Pile cap E2-PC2 for column E2-P1	3 days	3 days	Sat 21/12/19	Mon 23/12/19
A.2.1.10.2	Construction of column for E2-P1	42 days	42 days	Tue 24/12/19	Mon 3/2/20
A.2.1.10.3	General tidy up	3 days	3 days	Tue 4/2/20	Thu 6/2/20
A.3.1.11	Bridge between E2-P1 to E2-P3	545 days	545 days	Fri 21/12/18	Wed 17/6/20
A.3.1.11.1	Access date of E2 between Pier E2-P2 to E2-P3 (Portion 3)	1 day	1 day	Fri 21/12/18	Fri 21/12/18
A.3.1.11.2	Initial site survey	15 days	15 days	Sat 22/12/18	Sat 5/1/19
A.3.1.11.3	Erection of Hoarding at South bound footpath of Hiu Kwong St	8 days	8 days	Sat 22/12/18	Sat 29/12/18
A.3.1.11.4	Excavation of inspection pits to locate utilities	20 days	20 days	Sun 6/1/19	Fri 25/1/19
A.3.1.11.5	Diversion of utilities by UU	90 days	90 days	Sat 26/1/19	Thu 25/4/19
A.3.1.11.6	Excavation with shoring for construction of E2-F3	30 days	30 days	Fri 26/4/19	Sat 25/5/19
A.3.1.11.7	Construction of pad footing of E2-F3	30 days	30 days	Sun 26/5/19	Mon 24/6/19
A.3.1.11.8	Construction of column for E2-P2	30 days	30 days	Tue 25/6/19	Wed 24/7/19
A.3.1.11.9	Excavation with shoring for construction of E2-F4	30 days	30 days	Thu 25/7/19	Fri 23/8/19
A.3.1.11.10	Construction of pad footing of E2-F4	30 days	30 days	Sat 24/8/19	Sun 22/9/19
A.3.1.11.11	Construction of column for E2-P3 and the bridge deck	35 days	35 days	Mon 23/9/19	Sun 27/10/19
A.3.1.11.12	Off site Fabrication of Steel deck truss between E2-LT1 to E2-P1, E2-P1 to E2-P2	90 days	90 days	Fri 26/4/19	Wed 24/7/19
A.3.1.11.13	Off site Fabrication of Steel deck truss between E2-P2 to E2-P3 and E2-P3 to bridge constructed by others	90 days	90 days	Thu 25/7/19	Tue 22/10/19
A.3.1.11.14	Lifting of steel truss between E2-LT1 to E2-P1	7 days	7 days	Tue 4/2/20	Mon 10/2/20
A.3.1.11.15	Lifting of steel truss between E2-P1 to E2-P2	7 days	7 days	Tue 11/2/20	Mon 17/2/20
A.3.1.11.16	Lifting of Truss between E2-P2 to E2-P3	7 days	7 days	Tue 18/2/20	Mon 24/2/20
A.3.1.11.17	Lifting of truss for E2-P3 to connect to bridge constructed by others	7 days	7 days	Tue 25/2/20	Mon 2/3/20
A.3.1.11.18	Roof installation of the bridge from E2-LT1 to E2-P3	60 days	60 days	Tue 3/3/20	Fri 1/5/20
A.3.1.11.19	Screeding and paving blocks for the bridge from E2-LT1 to E2-P3	42 days	42 days	Sun 12/4/20	Sat 23/5/20

[illegible]

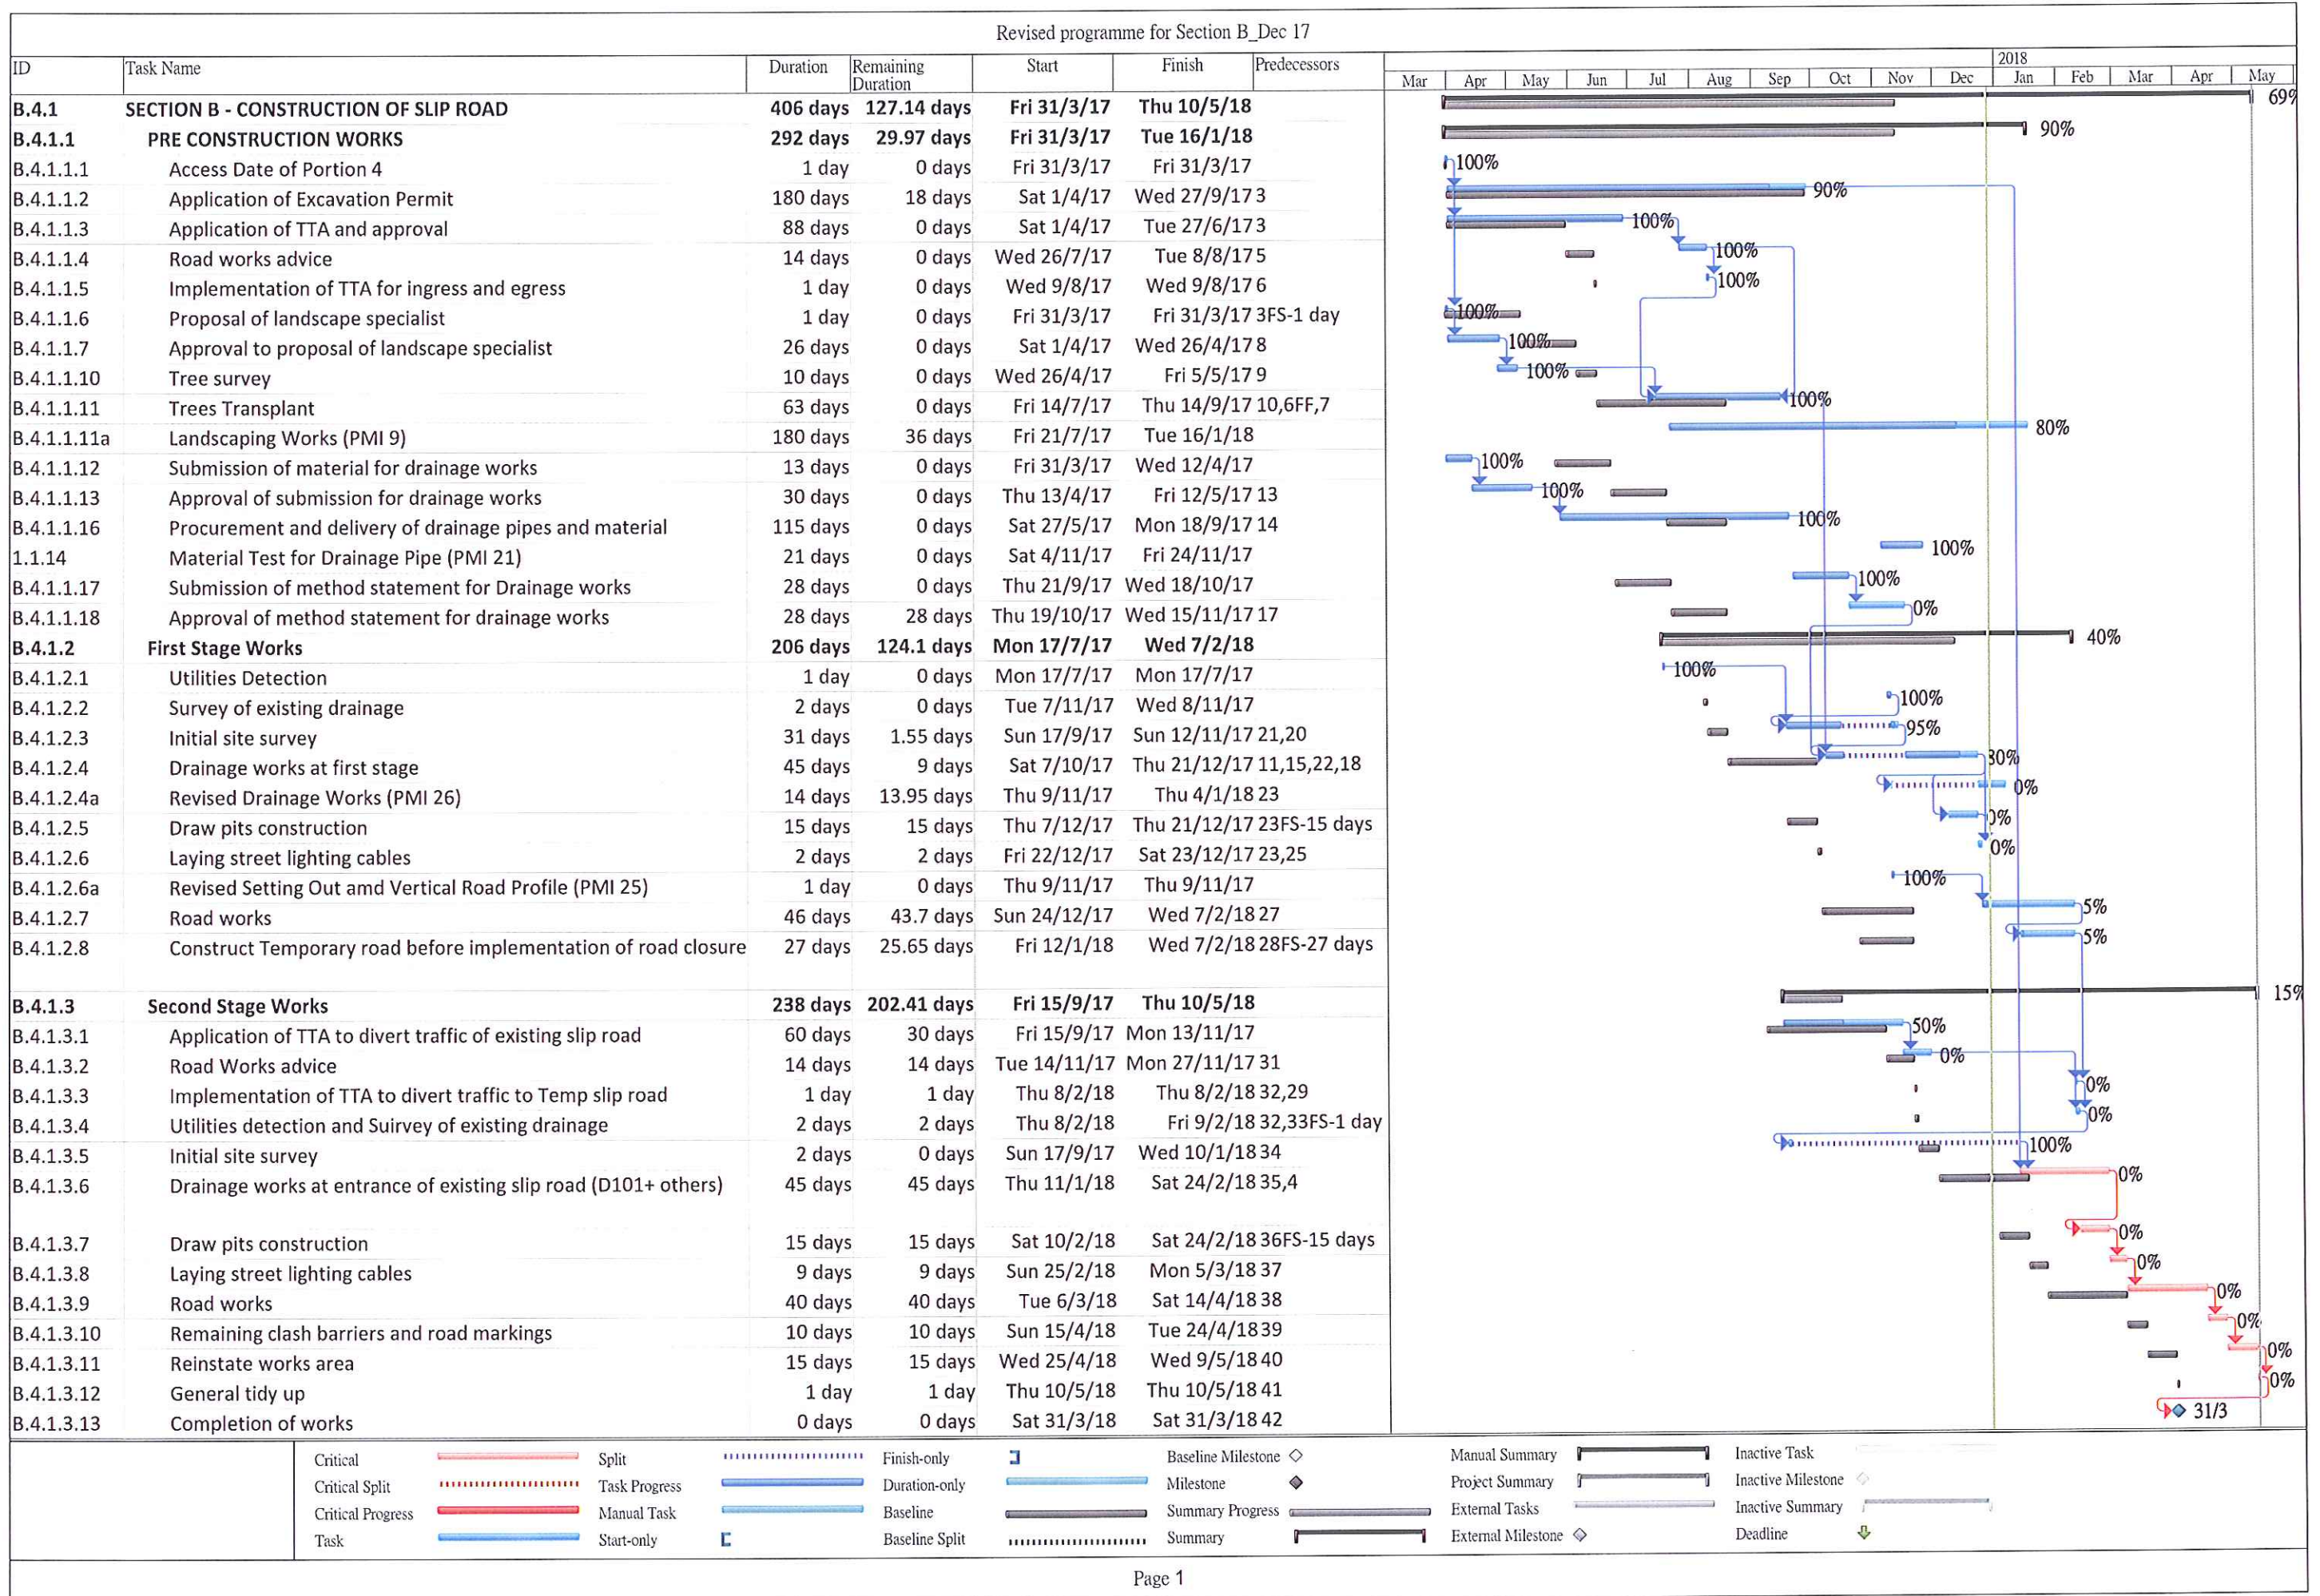



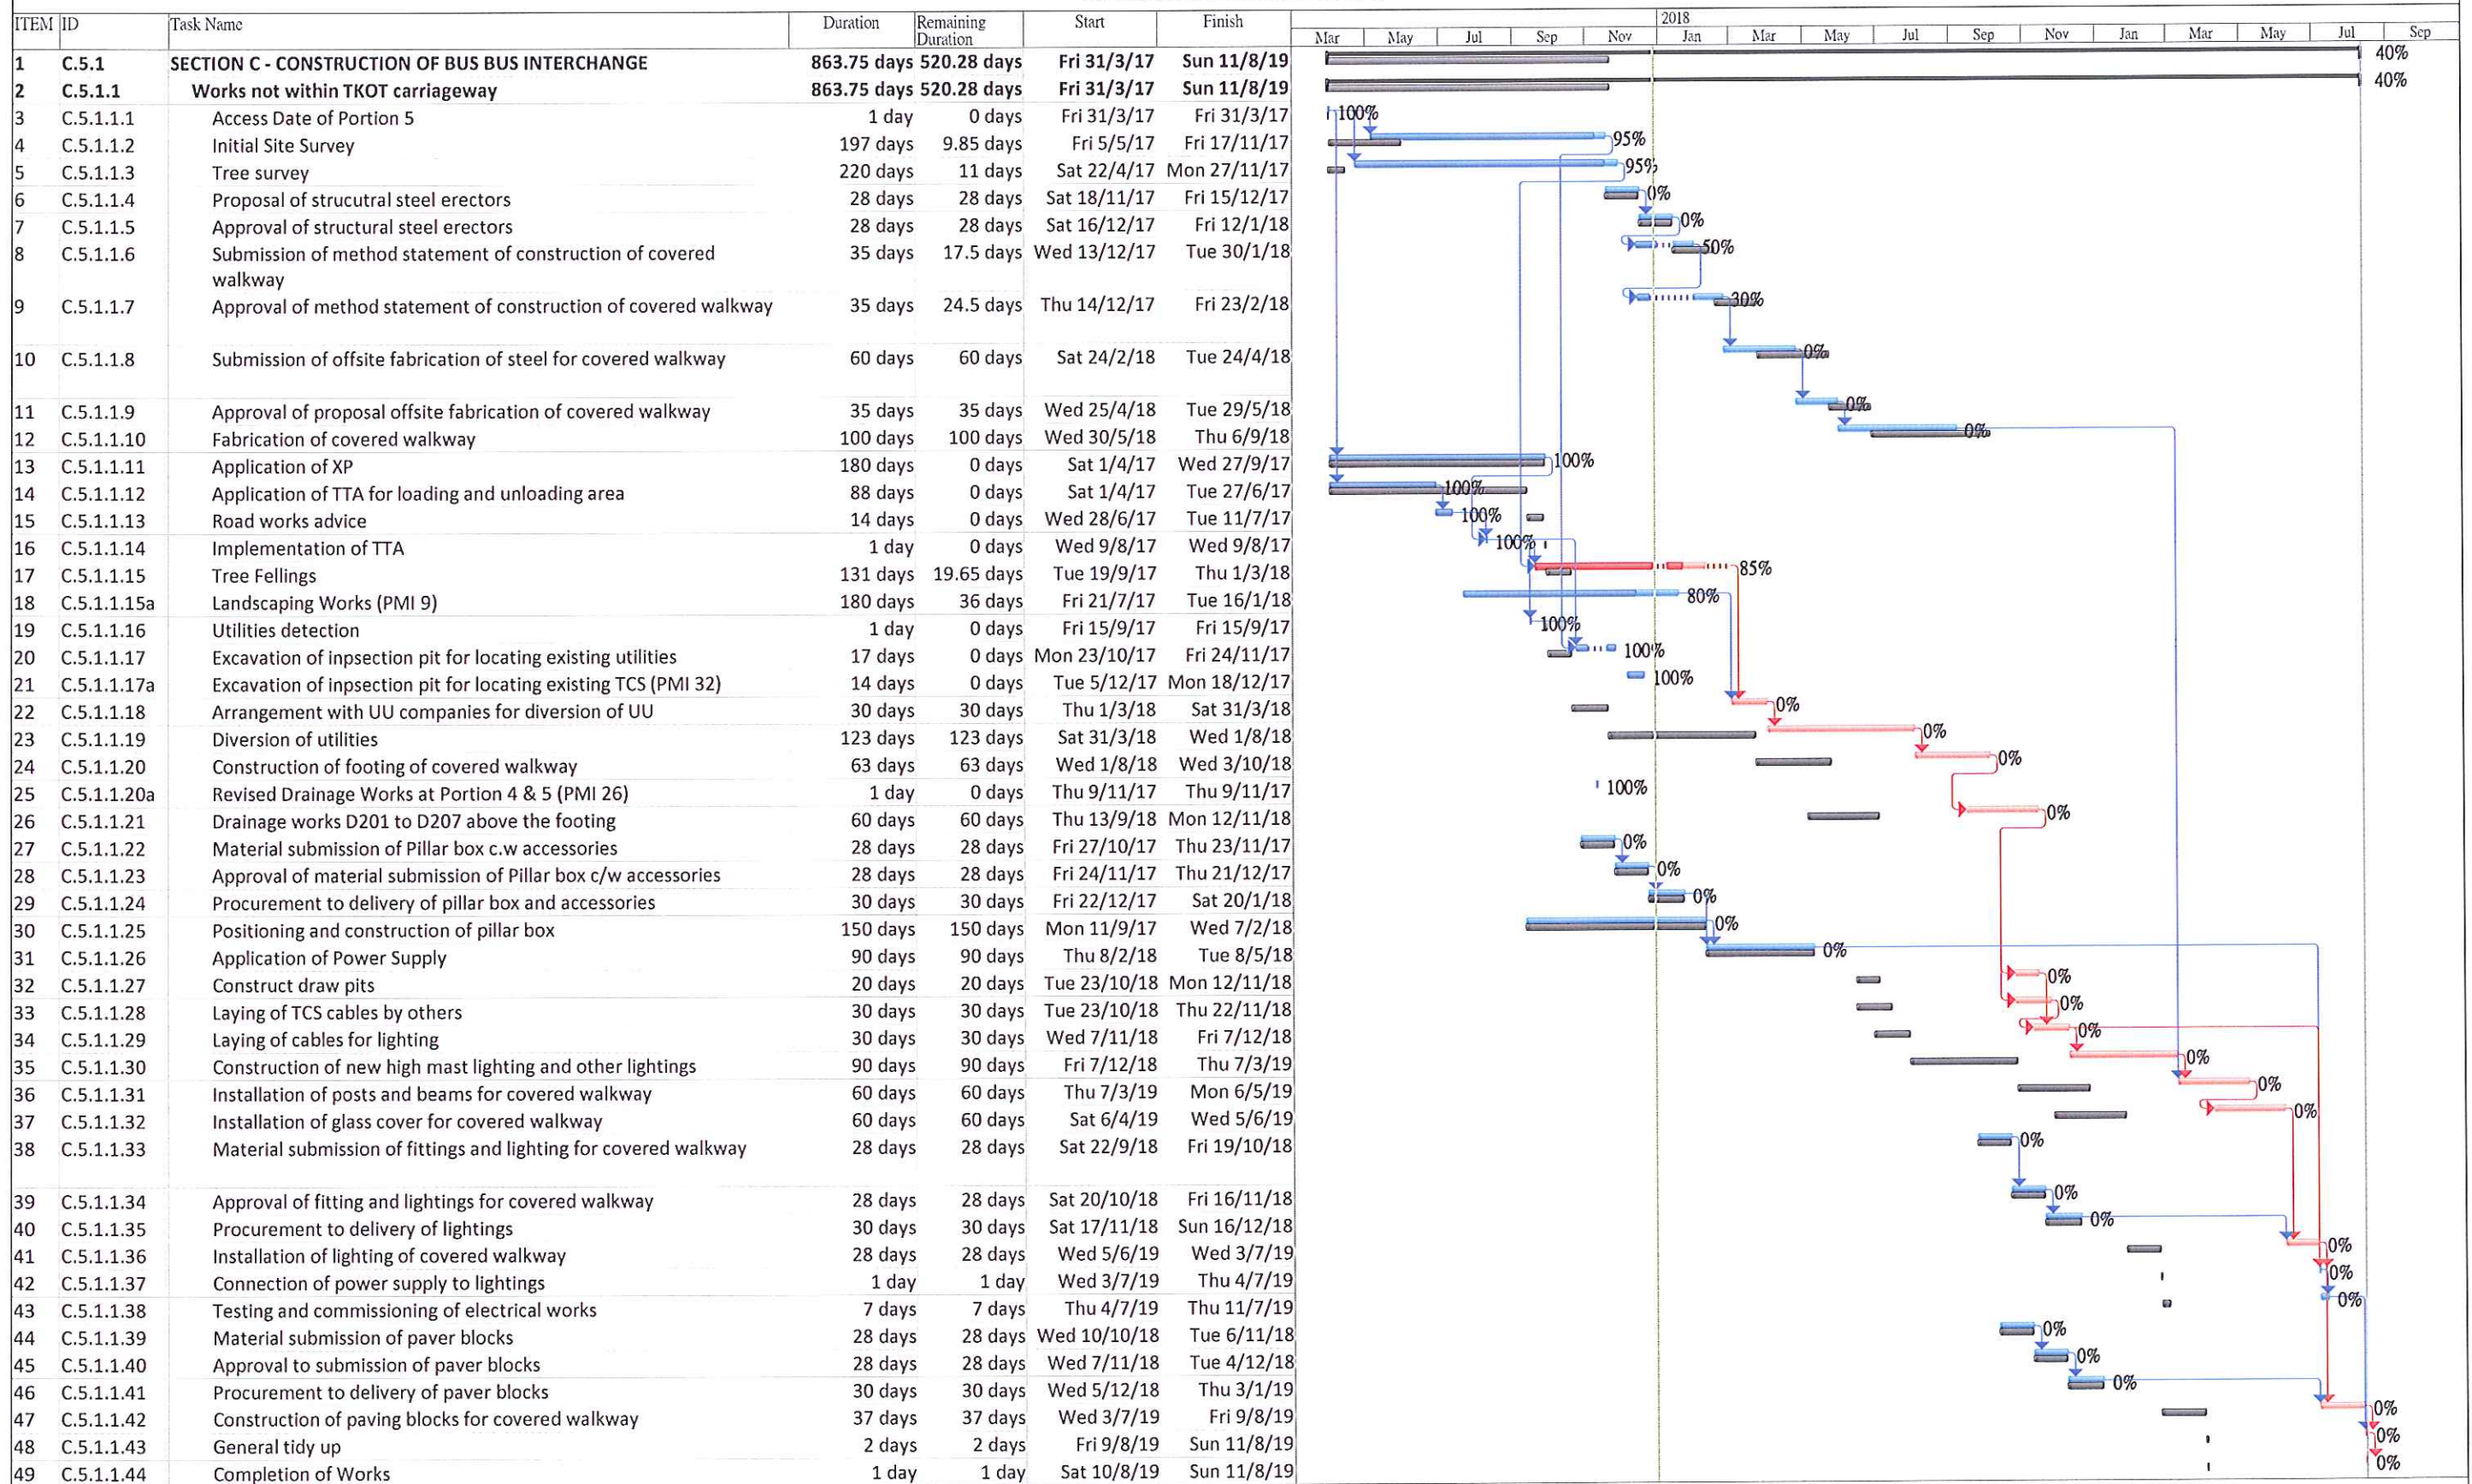



Critical	Task	Manual Task	Duration-only	Baseline Milestone	Summary	External Tasks	Inactive Milestone
Critical Split	Split	Start-only	Baseline	Milestone	Manual Summary	External Milestone	Inactive Summary
Critical Progress	Task Progress	Finish-only	Baseline Split	Summary Progress	Project Summary	Inactive Task	Deadline

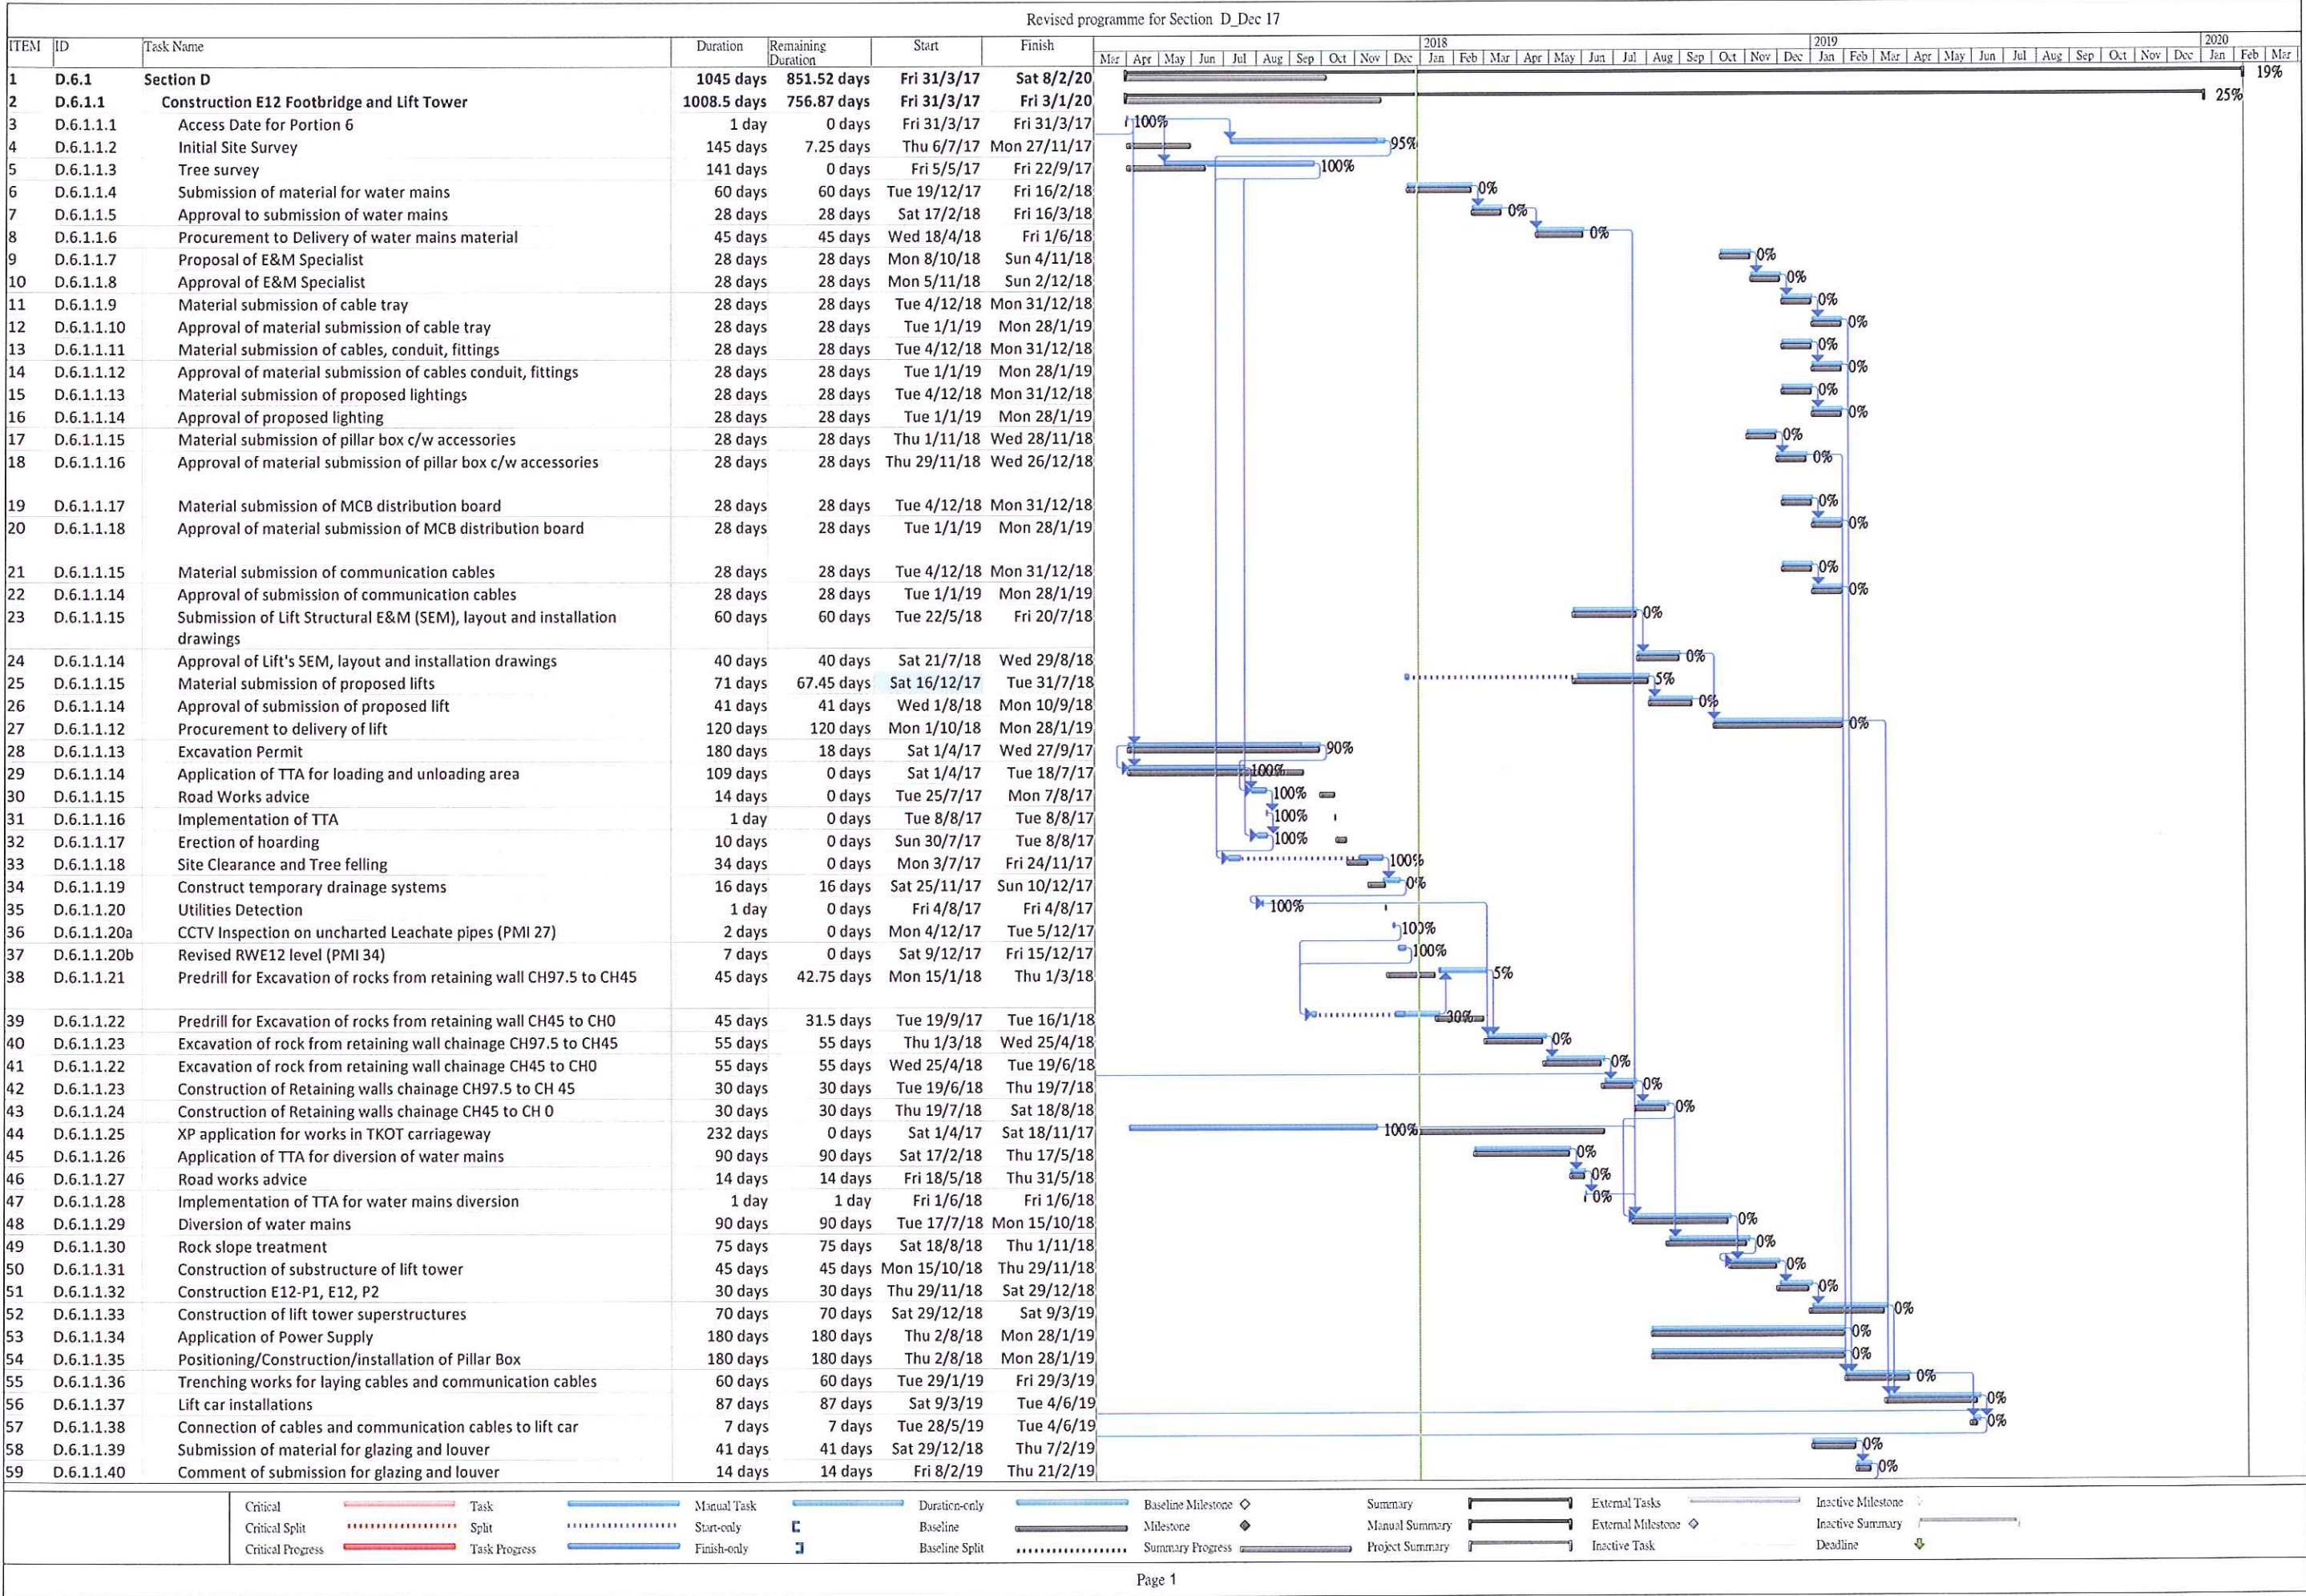

[illegible]

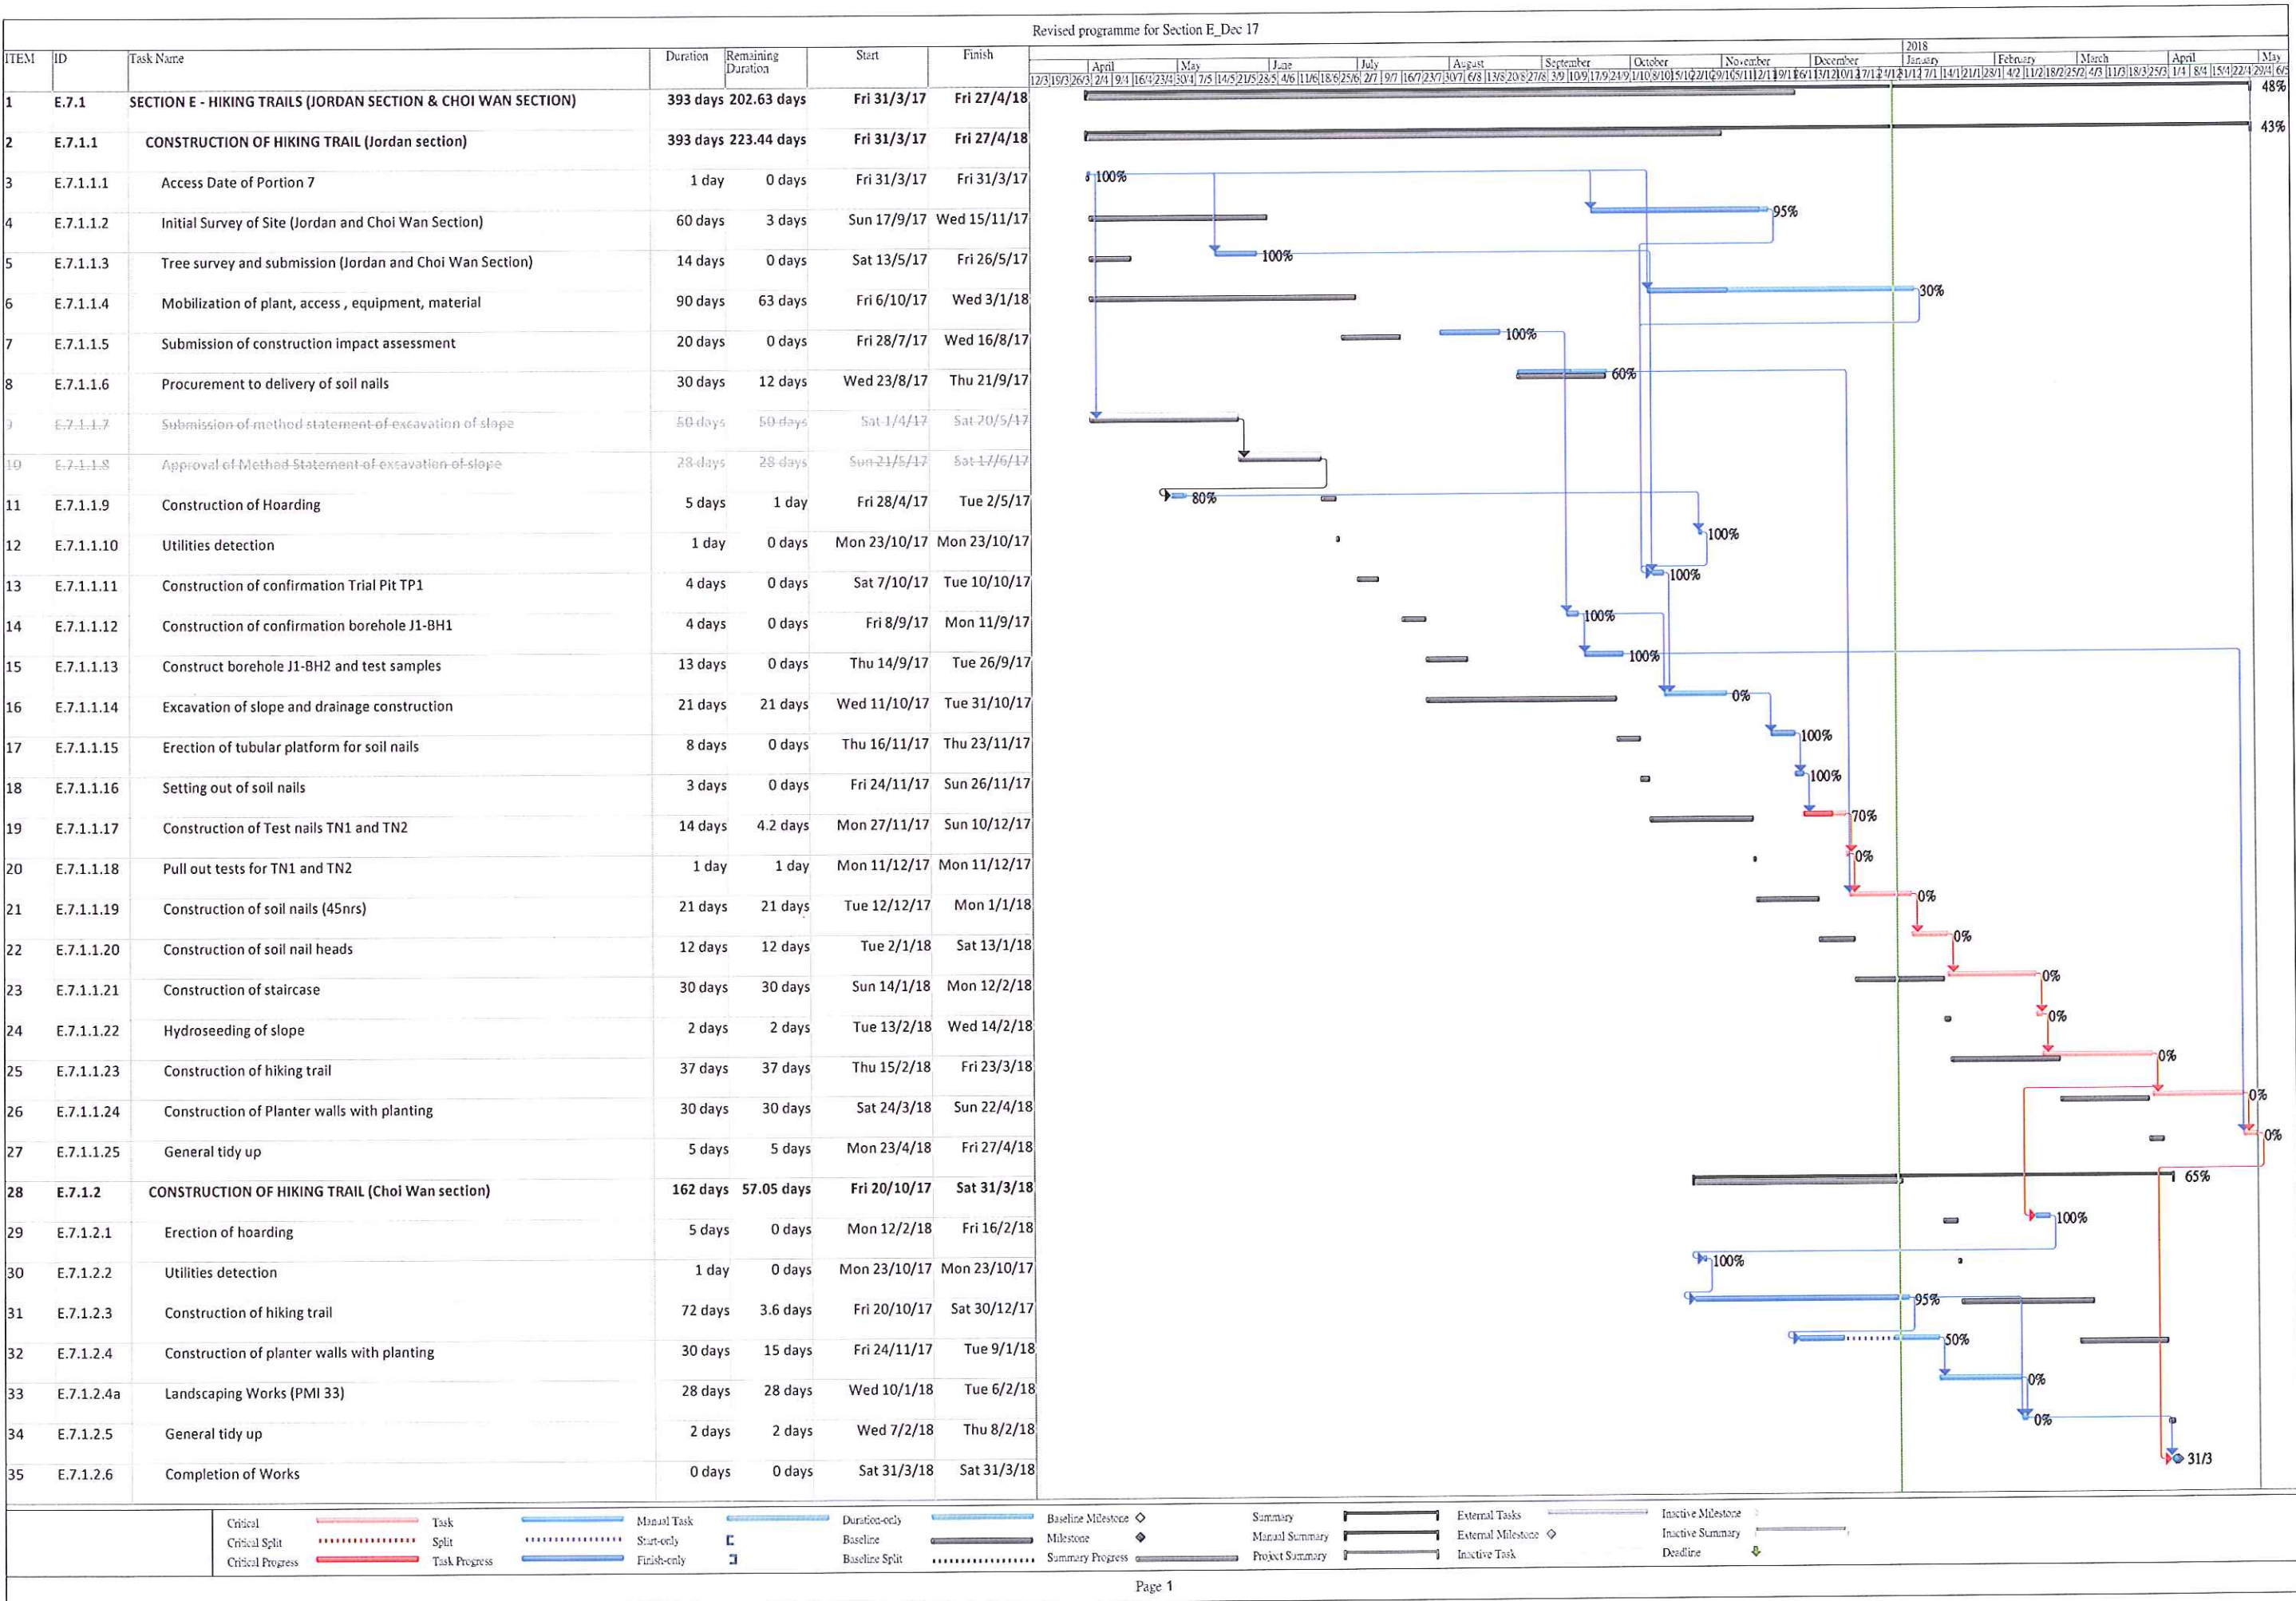

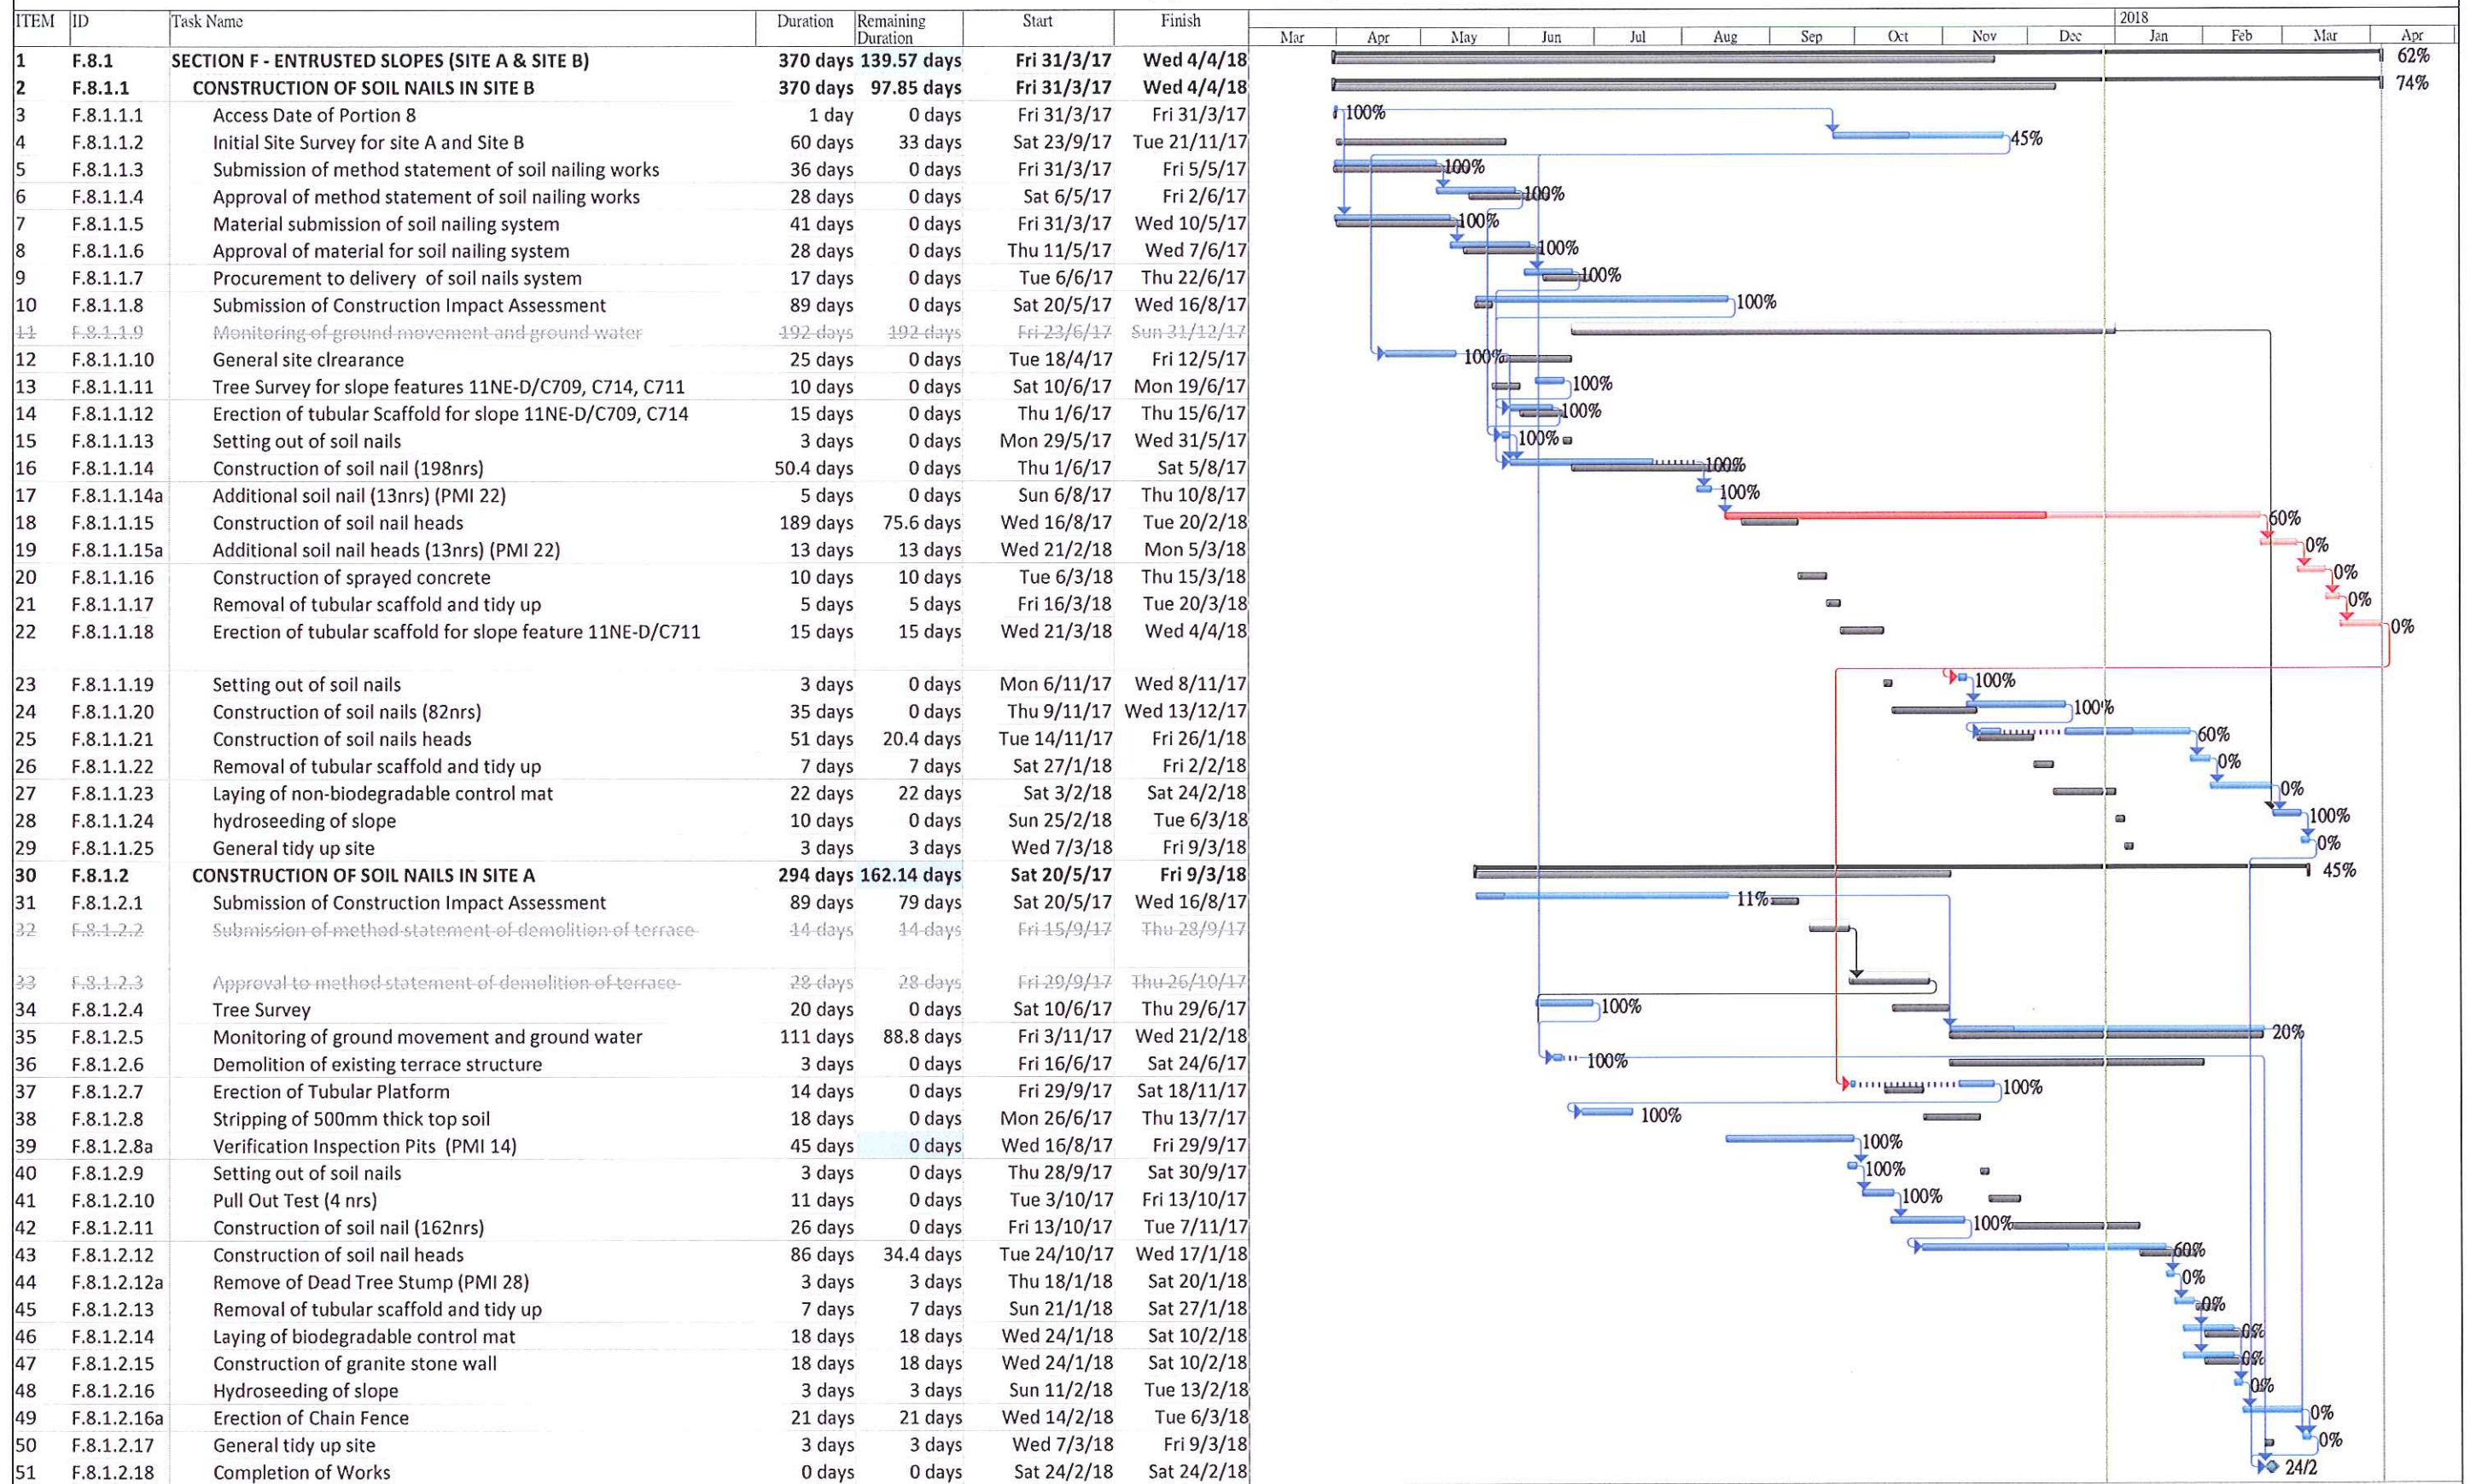

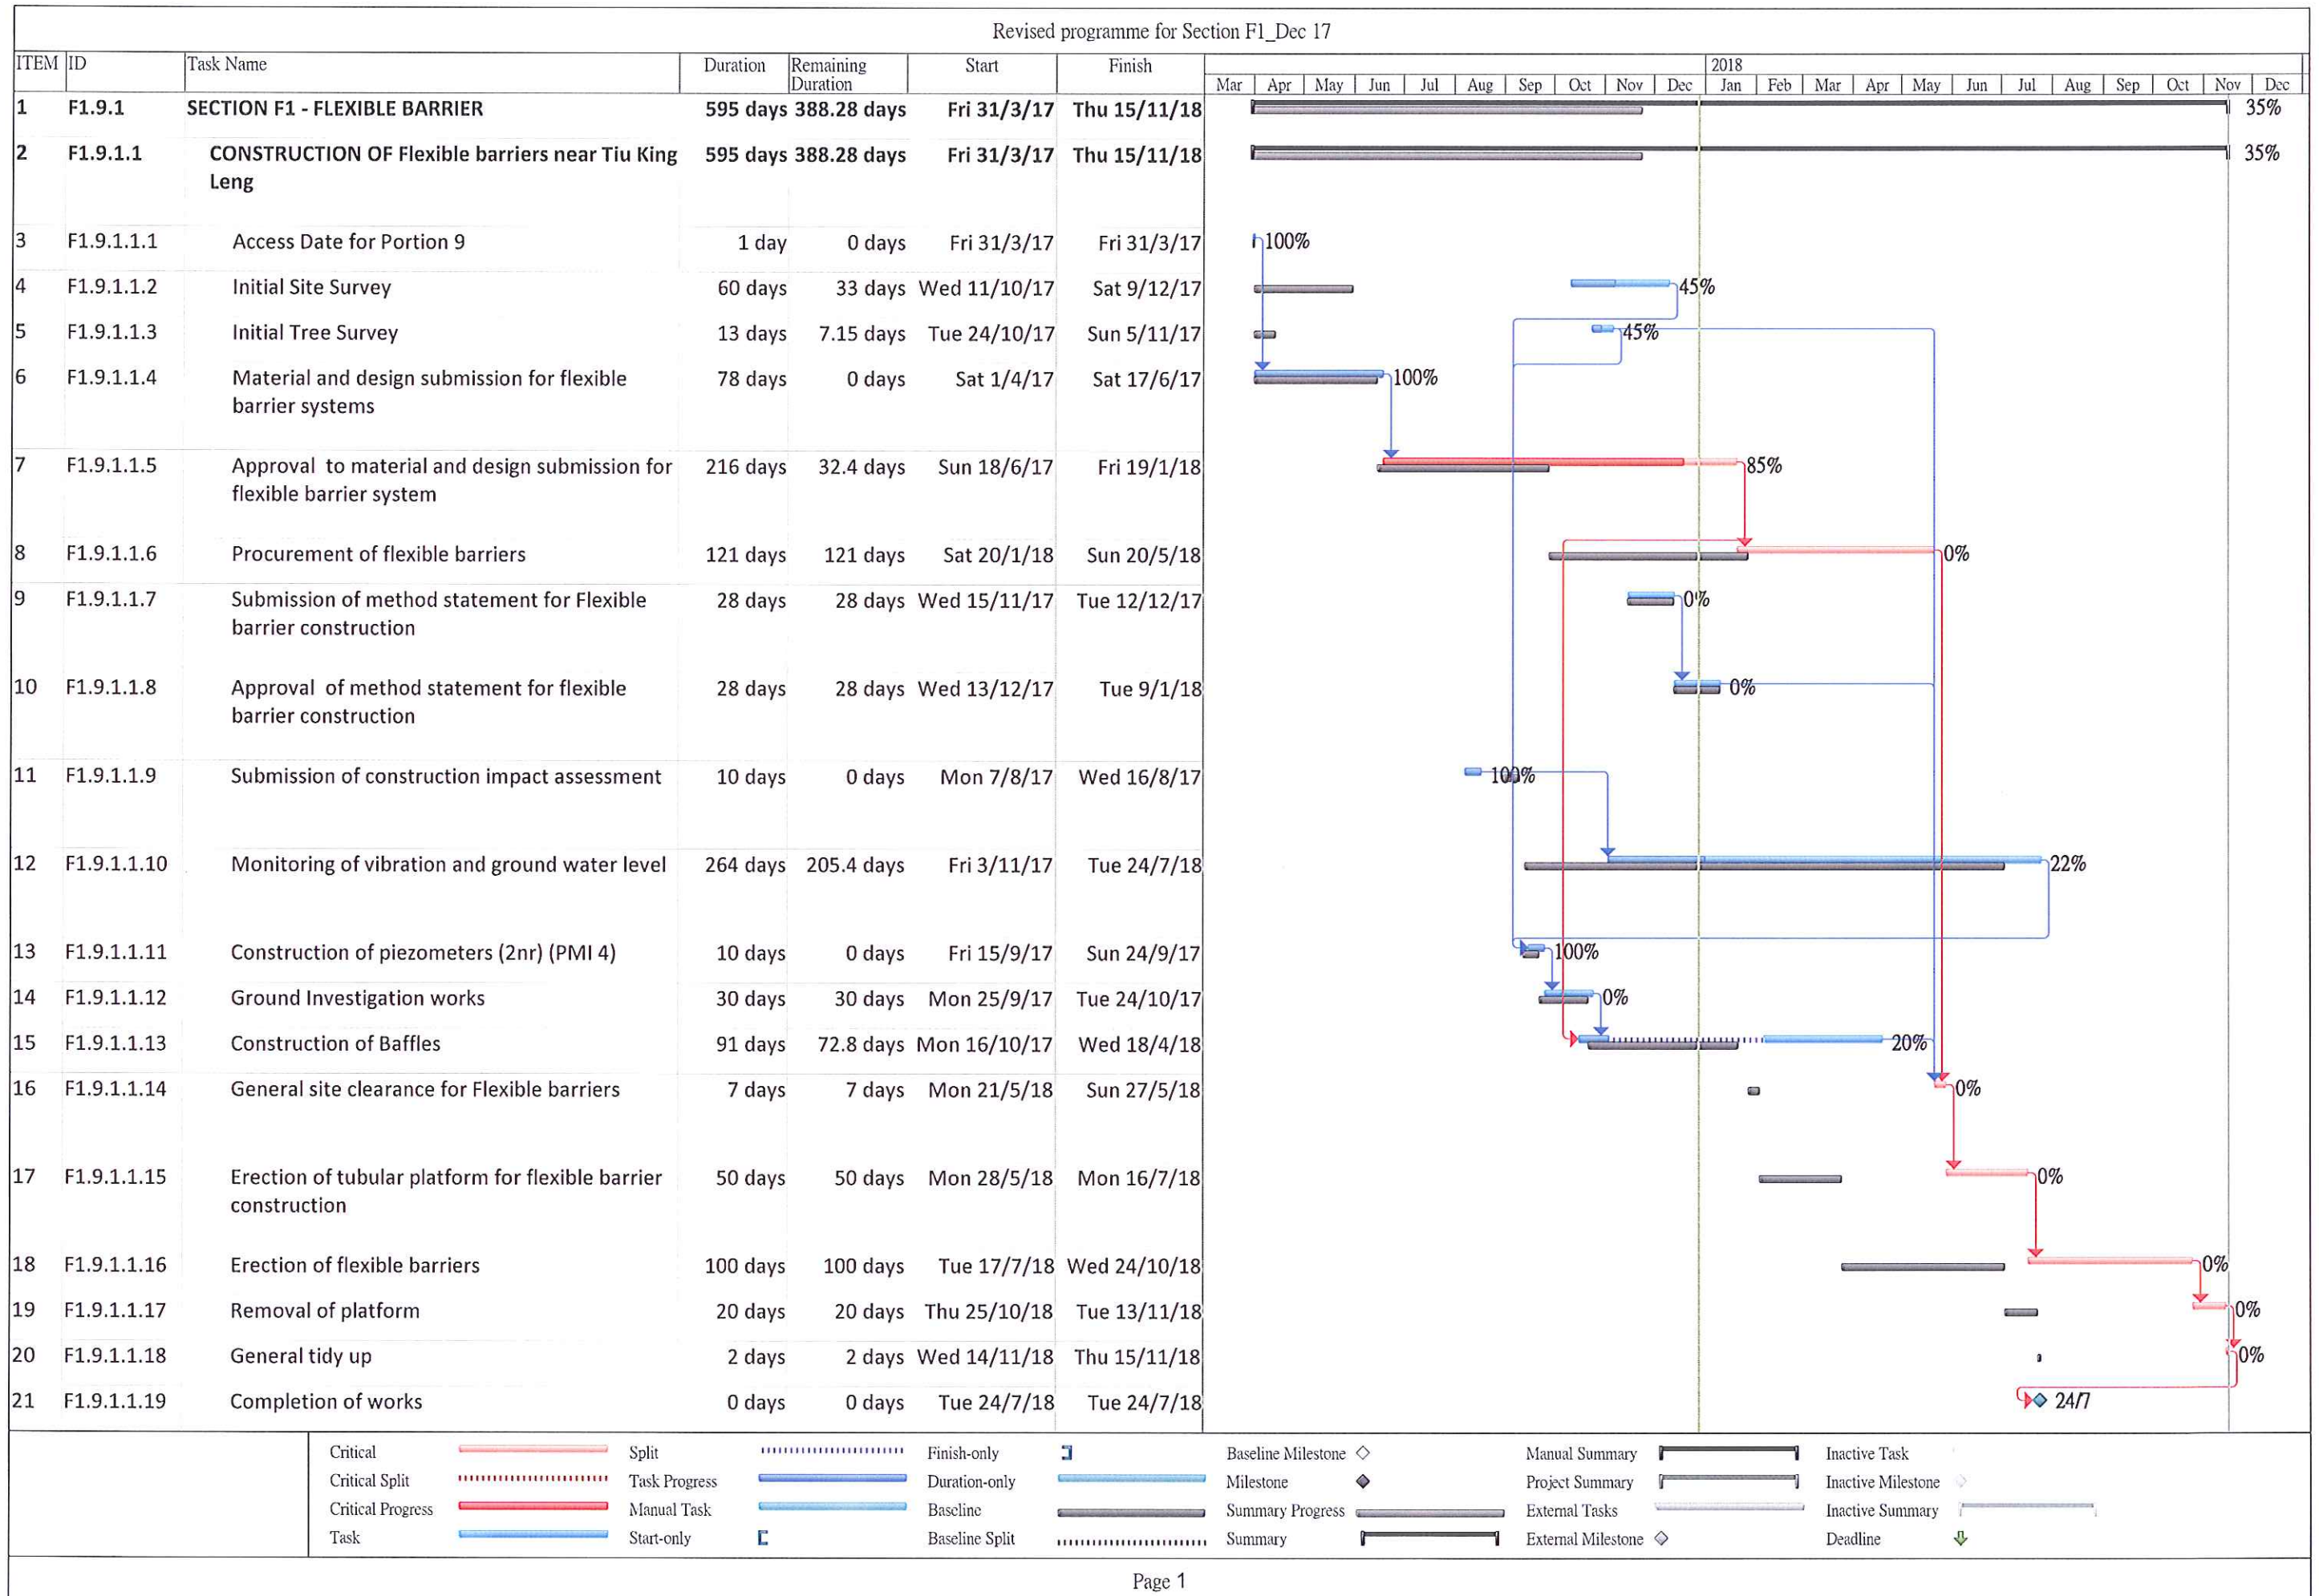

Appendix D

Monitoring Locations for Impact Monitoring


DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED
© DYE ARUP



HVS in AMS-1 for 24-Hour TSP



- Legend
- Study Area
 - 500m Assessment Area
 - Dust Monitoring Locations

B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Construction Dust Monitoring (Sheet 1 of 3)			
Drawing no.		Rev.	
227724/E/1045		B	
Drawn GL	Date 03/14	Checked TC	Approved ST
Scale 1:50000 A3		Status PRELIMINARY	
COPYRIGHT RESERVED			
 土木工程拓展署 Civil Engineering and Development Department			

DO NOT SCALE DRAWING/ CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© DVE ARUP & PARTNERS HONG KONG LIMITED

- Legend
- Study Area
 - 500m Assessment Area
 - Dust Monitoring Locations



HVS in AMS-5 for 24-Hour TSP



HVS in AMS-6 for 24-Hour TSP



B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Construction Dust Monitoring (Sheet 2 of 3)			
Drawing no.		Rev.	
227724/E/1046		B	
Drawn	Date	Checked	Approved
GL	03/14	TC	ST
Scale	1:5000 (M3)	Status	PRELIMINARY
COPYRIGHT RESERVED			

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED. (10/13)
BY THE ARUP PARTNERS HONG KONG LIMITED.



Legend

- Study Area
- 500m Assessment Area
- Dust Monitoring Locations

B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date

Consultant

ARUP

Contract No. and Title
Agreement No. CE 18/2012(CE)

**Development of
Anderson Road Quarry -
Investigation**

Drawing title
**Locations of Construction
Dust Monitoring
(Sheet 3 of 3)**

Drawing no.	227724/E/1047	Rev.	B
Drawn	Date	Checked	Approved
GL	03/14	TC	ST
Scale	1:5000 (M3)	Status	PRELIMINARY


COPYRIGHT RESERVED



土木工程拓展署
Civil Engineering and
Development Department



DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© THE ARUP & PARTNERS HONG KONG LIMITED

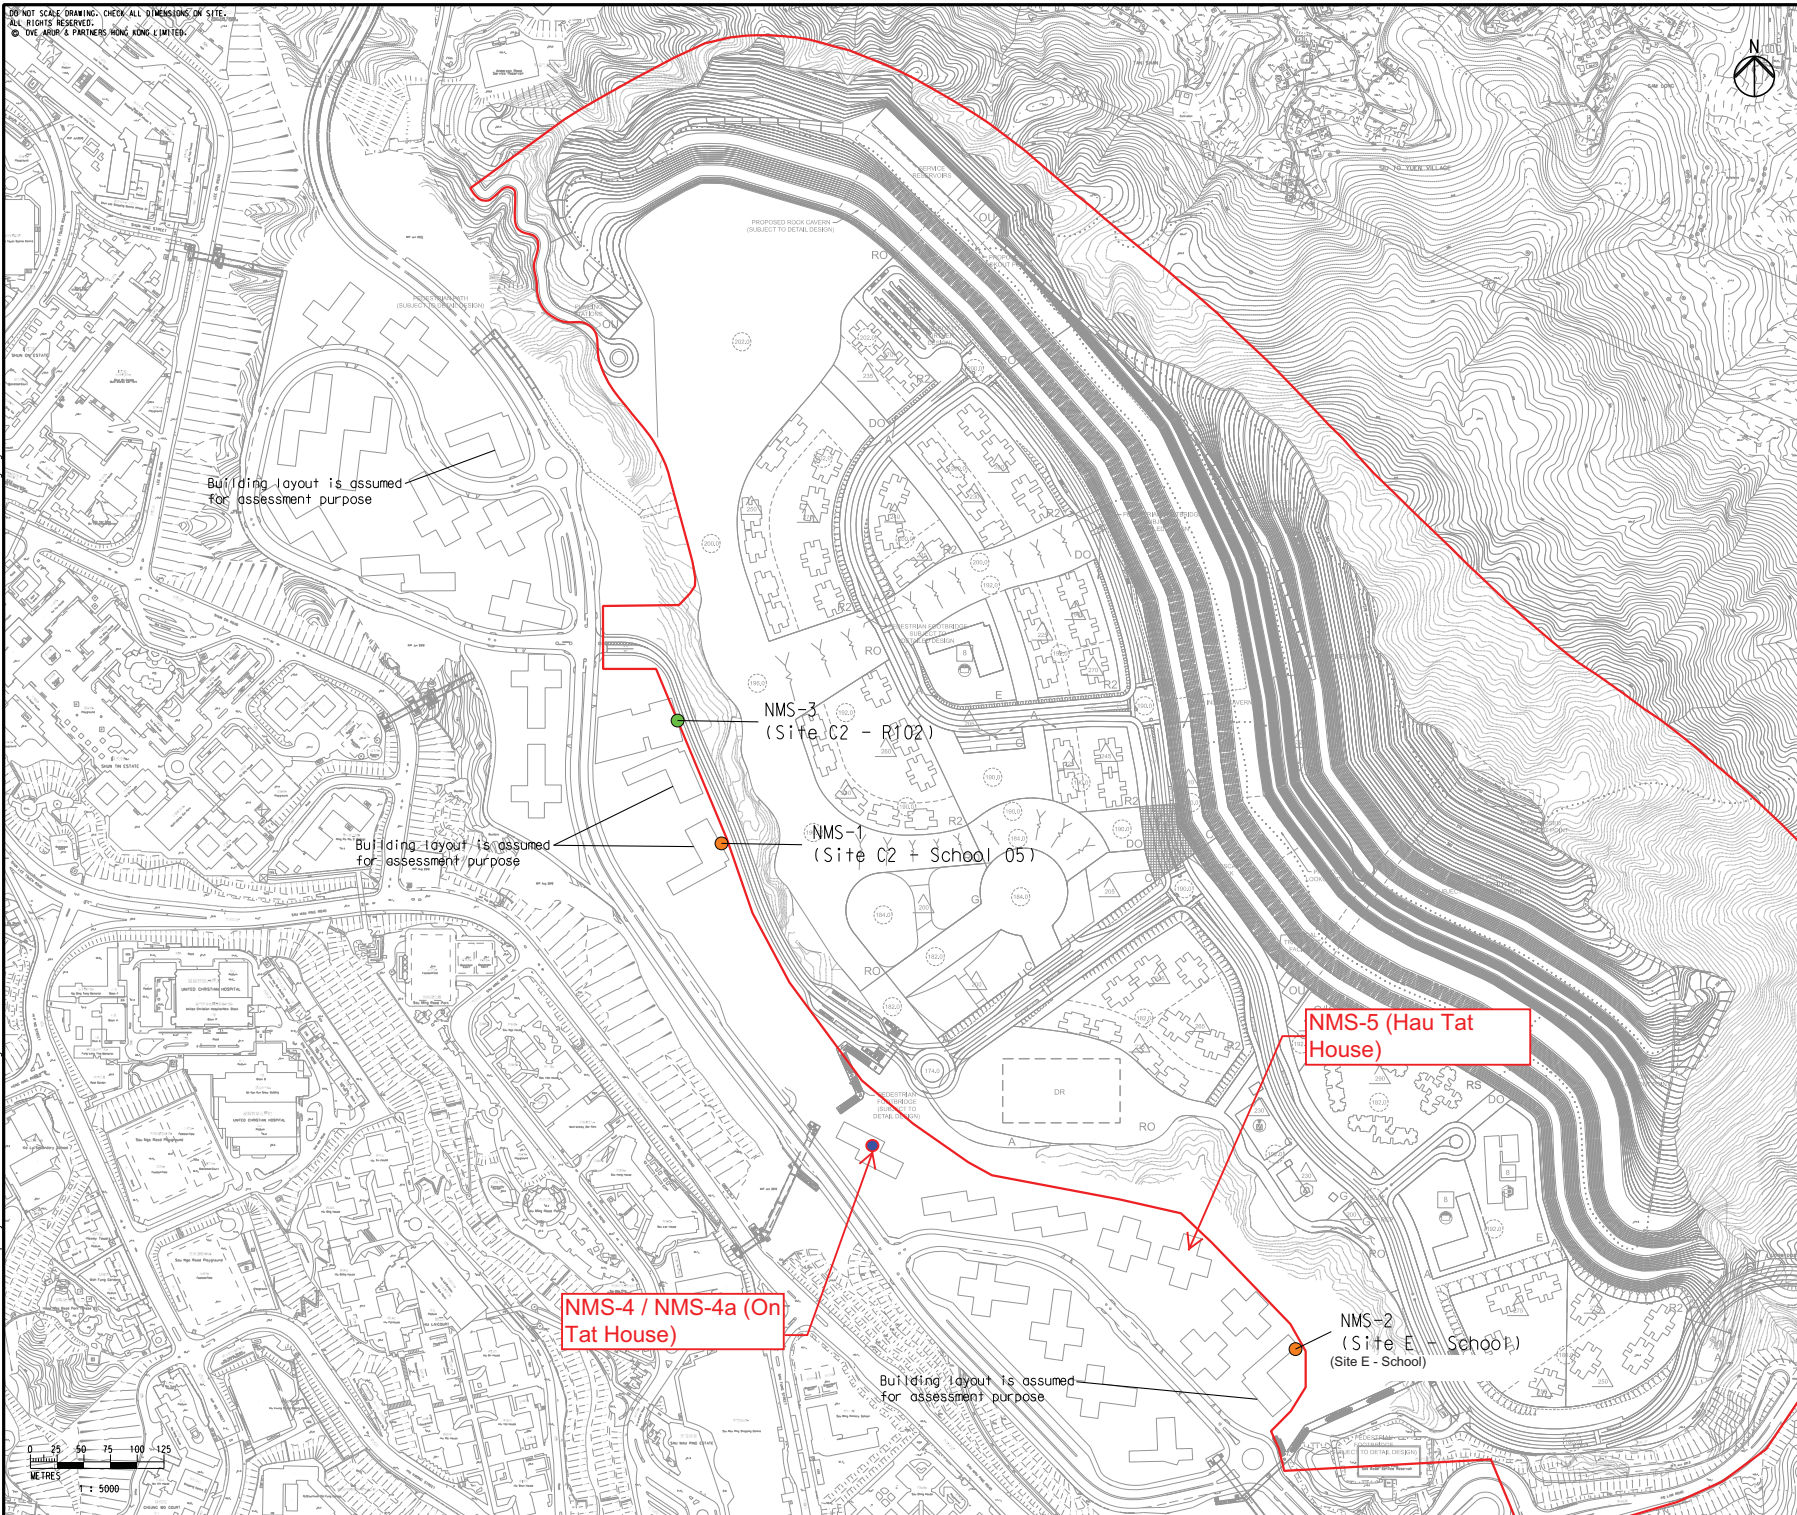

Legend

- Study Area
- Construction Noise Monitoring Location
- Construction and Operational Road Traffic Noise Monitoring Location

C	THIRD ISSUE	GL	05/14
B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date

Consultant

ARUP

Contract No. and Title
Agreement No. CE 18/2012(CE)
Development of
Anderson Road Quarry -
Investigation

Drawing title
Locations of Noise
Monitoring

Drawing no.	227724/E/2400	Rev.	C
Drawn	Date	Checked	Approved
GL	05/14	TC	ST
Scale	1:50000 RA3	Status	PRELIMINARY

COPYRIGHT RESERVED




土木工程拓展署
Civil Engineering and
Development Department

Appendix E

Calibration Certificate of Monitoring Equipment and HOKLAS-accreditation Certificate of the Testing Laboratory

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Chi Yum Ching She				Date of Calibration: 2-Feb-18			
Location ID : AMS1				Next Calibration Date: 2-Apr-18			
Model: TISCH High Volume Air Sampler TE-5170				Technician: Mr. Ip Ka Hing			
CONDITIONS							
Sea Level Pressure (hPa)		1024.6		Corrected Pressure (mm Hg)		768.45	
Temperature (°C)		11.1		Temperature (K)		284	
CALIBRATION ORIFICE							
Make->		TISCH		Qstd Slope ->		2.11965	
Model->		5025A		Qstd Intercept ->		-0.02696	
Serial # ->		1941					
CALIBRATION							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.6	6.6	13.2	1.778	53	54.58	Slope = 37.7058 Intercept = -11.9369 Corr. coeff. = 0.9983
13	5.4	5.4	10.8	1.609	47	48.40	
10	4.1	4.1	8.2	1.404	41	42.22	
7	2.5	2.5	5	1.099	29	29.87	
5	1.6	1.6	3.2	0.882	20	20.60	
<p>Calculations :</p> <p>Qstd = $1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$</p> <p>IC = $I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$</p> <p>Qstd = standard flow rate</p> <p>IC = corrected chart responses</p> <p>I = actual chart response</p> <p>m = calibrator Qstd slope</p> <p>b = calibrator Qstd intercept</p> <p>Ta = actual temperature during calibration (deg K)</p> <p>Pstd = actual pressure during calibration (mm Hg)</p> <p>For subsequent calculation of sampler flow:</p> <p>$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$</p> <p>m = sampler slope</p> <p>b = sampler intercept</p> <p>I = chart response</p> <p>Tav = daily average temperature</p> <p>Pav = daily average pressure</p>							

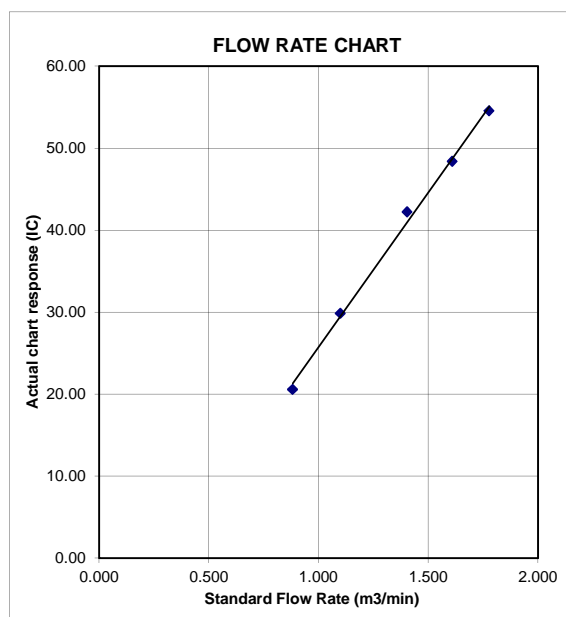

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Oi Tat House	Date of Calibration: 2-Feb-18
Location ID : AMS 5	Next Calibration Date: 2-Apr-18
Model: TISCH High Volume Air Sampler TE-5170	Technician: Mr. Ip Ka Hing

CONDITIONS

Sea Level Pressure (hPa)	1024.6	Corrected Pressure (mm Hg)	768.45
Temperature (°C)	11.1	Temperature (K)	284

CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope ->
Model-> 5025A	Qstd Intercept ->
Serial # -> 1941	

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.737	55	56.64	Slope = 37.3684
13	4.8	4.8	9.6	1.518	48	49.43	Intercept = -7.4063
10	3.8	3.8	7.6	1.352	43	44.28	Corr. coeff. = 0.9982
7	2.5	2.5	5	1.099	33	33.99	
5	1.3	1.3	2.6	0.796	21	21.63	

Calculations :

$$Q_{std} = 1/m[\sqrt{H_{20}(P_a/P_{std})(T_{std}/T_a)} - b]$$

$$IC = I[\sqrt{P_a/P_{std}}(T_{std}/T_a)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I) [\sqrt{298/T_{av}}(P_{av}/760)] - b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

FLOW RATE CHART

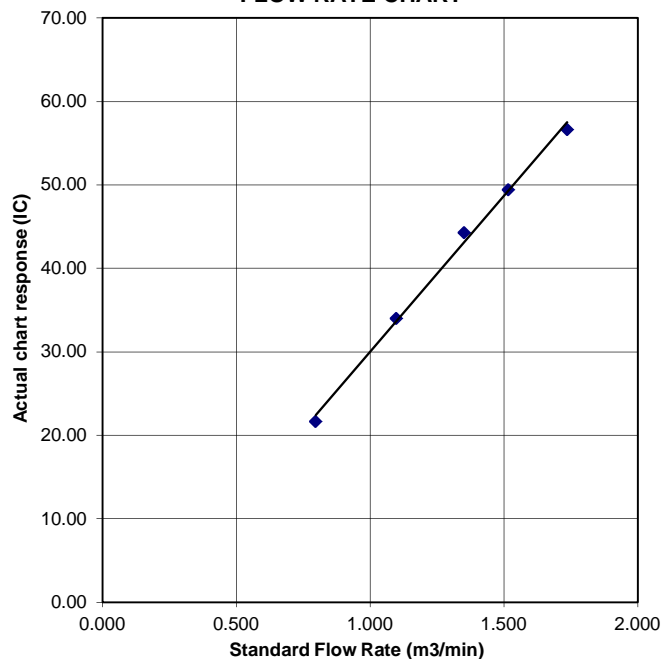

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Hau Tat House	Date of Calibration: 2-Feb-18
Location ID : AMS 6	Next Calibration Date: 2-Apr-18
Model: TISCH High Volume Air Sampler TE-5170	Technician: Mr. Ip Ka Hing

CONDITIONS

Sea Level Pressure (hPa)	1024.6	Corrected Pressure (mm Hg)	768.45
Temperature (°C)	11.1	Temperature (K)	284

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Serial # ->	1941		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.2	6.2	12.4	1.724	53	54.58	Slope = 30.4759 Intercept = 1.9536 Corr. coeff. = 0.9983
13	4.7	4.7	9.4	1.502	47	48.40	
10	3.6	3.6	7.2	1.316	40	41.19	
7	2.2	2.2	4.4	1.032	32	32.96	
5	1.3	1.3	2.6	0.796	26	26.78	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

FLOW RATE CHART

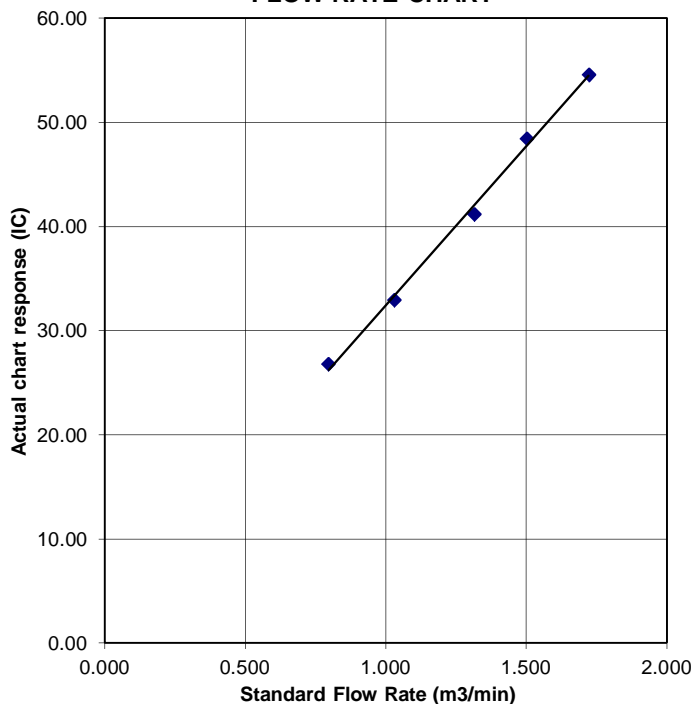

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Ma Yau Tong Village

Date of Calibration: 2-Feb-18

Location ID : AMS 7

Next Calibration Date: 2-Apr-18

Model: TISCH High Volume Air Sampler TE-5170

Technician: Mr. Ip Ka Hing

CONDITIONS

Sea Level Pressure (hPa)

1024.6

Corrected Pressure (mm Hg)

768.45

Temperature (°C)

11.1

Temperature (K)

284

CALIBRATION ORIFICE

Make-> TISCH

Qstd Slope ->

2.11965

Model-> 5025A

Qstd Intercept ->

-0.02696

Serial # -> 1941

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.737	46	47.37	Slope = 29.9579
13	5.2	5.2	10.4	1.580	41	42.22	Intercept = -4.6321
10	3.7	3.7	7.4	1.334	35	36.04	Corr. coeff. = 0.9991
7	2.4	2.4	4.8	1.077	27	27.81	
5	1.5	1.5	3	0.854	20	20.60	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

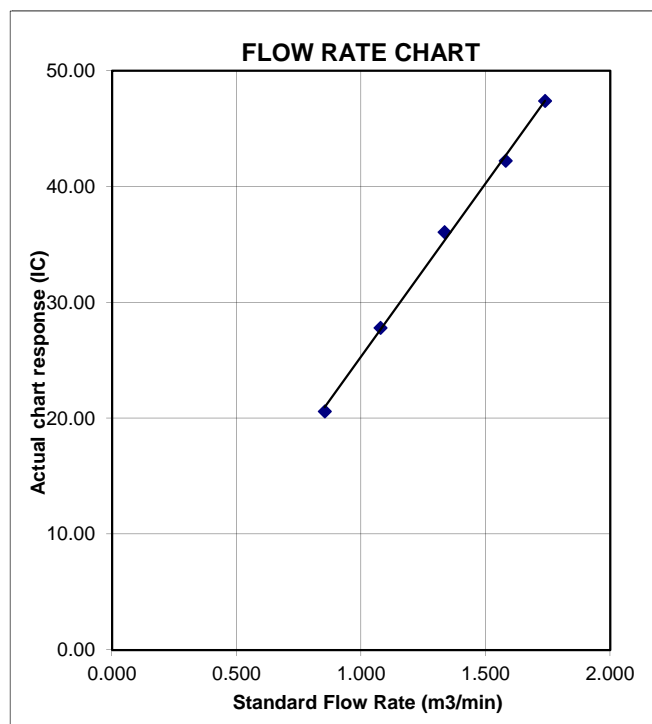

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Feb 28, 2017 Rootmeter S/N 0438320 Ta (K) - 294
Operator Tisch Orifice I.D. - 1941 Pa (mm) - 750.57

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.4600	3.2	2.00
2	NA	NA	1.00	1.0410	6.4	4.00
3	NA	NA	1.00	0.9280	7.9	5.00
4	NA	NA	1.00	0.8840	8.7	5.50
5	NA	NA	1.00	0.7290	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9967	0.6827	1.4149	0.9957	0.6820	0.8851
0.9925	0.9534	2.0010	0.9915	0.9524	1.2517
0.9904	1.0672	2.2372	0.9894	1.0661	1.3995
0.9894	1.1192	2.3464	0.9884	1.1181	1.4678
0.9840	1.3499	2.8299	0.9830	1.3485	1.7702
Qstd slope (m) = 2.11965			Qa slope (m) = 1.32729		
intercept (b) = -0.02696			intercept (b) = -0.01686		
coefficient (r) = 0.99991			coefficient (r) = 0.99991		
y axis = SQRT[H2O(Pa/760)(298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$$Vstd = \text{Diff. Vol}[(Pa - \text{Diff. Hg})/760](298/Ta)$$

$$Qstd = Vstd/Time$$

$$Va = \text{Diff Vol} [(Pa - \text{Diff Hg})/Pa]$$

$$Qa = Va/Time$$

For subsequent flow rate calculations:

$$Qstd = 1/m\{[\text{SQRT}(H2O(Pa/760)(298/Ta))]-b\}$$

$$Qa = 1/m\{[\text{SQRT}(H2O(Ta/Pa))]-b\}$$



SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1815078
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 5-JAN-2018
		DATE OF ISSUE	: 5-FEB-2018
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung  General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F., Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1815078
SUB-BATCH : 1
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1815078-001	S/N: 366409	AIR	05-Jan-2018	S/N: 366409

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD-3B
Serial No. 366409
Equipment Ref: EQ109
Job Order HK1815078

Standard Equipment:

Standard Equipment: Higher Volume Sampler
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 1 December 2017

Equipment Verification Results:

Testing Date: 5 January 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	10:27 ~ 12:34	19.3	1015.3	0.011	474	3.7
2hr01min	12:38 ~ 14:39	19.3	1015.3	0.012	577	4.8
2hr08min	14:42 ~ 16:50	19.3	1015.3	0.036	2097	16.4

Sensitivity Adjustment Scale Setting (Before Calibration) 520 (CPM)

Sensitivity Adjustment Scale Setting (After Calibration) 521 (CPM)

Linear Regression of Y or X


Slope (K-factor): 0.0022

Correlation Coefficient 0.9967

Date of Issue 9 January 2018

Remarks:

1. **Strong** Correlation ($R > 0.8$)
 2. Factor 0.0022 should be apply for TSP monitoring
- *If $R < 0.5$, repair or re-verification is required for the equipment

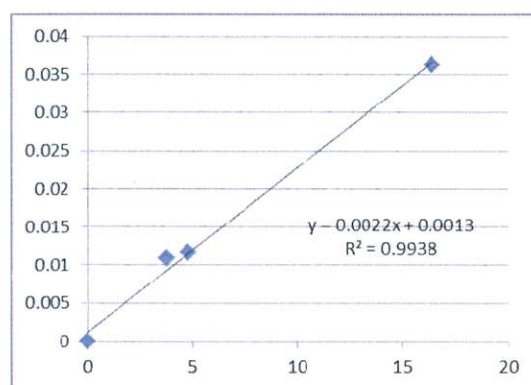

Operator: Martin Li Signature:  Date: 9 January 2018

QC Reviewer: Ben Tam Signature:  Date: 9 January 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration:	1-Dec-17
Location ID :	Calibration Room	Next Calibration Date:	1-Mar-18

CONDITIONS

Sea Level Pressure (hPa)	1018.8	Corrected Pressure (mm Hg)	764.1
Temperature (°C)	21.2	Temperature (K)	294

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.703	54	54.49	Slope = 31.2239
13	5	5	10.0	1.518	48	48.44	Intercept = 0.7901
10	3.9	3.9	7.8	1.342	42	42.38	Corr. coeff. = 0.9971
8	2.4	2.4	4.8	1.056	32	32.29	
5	1.0	1.0	2.0	0.686	23	23.21	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H20(Pa/Pstd)(Tstd/Ta)) - b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)] - b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

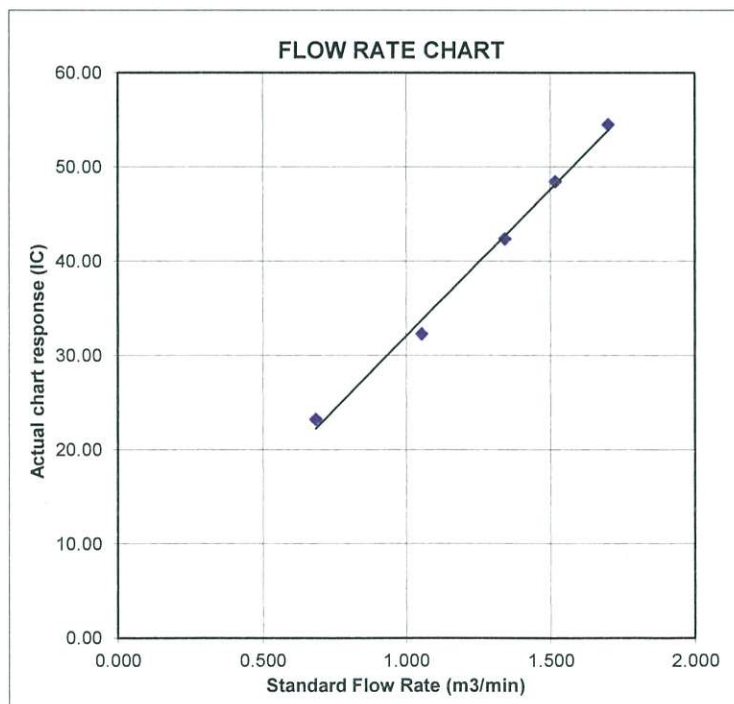



SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1815073
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 5-JAN-2018
		DATE OF ISSUE	: 5-FEB-2018
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung  General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1815073
SUB-BATCH : 1
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1815073-001	S/N: 2X6145	AIR	05-Jan-2018	S/N: 2X6145

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD-3B
Serial No. 2X6145
Equipment Ref: EQ105
Job Order HK1815073

Standard Equipment:

Standard Equipment: Higher Volume Sampler
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 1 December 2017

Equipment Verification Results:

Testing Date: 5 January 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	10:27 ~ 12:34	19.3	1015.3	0.011	511	4.0
2hr01min	12:38 ~ 14:39	19.3	1015.3	0.012	598	4.9
2hr08min	14:42 ~ 16:50	19.3	1015.3	0.036	2111	16.5

Sensitivity Adjustment Scale Setting (Before Calibration) 583 (CPM)

Sensitivity Adjustment Scale Setting (After Calibration) 583 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022


Correlation Coefficient 0.9981

Date of Issue 9 January 2018

Remarks:

1. **Strong** Correlation ($R > 0.8$)
2. Factor 0.0022 should be apply for TSP monitoring

*If $R < 0.5$, repair or re-verification is required for the equipment

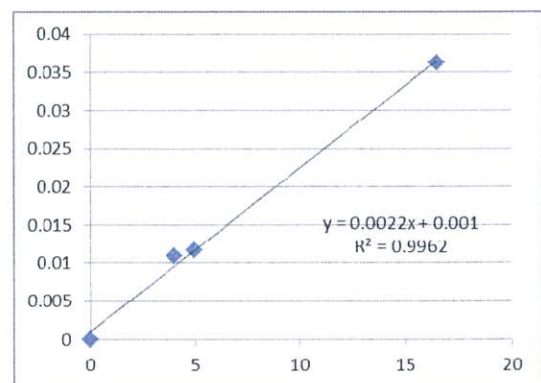

Operator : Martin Li Signature :  Date : 9 January 2018

QC Reviewer : Ben Tam Signature :  Date : 9 January 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration:	1-Dec-17
Location ID :	Calibration Room	Next Calibration Date:	1-Mar-18

CONDITIONS

Sea Level Pressure (hPa)	1018.8	Corrected Pressure (mm Hg)	764.1
Temperature (°C)	21.2	Temperature (K)	294

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.703	54	54.49	Slope = 31.2239
13	5	5	10.0	1.518	48	48.44	Intercept = 0.7901
10	3.9	3.9	7.8	1.342	42	42.38	Corr. coeff. = 0.9971
8	2.4	2.4	4.8	1.056	32	32.29	
5	1.0	1.0	2.0	0.686	23	23.21	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

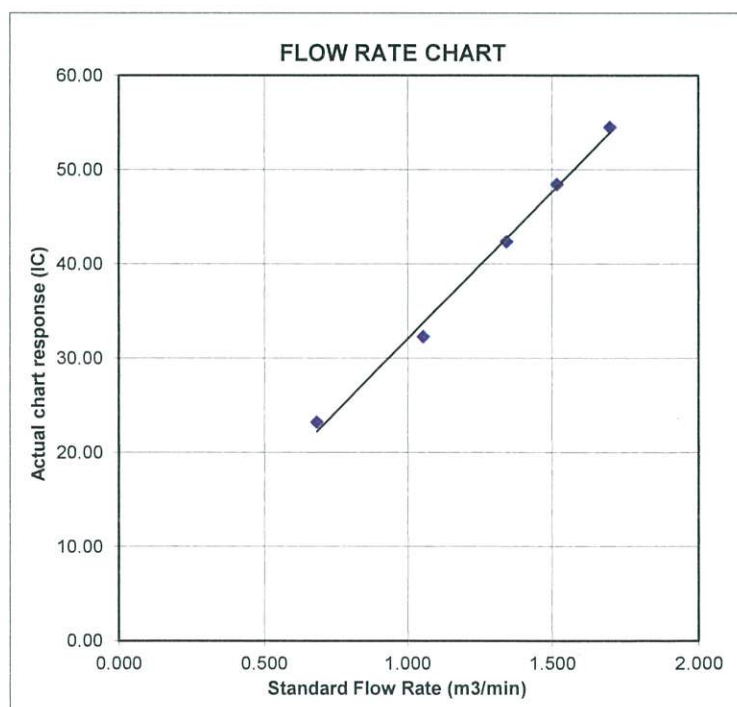



SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1815077
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 5-JAN-2018
		DATE OF ISSUE	: 5-FEB-2018
PROJECT	: ---	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ---

General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung  General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F, Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1815077
SUB-BATCH : 1
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1815077-001	S/N: 3Y6503	AIR	05-Jan-2018	S/N: 3Y6503

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD-3B
Serial No. 3Y6503
Equipment Ref: EQ112
Job Order HK1815077

Standard Equipment:

Standard Equipment: Higher Volume Sampler
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 1 December 2017

Equipment Verification Results:

Testing Date: 5 January 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	10:27 ~ 12:34	19.3	1015.3	0.011	521	4.1
2hr01min	12:38 ~ 14:39	19.3	1015.3	0.012	674	5.6
2hr08min	14:42 ~ 16:50	19.3	1015.3	0.036	2077	16.3

Sensitivity Adjustment Scale Setting (Before Calibration) 661 (CPM)

Sensitivity Adjustment Scale Setting (After Calibration) 661 (CPM)

Linear Regression of Y or X

Slope (K-factor): 0.0022


Correlation Coefficient 0.9976

Date of Issue 9 January 2018

Remarks:

1. **Strong** Correlation ($R > 0.8$)
2. Factor 0.0022 should be apply for TSP monitoring

*If $R < 0.5$, repair or re-verification is required for the equipment

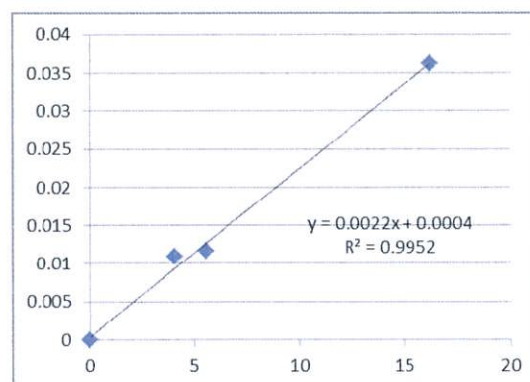

Operator : Martin Li Signature :  Date : 9 January 2018

QC Reviewer : Ben Tam Signature :  Date : 9 January 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Gold King Industrial Building, Kwai Chung
 Location ID : Calibration Room

Date of Calibration: 1-Dec-17
 Next Calibration Date: 1-Mar-18

CONDITIONS

Sea Level Pressure (hPa) 1018.8
 Temperature (°C) 21.2

Corrected Pressure (mm Hg) 764.1
 Temperature (K) 294

CALIBRATION ORIFICE

Make-> TISCH
 Model-> 5025A
 Calibration Date-> 28-Feb-17

Qstd Slope -> 2.11965
 Qstd Intercept -> -0.02696
 Expiry Date-> 28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.703	54	54.49	Slope = 31.2239
13	5	5	10.0	1.518	48	48.44	Intercept = 0.7901
10	3.9	3.9	7.8	1.342	42	42.38	Corr. coeff. = 0.9971
8	2.4	2.4	4.8	1.056	32	32.29	
5	1.0	1.0	2.0	0.686	23	23.21	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

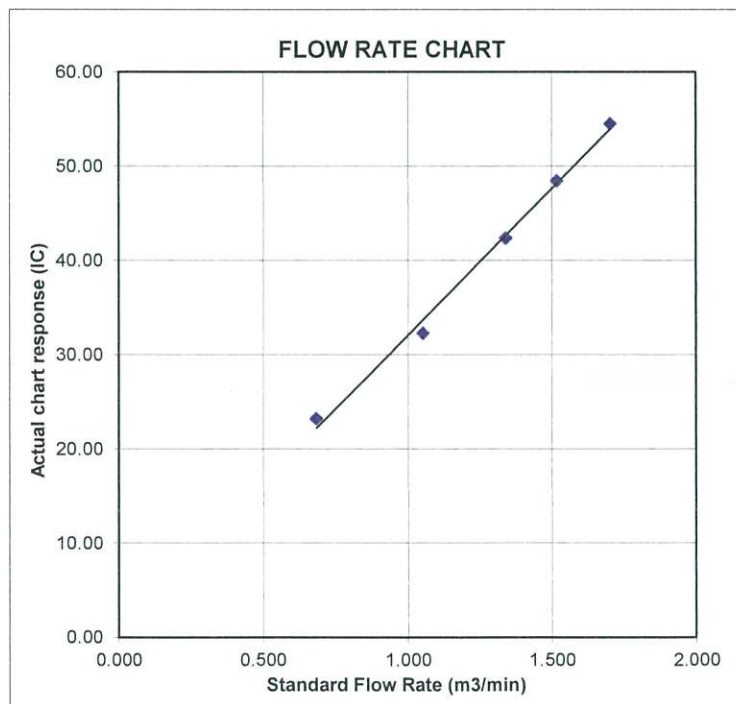



SUB-CONTRACTING REPORT

CONTACT	: MR BEN TAM	WORK ORDER	: HK1815072
CLIENT	: ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING		
ADDRESS	: RM A 20/F., GOLD KING IND BLDG, NO. 35-41 TAI LIN PAI ROAD, KWAI CHUNG, N.T. HONG KONG	SUB-BATCH	: 1
		DATE RECEIVED	: 5-JAN-2018
		DATE OF ISSUE	: 5-FEB-2018
PROJECT	: ----	NO. OF SAMPLES	: 1
		CLIENT ORDER	: ----

General Comments

- Sample(s) were received in ambient condition.
- Sample(s) analysed and reported on an as received basis.

Signatories

This document has been signed by those names that appear on this report and are the authorised signatories

Signatories

Position

Richard Fung  General Manager

This is the Final Report and supersedes any preliminary report with this batch number.

Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ALS Technichem (HK) Pty Ltd
Part of the ALS Laboratory Group

11/F., Chung Shun Knitting Centre 1 - 3 Wing Yip Street Kwai Chung N.T. Hong Kong
Tel. +852 2610 1044 Fax. +852 2610 2021 www.alsglobal.com

WORK ORDER : HK1815072
SUB-BATCH : 1
CLIENT : ACTION UNITED ENVIRONMENT SERVICES AND CONSULTING
PROJECT : ----



ALS Lab ID	Client's Sample ID	Sample Type	Sample Date	External Lab Report No.
HK1815072-001	S/N: 366410	AIR	05-Jan-2018	S/N: 366410

Equipment Verification Report (TSP)

Equipment Calibrated:

Type: Laser Dust monitor
Manufacturer: Sibata LD-3B
Serial No. 366410
Equipment Ref: EQ110
Job Order HK1815072

Standard Equipment:

Standard Equipment: Higher Volume Sampler
Location & Location ID: AUES office (calibration room)
Equipment Ref: HVS 018
Last Calibration Date: 1 December 2017

Equipment Verification Results:

Testing Date: 5 January 2018

Hour	Time	Mean Temp °C	Mean Pressure (hPa)	Concentration in mg/m ³ (Standard Equipment)	Total Count (Calibrated Equipment)	Count/Minute (Total Count/60min)
2hr07min	10:27 ~ 12:34	19.3	1015.3	0.011	498	3.9
2hr01min	12:38 ~ 14:39	19.3	1015.3	0.012	571	4.7
2hr08min	14:42 ~ 16:50	19.3	1015.3	0.036	2095	16.4

Sensitivity Adjustment Scale Setting (Before Calibration) 670 (CPM)

Sensitivity Adjustment Scale Setting (After Calibration) 669 (CPM)

Linear Regression of Y or X


Slope (K-factor): 0.0022

Correlation Coefficient 0.9977

Date of Issue 9 January 2018

Remarks:

1. Strong Correlation ($R > 0.8$)
 2. Factor 0.0022 should be apply for TSP monitoring
- *If $R < 0.5$, repair or re-verification is required for the equipment

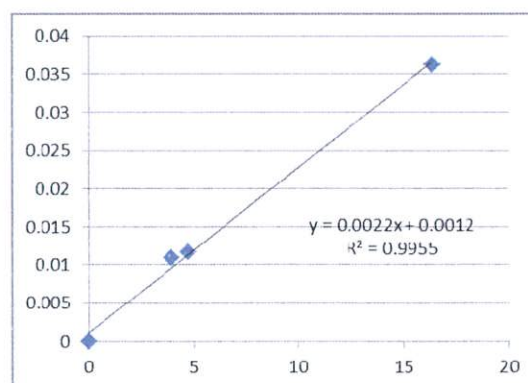

Operator: Martin Li Signature:  Date: 9 January 2018

QC Reviewer: Ben Tam Signature:  Date: 9 January 2018

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location :	Gold King Industrial Building, Kwai Chung	Date of Calibration: 1-Dec-17
Location ID :	Calibration Room	Next Calibration Date: 1-Mar-18

CONDITIONS

Sea Level Pressure (hPa)	1018.8	Corrected Pressure (mm Hg)	764.1
Temperature (°C)	21.2	Temperature (K)	294

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11965
Model->	5025A	Qstd Intercept ->	-0.02696
Calibration Date->	28-Feb-17	Expiry Date->	28-Feb-18

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.703	54	54.49	Slope = 31.2239
13	5	5	10.0	1.518	48	48.44	Intercept = 0.7901
10	3.9	3.9	7.8	1.342	42	42.38	Corr. coeff. = 0.9971
8	2.4	2.4	4.8	1.056	32	32.29	
5	1.0	1.0	2.0	0.686	23	23.21	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

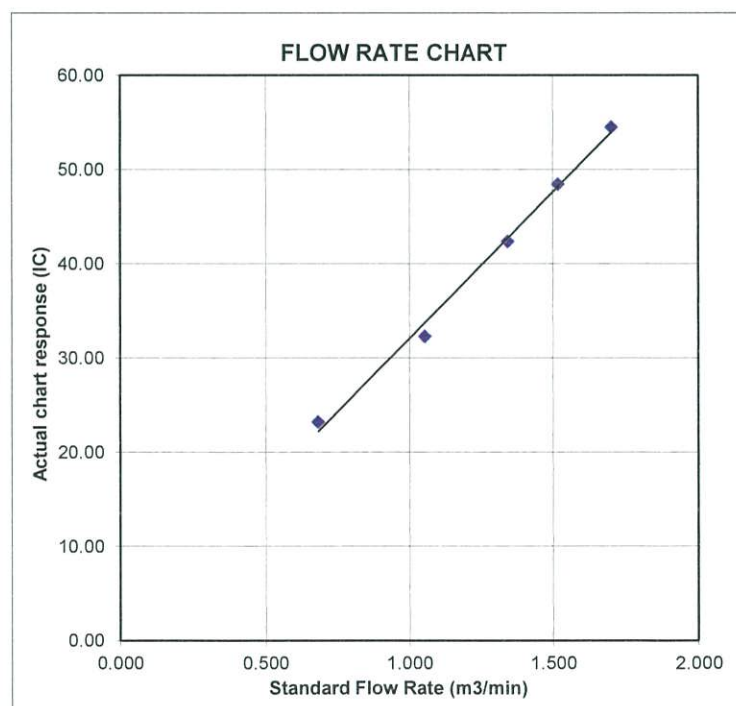

Certificate of Calibration

校正證書

Certificate No. : C174098

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC17-0924)

Date of Receipt / 收件日期 : 14 July 2017

Description / 儀器名稱 : Integrating Sound Level Meter (EQ010)

Manufacturer / 製造商 : Brüel & Kjær

Model No. / 型號 : 2238

Serial No. / 編號 : 2285721

Supplied By / 委託者 : Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building,

35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(55 \pm 20)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 22 July 2017

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.


The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By
測試

:


H T Wong
Technical Officer

Certified By
核證

:


K C Lee
Engineer

Date of Issue
簽發日期

25 July 2017

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C174098
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C170048
CL281	Multifunction Acoustic Calibrator	PA160023

- Test procedure : MA101N.
- Results :

5.1 Sound Pressure Level

5.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT	IEC 60651
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Type 1 Spec. (dB)
50 - 130	L _{AFP}	A	F	94.00	1	94.0	± 0.7

5.1.2 Linearity

UUT Setting				Applied Value		UUT
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
50 - 130	L _{AFP}	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

5.2 Time Weighting

5.2.1 Continuous Signal

UUT Setting				Applied Value		UUT	IEC 60651
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Type 1 Spec. (dB)
50 - 130	L _{AFP}	A	F	94.00	1	94.0	Ref.
	L _{ASP}		S			94.0	± 0.1
	L _{AIP}		I			94.1	± 0.1

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C174098
證書編號

5.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L _{AFP}	A	F	106.0	Continuous	106.0	Ref.
	L _{AFMax}				200 ms	105.0	-1.0 ± 1.0
	L _{ASP}	S	Continuous		106.0	Ref.	
	L _{ASMax}		500 ms		102.0	-4.1 ± 1.0	

5.3 Frequency Weighting

5.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{AFP}	A	F	94.00	31.5 Hz	54.7	-39.4 ± 1.5
					63 Hz	67.8	-26.2 ± 1.5
					125 Hz	77.7	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	92.8	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.7	-4.3 (+3.0 ; -6.0)

5.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{CFP}	C	F	94.00	31.5 Hz	91.2	-3.0 ± 1.5
					63 Hz	93.3	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.0
					250 Hz	94.0	0.0 ± 1.0
					500 Hz	94.1	0.0 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	93.9	-0.2 ± 1.0
					4 kHz	93.2	-0.8 ± 1.0
					8 kHz	91.0	-3.0 (+1.5 ; -3.0)
					12.5 kHz	87.8	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Certificate of Calibration 校正證書

Certificate No. : C174098
證書編號

5.4 Time Averaging

UUT Setting				Applied Value					UUT	IEC 60804
Range (dB)	Parameter	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)	Reading (dB)	Type 1 Spec. (dB)
30 - 110	L _{Aeq}	A	10 sec.	4	1	1/10	110.0	100	100.0	± 0.5
						1/10 ²		90	90.1	± 0.5
			60 sec.			1/10 ³		80	79.9	± 1.0
			5 min.			1/10 ⁴		70	69.8	± 1.0

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2658547

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :	94 dB	: 31.5 Hz - 125 Hz	: ± 0.35 dB
		250 Hz - 500 Hz	: ± 0.30 dB
		1 kHz	: ± 0.20 dB
		2 kHz - 4 kHz	: ± 0.35 dB
		8 kHz	: ± 0.45 dB
		12.5 kHz	: ± 0.70 dB
	104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
	114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
	Burst equivalent level		: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C172791

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC17-0924)

Date of Receipt / 收件日期 : 16 May 2017

Description / 儀器名稱 : Sound Level Calibrator (EQ084)

Manufacturer / 製造商 : Cesva

Model No. / 型號 : CB-5

Serial No. / 編號 : 030023

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(55 \pm 20)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 23 May 2017

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.


The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By
測試


H T Wong
Technical Officer

Certified By
核證


K C Lee
Engineer

Date of Issue
簽發日期

24 May 2017

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C172791

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C163709
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C161175

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	93.8	± 0.3	± 0.2
104 dB, 1 kHz	103.9		± 0.3

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	0.994	1 kHz ± 1.5 %	± 1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence
此實驗所符合ISO / IEC 17025 : 2005 – 《測試及校正實驗所能力的通用規定》所訂的要求，
of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as
獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
listed in the HOKLAS Directory of Accredited Laboratories within the test category of
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。

This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作
quality management system (see joint IAF-ILAC-ISO Communiqué).
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS** 066
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日



Appendix F

Event and Action Plan

Event / Action Plan for construction dust

Event	Action			
	ET	IEC	ER	Contractor
Action Level exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER and Contractor; 3. Repeat measurement to confirm finding; and 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; and 3. Review and advise the ET and ER on the effectiveness of the proposed remedial measures.	1. Notify Contractor.	1. Identify source, investigate the causes of exceedance and propose remedial measures 2. Rectify any unacceptable practice and implement remedial measures; and 3. Amend working methods agreed with ER if appropriate.
Action Level exceedance for two or more consecutive samples	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER and Contractor; 3. Advise the ER and Contractor on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC, ER and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; and 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET and ER on the effectiveness of the proposed remedial measures; and 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; and 3. Supervise and ensure remedial measures properly implemented.	1. Identify source, investigate the causes of exceedance and propose remedial measures 2. Submit proposals for remedial actions to ER with a copy to ET and IEC within 3 working days of notification; 3. Implement the agreed proposals; and 4. Amend proposal if appropriate.

Limit Level exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor, IEC and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET, ER and Contractor on possible remedial measures; 4. Advise the ER and ET on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; and 3. Supervise and ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER with a copy to ET and IEC within 3 working days of notification; 4. Implement the agreed proposals; and 5. Amend proposal if appropriate.
Limit Level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC, Contractor and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 5. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise and ensure remedial measures properly implemented; and 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER with a copy to ET and IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Resubmit proposals if problem still not under control; 6. Stop the relevant portion of works as determined by the ER until the exceedance is abated

Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	1. Notify IEC, ER and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness.	1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented	1. Submit noise mitigation proposals to IEC and ER; 2. Implement noise mitigation proposals.
Limit Level Exceedance	1. Identify source; 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Appendix G

Impact Monitoring Schedule

Impact Monitoring Schedule for the Reporting Period

Date		Noise Monitoring (0700 – 1900)	Air Quality Monitoring	
			1-hour TSP	24-hour TSP
Thu	1-Feb-18			
Fri	2-Feb-18	✓	✓	
Sat	3-Feb-18			
Sun	4-Feb-18			
Mon	5-Feb-18			
Tue	6-Feb-18			✓
Wed	7-Feb-18			
Thu	8-Feb-18	✓	✓	
Fri	9-Feb-18			
Sat	10-Feb-18			
Sun	11-Feb-18			
Mon	12-Feb-18			✓
Tue	13-Feb-18			
Wed	14-Feb-18	✓	✓	
Thu	15-Feb-18			✓
Fri	16-Feb-18			
Sat	17-Feb-18			
Sun	18-Feb-18			
Mon	19-Feb-18			
Tue	20-Feb-18	✓	✓	
Wed	21-Feb-18			✓
Thu	22-Feb-18			
Fri	23-Feb-18			
Sat	24-Feb-18			
Sun	25-Feb-18			
Mon	26-Feb-18	✓	✓	
Tue	27-Feb-18			✓
Wed	28-Feb-18			

✓	Monitoring Day
	Sunday or Public Holiday

Impact Monitoring Schedule for next Reporting Period

Date		Noise Monitoring (0700 – 1900)	Air Quality Monitoring	
			1-hour TSP	24-hour TSP
Thu	1-Mar-18			
Fri	2-Mar-18			
Sat	3-Mar-18		✓	
Sun	4-Mar-18			
Mon	5-Mar-18			✓
Tue	6-Mar-18			
Wed	7-Mar-18			
Thu	8-Mar-18			
Fri	9-Mar-18	✓	✓	
Sat	10-Mar-18			✓
Sun	11-Mar-18			
Mon	12-Mar-18			
Tue	13-Mar-18			
Wed	14-Mar-18			
Thu	15-Mar-18	✓	✓	
Fri	16-Mar-18			✓
Sat	17-Mar-18			
Sun	18-Mar-18			
Mon	19-Mar-18			
Tue	20-Mar-18			
Wed	21-Mar-18	✓	✓	
Thu	22-Mar-18			✓
Fri	23-Mar-18			
Sat	24-Mar-18			
Sun	25-Mar-18			
Mon	26-Mar-18	✓	✓	
Tue	27-Mar-18			
Wed	28-Mar-18			✓
Thu	29-Mar-18		✓	
Fri	30-Mar-18			
Sat	31-Mar-18			

✓	Monitoring Day
	Sunday or Public Holiday

Appendix H

Database of Monitoring Result

24-hour TSP Database

24-hour TSP Monitoring Data for AMS-1															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-hr TSP (µg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m³/min)	(std m³)	INITIAL	FINAL	(g)	
6-Feb-18	22215	19134.41	19158.41	1440.00	37	43	40.0	16	1019.4	1.40	2012	2.6641	2.7550	0.0909	45
12-Feb-18	22181	19158.41	19182.41	1440.00	38	41	39.5	17.1	1018.2	1.38	1988	2.6740	2.7620	0.0880	44
15-Feb-18	22204	19182.41	19206.42	1440.60	38	42	40.0	17.4	1017.1	1.39	2007	2.6789	2.7669	0.0880	44
21-Feb-18	22252	19206.42	19230.72	1458.00	38	41	39.5	16.7	1018.3	1.38	2014	2.6830	2.7465	0.0635	32
27-Feb-18	22329	19230.72	19255.14	1465.20	37	40	38.5	16.8	1018.4	1.35	1985	2.6637	2.7755	0.1118	56
24-hour TSP Monitoring Data for AMS-5															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-hr TSP (µg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m³/min)	(std m³)	INITIAL	FINAL	(g)	
6-Feb-18	22139	5513.18	5537.04	1431.60	38	40	39.0	16	1019.4	1.26	1805	2.6599	2.7863	0.1264	70
12-Feb-18	22142	5537.04	5561.04	1440.00	37	40	38.5	17.1	1018.2	1.24	1793	2.6297	2.7471	0.1174	65
15-Feb-18	22143	5561.04	5584.95	1434.60	38	40	39.0	17.4	1017.1	1.26	1804	2.6202	2.7426	0.1224	68
21-Feb-18	22208	5584.95	5608.87	1435.20	38	40	39.0	16.7	1018.3	1.26	1807	2.6702	2.7360	0.0658	36
27-Feb-18	22212	5608.87	5632.75	1432.80	37	40	38.5	16.8	1018.4	1.25	1785	2.6846	2.7642	0.0796	45
24-hour TSP Monitoring Data for AMS-6															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-hr TSP (µg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m³/min)	(std m³)	INITIAL	FINAL	(g)	
6-Feb-18	22140	10727.06	10751.06	1440.00	40	42	41.0	16	1019.4	1.31	1881	2.6578	2.7444	0.0866	46
12-Feb-18	22141	10751.06	10775.36	1458.00	39	41	40.0	17.1	1018.2	1.27	1851	2.6262	2.7532	0.1270	69
15-Feb-18	22203	10775.36	10799.56	1452.00	39	41	40.0	17.4	1017.1	1.27	1841	2.6669	2.8203	0.1534	83
21-Feb-18	22207	10799.56	10823.94	1462.80	39	41	40.0	16.7	1018.3	1.27	1858	2.6825	2.7597	0.0772	42
27-Feb-18	22328	10823.94	10848.26	1459.20	39	41	40.0	16.8	1018.4	1.27	1853	2.6832	2.7474	0.0642	35
24-hour TSP Monitoring Data for AMS-7															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP	AVG AIR PRESS	STANDARD FLOW RATE	AIR VOLUME	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED	24-hr TSP (µg/m³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG	(°C)	(hPa)	(m³/min)	(std m³)	INITIAL	FINAL	(g)	
6-Feb-18	22182	6149.91	6173.85	1436.40	36	40	38.0	16	1019.4	1.45	2078	2.7086	2.7736	0.0650	31
12-Feb-18	22200	6173.85	6197.76	1434.60	35	39	37.0	17.1	1018.2	1.41	2022	2.6888	2.7534	0.0646	32
15-Feb-18	22279	6197.76	6221.56	1428.00	34	40	37.0	17.4	1017.1	1.41	2011	2.6842	2.8148	0.1306	65
21-Feb-18	22251	6221.56	6245.56	1440.00	38	41	39.5	16.7	1018.3	1.50	2153	2.6839	2.7499	0.0660	31
27-Feb-18	22330	6245.56	6269.66	1446.00	39	41	40.0	16.8	1018.4	1.51	2186	2.6750	2.7458	0.0708	32



Noise Database


Noise Measurement Results (dB) of NMS4a																				
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	
2-Feb-18	9:45	63.3	66.5	57.5	63.4	65.5	58	64.8	67.5	57	64.5	67.5	57.5	63.3	66.5	55	62.1	65.5	53	64
8-Feb-18	14:23	71.8	74	67	68.3	70.5	63.5	72.4	75.5	66	70.7	75	64.5	70.3	73.5	65	65.5	67.5	62	70
14-Feb-18	10:00	67.4	69	63.5	65.8	67.5	63	65.5	67	61.5	67.1	70	61.5	70.3	68.5	62.5	68.7	70	61.5	68
20-Feb-18	14:00	66.4	68	60.5	69.3	73	63.5	71.4	75	63	73.8	76.5	62	66.8	70.5	58.5	62.2	63.5	57.5	70
26-Feb-18	10:07	73.7	76.5	65	74.9	78	67.5	73.2	77	65.5	69.6	73.5	62	72.6	76.5	64	73	76.5	64.5	73


Noise Measurement Results (dB) of NMS5																				
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	
2-Feb-18	13:08	60.2	62.5	53	64.1	67	58.5	63.4	66	59	64.1	67	59.5	62.6	65	58.5	64	66.5	60	63
8-Feb-18	13:43	63.9	66	60.5	62.4	64	59.5	63.5	65.5	59.5	65.6	68	61.5	64.2	66.5	60.5	65.5	67.5	61.5	64
14-Feb-18	9:16	62.2	64.5	59.5	63.7	68.5	60	64.5	66.5	59	63.6	65	59.5	62	63	59	62.9	65	58.5	63
20-Feb-18	13:03	65.9	69.5	59	62.7	65	59.5	65.2	67.5	58	66.3	68	56	60.9	62.5	56	60.6	63.5	56	64
26-Feb-18	11:00	56.7	57.5	53	61.3	58	53	55.6	56.5	51.5	57.1	59	54	54.2	57	50	55	53.5	48	57


Appendix I


Graphical Plots for Monitoring Result

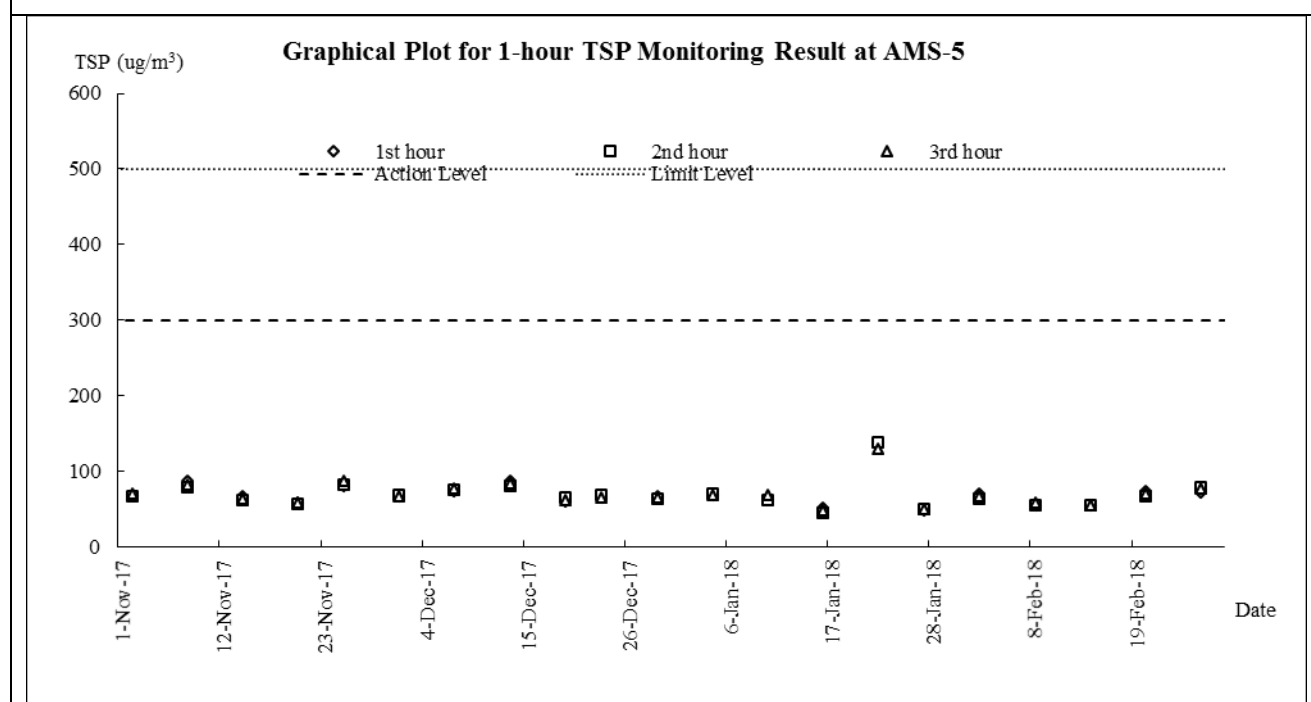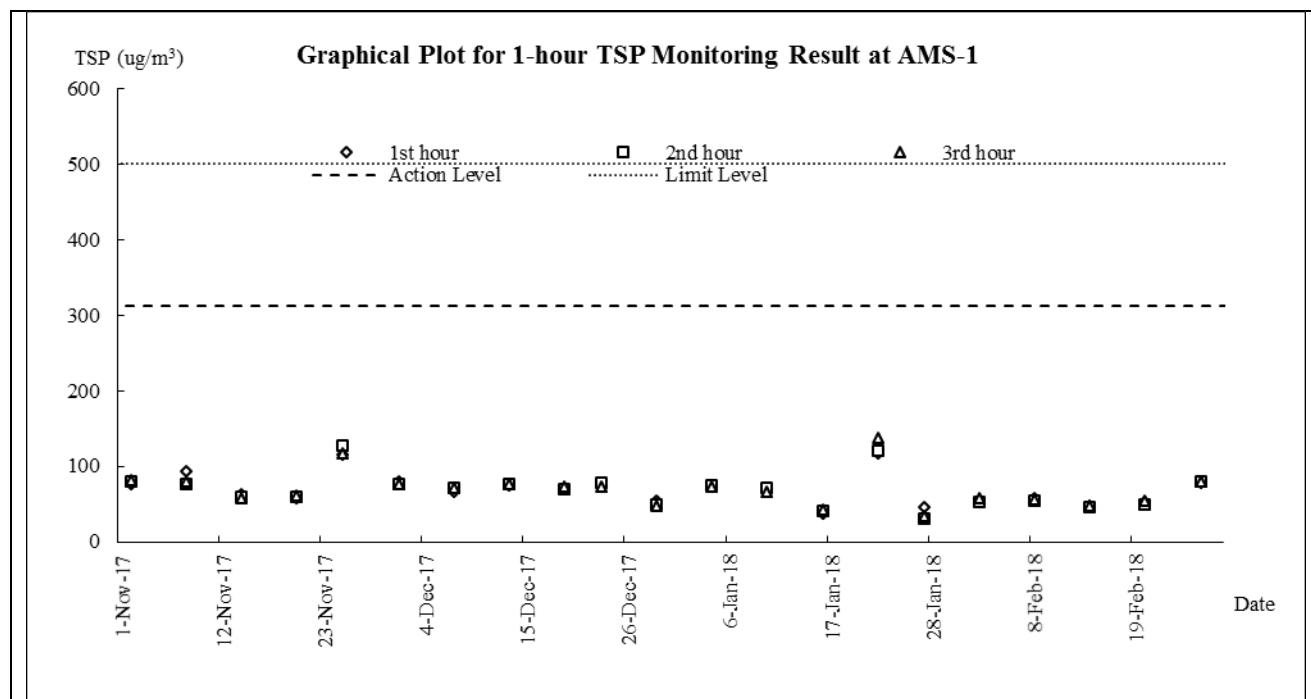Air Quality – 1-hour TSP

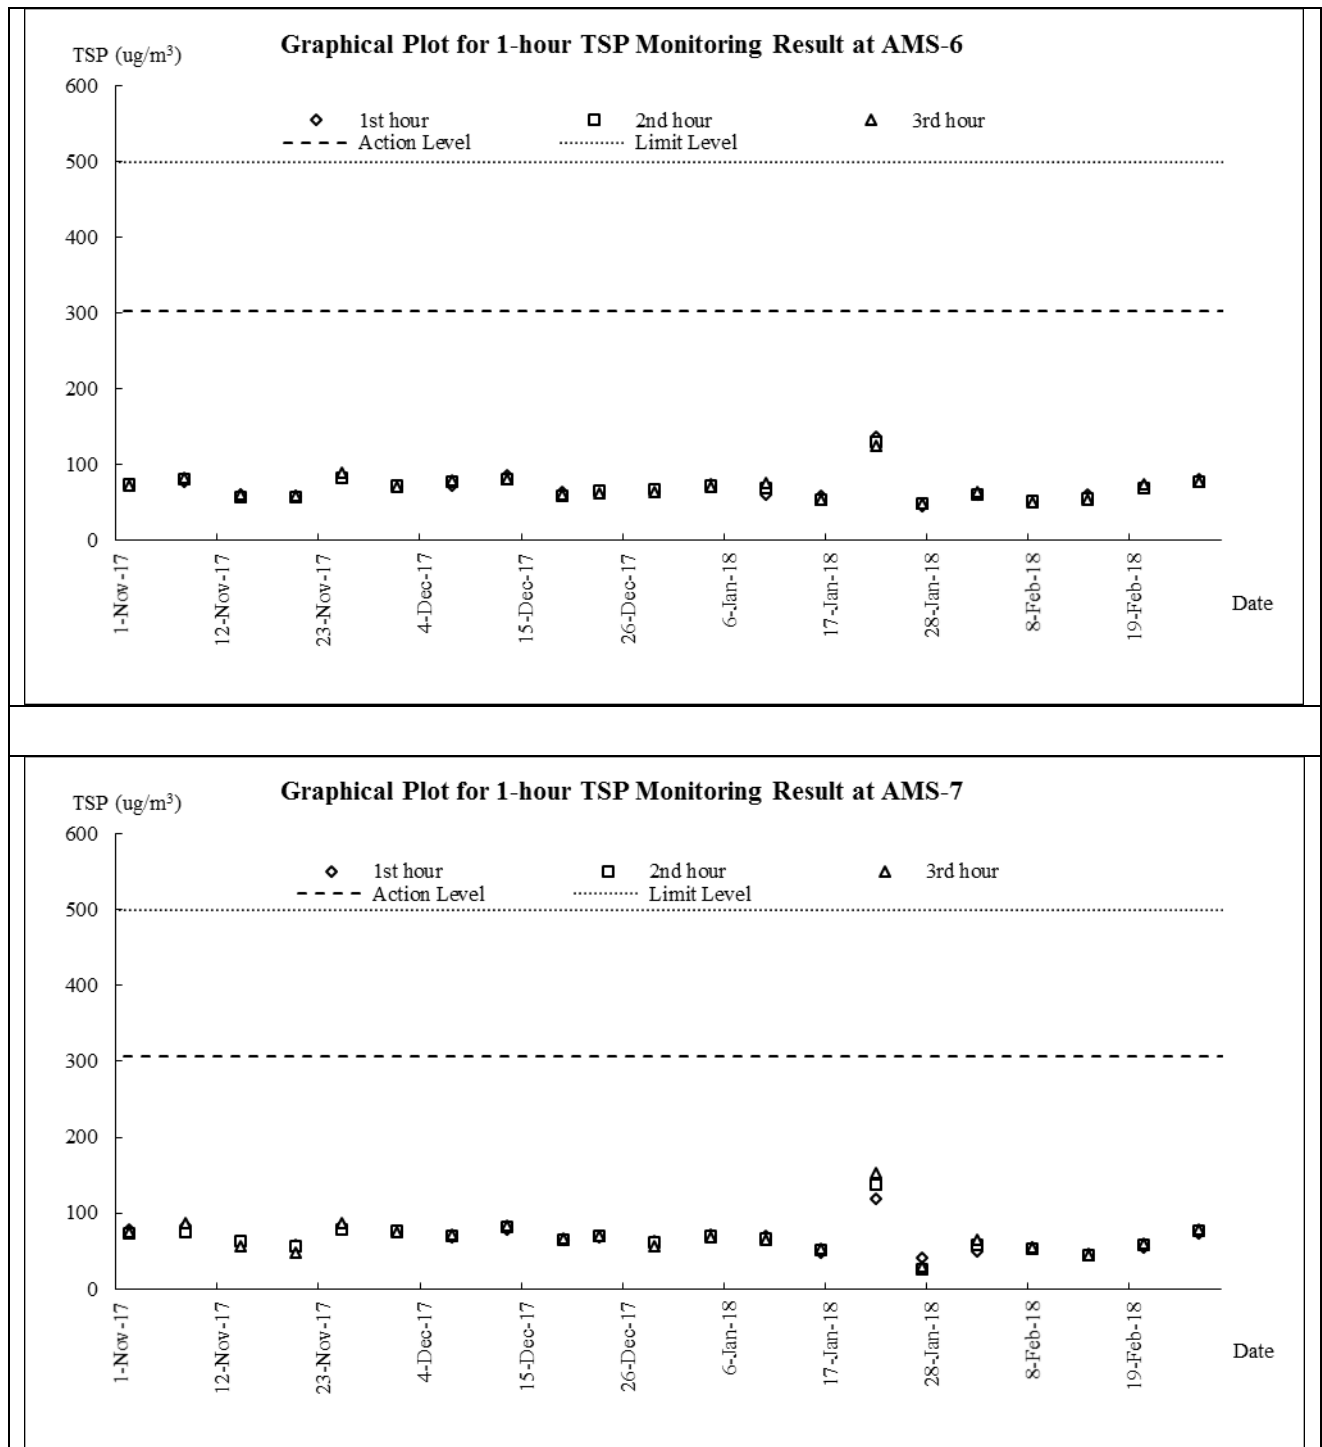

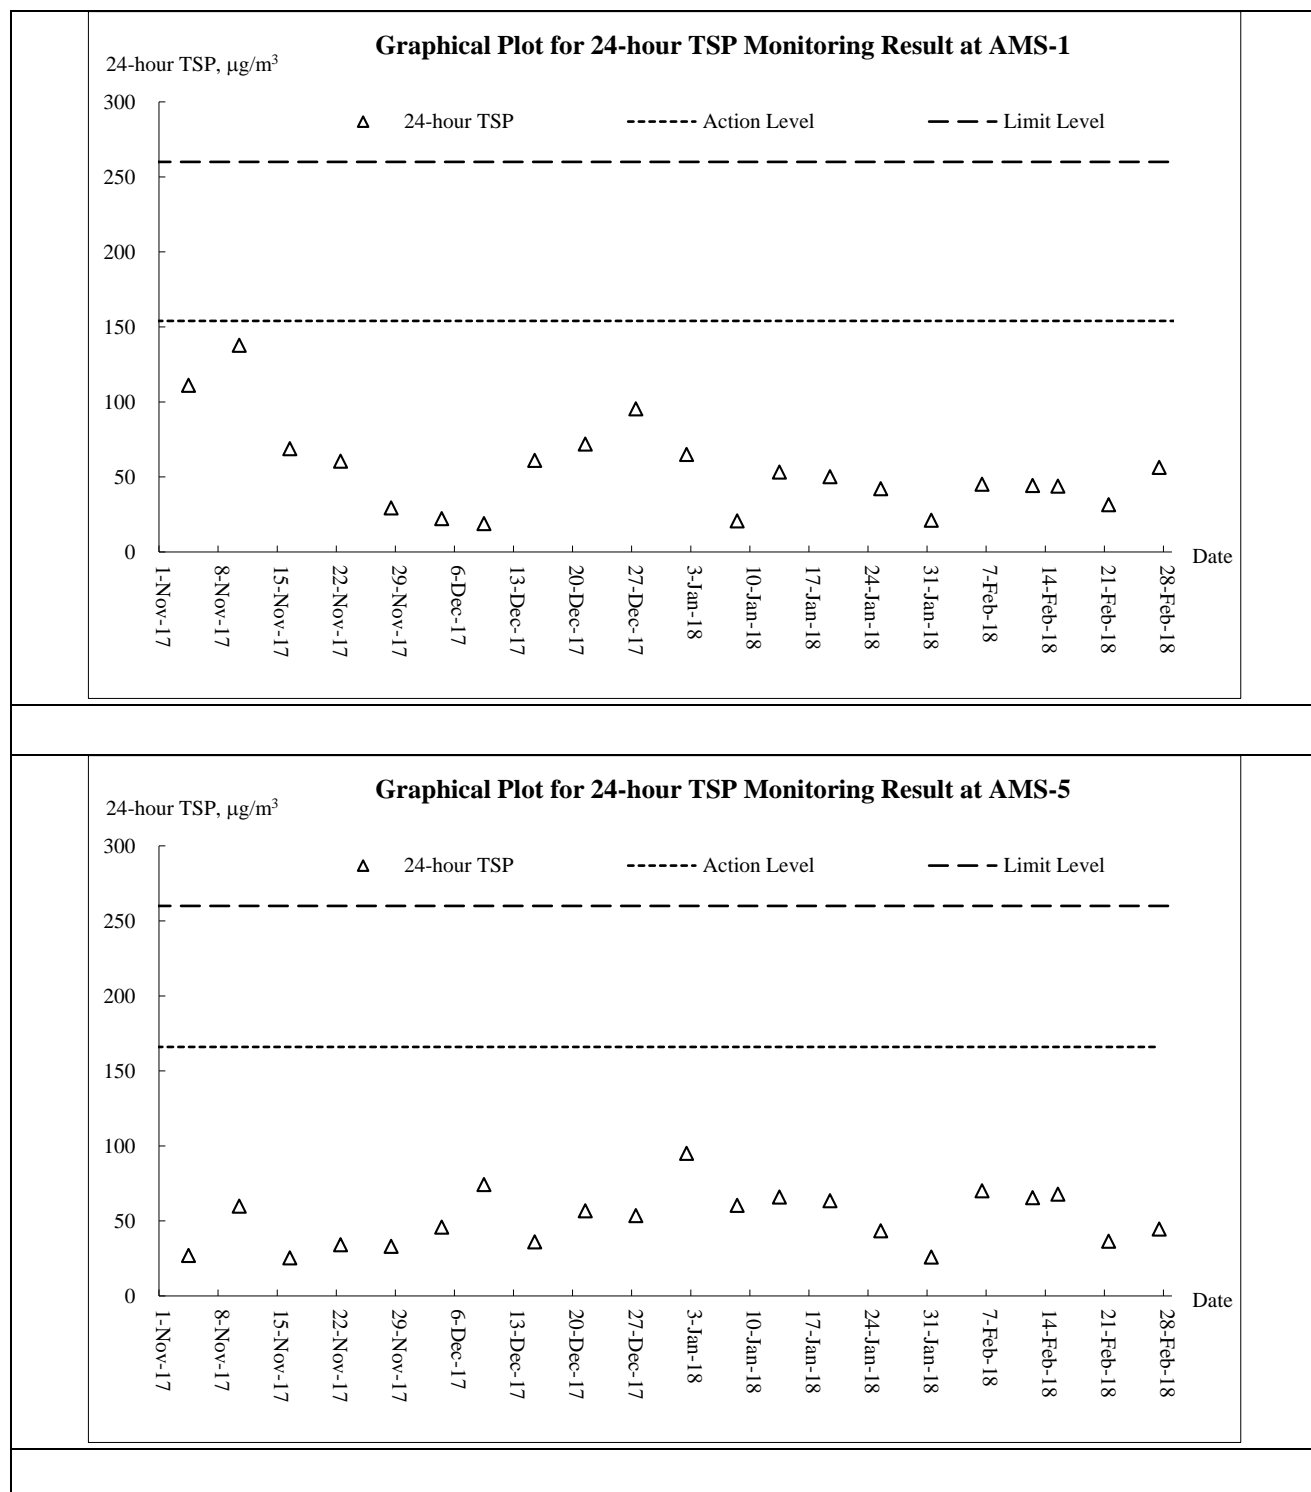Air Quality – 24-hour TSP

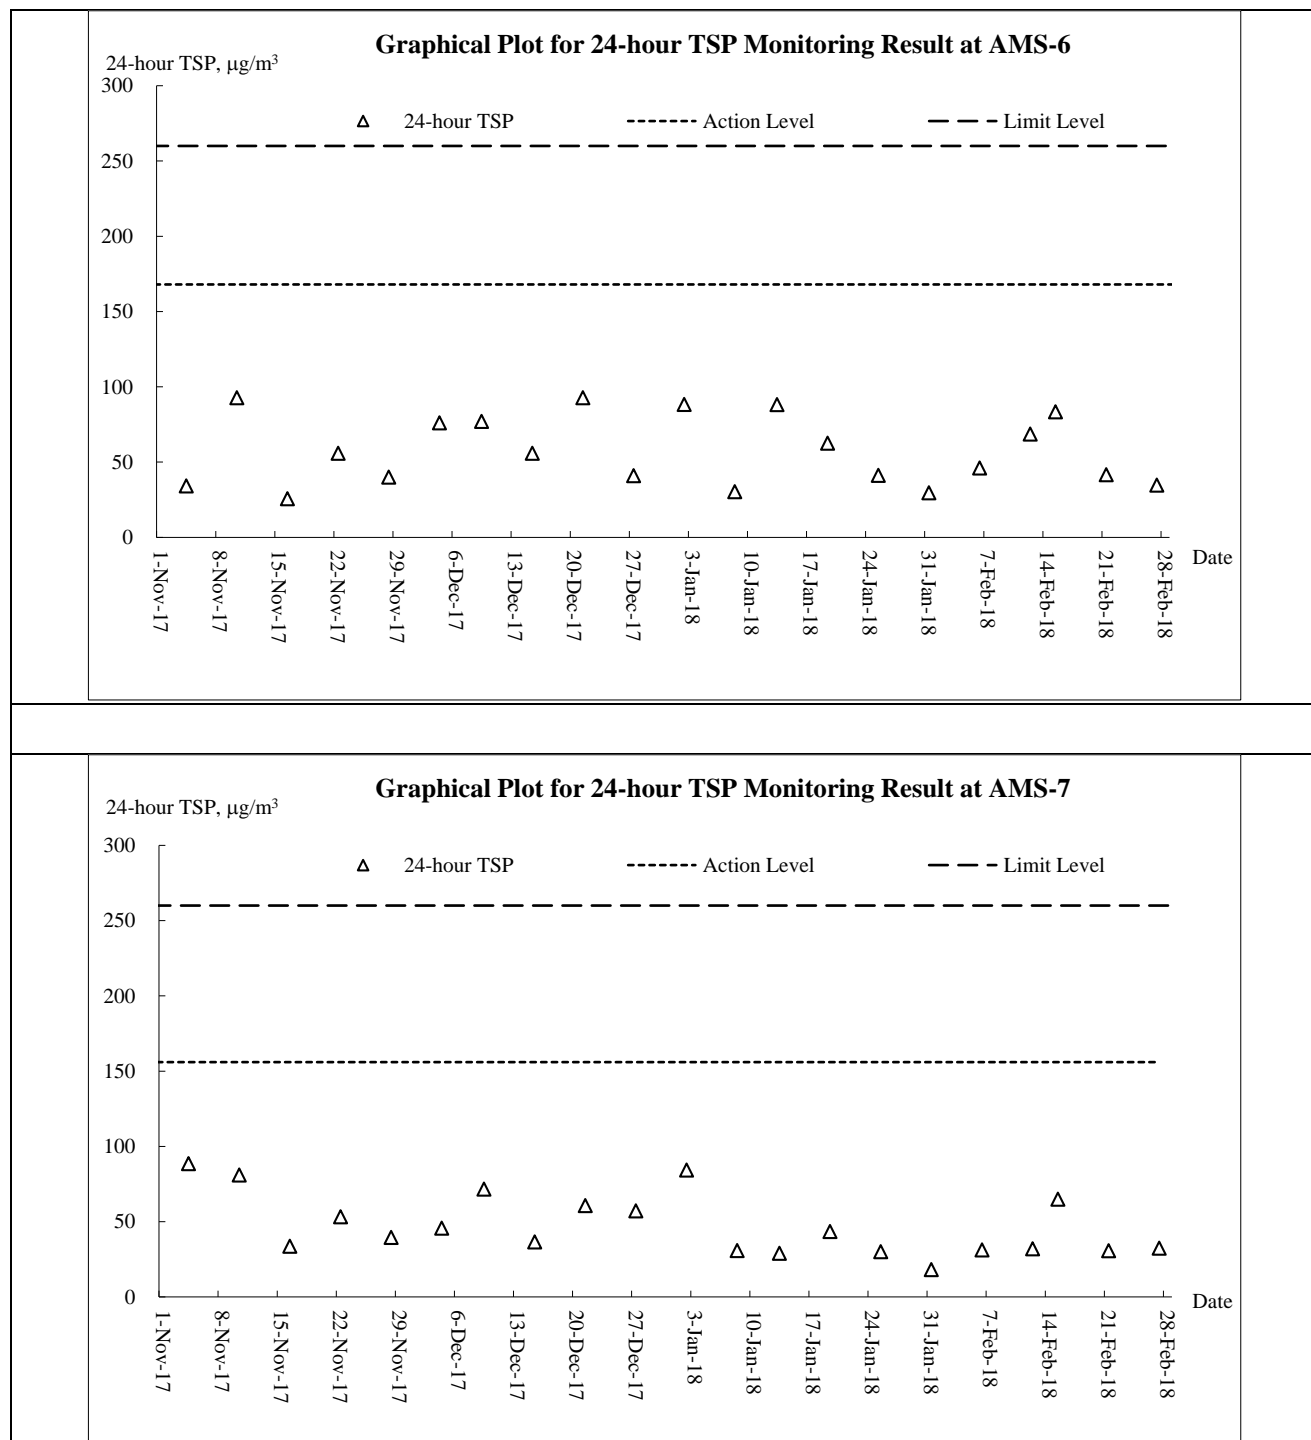

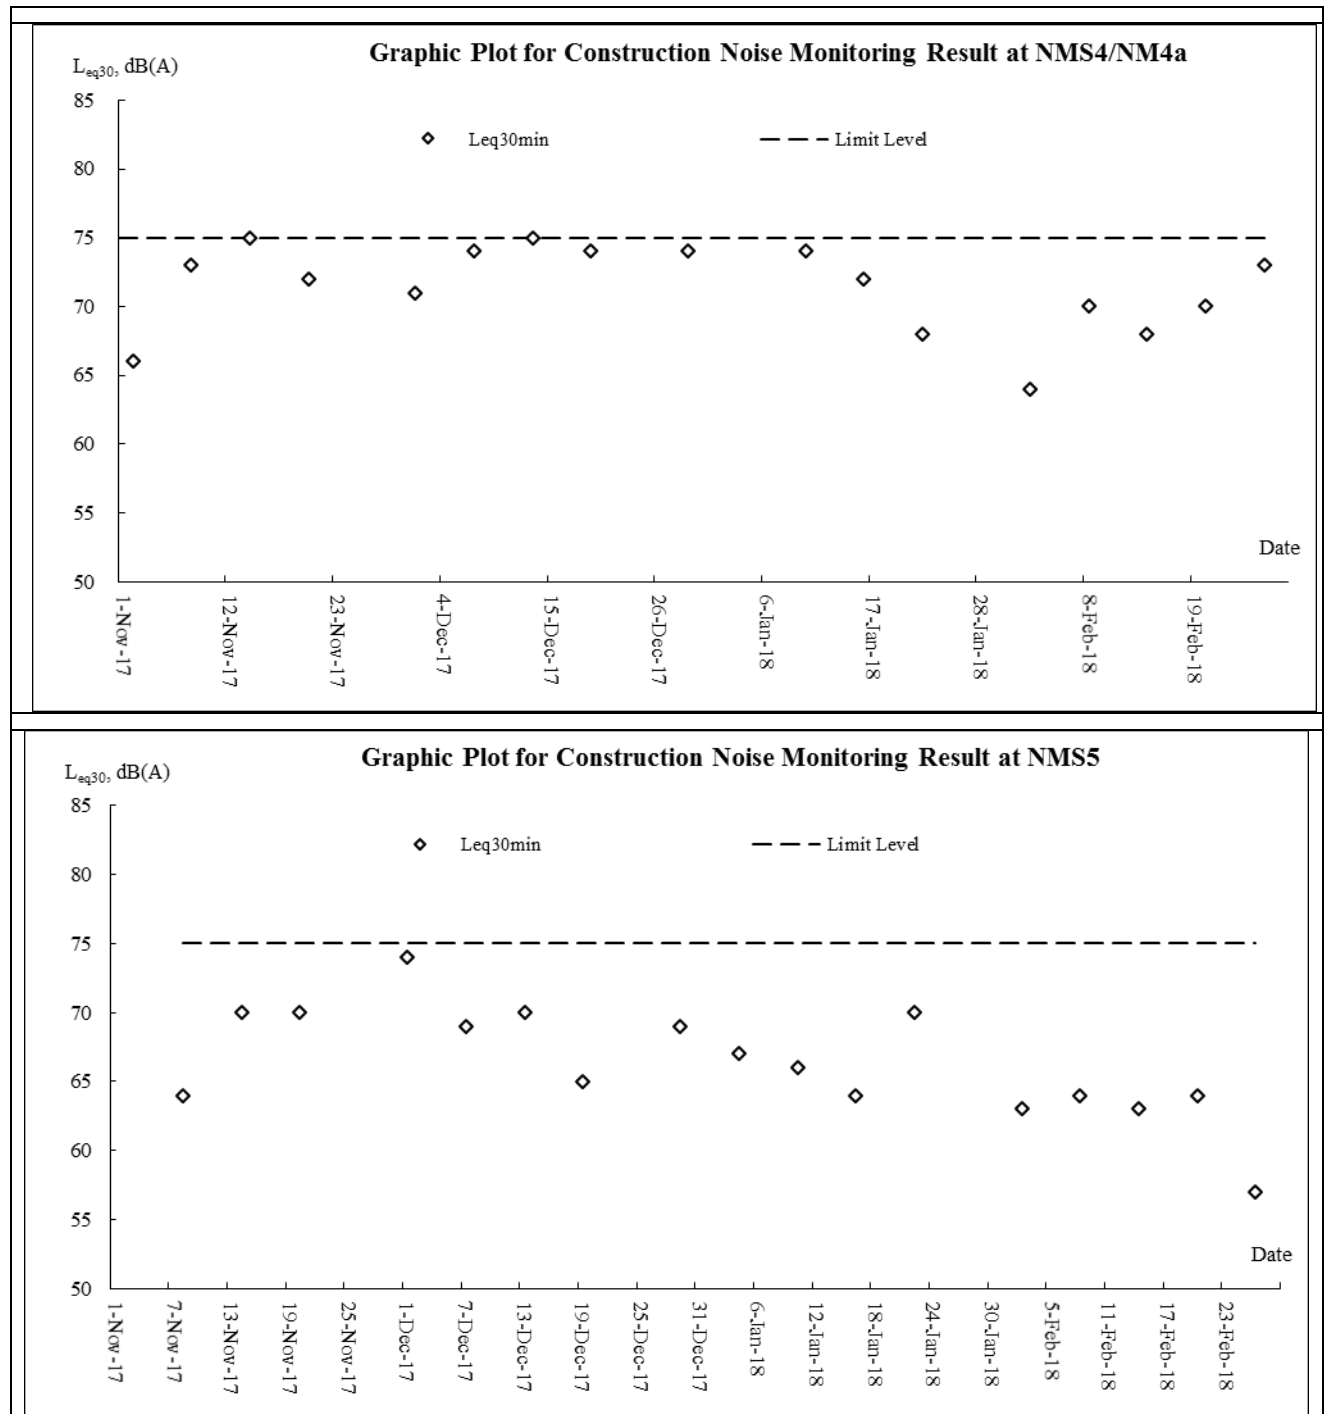Noise

Appendix J

Meteorological Data

Date		Weather	Total Rainfall (mm)	Kwun Tong Station	Kai Tak Station		King's Park Station
				Mean Air Temp. (°C)	Wind Speed (km/h)	Wind Direction	Mean Relative Humidity (%)
1-Feb-18	Thu	Cold and dry.	0	9.2	9.1	NW	58
2-Feb-18	Fri	Mainly cloudy with bright periods.	Trace	9.9	9.6	N/NW	62.5
3-Feb-18	Sat	Cold and dry.	0	9.8	8.9	NE	61.1
4-Feb-18	Sun	Cold and dry.	0	9.8	8.6	N/NW	41.2
5-Feb-18	Mon	Cold and dry.	0	10	11	NW	40.2
6-Feb-18	Tue	Mainly cloudy with bright periods.	0	10.4	10.9	E/SE	39.7
7-Feb-18	Wed	Cold and dry.	0	13.4	9.7	E/SE	52.2
8-Feb-18	Thu	Cold and dry.	0	13.2	12.1	E/SE	49.7
9-Feb-18	Fri	Mainly cloudy with bright periods.	0	14.6	12.8	E/SE	72
10-Feb-18	Sat	Cold and dry.	0	17.2	11.0	SE	73
11-Feb-18	Sun	Mainly cloudy with bright periods.	0	17	9.6	E/SE	61.7
12-Feb-18	Mon	Mainly cloudy with bright periods.	0	15.2	9.1	E/NE	58.5
13-Feb-18	Tue	Cold and dry.	0	14.9	12.7	E/SE	57.5
14-Feb-18	Wed	Mainly cloudy with bright periods.	0	16.6	11	E/SE	55
15-Feb-18	Thu	Cold and dry.	0	20.7	9	SE	57.5
16-Feb-18	Fri	Cold and dry.	0	21.5	10.1	SE	61.2
17-Feb-18	Sat	Mainly cloudy with one or two light rain patches.	Trace	17.6	11.1	E	62.2
18-Feb-18	Sun	Mainly cloudy with one or two light rain patches.	0	18.3	12.0	E	63.0
19-Feb-18	Mon	Mainly cloudy with one or two light rain patches.	Trace	21.6	7.5	SE	79.7
20-Feb-18	Tue	Moderate easterly winds, freshening later.	Trace	21.8	11	SE	80
21-Feb-18	Wed	Mainly cloudy with one or two light rain patches.	Trace	17	16.5	E/SE	81.2
22-Feb-18	Thu	Moderate easterly winds, freshening later.	2.3	13.9	12.5	E/SE	88.5
23-Feb-18	Fri	Moderate east to southeasterly winds.	2	14	11.5	E/SE	78.7
24-Feb-18	Sat	Warm with sunny intervals during the day.	0.2	18.2	11.0	E	71.0
25-Feb-18	Sun	Warm with sunny intervals during the day.	Trace	22.1	8	SW	71.5
26-Feb-18	Mon	Moderate east to southeasterly winds.	Trace	16.2	8.9	E	81
27-Feb-18	Tue	Misty with one or two light rain patches	0	18.7	12.9	E/SE	66.5
28-Feb-18	Wed	Warm with sunny intervals during the day.	Trace	22.9	8.2	SE	80.5

Appendix K

Waste Flow Table

Contract No.: NE/2016/01

Site Formation and Infrastructure Works for Development of Anderson Road Quarry Site

Monthly Summary Waste Flow Table for 2018 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract (see Note 6)	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste (see Note 5)	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	30.706	19.998	10.550	0.000	0.158	1.191	132.060	0.000	0.000	0.000	0.013
Feb	22.756	11.762	10.887	0.000	0.107	1.569	0.000	0.000	0.000	0.000	0.008
Mar											
Apr											
May											
Jun											
Sub-total	53.462	31.760	21.437	0.000	0.265	2.760	132.060	0.000	0.000	0.000	0.021
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	53.462	31.760	21.437	0.000	0.265	2.760	132.060	0.000	0.000	0.000	0.021

Notes:

- (1) The performance targets are given in PS Clause 1.119 (14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and waste will be collected by recycler for recycling.
- (4) Use the conversion factor, density of general refuse (1 t/m³) and inert C&D materials (2 t/m³).
- (5) Use the conversion factor for chemical waste (0.88kg/L).
- (6) Assume a dump truck delivers 7.5 m³ material in 1 trip.
- (7) The cut-off date of this summary is 20th of each month.

Contract No.: NE/2016/01

Site Formation and Infrastructure Works for Development of Anderson Road Quarry Site

Forecast of Total Quantities of C&D Materials to be Generated from the Contract*										
Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract (see Note 6)	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste (see Note 5)	Others, e.g. general refuse
(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
875.389	350.330	510.059	0.000	15.000	3.000	500.000	2.000	4.830	10.000	3.500

Notes:

- (1) The performance targets are given in PS Clause 1.119 (14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and waste will be collected by recycler for recycling.
- (4) Use the conversion factor, density of general refuse (1 t/m³) and inert C&D materials (2 t/m³).
- (5) Use the conversion factor for chemical waste (0.88kg/L).
- (6) Assume a dump truck delivers 7.5 m³ material in 1 trip.
- (7) The cut-off date of this summary is 20th of each month.

Name of Department: CEDDContract No. : NE/2016/05**Monthly Summary Waste Flow Table for 2018** (year)**[PS Clause 1.129]**

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 m ³)
Jan	0.046	0.00	0.001	0.00	0.045	0.00	0.00	0.00	0.00	0.00	0.0006
Feb	0.089	0.00	0.001	0.00	0.088	0.00	0.00	0.00	0.00	0.00	0.0028
Mar											
Apr											
May											
June											
Sub-total											
July											
Aug											
Sept											
Oct											
Nov											
Dec											
Total											

- Notes:
- (1) The performance targets are given in PS Clause 6.14
 - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
 - (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works. Together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

Appendix L

Implementation Schedule for Environmental Mitigation Measures

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
Dust Impact (Contraction Phase)						
S4.7.2 to S4.7.5	Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road is proposed to achieve dust removal efficiency of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.75 L/m ² to achieve the respective dust removal efficiencies.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	V	V
S4.7.6	The Contractor shall follow the procedures and requirements given in the Air Pollution Control (Construct ion Dust) Regulation.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	V	V
S4.7.6	Following dust suppression measures should also be incorporated by the Contractor to control the dust nuisance throughout the construction phase: <ul style="list-style-type: none">Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;Any dusty materials remaining after a stockpile is removed should be wet ted with water and cleared from the surface of roads;A stockpile of dusty material should not be extend beyond the pedestrian barriers, fencing or traffic cones;The load of dusty materials on a vehicle leaving a construct ion site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle;Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road sect ion between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construct ion period.The port ion of any road leading only to construct ion site that is	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>within 30m of a vehicle entrance or exit should be kept clear of dusty materials;</p> <ul style="list-style-type: none"> Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet ; Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; Any skip hoist for material transport should be totally enclosed by impervious sheeting; Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; Cement or dry PFA delivered in bulk should be stored in a closed silo fit ted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed; and Exposed earth should be properly treated by compact ion, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shortcrete or other suitable surface stabiliser within six months after the last construct ion activity on the construction site or part of the construct ion site where the exposed earth lies. 					
S4.7.7	Implement regular dust monitoring under EM&A programme during the Construct ion phase.	Control construction airborne noise	Selected Representative dust monitoring station	All construction sites where practicable	V	N/A
Noise Impact (Contraction Phase)						
S5.6.9	<p>Implement the following good site management practices:</p> <ul style="list-style-type: none"> only well-maintained plant should be operated on-site and plant should be serviced regularly during the construct ion programme; machines and plant (such as trucks, cranes) that may be in 	Control construct ion airborne noise	Contractor	All construction sites where practicable	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>intermittent use should be shut down between work periods or should be throttled down to a minimum;</p> <ul style="list-style-type: none"> plant known to emit noise strongly in one direct ion, where possible, be orientated so that the noise is directed away from nearby NSRs; silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works; mobile plant should be sited as far away from NSRs as possible and practicable; and material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 					
S5.6.11 to S5.6.13	Use of “ Quiet ” Plant and Working Methods.	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	V	V
S5.6.14	Install temporary site hoarding (approx 2.5m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening.	Contractor	All construction sites where practicable	@	V
S5.6.15 to S5.6.18	Install movable noise barriers, full enclosure and acoustic mat, screen the noisy plants including air compressor and generator.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction sites where practicable	@	V
S5.6.19	Sequencing operation of construction plants equipment.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	V	V
S5.6.34	Implement temporary noise barrier along Road L4.	Further reduce the construction airborne noise	Contractor	Road L4 of ARQ	N/A	N/A
S5.6.35	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected Representative Noise monitoring stations	V	N/A
Water Quality Impact (Contraction Phase)						
S6.6.3	<u>Construction Runoff</u> In accordance with the Practice Note for Professional Persons on Construction Site Drainage, Environmental Protection Department, 1994	Control construction runoff	Contractor	All construction sites	@	@

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>(ProPECC PN 1/94), best management practices should be implemented as far as practicable as below:</p> <ul style="list-style-type: none"> At the start of site establishment , perimeter cut -off drains to direct off-site water around the site should be constructed with internal drainage works. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sediment at ion tanks with sufficient capacity, constructed from preformed individual cells of approximately 6 to 8 m³ capacities, are recommended as a general mitigation measure which can be used for set t ling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped. The dikes or embankments for flood protect ion should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt /sediment t rap. The silt /sediment t raps should be incorporated in the permanent drainage channels to enhance deposit ion rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps should be undertaken by the contractor prior to the commencement of construct ion. Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. 					

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.</p> <ul style="list-style-type: none"> Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. All open stockpiles of construction materials (for example, aggregates, sand and fill material) should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of <i>ProPECC PN 1/94</i>. Particular attention should be paid to the control of silty surface runoff during storm events. All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfill toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and rains. Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental 					

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain.</p> <ul style="list-style-type: none"> Construct ion solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts. All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby. Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the rivers. 					
S6.6.6 and 6.6.7	<p><u>Sewage from Workforce</u></p> <ul style="list-style-type: none"> Portable chemical toilets should be provided for handling the construction sewage generated by the workforce. Assume that the capacity of the chemical toilets would be 0.4m³ and suck up twice a day under normal practices, around 45 chemical toilets would be required for the whole site at peak hour. And it should be noted that under normal construction periods, less chemical toilets would be needed. In addition, the total number of the chemical toilets would be subject to later detailed design, the capacity of the chemical toilets, and contractor's site practices. Nevertheless, a licensed contractor should be employed to provide appropriate and adequate portable toilets to cater around 37.5 m³/day sewage and be responsible for appropriate disposal and maintenance. Since portable chemical toilets will be provided, no adverse water quality impact from the workforce sewage is anticipated. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project. Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the Project would not cause water quality impact after undertaking 	Handling of site sewage	Contractor	All construction sites	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	all required measure					
S6.6.8 and 6.6.9	<u>Accidental Spillage</u> To prevent accidental spillage of chemicals, proper storage and handling facilities should be provided. All the tanks, containers and storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and storm drains. The Contractor is required to register as a chemical waste producer if chemical wastes would be generated from the construction activities. Storage of chemical waste arising from the construction activities should be well managed with suitable labels and warnings while disposal of those chemical wastes should be comply with the requirement states in Waste Disposal Ordinance (Cap 354) as well as Waste Disposal (Chemical Waste) (General) Regulations.	Prevention of accidental spillage	Contractor	All construction sites	V	V
S6.6.11- S6.6.14	<u>Groundwater from Contaminated Area</u> The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater discharge. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliancy to the TM-DSS and the existence of prohibited substance should be confirmed after further SI. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with TMDSS or properly recharged into the ground. If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (e.g. Petroleum Carbon Ranges (PCRs)). All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be discharged into the foul sewers. If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back	Minimize contaminated groundwater impacts	Contractor	All construction sites	NA	NA

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as PCBs should be removed as necessary by installing the petrol interceptor.					
Waste Management (Construction Phase)						
S8.5.2	<u>Good Site Practice</u> The following good site practices are recommended throughout the construction activities: <ul style="list-style-type: none"> • nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; 	Minimize waste generation during construction	Contractor	All construction sites	V	V
S8.5.2 (6)	The contractor should submit a Waste Management Plan (WMP) as part of the Environmental Management Plan (EMP) in accordance with the ETWB TC(W) No. 19/2005 for construction phase. The EMP should be submitted to the Engineer for approval. Mitigation measures proposed in the EIA Report and the EM&A Manual should be adopted.	Minimize waste generation during construction	Contractor	All construction sites	V	V
S8.5.3	<u>Waste Reduction Measures</u> Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following	Reduce waste generation	Contractor	All construction sites where	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>recommendations are proposed to achieve reduction:</p> <ul style="list-style-type: none"> segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling of materials and their proper disposal; proper storage and site practices to minimize the potential for damage and contamination of construction materials; plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable portions (i.e. soil, broken concrete, metal etc.); provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 			practicable		
S8.5.5	<p><u>Storage of Waste</u></p> <p>The following recommendation should be implemented to minimize the impacts:</p> <ul style="list-style-type: none"> waste such as soil should be handled and stored well to ensure secure containment; stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; different locations should be designated to stockpile each material to enhance reuse; 	Minimize waste impacts from storage	Contractor Contractor	All construction sites	V	V
S8.5.6	<p><u>Collection and Transportation of Waste</u></p> <p>The following recommendation should be implemented to minimize the impacts:</p> <ul style="list-style-type: none"> remove waste in timely manner; employ the trucks with cover or enclosed containers for waste transportation; obtain relevant waste disposal permits from the appropriate authorities; and disposal of waste should be done at licensed waste disposal facilities. 	Minimize waste impacts from storage	Contractor	All construction sites	V	@
S8.5.8	<p><u>Excavated and C&D Material</u></p> <p>Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&D materials:</p>	Minimize waste impacts from excavated and C&D materials	Contractor	All construction sites	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<ul style="list-style-type: none"> maintain temporary stockpiles and reuse excavated fill material for backfilling; carry out on-site sorting; make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; implement a recording system for the amount of waste generated, recycled and disposed of for checking; <p>The recommended C&D materials handling should include:</p> <ul style="list-style-type: none"> On-site sorting of C&D materials Reuse of C&D materials Use of Standard Formwork and Planning of Construction Materials purchasing Provision of wheel wash facilities 					
S8.5.15	<u>Contaminated Soil</u> As a precaution, it is recommended that standard good site practice should be implemented during the construction phase to minimize any potential exposure to contaminated soils or groundwater. The details of mitigation measures to minimize the potential environmental implications arising from the handling of contaminated materials refer to Land Contamination Section.	Remediate contaminated soil	Contractor	All construction sites where applicable	@	@
S8.5.17	<u>Chemical Waste</u> <ul style="list-style-type: none"> If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. 	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	V	V
S8.5.18	<u>General Waste</u> <ul style="list-style-type: none"> General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling. Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should 	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	@	@

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>also be implemented to keep areas clean.</p> <ul style="list-style-type: none"> A reputable waste collector should be employed to remove general refuse on a daily basis. 					
S8.5.19	<p><u>Sewage</u></p> <ul style="list-style-type: none"> The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability, site condition and activities. Regularly collection by licensed collectors should be arranged to minimize potential environmental impacts. 	Minimize production of sewage impacts	Contractor	All construction sites	V	V
Ecology (Contraction Phase)						
S. 10.7.2 to 10.7.6	Re-provision of Wooded Area for ecological function at the future Quarry Park.	Compensate for the loss of three woodland patches of a total area of about 1.13ha.	Contractor/ Detailed Design Consultant (qualified botanist / horticulturist / Certified Arborist to supervise the planting).	Northern part of the proposed Quarry Park.	N/A	NA
10.7.10	<p>Construction phase in situ mitigation measures to minimize impacts on hydrological condition and water quality of hillside watercourses include:</p> <ul style="list-style-type: none"> Temporary sewerage and drainage will be designed and installed to collect wastewater and prevent it from entering nearby watercourses; Proper locations well away from nearby watercourses will be used for temporary storage of materials (i.e. equipment, fill materials, chemicals and fuel) and temporary stockpile of construction debris and spoil, and these will be identified before commencement of works; To prevent muddy water entering nearby watercourses, work sites close to nearby watercourses will be isolated, using such items as sandbags or silt curtains with lead edge at bottom and properly supported props. Other protective measures will also be taken to ensure that no pollution or siltation occurs to the water gathering grounds of the works site; Stockpiling of construction materials, if necessary, will be properly 	Minimize impacts on Hydrological condition and water quality of hillside watercourses.	Contractor	All construction sites	V	NA

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<p>covered and located away from nearby watercourses;</p> <ul style="list-style-type: none"> Erection of temporary geotextile silt fences will be carried out around earth-moving works to trap any sediments and prevent them from entering watercourses; Construction debris and spoil will be covered and/or properly disposed as soon as possible to avoid being washed into nearby watercourses; Exposed soil will be covered as quickly as possible following formation works, followed, where appropriate, by covering with biodegradable geotextile blanket for erosion control purposes; Where appropriate, earth-bunding will be carried out of areas where soils have been disturbed or where vegetation has been cleared, to ensure that surface runoff will not move soils off-site; Construction effluent, site run-off and sewage will be probably collected and/or treated. Wastewater from any construction site will be minimised via the following in descending order: reuse, recycling and treatment ; Proper locations for discharge outlets of wastewater treatment facilities well away from sensitive receivers will be identified and used; Silt traps will be installed at points where drainage from the site enters local watercourses; Appropriate sanitary facilities for on-site workers will be provided; The site boundary will be clearly marked and any works beyond the boundary strictly prohibited, and Regular water monitoring and site audit will be carried out at suitable points. If the monitoring and audit results show that pollution occurs, adequate measures including temporary cessation of works will be considered. 					
S.10.7.1 1	<p>Implement an emergency contingency plan during the construction phase and the plan will include, but not be limited to, the following:</p> <ul style="list-style-type: none"> Potential emergency situations; Chemicals or hazardous materials used on-site (and their location); Emergency response team; Emergency response procedures; List of emergency telephone hot lines; Locations and types of emergency response equipment , and 	Minimize impacts on Hydrological condition and water quality of hillside watercourses.	Contractor	All construction sites	N/A	NA

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status	
					Contract 1	Contract 2
	<ul style="list-style-type: none"> Training plan and testing for effectiveness. 					
Landscape and visual (Contraction Phase)						
S11.14.2 3, Table 11.9, CM1 [4]	All existing trees to be retained shall be carefully protected during construction.	Avoid disturbance and protection of the existing trees	Detailed Design Consultant /	The whole project area where applicable	V	V
S11.14.2 3, Table 11.9, CM2 [3]	Tree Transplantation - Should removal of trees be unavoidable due to construction impacts, trees will be transplanted or felled. Detailed transplanting proposal will be submitted to relevant government departments for approval in accordance with LAO GN No. 7/2007, ETWB TCW No. 29/2004 and 10/2013 . Final locations of transplanted trees shall be agreed prior to commencement of the work.	Minimize landscape impact and retention of landscape resources	Detailed Design Consultant /	Onsite where possible. Otherwise consider offsite locations	*	N/A
S11.14.2 3, Table 11.9, CM3 [4]	Control of operation night -time glare with well-planned lighting operation system to minimize potential glare impact to adjacent VSRs	Minimize glare impact to adjacent VSRs	Contractor/ CEDD	The whole project area where applicable	V	V
S11.14.2 3, Table 11.9, CM [4]	Erection of decorative screen hoarding.	Minimize visual impact	Contractor/ CEDD	The whole project area where applicable	N/A	N/A
S11.14.2 3, Table 11.9, CM5 [2]	Minimise disturbance and limitation of run-off – temporary structures and construction works should be planned with care to minimize disturbance to adjacent landscape, vegetation, natural stream habitats.	Minimize visual impact	Contractor/ CEDD	The whole project area where applicable	V	V

Legend: V = implemented; x = not implemented; @ = partially implemented; * = pending to be implemented; N/A = not applicable

Appendix M

Complaint Log
And
Investigation Report for Complaint

Appendix M1

Cumulative Complaint and Summons/ prosecution

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/ Prosecution in Reporting Month
March 2017	1	0
April 2017	0	0
May 2017	0	0
June 2017	2	0
July 2017	3	0
August 2017	3	0
September 2017	4	0
October 2017	2	0
November 2017	3	0
December 2017	3	0
January 2018	1	0
February 2018	3	0
Overall Total	25	0

Appendix M2 Complaint Log

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Status	Investigation Report Ref.
1	23-Mar-17	NA	On Tat Estate	Resident of On Tat Estate	Construction noise	SPRO hotline	NA	A resident living in On Tat House reported that some night works with noise and flashing caused nuisance to nearby resident after 11:00 pm on 23 March 2017.	According the incident report conducted by the CWSTVJV, demobilization of crawler crane was undertaken on 23 March 2017 11pm and it is TD requirement to carry out demobilization of heavy machine at nighttime. It is considered this complaint was a single incident and would not be happened again in future.	no comment by IEC on 11 Oct 2017	TCS00864/16/300/F0087
2	28-Jul-17	28-Jul-17	38/F of Yin Tat House (賢達樓), On Tat Estate	Resident of On Tat Estate	Construction noise	SPRO hotline	NA	Mr. Hsu received a complaint from a resident living in the flat on 38/F of Yin Tat House (賢達樓), On Tat Estate. The resident complained about the noise level of our works during daytime.	Noise monitoring by Contractor was conducted in Yin Tat House, On Tat Estate, at around 2 pm on 28-Jul-2017. Another noise monitoring was carried out by ET and representatives of AECOM and JV in the presence of the complainant in her flat at 10 am on 1-Aug-2017 and was witnessed by Mr. Hsu. No exceedance of noise was recorded. The complainant was satisfied about the monitoring results.	no comment by IEC on 9 Aug 2017	TCS00864/16/300/F0060
3	29-Aug-17	29-Aug-17	Shing Tat House 24/F	Resident of On Tat Estate	Construction noise	SPRO hotline	NA	Mr. Hsu Yau Wai reported that he received complaint from a resident (Ms Cheng) living at Shing Tat House 24/F Room 22 about the noise generated from our site this week. The noise heard was mainly rock breaking noise from our site.	Noise monitoring was carried out by ET and representatives of AECOM and JV in the presence of the complainant in her flat at 3pm on 30-Aug-2017. No exceedance of noise was recorded. The complainant was satisfied about the monitoring results.	no comment by IEC on 8 Sep 2017	TCS00864/16/300/F0081
4	21-Jun-17	29-Aug-17	Tat Yan House, Po Tat Estate	Resident of Po Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/00019 373-17)	day time construction noise of breakers (8am to 6pm)	These two complaints were forwarded by CEDD to ET on 31 August 2017 which after the complaint dates. Investigation was conducted based on the site information by the Contractor of Contract 1 as well as the observation during weekly site inspection carried out ET during June 2017. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident and the working hour 08:00 to 18:00 did not breach any legal requirement. To eliminate the inconvenience caused to the nearby resident CWSTVJV was advised to further enhance the noise mitigation measures as appropriately.	no comment by IEC on 3 Nov 2017	TCS00864/16/300/F0093
5	22-Jun-17	29-Aug-17	Tat Yan House, Po Tat Estate	Resident of Po Tat Estate	Dust & Construction noise	EPD	EPD (ref. N08/RE/00019428-17)	Day time construction noise of breakers (8AM to 6PM). Requested to delay the operating hour of breakers to 10AM or 11AM			TCS00864/16/300/F0093
6	15-Jul-17	29-Aug-17	Tat Yi House, Po Tat Estate	Resident of Po Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/00022 479-17)	Construction noise	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident and the working hour 08:00 to 18:00 did not breach any legal requirement. To eliminate the inconvenience caused to the nearby resident, CWSTVJV was advised to further enhance the noise mitigation measures as appropriately.	no comment by IEC on 3 Nov 2017	TCS00864/16/300/F0094
7	28-Jul-17	29-Aug-17	Anderson Road	unknown	Dust	EPD	EPD (ref.N08/RE/00023 986-17)	Poor control on dust emission at Anderson Road Construction Site	CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident and status of the implementation of dust mitigation measures was considered effective based on the site observation.	no comment by IEC on 15 Nov 2017	TCS00864/16/300/F0097

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Status	Investigation Report Ref.
8	2-Aug-17	29-Aug-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/00024557-17)	Day time construction noise of breakers (8AM to 6PM)	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in August 2017, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should further enhance the noise mitigation measures as appropriately. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 15 Nov 2017	TCS00864/16/300/F0098
9	19-Sep-17	19-Sep-17	Sau Mau Ping Estate Sau Nga House	Resident of Sau Mau Ping Estate	Construction noise	SPRO hotline	NA	The complainant is living at Sau Mau Ping Estate Sau Nga House 38/F. He complained about the noise nuisance recently from August to September especially during night time after 12:00 am, even in Saturdays and Sundays. The noise nuisance caused a great disturbance to him. He made a request to conduct investigation about the source of the noise during night time.	ET has conducted an ad-hoc noise measurement for Leq (30min) on the rooftop of 秀雅樓 and 秀義樓 in the afternoon of 22 September 2017. During the course of noise measurement, construction activities such as excavation and breaking were conducted in the Quarry Site. The measurement results taken at both 秀雅樓 and 秀義樓 were 63dB(A) which below the Limit Level under the EM&A Programme.	no comment by IEC on 18 Oct 2017	TCS00864/16/300/F0088
10	21-Sep-17	13-Oct-17	Sau Mau Ping Estate Sau Nga House and Sau Yee House	Resident of Sau Mau Ping Estate	Construction noise	EPD	EPD (ref.N08/RE/00031074-17)	On 21 September 2017, the same complaint further reported that the noise can be heard at both Sau Yee House and Sau Nga House even in daytime and he strongly requested the Contractor to follow up the case immediately.			TCS00864/16/300/F0088
11	27-Sep-17	13-Oct-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/00029489-17)	The complainant questioned why there were 6 to 7 breakers operating in the morning but only 1 operating in the afternoon. He requested to shift the operation of the breakers to afternoon.	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in September and October 2017, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 30 Nov 2017	TCS00864/16/300/F0106
12	3-Oct-17	13-Oct-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction noise	EPD	EPD (ref. N08/RE/00032407-17)	Day time construction noise, the complainant requested using less breaker at one time, erecting taller noise barrier to cover the equipment. In addition, the complainant would like to know the construction schedule whether there will be more breaking activities in near future			TCS00864/16/300/F0106
13	25-Oct-17	26-Oct-17	Tat Kwai House, Po Tat Estate	Resident of Po Tat Estate	Dust	EPD	NA	投訴安達臣道地盤的泥車落泥，令他達貴樓的住所受到大塵影響，要求跟進及回覆	Investigation revealed that CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident. Nevertheless, based on the observation during site inspection on 31 October 2017, CWSTVJV was advised to enhance the dust mitigation measures particularly during dry season.	no comment by IEC on 15 Nov 2017	TCS00864/16/300/F0100

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Status	Investigation Report Ref.
14	6-Nov-17	7-Nov-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Noise	EPD	NA	安達邨俊達樓居民投訴石礦場地盤又再於早上 07:45 開始傳出機器不停 採石的噪音(幾乎每日在 08:00-19:00 進行工程),已持續一年,他全家人受到滋擾。	Ad-hoc noise measurement was conducted by ET at rooftop of Chun Tat House in the morning of 20 November 2017 and measurement result was below the Limit Level under the EM&A Programme. CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 30 Nov 2017	TCS00864/16/300/F0109
15	13-Nov-17	14-Nov-17	Chi Tai House, On Tai Estate	Mr. Lam Wai	light pollution and noise	SPRO hotline	NA	1. 智泰樓面向安達臣地盤方向,有照射燈深夜時分仍然常開,影響居民正常睡眠質素,照成一定的精神壓力。 2. 隔音布未固定,大風吹過發出極大的聲浪	To ease the concern by the complaint, CWSTVJV has adjusted the lights to the orientation pointing the ground and that to minimise the nuisance. For the maintenance of noise barrier, CWSTVJV has immediately fixed the noise barrier nearest to On Tai Estate and prolonged the cover area of the noise barrier to reduce the noise impact to the public.	no comment by IEC on 24 Nov 2017	TCS00864/16/300/F0104
16	1-Nov-17	14-Nov-17	Shing Tat House, On Tat Estate	Resident of Po Tat Estate	Noise	EPD	NA	居住於安達邨誠達樓高層的投訴人投訴由早上八時半至下午六時聽到採鐵噪音。	CWSTVJV had already deployed the acoustic mat as noise barrier at the site boundary near Shing Tat House. To enhance the noise mitigation measures, CWSTVJV deployed an acoustic mat as noise barrier for the breaking work in order to reduce construction noise affecting the upper floor of On Tat Estate.	no comment by IEC on 13 Dec 2017	TCS00864/16/300/F0110
17	25-Aug-17	26-Oct-17	Sau Yee House, Sau Mau Ping Estate	Resident of Sau Mau Ping Estate	Construction Noise	EPD	EPD (ref.N08/RE/00027 738-17)	Night time construction noise of hammering (around 12AM)	It is confirmed by CWSTVJV and checked against the site diary that no construction activities were carried out after 19:00 at the subject site. Therefore, the complaint about noise nuisance during night time should not be related to the Project.	no comment by IEC on 14 Dec 2017	TCS00864/16/300/F0114
18	12-Sep-17	26-Oct-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction Noise	EPD	EPD (ref. N08/RE/00029489-17)	Day time construction noise of breakers (8AM to 5PM)	Noise mitigation measures were implemented to reduce the noise impact to the nearby resident. According to the impact noise monitoring result in September 2017, there were no breaches of EM&A requirement. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 10 Jan 2018	TCS00864/16/300/F0117
19	15-Dec-17	21-Dec-17	Sau Yee House	Resident of Sau Mau Ping Estate	Construction Noise	EPD	NA	Resident of Sau Yee House complained suspected construction noise from Anderson Construction Site at restricted hour (7pm to 7am).	It is confirmed by CWSTVJV and checked against the site diary that no construction activities were carried out after 19:00 at the subject site. Therefore, the complaint about noise nuisance during night time should not be related to the Project.	no comment by IEC on 10 Jan 2018	TCS00864/16/300/F0118
20	20-Dec-17	21-Dec-17	On Tat Estate	Resident of On Tat Estate	Dust	EPD	NA	投訴安達臣道信和地盤水車已經壞了十多天,一直無灑水,四周非常大塵。投訴人住於安達邨,投訴安達臣道石礦場有大地盤,地盤大車工作時間不停出入揚起沙塵,吹到安達邨,影響空氣環境,要求部門到場視察。	CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident. It is considered that the complaint was an isolated case due to malfunction of water tanker and CWSTVJV has promptly rectified the deficiency. As advised by CWSTVJV, another water tanker will be deployed in mid-January 2018 to enhance the dust suppression measures throughout the construction site.	no comment by IEC on 25 Jan 2018	TCS00864/16/300/F0121
21	28-Dec-17	10-Jan-18	Sau Yee House	Resident of Sau Mau Ping Estate	Construction Noise	CE's office	NA	日間及凌晨均聽到轟隆聲的噪音及震動,懷疑是由附近工程引起	ET has conducted an ad-hoc noise measurement for Leq (30min) in the complainant's flat in the monitoring of 17 January 2018. It was noted that the complainant's flat is not in direct line of sight to the Anderson Road Quarry Site. The measurement noise	no comment by IEC on 8 Feb 2018	TCS00864/16/300/F0129

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Status	Investigation Report Ref.
									result was below the Limit Level under the EM&A Programme. Moreover, it is confirmed by CWSTVJV and checked against the site diary that no construction activities were carried out during restricted hour at the subject site. Therefore, the complaint about noise nuisance during restricted hour should not be related to the Project.		
22	15-Jan-18	15-Jan-18	Chun Tat House	Resident of Chun Tat House of On Tat Estate, 40/F	Construction Noise	SPRO mobile	NA	She is irritated by the construction noise of breaking rock for a long time and strongly requested to know exactly when will be the completion date of the breaking rock part of works opposite to Chun Tat House. She said we should do more on the mitigation measures because our site is very close to the residents nearby.	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in January 2018, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 8 Feb 2018	TCS00864/16/300/F0130
23	1-Feb-18	2-Feb-18	Chi Tai House On Estate	Resident of On Tai Estate (referred by Mr. Lam Wai)	Construction Noise	SPRO hotline	NA	"智泰對出，白天噪音過大，可否加裝隔音板？高層受影響"	the Environmental Team has conducted an ad-hoc noise measurement for Leq(30min) at the corridor of 22/F of Chi Tai House on 2 February 2018 facing the construction site. The measurement noise result was 65dB(A) which below the Limit Level under the EM&A Programme. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in January 2018, there were no breaches of EM&A requirement.	no comment by IEC on 22 Feb 2018	TCS00864/16/300/F0137
24	1-Feb-18	2-Feb-18	Shing Tat House On Estate	Resident of Shing Tat House (referred by Mr. Hsu Yau Wai)	Construction Noise	SPRO hotline	NA	Mr. Hsu reported that some disturbing noise was heard after 6:00 pm from the site near Shing Tat House of On Tat Estate.	AECOM has liaised with Mr. Hsu on 2 February 2018 for the complaint matter and he reported to AECOM that the noise was generated until 7:00 pm on 1 February 2018. 3. As advised by Contractor of Contract 1, breaking works at USRT area which opposite to Shing Tat House was only carried out from 8:00 to 18:00. However, rock breaking at System A was extended to 19:00 on 1 February 2018. As noise mitigation measures, noise barriers were erected for the works area. Further to the complaint case, CWSTVJV would seek for other quiet work method such as using drilling machine to reduce noise level and speed up the rock breaking process, so that to reduce the noise intensity level and the duration of exposure.	no comment by IEC on 28 Feb 2018	TCS00864/16/300/F0140
25	28-Feb-18	28-Feb-18	Shing Tat House On Estate	Resident of Shing Tat House	Construction Noise	EPD	NA	安達邨誠達樓居民，投訴人是返夜班，一年半以來長期受對出地盤日間探石仔噪音滋擾，由於單位與地盤太近，堅持環保署跟進及回覆如何處理及減低噪音，他亦要求知道何日完工。	The IR is under reviewed by IEC.		

To **Mr. Dennis Leung**

Fax No

By e-mail

Company **AECOM**

cc

From **Nicola Hon**

Date

22 February 2018

Our Ref **TCS00864/16/300/F0137a**

No of Pages

5

(Incl. cover sheet)

RE

CEDD Service Contract No. NTE/07/2016

Environmental Team for Development of Anderson Road Quarry Site –

Site Formation and Associated Infrastructure Works

Investigation Report for Noise Complaint from resident of Chi Tai House of On Tai Estate

If you do not receive all pages, or transmission is illegible, please contact the originator on (852) 2959-6059 to re-send. Should this facsimile be sent to the wrong fax number, would receiver please destroy this copy and notify Action-United Environmental Services & Consulting immediately. Thank you.

Dear Sir,

Enclosed please find the investigation report for the captioned for your follow up action.

Should you have any queries or need further information, please do not hesitate to contact us or the undersigned at **Tel: 2959-6059 or Fax: 2959-6079**.

Yours Faithfully,

For and on Behalf of

Action-United Environmental Services & Consulting



Nicola Hon

Environmental Consultant

Encl.

EPD

Mr. Leo Luk

Fax: 2591 0558

EPD

Mr. Paul Wong

Fax: 2756 8588

CEDD/BCP

Mr. Stephen Li (Ch Eng/NTE2)

Fax: 2739 0076

ANewR (IEC)

Mr. Adi Lee

By e-mail

CWSTVJV

Mr. TY Leung

By e-mail

CEDD Service Contract No. NTE/07/2016
Environmental Team for Development of Anderson Road Quarry Site –
Site Formation and Associated Infrastructure Works

Investigation Report on Environmental Complaint / Enquires

Complaint Log No.	NTE/07/2016 – 24
Received Date by ET	2 February 2018
Related Contracts	Contract 1 (NE/2016/01)
Complaint Details	"智泰對出，白天噪音過大，可否加裝隔音板?高層受影響"
Complaint Location	Chi Tai House of On Tai Estate
Date of Complaint	1 February 2018
Environmental Aspect	Noise
Complainant	Resident of On Tai Estate (referred by Mr. Lam Wai)
Complaint Route	Received by SPRO hotline
Investigation Result	<ol style="list-style-type: none"> 1. A public complaint was received by SPRO on 1 February 2018 regarding construction noise heard at upper floor of Chi Tai House as described in "Complaint Details". The site layout and complaint location are shown in <i>Figure 1</i>. 2. Upon receipt of the complaint, the Environmental Team (ET) has conducted an ad-hoc noise measurement for Leq(30min) at the corridor of 22/F of Chi Tai House on 2 February 2018 facing the construction site. (<i>Photos 1 & 2</i>) The measurement noise result was 65dB(A) which below the Limit Level under the EM&A Programme. The observations and findings on 2 February 2018 are presented below. <ol style="list-style-type: none"> (a) Excavation was carried out at opposite to Chi Tai House. There was direct line of sight from the construction site to the higher floor of Chi Tai House. (<i>Photo 3</i>) (b) As noise mitigation measures, erection of acoustic mat as temporary noise barrier was installed along the site boundary toward Chi Tai House. (<i>Photos 4 & 5</i>) 3. As advised by Contractor of Contract 1 - NE/2016/01 (CWSTVJV), the following noise mitigation measures and action have been undertaken to response the complaint. <ol style="list-style-type: none"> (a) Breaker head was wrapped with sound absorbing material; (b) Noise Barriers were erected with about 1.8 m height along footpath adjacent to the breaking area (screened against the On Tai Estate, NSR); it was explained that higher noise barrier will be easier to be affected by higher wind loading effect and may lead to the consequence of collapse. CWSTVJV is exploring other safer erection method to enhance the noise reduction; (c) CWSTVJV agreed to minimize the breaking works before noise mitigation works done; (d) CWSTVJV agreed to carry out noise mitigation works before breaking works start near RWA14 area even with a relatively small scale breaking works; and

CEDD Service Contract No. NTE/07/2016
Environmental Team for Development of Anderson Road Quarry Site –
Site Formation and Associated Infrastructure Works
Investigation Report on Environmental Complaint / Enquires

	<p>(e) CWSTVJV will carry out self-noise monitoring after resume work to check the compliance with the relative noise regulations.</p> <p>4. Joint site inspection among the RE, CWSTVJV and ET was carried out on in January 2018 the status of implemented mitigation measures provided by CWSTVJV was inspected. Noise mitigation measures including temporary noise barrier, acoustic mat and wrapped by acoustic materials are implemented on site. (Photos 4 to 6) Moreover, quiet plants (e.g. QPME) are used to reduce the cumulative noise impact from the construction activities of the whole site.</p> <p>5. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in January 2018, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate, such as maintain good site practices such as intermittent use of machine and plant and Sequencing operation of construction plant equipment. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.</p> <p>6. Nevertheless, in view of the subject site of the project is close to the residential area, CWSTVJV was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.</p>
--	--

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature :



Date : 22 February 2018

Photo Record



Photo 1

Upon receipt of the complaint, the Environmental Team (ET) has conducted an ad-hoc noise measurement for $Leq(30min)$ at the corridor of 22/F of Chi Tai House on 2 February 2018.



Photo 2

Upon receipt of the complaint, the Environmental Team (ET) has conducted an ad-hoc noise measurement for $Leq(30min)$ at the corridor of 22/F of Chi Tai House on 2 February 2018.

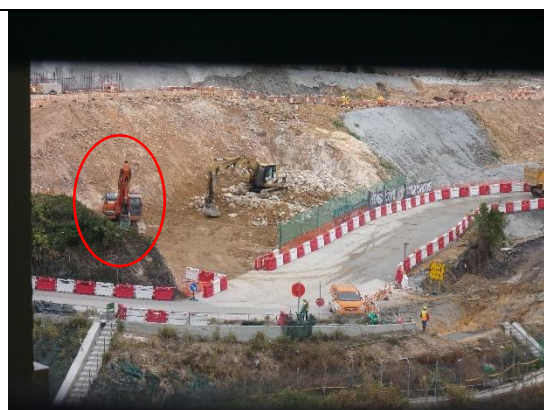


Photo 3

On 2 February 2018, excavation was carried out at opposite to Chi Tai House. There was direct line of sight between the construction site and the higher floor of Chi Tai Estate



Photo 4

As noise mitigation measures, erection of acoustic mat as temporary noise barrier was installed along the site boundary toward Chi Tai Estate.



Photo 5

As noise mitigation measures, temporary noise barrier was erected opposite to Chi Tai Estate.



Photo 6

As noise mitigation measures, the head of the breakers were wrapped by acoustic material.

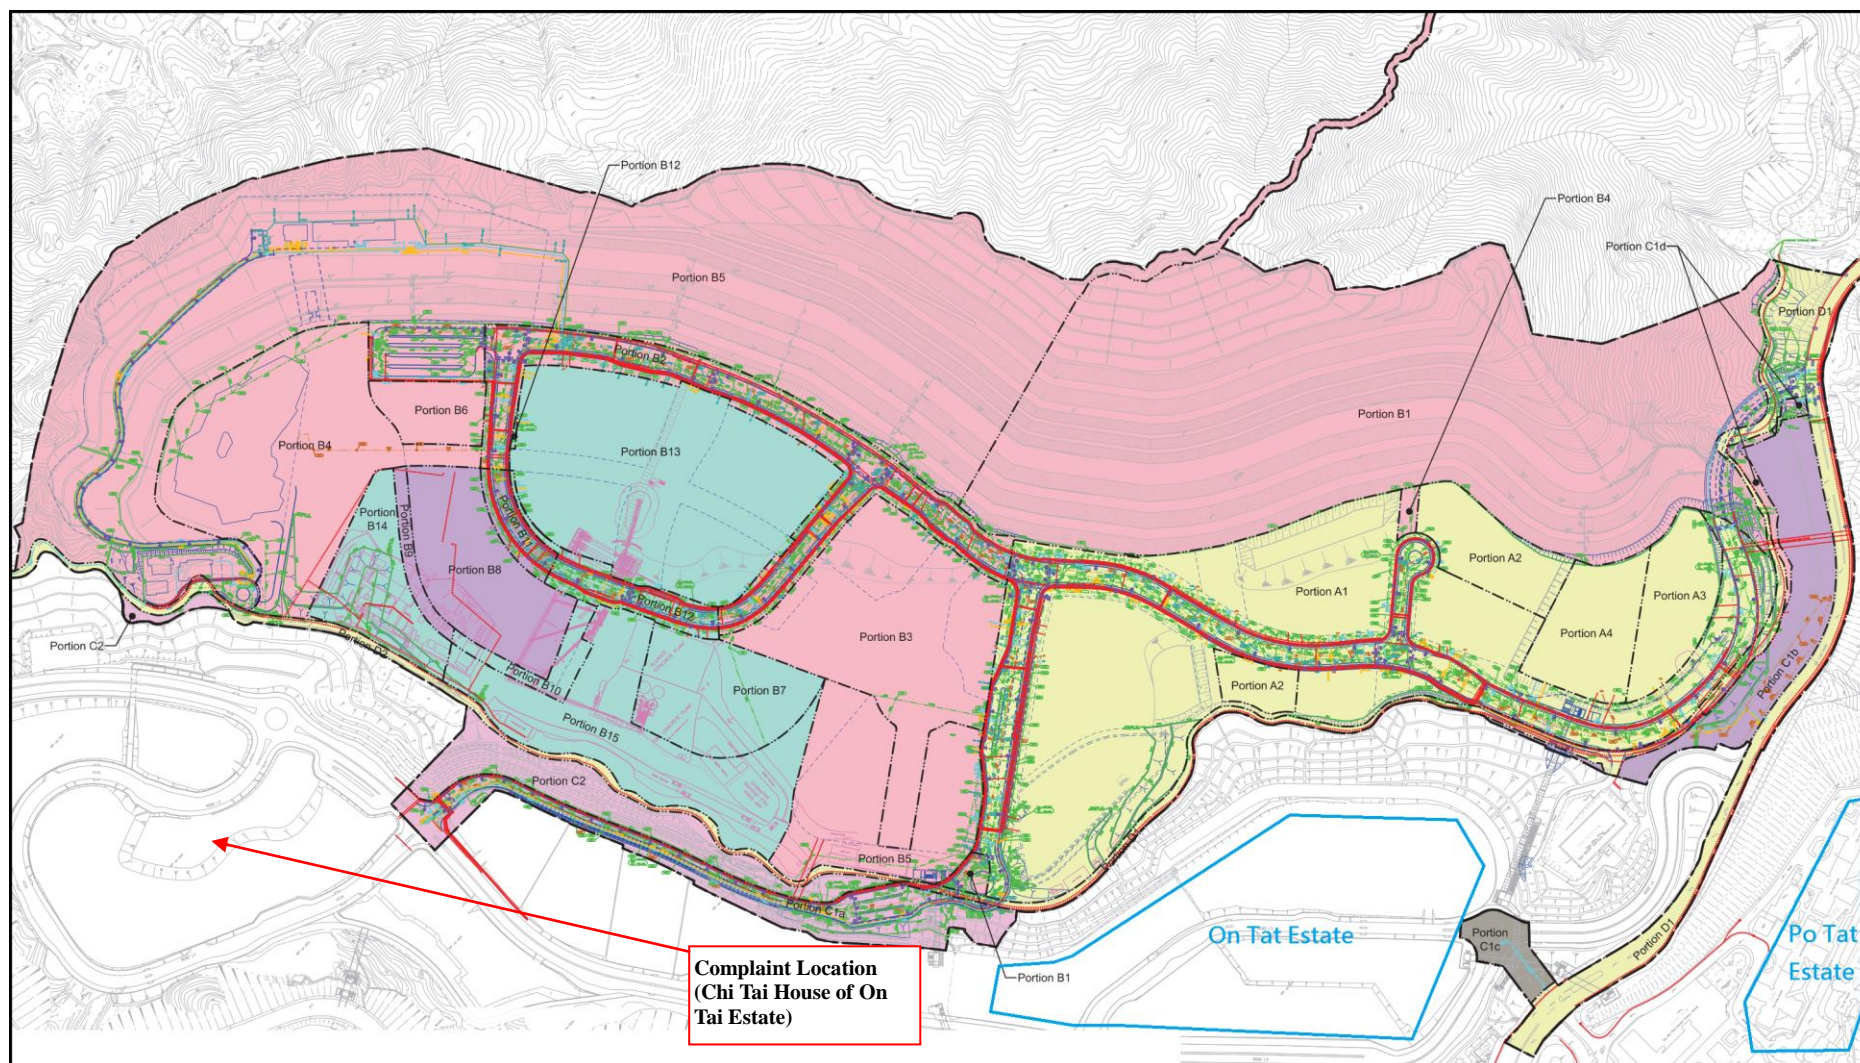


Figure 1 The Layout of NE/2016/01 and the Complaint Location



Fax: 2591 0558
Fax: 2756 8588
Fax: 2739 0076
By e-mail
By e-mail

CEDD Service Contract No. NTE/07/2016
Environmental Team for Development of Anderson Road Quarry Site –
Site Formation and Associated Infrastructure Works

Investigation Report on Environmental Complaint / Enquires

Complaint Log No.	NTE/07/2016 – 25
Received Date by ET	2 February 2018
Related Contracts	Contract 1 (NE/2016/01)
Complaint Details	Mr. Hsu reported that some disturbing noise was heard after 6:00 pm from the site near Shing Tat House of On Tat Estate.
Complaint Location	Shing Tat House of On Tat Estate
Date of Complaint	1 February 2018
Environmental Aspect	Noise
Complainant	Resident of Shing Tat House (referred by Mr. Hsu Yau Wai)
Complaint Route	Received by SPRO mobile
Investigation Result	<ol style="list-style-type: none"> 1. A public complaint was received by SPRO on 1 February 2018 regarding some disturbing noise heard after 6:00 pm from the site near Shing Tat House of On Tat Estate. The site layout and complaint location are shown in <i>Figure 1</i>. 2. AECOM has liaised with Mr. Hsu on 2 February 2018 for the complaint matter and he reported to AECOM that the noise was generated until 7:00 pm on 1 February 2018. 3. As advised by Contractor of Contract 1 - NE/2016/01 (CWSTVJV), breaking works at Underground Stormwater Retention Tank (USRT) area which opposite to Shing Tat House was only carried out from 8:00 to 18:00. However, rock breaking at System A was extended to 19:00 on 1 February 2018. As noise mitigation measures, noise barriers were erected for the works area. (<i>Photos 1 to 2</i>) Further to the complaint case, CWSTVJV would seek for other quiet work method such as using drilling machine to reduce noise level and speed up the rock breaking process, so that to reduce the noise intensity level and the duration of exposure. 4. Joint site inspection among the RE, CWSTVJV and ET was carried out on in January 2018 the status of implemented mitigation measures provided by CWSTVJV was inspected. Noise mitigation measures including temporary noise barrier, acoustic mat and wrapped by acoustic materials are implemented on site. (<i>Photos 2 to 4</i>) Moreover, quiet plants (e.g. QPME) are used to reduce the cumulative noise impact from the construction activities of the whole site. 5. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in January 2018, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate, such as maintain good site practices such as intermittent use of machine and plant and Sequencing operation

CEDD Service Contract No. NTE/07/2016
Environmental Team for Development of Anderson Road Quarry Site –
Site Formation and Associated Infrastructure Works

Investigation Report on Environmental Complaint / Enquires

	<p>of construction plant equipment. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.</p> <p>6. Nevertheless, in view of the subject site of the project is close to the residential area, CWSTVJV was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.</p>
--	--

Prepared By : Nicola Hon

Designation : Environmental Consultant

Signature :



Date : 28 February 2018

Photo Record



Photo 1
Noise Barriers Installation at System A



Photo 2
Excavation and breaking works were carried out at USRT and there was direct line of sight between the construction site and the upper floor of Shing Tat House. As noise mitigation measures, erection of acoustic mat as temporary noise barrier was installed along the boundary of Portion A toward On Tat Estate



Photo 3
As noise mitigation measures, the head of the breakers were wrapped by acoustic materials.



Photo 4
As noise mitigation measures, the head of the breakers were wrapped by acoustic materials.

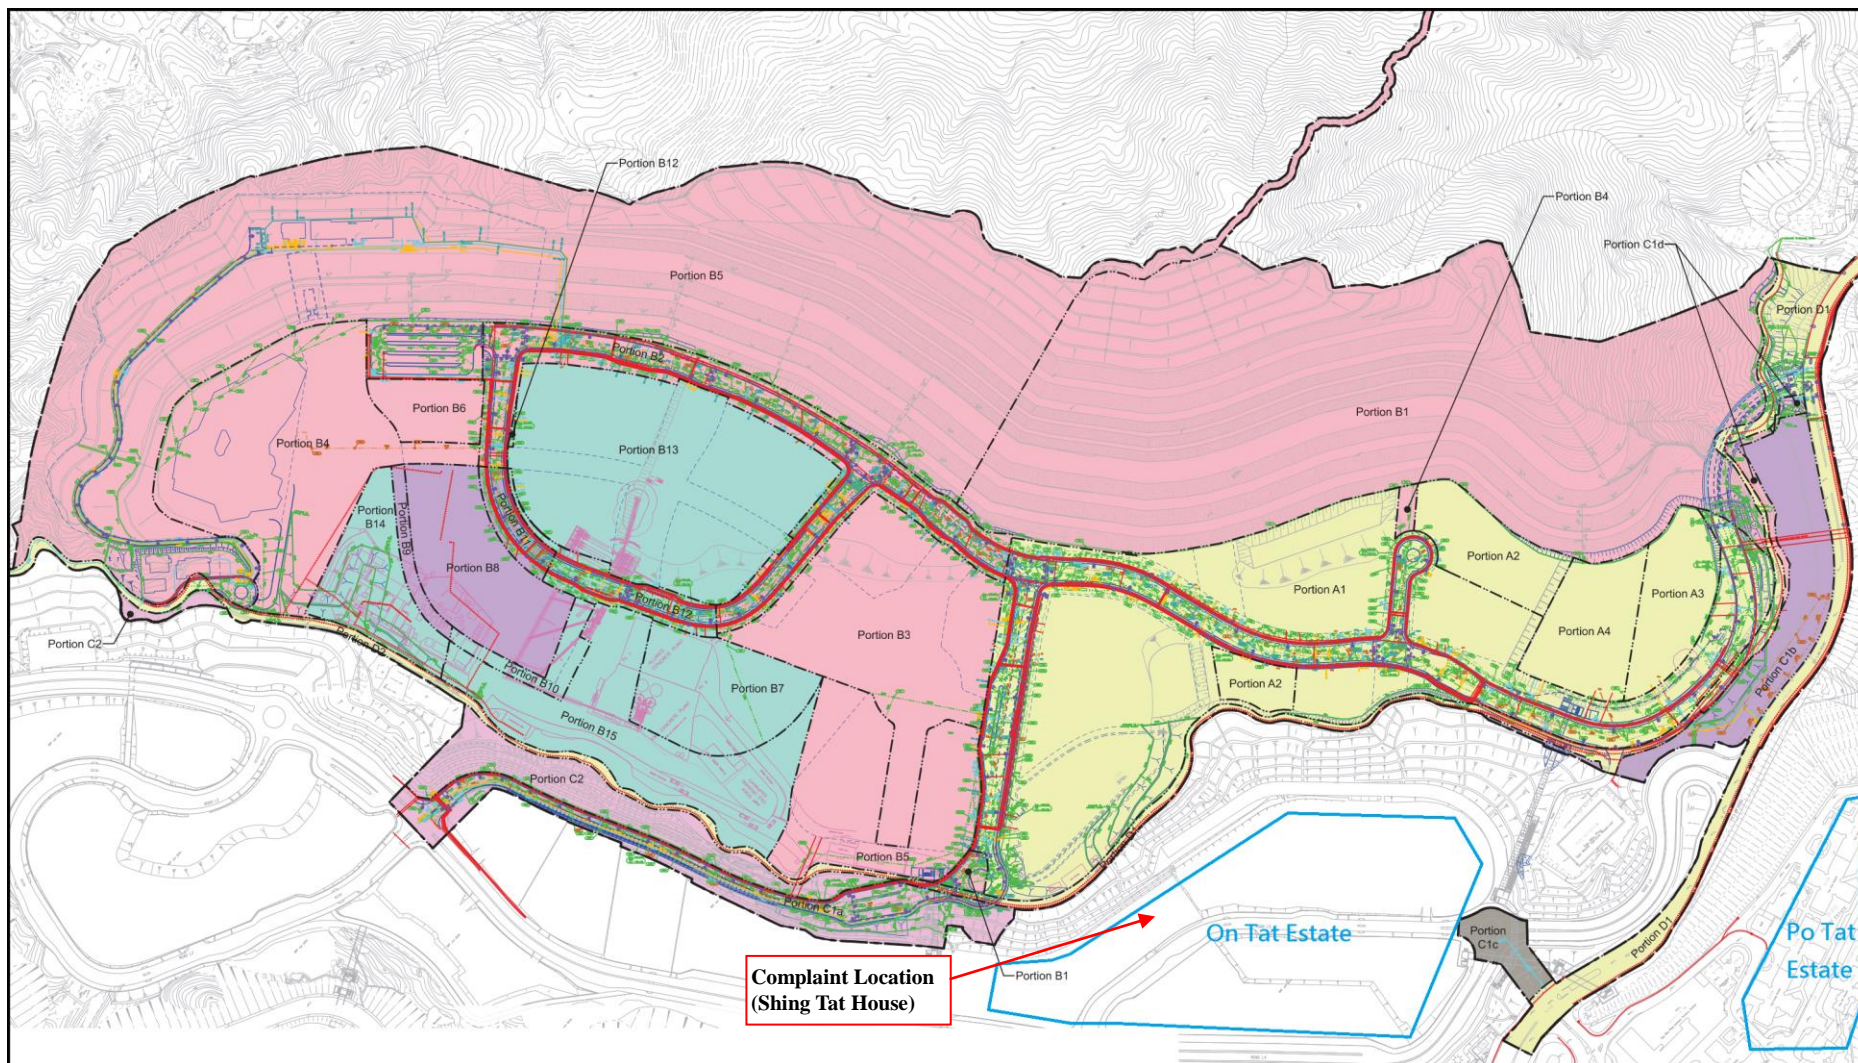


Figure 1 The Layout of NE/2016/01 and the Complaint Location
