

Our Ref: TCS00864/16/300/L0598



531370

Environmental Protection Department
Environmental Assessment Division
Metro Assessment Group
Kowloon Section (2)
27th floor, Southorn Centre,
130 Hennessy Road,
Wan Chai, Hong Kong

10 NOV 2022

Attn: Ms. Hsu Ping Ping, Alice

1 November 2022

By Courier

Dear Sir,

Re: Service Contract No. NTE/07/2016
Environmental Team for Development of Anderson Road Quarry Site – Site
Formation and Associated Infrastructure Works
Submission of Monthly Environmental Monitoring and Audit Report (September
2022)

Pursuant to Environmental Monitoring and Audit Manual Section 13.3.1, we submit herewith two (2) hard copies and one (1) electronic copy of the captioned report for you endorsement. Kindly note the report has been certified by the Environmental Team Leader and verified by Independent Environmental Checker and the verification letter is enclosed in the report.

Should you have any queries or require further information, please feel free to contact us or the undersigned at Tel: 2959-6059 or Fax: 2959-6079.

Yours sincerely,

For and on Behalf of

Action-United Environmental Services & Consulting

Nicola Hon
Environmental Consultant

Encl.



cc	CEDD	Attn: Mr. Leung Chi Foon (Ch Engr/E2)	w/ 3 hardcopies + 1 softcopy
	EPD	Attn: Mr. Paul Wong (EPO (Regional E)41)	w/ 1 hardcopy
	AECOM	Attn: Mr. Ivan Tsang	w/ 1 hardcopy
	AECOM	Attn: Mr. Tommy Li (SRE)	w/ 1 hardcopies + 1 softcopy

JOB No.: TCS00864/16

**CEDD SERVICE CONTRACT No. NTE/07/2016
ENVIRONMENTAL TEAM FOR DEVELOPMENT OF
ANDERSON ROAD QUARRY SITE – SITE FORMATION
AND ASSOCIATED INFRASTRUCTURE WORKS**

**MONTHLY ENVIRONMENTAL MONITORING AND AUDIT
REPORT (SEPTEMBER 2022)**

**PREPARED FOR
CIVIL ENGINEERING AND DEVELOPMENT DEPARTMENT
(CEDD)**

Date	Reference No.	Prepared By	Certified By
1 November 2022	TCS00864/16/600/R0589v2	 Nicola Hon (Environmental Consultant)	 Tam Tak Wing (Environmental Team Leader)

Version	Date	Remarks
1	28 October 2022	First submission
2	1 November 2022	Amended As Per IEC's comment



Civil Engineering and Development Department
East Development Office
8/F, South Tower, West Kowloon Government Offices
11 Hoi Ting Road
Yau Ma Tei
Kowloon

Your reference:

Our reference: HKCEDD10/50/108338

Date: 1 November 2022

Attention: Mr Leung Chi Foon

BY POST

Dear Sirs

Agreement No.: NTE 08/2016
Independent Environmental Checker for Development of
Anderson Road Quarry Site – Site Formation and Associated Infrastructure Works
Monthly Environmental Monitoring and Audit Report (September 2022)

We refer to the emails of 31 October and 1 November 2022 from Action-United Environmental Services and Consulting attaching a Monthly Environmental Monitoring and Audit Report (September 2022) for the captioned project.

We have no further comment and hereby verify the captioned report.

Should you have any queries, please do not hesitate to contact the undersigned or our Mr Frankie Yuen on 2618 2831.

Yours faithfully
ANewR CONSULTING LIMITED

James Choi
Independent Environmental Checker

CPSJ/LCCR/YCFF/lsm

cc CEDD – Mr Ryan Chi (email: rychi@cedd.gov.hk)
CEDD – Mr C M Or (email: cmor@cedd.gov.hk)
AECOM – Mr Tommy Li (email: c1-srec2@arqaecom.com)
AECOM – Mr Bill C P Hon (email: c2-srec3@arqaecom.com)
AECOM – Mr Brad C W Chan (email: c3-srec4@arqaecom.com)
AUES – Mr T W Tam (email: twtam@fordbusiness.com)

EXECUTIVE SUMMARY

- ES01 Action-United Environmental Services & Consulting (AUES) has been awarded the Civil Engineering and Development Department (CEDD) Service Contract No. NTE/07/2016 Environmental Team for Development of Anderson Road Quarry Site – Site Formation and Associated Infrastructure Works (hereinafter called “the Service Contract”) on 15 December 2016. The commencement date of the Service Contract is from December 2016 and the Contract Period is 70 months.
- ES02 The Services under the Service Contract is to provide environmental monitoring and audit (EM&A) services for the Works Contracts pursuant to the requirement of Environmental Team (ET) under the EM&A manual to ensure that the environmental performance of the Works Contracts comply with the requirement specified in the EM&A Manual and EIA Report of Development of Anderson Road Quarry and other relevant statutory requirements.
- ES03 To facilitate the project management and implementation, the Service Contract has been divided to three CEDD contracts including Contract NE/2016/01 (Contract 1), Contract NE/2016/05 (Contract 2) and Contract NE/2017/03 (Contract 3). As advised by the Resident Engineer (RE), the commencement date of Contract 1 was 21 December 2016 and the major construction works has been commenced on 12 April 2017. The commencement date of Contract 2 was 31 March 2017 and the major construction activities have been commenced on 2 May 2017. Furthermore, Contract 3 was commenced on 31 May 2018 and the major construction activities works was commenced in November 2018. The EM&A programme under the Project was commenced on 12 April 2017 pursuant to the requirement under the EM&A manual. In addition, variation order for extend service scope to E5, E6, E7 and C10 under Contract ED/2019/02 (Contract 5) was issued by AECOM. The commencement date of Contract 5 was on 30 March 2021. Moreover, variation order for extend service under Contract ED/2020/02 (Contract 4) was issued by AECOM. The commencement date of Contract 4 was on 27 September 2021.
- ES04 This is the 66th monthly EM&A report presenting the monitoring results and inspection findings for the period from **1 to 30 September 2022** (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

- ES05 Environmental monitoring activities under the EM&A programme in the Reporting Period are summarized in the following table.

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Reporting Period	
		Number of Active Monitoring Locations	Total Occasions
Air Quality	1-hour TSP	6	108
	24-hour TSP	4	20
Construction Noise	Leq(30min) Daytime for Contract NE/2016/01	7	28
	Leq(30min) Daytime for Contract NE/2017/03	3	12

BREACH OF ACTION AND LIMIT (A/L) LEVELS

- ES06 No exceedance of air quality was recorded in the Reporting Period. For construction noise monitoring, no Limit Level exceedance was recorded and no noise complaint (which triggered Action Level) was received in the reporting period. The environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	NA	NA

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
	24-hour TSP	0	0	0	NA	NA
Construction Noise	L _{eq} (30min) Daytime	0	0	0	NA	NA

ENVIRONMENTAL COMPLAINT

- ES07 In the reporting period, one (1) environmental complain was received regarding to Water Quality for Contract 1 and Contract 4.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

- ES08 No environmental summons or successful prosecutions for the Project were recorded in the Reporting Period.

REPORTING CHANGE

- ES09 There is no reporting change in the Reporting Period.

SITE INSPECTION

- ES10 In this Reporting Period, joint site inspections to evaluate the site environmental performance for **Contract 1** were carried out by the RE, ET and Contractor on **8, 14, 20 and 27 September 2022** in which IEC joined the site inspection with SSEMC on **8 September 2022**. No non-compliance was noted during the site inspection.
- ES11 In this Reporting Period, joint site inspections to evaluate the site environmental performance for **Contract 2** were carried out by the RE, ET and Contractor on **7, 14, 20 and 28 September 2022** in which IEC joined the site inspection on **20 September 2022**. No non-compliance was noted during the site inspection.
- ES12 In this Reporting Period, joint site inspections to evaluate the site environmental performance for **Contract 3** were carried out by the RE, ET and Contractor on **2, 9, 16, 23 and 30 September 2022** in which IEC joined the site inspection with SSEMC on **16 September 2022**. No non-compliance was noted during the site inspection.
- ES13 In this Reporting Period, joint site inspections to evaluate the site environmental performance for **Contract 4** were carried out by the RE, ET and Contractor on **7, 14, 22 and 28 September 2022** in which IEC joined the site inspection with SSEMC on **22 September 2022**. No non-compliance was noted during the site inspection.
- ES14 In this Reporting Period, joint site inspections to evaluate the site environmental performance for **Contract 5** were carried out by the RE, ET and Contractor on **1, 8, 15, 22 and 27 September 2022** in which IEC joined the site inspection on **27 September 2022**. No non-compliance was noted during the site inspection.

FUTURE KEY ISSUES

- ES15 During wet season, the Contractors are reminded to pay special attention on water quality mitigation measures and should fully implement the measures as recommended in the EM&A Manual, in particular to prevent muddy water or other water pollutants from site surface overflow to public area should be properly maintained.
- ES16 Since construction site is highly visible to the resident at nearby estates, the Contractors should pay special attention on potential environmental impact generated by the site activities and adhere implement adequate air quality and noise mitigation measures as far as practicable to reduce the impact to the public.

- ES17 Construction noise is one of the key environmental issues during construction work of the Project. Noise mitigation measures such as using quiet plants and noise barriers shall be implemented where practicable according to the EM&A manual.
- ES18 In addition, the Contractors should ensure all effluent discharge shall be fulfilled the Technical Memorandum of Effluent Discharged into Drainage and Sewerage Systems, inland and Coastal Waters criteria or relevant discharge license requirement.

Table of Contents

1. INTRODUCTION	1
1.1 PROJECT BACKGROUND	1
1.2 REPORT STRUCTURE	1
2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	3
2.1 CONSTRUCTION CONTRACT PACKAGING	3
2.2 PROJECT ORGANIZATION	4
2.3 CONSTRUCTION PROGRESS	4
3. SUMMARY OF IMPACT MONITORING REQUIREMENTS	10
3.1 GENERAL	10
3.2 MONITORING PARAMETERS	10
3.3 MONITORING LOCATIONS	10
3.4 MONITORING FREQUENCY AND PERIOD	12
3.5 MONITORING EQUIPMENT	13
3.6 MONITORING METHODOLOGY	13
3.7 DERIVATION OF ACTION/LIMIT (A/L) LEVELS	15
3.8 DATA MANAGEMENT AND DATA QA/QC CONTROL	16
4. AIR QUALITY MONITORING	18
4.1 GENERAL	18
4.2 RESULTS OF AIR QUALITY MONITORING	18
5. CONSTRUCTION NOISE MONITORING	20
5.1 GENERAL	20
5.2 NOISE MONITORING RESULTS IN REPORTING MONTH	20
6. WASTE MANAGEMENT	22
6.1 GENERAL WASTE MANAGEMENT	22
6.2 RECORDS OF WASTE QUANTITIES	22
7. SITE INSPECTION	24
7.1 REQUIREMENTS	24
7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	24
8. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	27
8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	27
9. IMPLEMENTATION STATUS OF MITIGATION MEASURES	30
9.1 GENERAL REQUIREMENTS	30
9.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	30
9.3 KEY ISSUES FOR THE COMING MONTH	32
10. CONCLUSIONS AND RECOMMENDATIONS	33
10.1 CONCLUSIONS	33
10.2 RECOMMENDATIONS	33

LIST OF TABLES

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 1
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 2
TABLE 2-3	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 3
TABLE 2-4	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 4
TABLE 2-5	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT 5
TABLE 3-1	SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2	IMPACT MONITORING STATIONS - AIR QUALITY
TABLE 3-3	IMPACT MONITORING STATIONS - CONSTRUCTION NOISE
TABLE 3-4	ADDITIONAL IMPACT MONITORING STATIONS – CONSTRUCTION NOISE
TABLE 3-5	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-6	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-7	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-8	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 4-1	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-1)
TABLE 4-2	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-2)
TABLE 4-3	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-3)
TABLE 4-4	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-5)
TABLE 4-5	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-6)
TABLE 4-6	SUMMARY OF 24-HOUR AND 1-HOUR TSP MONITORING RESULTS (AMS-7)
TABLE 5-1	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 5-1a	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 5-2	SUMMARY OF CONSTRUCTION NOISE MONITORING RESULTS
TABLE 6-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 6-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 7-1	SITE OBSERVATIONS OF CONTRACT 1
TABLE 7-2	SITE OBSERVATIONS OF CONTRACT 2
TABLE 7-3	SITE OBSERVATIONS OF CONTRACT 3
TABLE 7-4	SITE OBSERVATIONS OF CONTRACT 4
TABLE 7-5	SITE OBSERVATIONS OF CONTRACT 5
TABLE 8-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 8-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 8-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 9-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	LAYOUT PLAN OF THE PROJECT
APPENDIX B	PROJECT ORGANIZATION STRUCTURE
APPENDIX C	THREE-MONTHS ROLLING CONSTRUCTION PROGRAMME
APPENDIX D	MONITORING LOCATIONS FOR IMPACT MONITORING
APPENDIX E	CALIBRATION CERTIFICATE OF MONITORING EQUIPMENT AND HOKLAS-ACCREDITATION CERTIFICATE OF THE TESTING LABORATORY
APPENDIX F	EVENT AND ACTION PLAN
APPENDIX G	IMPACT MONITORING SCHEDULE
APPENDIX H	DATABASE OF MONITORING RESULT
APPENDIX I	GRAPHICAL PLOTS FOR MONITORING RESULT

APPENDIX J	METEOROLOGICAL DATA
APPENDIX K	WASTE FLOW TABLE
APPENDIX L	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES
APPENDIX M	COMPLAINT LOG
APPENDIX N	IMPLEMENTATION STATUS FOR WATER QUALITY MITIGATION MEASURES

INTRODUCTION

1.1 PROJECT BACKGROUND

- 1.1.1 Action-United Environmental Services & Consulting (hereinafter referred as “AUES”) has been awarded the CEDD Service Contract No. NTE/07/2016 Environmental Team for Development of Anderson Road Quarry Site – Site Formation and Associated Infrastructure Works (hereinafter called “the Service Contract”) on 15 December 2016. The commencement date of the Service Contract was December 2016 and the Contract Period is 70 months.
- 1.1.2 The Services under the Service Contract is to provide environmental monitoring and audit (EM&A) services for the Works Contracts pursuant to the requirement of Environmental Team (ET) under the EM&A manual to ensure that the environmental performance of the Works Contracts comply with the requirement specified in the EM&A Manual and Environmental Impact Assessment (EIA) Report of Development of Anderson Road Quarry and other relevant statutory requirements.
- 1.1.3 Development of Anderson Road Quarry is to provide land and the associated infrastructures for the proposed land used at the existing Anderson Road Quarry Site at the North-eastern of East Kowloon according to the final Recommended Outline Development Plan (hereinafter named as the Project Works).
- 1.1.4 To facilitate the project management and implementation, the Service Contract has been divided to three CEDD contracts including Contract NE/2016/01 (Contract 1), Contract NE/2016/05 (Contract 2) and Contract NE/2017/03 (Contract 3). As advised by the Resident Engineer (RE), the commencement date of Contract 1 was 21 December 2016 and the major construction works has been commenced on 12 April 2017. The commencement date of Contract 2 was 31 March 2017 and the major construction activities have been commenced on 2 May 2017. Furthermore, Contract 3 was commenced on 31 May 2018 and the major construction activities works was commenced in November 2018. The EM&A programme under the Project was commenced on 12 April 2017 pursuant to the requirement under the EM&A manual. In addition, variation order for extend service scope to E5, E6, E7 and C10 under Contract ED/2019/02 (Contract 5) was issued by AECOM. The commencement date of Contract 5 was on 30 March 2021. Moreover, variation order for extend service under Contract ED/2020/02 (Contract 4) was issued by AECOM. The commencement date of Contract 4 was on 27 September 2021.
- 1.1.5 According to the Approved EM&A Manual, air quality and noise monitoring are required to be monitored during the construction phase of the Project. As part of the EM&A program, baseline monitoring is required to determine the ambient environmental conditions. Baseline monitoring including air quality and noise conducted between *January* and *April 2019* at all designated monitoring locations were before construction work commencement. Furthermore, the Baseline Monitoring Report which verified by the Independent Environmental Checker (hereinafter referred as “the IEC”) has been submitted to Environmental Protection Department (EPD) on *9 May 2017* for endorsement.
- 1.1.6 This is the **66th** monthly EM&A report presenting the monitoring results and inspection findings for the period from **1 to 30 September 2022** (hereinafter referred as “Reporting Period”).

1.2 REPORT STRUCTURE

- 1.2.1 The monthly EM&A Report is structured into the following sections:-

Section 1	<i>Introduction</i>
Section 2	<i>Project Organization and Construction Progress</i>
Section 3	<i>Summary of Impact Monitoring Requirements</i>
Section 4	<i>Air Quality Monitoring</i>
Section 5	<i>Construction Noise Monitoring</i>

Section 6	<i>Waste Management</i>
Section 7	<i>Site Inspections</i>
Section 8	<i>Environmental Complaints and Non-Compliance</i>
Section 9	<i>Implementation Status of Mitigation Measures</i>
Section 10	<i>Conclusions and Recommendations</i>

2. PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

2.1 CONSTRUCTION CONTRACT PACKAGING

- 2.1.1 To facilitate the project management and implementation, the Project was divided by 5 works contracts as described in following. The details of each contract are summarized below and the delineation of each contract is shown in [Appendix A](#).

Contract 1 (Contract No. NE/2016/01)

- 2.1.2 Commencement date of Contract 1 was in late December 2016 and the major scope of work of Contract 1 is listed below:

- Formation of about 40 hectares (ha) of land platforms at the ARQ site and the associated geotechnical works;
- Road works including construction of approximately 3-kilometer long vehicular roads, footpaths, cycle tracks, an approximately 130-meter long underpass at the southern end and a public transport terminus at the northern end at the ARQ site;
- Provision of and improvement to water supply, drainage and sewerage systems as well as landscaping works; and
- Construction of proposed subway structures and lift tower structures of pedestrian connectivity facilities.

Contract 2 (Contract No. NE/2016/05)

- 2.1.3 Commencement date of Contract 2 was 31 March 2017 and the major Scope of Work of the Contract 2 is listed below:

- (i) Construction of the following pedestrian connectivity facilities with covered elevated walkways, covered at grade walkways, escalators, lift towers with associated staircase and lifts:-
 - (a) Linking Hiu Kwong street with Hiu Ming Street (E1)
 - (b) Linking the proposed “Footbridge Link at Sau Ming Road” with Hiu Ming Street (E2, C1 and E3)
 - (c) Linking the proposed bus-to-bus interchange at Tseung Kwan O Tunnel Toll Plaza with Lin Tak Road (E12)
- (ii) Construction of bus-to-bus interchange (BBI) at Tseung Kwan O Tunnel Toll Plaza;
- (iii) Associated landscape works;
- (iv) Construction of green routes connecting to Jordan Valley Park and Choi Wing Road; and
- (v) Slope improvement works in the vicinity of Po Lam Road South and other associated works.

Contract 3 (Contract No. NE/2017/03)

- 2.1.4 The commencement date of Contract 3 is on 31 May 2018 and the major Scope of Work of the Contract 3 is listed below:

- (i) Site formation and road works in the following sections:-
 - (a) at junction of Clear Water Bay Road (CWBR) and On Sau Road constructed under the Development at Anderson Road (DAR) project including the provision of U-turn facility and noise mitigation measures (RIW1);
 - (b) at New Clear Water Bay Road (NCWBR) near Shun Lee Tsuen Road including the road widening works at NCWBR, modification of existing subway structure and provision of noise mitigation measures (RIW2); and
 - (c) at the junction of Lin Tak Road and Sau Mau Ping Road, construction of flyover above Tseung Kwan O Road, provision of loading and unloading bays along Lin Tak Road and noise mitigation measures (RIW3).
- (ii) construction of the following pedestrian connectivity facilities with covered elevated walkways, escalators and lift towers with associated staircases and lifts:-

- (a) linking Anderson Road Quarry site with the DAR Site (except the works covered under Contract 1) (System A and System B);
 - (b) linking Hiu Ming Street with Hiu Yuk Path (E8); and
 - (c) linking the proposed bus-bus interchange at Tseung Kwan O Tunnel Toll Plaza with Sau Mau Ping Road (E11).
- (iii) Associated landscape works.

Contract 4 (Contract No. ED/2020/02)

2.1.5 The commencement date of Contract 4 is on 27 September 2021 and the major Scope of Work of the Contract 4 is listed below:

- Construction of hard landscaping and other ancillary works (e.g. paver footpath, planter walls, benches, lighting etc.);
- Construction of soft landscaping works;
- Lighting, irrigation, electrical and mechanical engineering works within the landscaping area;
- Construction of landscape deck; and
- Electrical and mechanical works for underground water treatment facilities and pumping system for Regional Open Space and Artificial Flood Attenuation Lake.

Contract 5 (Contract No. ED/2019/02)

2.1.6 The commencement date of Contract 5 is on 30 March 2021 and the major Scope of Work of the Contract 5 is listed below:

- Construction of two-way escalator link between Sau Mau Ping Road and the existing footbridge to Po Tat Estate;
- Construction of two-way escalator link between Sau Mau Ping South Estate and the existing footbridge to Sau Mau Ping Road;
- Construction of footbridge, 3m, clear width, with and about 20m high lift tower between Hiu Kwong Street and the podium of Sau Ming House, Sau Mau Ping Estate;
- Construction of footbridge, 3m clear width, with an about 40m high lift tower between Sau Mau Ping Road and the podium of Po Tat Estate; and
- Ancillary works including associated civil, geotechnical, structural, electrical and mechanical engineering and landscaping works.

2.2 PROJECT ORGANIZATION

2.2.1 The project organization and contact details for Contracts 1, 2, 3, 4 and 5 are shown in [Appendix B](#).

2.3 CONSTRUCTION PROGRESS

2.3.1 The 3-month rolling construction programme for Contracts 1, 2, 3, 4 and 5 are shown in [Appendix C](#). The major construction activities conducted in the Reporting Period are summarized in below.

Contract 1 (NE/2016/01)East Portal Area

- Rock filling works for slope Feature 11NE-D/C688 and Slope A1 in progress and completed 80%
- Buttress wall (left and right) construction works complete from 164mPD to 172mPD (LHS) and 164mPD to 170mPD (RHS).
- Rock cut slope A1
- Subbase laying work at Ch565-Ch623
- Construction 750sc at east portal

Fresh Water Reservoir:

- Rock trench excavation for watermain and utilities along WSD access road complete.
- Pipe laying along WSD access road complete.
- Concreting of pipe plinths and staircase for downpipe from reservoir to PTT was completed. Downpipe installation from ~210mPD to 250mPD completed.
- Downpipe installation from PTT to Reservoir complete.

RWS Access Road & External Works:

- CLP Power supply duct
- Road Works & Fencing

Pedestrian Connection System A&B:

- Backfill, E&M, T&C and Lift installation at System B
- E&M and BS works, ABWF Works and Backfill lift tower at System A

Underpass Tunnel (West Portal Area):

- Slope A3, Construction of 200mPD, 186mPD and 178mPD berm
- Slope A5, cut and fill slope and construction run-in

Road L4 (RWA18, Noise Barrier, RWA12, utilities & Road Works):

- Storm drain & manhole M35-4 to S007C, R426 to M35-4 BD and R429 to M35-4BD complete, Gully of S002 to S007B & R426 to R429 complete.
- Construction of DN 450 Sewage Pipe from existing manhole to B223 complete, Manhole B223 to B229a complete
- Laying of wearing course of flexible pavement at CH100 to CH130 complete.
- K1 kerb installation at CH100 to CH130 complete.

Road Works L5, L1 east (between Junction L3&L5):

- Road L1 east part (L5 toward PC system)
- Road L1 east part 3 (Junction L3 toward L5)
- Works for USRT
- Road Works

Hiking Trail connecting to Wison Trail(Portion B5):

- Construction works at Hiking Trail

Contract 2 (NE/2016/05)

- Temporary Traffic Arrangement (TTA)
- Mass Concrete construction
- Formwork and Falsework installation and dismantling
- Lift Installation and lift Tower Construction
- Rebar fixing

Contract 3 (NE/2017/03)Pedestrian Connectivity Facility E8 (PC-E8)

- Touch-up outstanding works are in progress.

Pedestrian Connectivity Facility E11 (PC-E11)

- ABWF works and E&M works at LT2 & ST2 are in-progress.
- Backfilling works at PC6 area is in-progress.
- ABWF works and E&M works at LT1 & ST1 are in-progress.
- ABWF work and E&M works inside the footbridge steel frame are in-progress.

Pedestrian Connectivity Facilities Systems A (PC-SYA)

- ABWF works and E&M works at LT1, LT2 & ST1 are in-progress.

- Erect steel works inside RC structure is in-progress.
- Erect footbridge steel frame is in-progress.

Pedestrian Connectivity Facilities Systems B (PC-SYB)

- RC works at SyB-LT1 & ST1 is in-progress.
- Erect footbridge steel frame is in-progress.
- Install sheet-pile and excavation works at PC1 are in-progress.

Tseung Kwan O Bus-Bus Interchange New Public Toilet (BBI-Toilet)

- The completed toilet was handed over to Food and Environmental Hygiene Department on 30 September 2020; Additional works under an instruction is in-progress.

Contract 4 (ED/2020/02)

- Excavation work for Drainage Works at Portion 8, 9 & 12
- Excavation work for TDMP at Portion 12.
- GI work at Portion 3 & 6
- Slope works at Portion 10 & 17
- Excavation work and modification to existing retaining wall at 13b

Contract 5 (ED/2019/02)Portion 1

- Piling Works at E5-PC1 Lower Platform
- Piling Platform Forming at E5-PC3
- Tree Felling of P-T0310 at E5 Slope
- Tree Felling of P-T0311 at E5 Slope

Portion 2

- Welding Test
- Piling Works
- Grouting Works

Portion 3

- 72mpd Piling platform forming at E7
- Hand digging for CLP cable diversion at E7-F2
- Cable diversion work (CLP & Kumshing) at E7-F2.

Portion 4

- Construction at E10-F3
- Preparation for rock protection and drainage diversion at E10-F1.

- 2.3.3 Summary of the relevant permits, licenses, and/or notifications on environmental protection for the Project of contracts 1, 2, 3, 4 and 5 are presented in **Tables 2-1, 2-2, 2-3, 2-4 and 2-5.**

Table 2-1 Status of Environmental Licenses and Permits of the Contract 1

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Form NA – Notification pursuant to Air pollution Control (Construction Dust) Regulation	EPD ref. no. 411762	NA	NA	Valid
	Form NB – Notification pursuant to Air pollution Control (Construction Dust) Regulation	EPD ref. no. 412730	NA	NA	Valid

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
2	Chemical Waste Producer Registration	Registration no. WPN 5213-292-C4115-01	15 Feb 17	End of project	Valid
3	Water Pollution Control Ordinance – Discharge License	WT00041620-2022	30 May 22	31 May 27	Valid
4	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account no. 7026925	20 Jan 17	End of project	Valid
5	Construction Noise Permit	GW-RE0796-22	17 Aug 22	31 Dec 22	Valid

Table 2-2 Status of Environmental Licenses and Permits of the Contract 2

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Notification pursuant to Air pollution Control (Construction Dust) Regulation	EPD ref. no. 312173	NA	NA	Valid
2	Chemical Waste Producer Registration	Registration no. WPN 5213-294-K2890-08	7 Jul 17	End of Project	Valid
3	Water Pollution Control Ordinance – Discharge License	Case no. 485699	In Progress		
4	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account no.7027548	12 Apr 17	End of project	Valid

Table 2-3 Status of Environmental Licenses and Permits of the Contract 3

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Form NA – Notification pursuant to Air Pollution Control (Construction Dust) Regulation	EPD ref. no. 434186	31-May-18	NA	Valid
2	Chemical Waste Producer Registration	<u>For Area R1W3 (E11)</u> Registration no. WPN : 5213-294-C4239-04	6-Aug-18	End of Project	Valid
		<u>For Area System A</u> Registration no. WPN:	6-Aug-18	End of Project	Valid

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
		5213-293-C4239-05			
		For Area System B Registration no. WPN 5213-294-C4239-03	6-Aug-18	End of Project	Valid
		For Area E8 Registration no. WPN 5213-292-C4239-06	6-Aug-18	End of Project	Valid
3	Water Pollution Control Ordinance – Discharge License	For Area R1W3 (E11) WT00032742-2018	18-Jan-19	31-Jan-24	Valid
		For Area System A WT00033223-2019	31-Jan-19	31-Jan-24	Valid
		For Area System B WT00033229-2019	24-Jun-19	30-Jun-24	Valid
		For Area E8 WT00033224-2019	21-Mar-19	31-Mar-24	Valid
4	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account no.7031075	20-Jun-18	End of project	Valid

Table 2-4 Status of Environmental Licenses and Permits of the Contract 4

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Form NA – Notification pursuant to Air Pollution Control (Construction Dust) Regulation	EPD ref. no. 470496	19 August 2021	NA	Valid
2	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account no. 7041336	6 September 2021	NA	Valid
3	Chemical Waste Producer Registration	Registration no. WPN 5213-296-C1206-12	14 September 21	End of project	Valid
4	Water Pollution Control Ordinance – Discharge License	Case no. 477293	In Progress		

Table 2-5 Status of Environmental Licenses and Permits of the Contract 5

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
1	Form NA – Notification	EPD ref. no. 466255	NA	NA	Valid

Item	Description	License/Permit Status			
		Permit no./ account no./ Ref. no.	Valid Period		Status
			From	To	
	pursuant to Air Pollution Control (Construction Dust) Regulation				
2	Chemical Waste Producer Registration	Registration no. WPN 5298-293-W3611-01	12 May 21	End of project	Valid
3	Water Pollution Control Ordinance – Discharge License	WT00039694-2021	16 Nov 21	30 Nov 26	Valid
		WT00040919-2022	5 May 22	31 May 27	Valid
		WT00041457-2022	30 June 22	30 June 27	Valid
		WT00040670-2022	28 Mar 22	31 Mar 27	Valid
4	Waste Disposal Regulation – Billing Account for Disposal of Construction Waste	Account no. 7040359	3 May 21	NA	Valid

3. SUMMARY OF IMPACT MONITORING REQUIREMENTS

3.1 GENERAL

3.1.1 The Environmental Monitoring and Audit requirements are set out in the Approved EM&A manual. Environmental issues such as air quality, construction noise and water quality were identified as the key issues during the construction phase of the Project.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

3.2 MONITORING PARAMETERS

THE EM&A PROGRAM OF CONSTRUCTION PHASE MONITORING SHALL COVER THE FOLLOWING ENVIRONMENTAL ISSUES:

- Air quality; and
- Construction noise

3.2.1 A summary of the monitoring parameters is presented in *Table 3-1*.

Table 3-1 Summary of EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> • 1-hour TSP by Real-Time Portable Dust Meter; and • 24-hour TSP by High Volume Air Sampler
Noise	<ul style="list-style-type: none"> • Leq(30min) in normal working days (Monday to Saturday) 07:00-19:00 except public holiday • Supplementary information for data auditing, statistical results such as L₁₀ and L₉₀ shall also be obtained for reference.

3.3 MONITORING LOCATIONS

3.3.1 According to the EM&A Manual Section 4.6, seven (7) most representative and affected air sensitive receivers (ASR) were selected as air monitoring stations (AQM). During site visit at the subject site before the baseline monitoring, it was noted that some planned ASRs identified in the EM&A Manual are still under construction/ has not yet constructed and there were no suitable location to set up the high volume sampler to carry out the baseline 24-hour TSP monitoring. Therefore, a proposed change for the baseline monitoring programme was submitted and agreed by EPD before the baseline monitoring. The impact air quality monitoring locations are listed in *Table 3-2* and illustrated in *Appendix D*.

Table 3-2 Impact Monitoring Stations – Air Quality

ID	ASR ID in EIA	Location in the EM&A Manual	Identified Location during Site Visit	Status
AMS-1	ACYC-01	Chi Yum Ching She	Ground of Chi Yum Ching facing the project site	Replaced by AMS-1a
AMS-1a (*)	ACYC-01	Tan Shan Village No. 5 - 6	Ground of Tan Shan Village No. 5 - 6 facing the project site	Active
AMS-2 (#)	DARB-13	Block 8, Site B	Ground of Fung Tai House of On Tai Estate	Active
AMS-3 (:)	DARC-16	Planned Clinic and Community Centre, Site C2	Ground of Planned Clinic and Community Centre facing Anderson Road (Ancillary Facilities Building)	Active
AMS-4	DARC-26	Planned School, Site C2 ^{Note 1}	Ground of Planned School facing Anderson Road	Not yet commenced
AMS-5	DARE-06	Block 5, DAR	Main roof of Oi Tat House of	Active

ID	ASR ID in EIA	Location in the EM&A Manual	Identified Location during Site Visit	Status
		Site E	On Tat Estate facing the project site	
AMS-6	DARE-17	Block 9, Site E	Main roof of Hau Tat House of On Tat Estate facing the project site	Active
AMS-7	AMYT-04	Ma Yau Tong Village	Balcony at 2 nd floor of Village House Anderson Road No. 1 facing the project site	Active

Note 1: The ASR is under construction.

(#) AMS-2 was activated on 26 November 2018 since Fung Tai House became an air sensitive receiver. 1-hour TSP monitoring was commenced on 26 November 2018 while installation of HVS for 24-hour TSP was pending approval from Housing Authority.

() 24-hour TSP monitoring at AMS1 was abandoned since May 2019 due to lack of power supply and the landlord was unreachable. The alternation location of AMS1a was activated on 15 June 2019 for 1-hour and 24-hour TSP monitoring. The proposal was agreed by EPD on 9 Aug 2019.*

(:) AMS-3 was effective on 3 December 2019.

Construction Noise

- 3.3.2 According to the EM&A Manual Section 5.5, three (3) most representative and affected noise sensitive receivers (NSR) were selected as monitoring stations. As recommended by the RE and agreed by IEC, one (1) additional noise monitoring location is proposed to add in Oi Tat House of On Tat Estate (hereafter “NMS-4”) to oversee the possible noise impact pose to the resident in On Tat Estate, which is an existing NSR close to the major works activities. Moreover, review of impact monitoring location was proposed to IEC in view of the current site condition and it was agreed by all parties. The details of noise monitoring location are listed in **Table 3-3** and illustrated in **Appendix D**.

Table 3-3 Impact Monitoring Stations – Construction Noise

ID	NSR ID in EIA	Location	Status
NMS-1	Site C2 – School 05 ^{Note 1}	Ground of planned school at DAR facing the project site	Not yet commenced
NMS-2 (@)	Site E – School	Rooftop of S.K.H. St. John’s Tsang Shiu Tim Primary School, where 1m from the exterior of the building facing the project site	Active
NMS-3(:)	Site C2 – R102-	Ground of Ancillary Facilities Building facing the project site	Active
NMS-4*	Oi Tat House	1m from the exterior of ground floor façade of Oi Tat House of On Tat Estate facing the project site	Suspended
NMS-4a #	Oi Tat House	Rooftop of Oi Tat House where 1m from the exterior of Oi Tat House facing the project site	Active
NMS-5#	Hau Tat House	22/F, refuge floor of Hau Tat House where 1m from the exterior of Hau Tat House facing the project site.	Active
NMS-6~	Yung Tai House of On Tai Estate	Rooftop of Yung Tai House where 1m from the exterior of the building facing the project site)	Active
NMS-7~	Chi Tai House of On Tai Estate	Rooftop of Chi Tai House where 1m from the exterior of the building facing the project site	Active

ID	NSR ID in EIA	Location	Status
NMS-8 [^]	No. 3-4 Ma Yau Tong Village	1m from the exterior of the building façade and facing the construction site	Active

Note 1: Construction of the NSR is not yet commenced.

(*) Additional noise monitoring location was recommended by RE and agreed by IEC. It was temporary suspended and the monitoring location is relocated to NMS4a with effective on 15 Nov 2017.

(@) NMS-2 was effective on 15 November 2019.

(:) NMS-3 was effective on 3 December 2019

(#) Review of noise monitoring locations was proposed by ET and NMS-5 was effective on 15 November 2017.

(~) Review of noise monitoring locations was proposed by ET and NMS-6 and NMS-7 were effective on 28 Feb 2018.

(^) Review of noise monitoring locations was proposed by ET and NMS-8 was effective on 18 April 2018. Noise monitoring at NMS-8 was started on 3 May 2018 upon commencement of construction at relevant section.

Addition Construction Noise Monitoring Location

- 3.3.3 A Work Instruction was issued from AECOM to AUES in November 2018 for installing three additional noise monitoring stations under Contract 3. According to the Work Instruction, one noise monitoring station was proposed to install at System A Area and two station monitoring points were proposed to install at E8 Area. The noise monitoring locations are shown in **Table 3-4** below and illustrated in **Appendix D**.

Table 3-4 Additional Impact Monitoring Stations – Construction Noise

ID	Location	Description
CN1*	Holm Glad College	Ground floor of Holm Glad College, where 1m from the exterior of the building facing E8
CN2*	Leung Shek Chee College	Ground floor of Leung Shek Chee College, where 1m from the exterior of the building facing E8
CN3	Oi Tat House of On Tat Estate	Ground floor of Oi Tat House of On Tat Estate, where 1m from the exterior of the building facing System A

Note 1: Construction of the NSR is not yet commenced.

(*) Additional noise monitoring location was terminated by RE as the construction work at E8 was completed in September 2022. The last monitoring for CN1 & CN2 was on 15 September 2022.

3.4 MONITORING FREQUENCY AND PERIOD

- 3.4.1 The requirements of impact monitoring in the approved *EM&A Manual* and presented as follows.

Air Quality Monitoring

- 3.4.2 Frequency of impact air quality monitoring is as follows:

- 1-hour TSP 3 times every six days during course of works throughout the construction period
- 24-hour TSP Once every 6 days during course of works throughout the construction period

Noise Monitoring

- 3.4.3 Noise monitoring will be to conduct at the all available designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when

noise generating activities are underway:

- one set of $Leq_{(30min)}$ measurements between 07:00 and 19:00 hours on normal weekdays

3.5 MONITORING EQUIPMENT

Air Quality Monitoring

- 3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to prove that the instrument is capable of achieving a comparable results to the HVS. The instrument should be calibrated regularly, and the 1-hour sampling shall be determined on yearly basis by the HVS to check the validity and accuracy of the results measured by direct reading method. The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

- 3.5.2 All equipment to be used for air quality monitoring is listed in **Table 3-5**.

Table 3-5 Air Quality Monitoring Equipment

Equipment		Model
24-hour TSP	High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170
	Calibration Kit	TISCH Model TE-5025A
1- hour TSP	Portable Dust Meter	Sibata LD-3B Laser Dust Monitor

Noise Monitoring

- 3.5.3 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms⁻¹.

- 3.5.4 Noise equipment as perform for construction phase monitoring is listed in **Table 3-6**.

Table 3-6 Construction Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	NL-31, NL-52
Calibrator	NC-75
Portable Wind Speed Indicator	Anemometer AZ Instrument 8908

3.6 MONITORING METHODOLOGY

1-hour TSP

- 3.6.1 The 1-hour TSP monitor was a brand named “Sibata LD-3 Laser Dust monitor Particle Mass Profiler & Counter” which is a portable, battery-operated laser photometer. The 1-hour TSP meter provides a real time 1-hour TSP measurement based on 90° light scattering. The 1-hour TSP monitor consists of the following:

- A pump to draw sample aerosol through the optic chamber where TSP is measured;
- A sheath air system to isolate the aerosol in the chamber to keep the optics clean for maximum reliability; and
- A built-in data logger compatible with Windows based program to facilitate data collection, analysis and reporting.

- 3.6.2 The 1-hour TSP meter to be used will be within the valid period, calibrated by the manufacturer prior to purchasing. Zero response of the instrument will be checked before and after each monitoring event.

24-hour TSP

- 3.6.3 The equipment used for 24-hour TSP measurement is Thermo Andersen Model GS2310 TSP high volume air sampling system, which complied with *EPA Code of Federal Regulation, Appendix B to Part 50*. The High Volume Air Sampler (HVS) consists of the following:
- An anodized aluminum shelter;
 - A 8"x10" stainless steel filter holder;
 - A blower motor assembly;
 - A continuous flow/pressure recorder;
 - A motor speed-voltage control/elapsed time indicator;
 - A 7-day mechanical timer, and
 - A power supply of 220v/50 Hz
- 3.6.4 For HVS for 24-hour TSP monitoring, the HVS is mounted in a metallic cage with a top for protection and also it is sat on the existing ground or the roof of building. The flow rate of the HVS between 0.6m³/min and 1.7m³/min will be properly set in accordance with the manufacturer's instruction to within the range recommended in *EPA Code of Federal Regulation, Appendix B to Part 50*. Glass Fiber Filter 8" x 10" of TE-653 will be used for 24-Hour TSP monitoring and would be supplied by laboratory. The general procedures of sampling are described as below:-
- A horizontal platform with appropriate support to secure the samples against gusty wind should be provided;
 - No two samplers should be placed less than 2 meters apart;
 - The distance between the sampler and an obstacle, such as building, must be at least twice the height that the obstacle protrudes above the sample;
 - A minimum of 2 meters of separation from any supporting structure, measured horizontally is required;
 - Before placing any filter media at the HVS, the power supply will be checked to ensure the sampler work properly;
 - The filter paper will be set to align on the screen of HVS to ensure that the gasket formed an air tight seal on the outer edges of the filter. Then filter holder frame will be tightened to the filter hold with swing bolts. The holding pressure should be sufficient to avoid air leakage at the edge;
 - The mechanical timer will be set for a sampling period of 24 hours (00:00 mid-night to 00:00 mid-night next day). Information will be recorded on the field data sheet, which would be included the sampling data, starting time, the weather condition at current and the filter paper ID with the initial weight;
 - After sampling, the filter paper will be collected and transfer from the filter holder of the HVS to a sealed envelope and sent to a local HOKLAS accredited laboratory for quantifying.
- 3.6.5 All the sampled 24-hour TSP filters will be kept in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal.
- 3.6.6 The HVS used for 24-hour TSP monitoring will be calibrated before the commencement for sampling, and after in two months interval for 1 point checking of maintenance and six months interval for five points calibrate in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A) to establish a relationship between the follow recorder meter reading in cfm (cubic feet per minute) and the standard flow rate, Qstd, in m³/min. Motor brushes of HVS will be regularly replaced of about five hundred hours per time. The calibration certificates of all monitoring equipment used for the impact monitoring program in the Reporting Period and the HOKLAS accredited certificate of laboratory are attached in [Appendix E](#).

Noise Monitoring

- 3.6.7 As referred to in the Technical Memorandum (TM) issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804:1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurement agree to within 1.0 dB.
- 3.6.8 All noise measurements will be performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq). Leq_(30 min) in six consecutive Leq_(5 min) measurements will be used as the monitoring parameter for the time period between 07:00-19:00 hours on weekdays throughout the construction period.
- 3.6.9 The sound level meter will be mounted on a tripod at a height of 1.2 m and placed at the assessment point and oriented such that the microphone is pointed to the site with the microphone facing perpendicular to the line of sight. The windshield will be fitted for all measurements. Where a measurement is to be carried out at a building, the assessment point would normally be at a position 1 m from the exterior of the building façade. Where a measurement is to be made for noise being received at a place other than a building, the assessment point would be at a position 1.2 m above the ground in a free-field situation, i.e. at least 3.5 m away from reflective surfaces such as adjacent buildings or walls.
- 3.6.10 Immediately prior to and following each noise measurement the accuracy of the sound level meter will be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agrees to within 1.0 dB.
- 3.6.11 Noise measurements will not be made in fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed will be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 3.6.12 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis. The calibration certificates of all monitoring equipment used for the impact monitoring program in the Reporting Period is attached in [Appendix E](#).

Meteorological Information

- 3.6.13 The meteorological information including wind direction, wind speed, humidity, rainfall, air pressure and temperature etc. during baseline monitoring is extracted from the closest Hong Kong Observatory Station. To obtain the most appropriate meteorological information where available, the data of temperature is extracted from the Kwun Tong Observatory Station; the data of wind speed and wind direction are extracted from Kai Tak Observatory Station and the data of humidity is extracted from King's Park Station.

3.7 DERIVATION OF ACTION/LIMIT (A/L) LEVELS

- 3.7.1 The baseline results form the basis for determining the environmental acceptance criteria for the impact monitoring. According to the approved Environmental Monitoring and Audit Manual, the air quality, construction noise were set up, namely Action and Limit levels are listed in [Tables 3-7 and 3-8](#).

Table 3-7 Action and Limit Levels for Air Quality Monitoring

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AMS-1	313	154	500	260

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AMS-1a(*)	313	154	500	260
AMS-2	319	165	500	260
AMS-3	319	165	500	260
AMS-4	315	165	500	260
AMS-5	299	166	500	260
AMS-6	303	168	500	260
AMS-7	307	156	500	260

(*) 24-hour TSP monitoring at AMS1 was abandoned since May 2019 due to lack of power supply and the landlord was unreachable. The alternation location of AMS1a was activated on 15 June 2019 for 1-hour and 24-hour TSP monitoring. The proposal was agreed by EPD on 9 Aug 2019.

Table 3-8 Action and Limit Levels for Construction Noise

Monitoring Location	Action Level	Limit Level in dB(A)
	Time Period: 0700-1900 hours on normal weekdays	
NMS-1	When one or more documented complaints are received	70 dB(A) ^{Note 1} / 65 dB(A) ^{Note 1}
NMS-2(@)		
NMS-3(:)		75 dB(A)
NMS-4*		75 dB(A)
NMS-4a#		75 dB(A)
NMS-5#		75 dB(A)
NMS-6~		75 dB(A)
NMS-7~		75 dB(A)
NMS-8^		75 dB(A)
CN1+		70 dB(A) ^{Note 1} / 65 dB(A) ^{Note 1}
CN2+		70 dB(A) ^{Note 1} / 65 dB(A) ^{Note 1}
CN3+		75 dB(A)

Note 1: Noise Limit Levels for school is 70dB(A) and should be reduced to 65dB(A) during examination period.

Note: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the Noise Control Authority have to be followed.

Remark: (*) Additional noise monitoring location was recommended by RE and agreed by IEC. It was temporary suspended and the monitoring location is relocated to NMS4a with effective on 15 Nov 2017.

(@) NMS-2 was effective on 15 November 2019.

(:) NMS-3 was effective on 3 December 2019

(#) Review of noise monitoring locations was proposed by ET and NMS-5 was effective on 15 Nov 2017.

(~) Review of noise monitoring locations was proposed by ET and NMS-6 and NMS-7 were effective on 28 Feb 2018.

(^) Review of noise monitoring locations was proposed by ET and NMS-8 was effective on 18 April 2018. Noise monitoring at NMS-8 was started on 3 May 2018 upon commencement of construction at relevant section.

(+) Additional noise monitoring locations as instructed by AECOM which effective in Dec 18.

3.7.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in [Appendix F](#).

3.8 DATA MANAGEMENT AND DATA QA/QC CONTROL

3.8.1 All monitoring data will be handled by the ET's in-house data recording and management system. The monitoring data recorded in the equipment will be downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data will input into a computerized database properly maintained by the ET. The laboratory results will be input directly into the computerized database and checked by personnel other than those who input

the data.

- 3.8.2 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.

4. AIR QUALITY MONITORING

4.1 GENERAL

4.2.1 In the Reporting Period, air quality monitoring was performed at the active designated monitoring locations AMS-1a, AMS-2, AMS-3, AMS-5, AMS-6 and AMS-7. Since installation of HVS for 24-hour TSP at AMS-2 and AMS-3 were pending approval from relevant departments, only 1-hour TSP monitoring was conducted at AMS-2 and AMS-3. No monitoring was conducted at AMS-4 since they are planned ASR which are still under construction/ not yet constructed.

4.2.2 The air quality monitoring schedule is presented in *Appendix G* and the monitoring results are summarized in the following sub-sections.

4.3 RESULTS OF AIR QUALITY MONITORING

4.3.1 In the Reporting Period, a total of **108** events of 1-hour TSP monitoring and **20** events of 24-hours TSP were carried out and the monitoring results are summarized in *Tables 4-1 to 4-5*. The detailed 24-hour TSP monitoring data are presented in *Appendix H* and the relevant graphical plots are shown in *Appendix I*.

Table 4-1 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-1a)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Sep-22	38	1-Sep-22	13:42	70	62	66
10-Sep-22	49	7-Sep-22	13:30	63	65	68
16-Sep-22	41	13-Sep-22	13:11	86	90	88
22-Sep-22	49	19-Sep-22	13:15	71	63	67
28-Sep-22	22	24-Sep-22	13:16	64	68	65
		29-Sep-22	15:03	67	61	64
Average (Range)	40 (22 – 49)	Average (Range)		69 (61 – 90)		

Table 4-2 Summary of 1-hour TSP Monitoring Results (AMS-2)

1-hour TSP ($\mu\text{g}/\text{m}^3$)				
Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-22	9:39	65	62	67
7-Sep-22	15:35	67	66	68
13-Sep-22	15:11	89	96	93
19-Sep-22	14:01	69	60	66
24-Sep-22	13:55	66	68	65
29-Sep-22	13:24	71	65	68
Average (Range)		71 (60 – 96)		

Table 4-3 Summary of 1-hour TSP Monitoring Results (AMS-3)

1-hour TSP ($\mu\text{g}/\text{m}^3$)				
Date	Start Time	1 st reading	2 nd reading	3 rd reading
1-Sep-22	9:05	69	64	67
7-Sep-22	14:40	65	66	68
13-Sep-22	14:21	86	88	90
19-Sep-22	13:49	73	61	66
24-Sep-22	14:16	65	68	66
29-Sep-22	9:41	70	62	67
Average (Range)		70 (61 – 90)		

Table 4-4 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-5)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Sep-22	42	1-Sep-22	9:18	102	110	106
10-Sep-22	71	7-Sep-22	9:30	80	78	77
16-Sep-22	81	13-Sep-22	9:25	89	93	98
22-Sep-22	74	19-Sep-22	9:46	98	83	85
28-Sep-22	24	24-Sep-22	9:20	80	78	81
		29-Sep-22	9:56	83	74	77
Average (Range)	58 (24 – 81)	Average (Range)		87 (74 – 110)		

Table 4-5 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-6)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Sep-22	27	1-Sep-22	9:06	98	101	105
10-Sep-22	40	7-Sep-22	10:03	79	81	80
16-Sep-22	24	13-Sep-22	10:08	96	101	98
22-Sep-22	68	19-Sep-22	9:58	92	78	84
28-Sep-22	12	24-Sep-22	9:31	81	79	83
		29-Sep-22	10:08	79	69	77
Average (Range)	34 (12 – 68)	Average (Range)		87 (69 – 105)		

Table 4-6 Summary of 24-hour and 1-hour TSP Monitoring Results (AMS-7)

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st reading	2 nd reading	3 rd reading
6-Sep-22	21	1-Sep-22	13:11	70	66	74
10-Sep-22	43	7-Sep-22	9:00	76	78	75
16-Sep-22	87	13-Sep-22	9:00	89	93	90
22-Sep-22	74	19-Sep-22	9:14	81	70	76
28-Sep-22	45	24-Sep-22	9:08	76	78	76
		29-Sep-22	14:33	80	71	73
Average (Range)	54 (21 – 87)	Average (Range)		77 (66 – 93)		

- 4.3.2 As shown in *Tables 4-1 to 4-6*, all the 1-hour TSP and 24-hour TSP monitoring results in the Reporting Period were below the Action and Limit Levels. No Notification of Exceedance (NOE) was issued in this Reporting Period.
- 4.3.3 The meteorological data during the impact monitoring days are summarized in *Appendix J*.

5. CONSTRUCTION NOISE MONITORING

5.1 GENERAL

- 5.2.1 In the Reporting Period, noise monitoring was performed at designated monitoring locations NMS2 and NMS3 and the additional monitoring locations NMS4a, NMS5, NMS6, NMS7 and NMS8. No monitoring was conducted at the designated monitoring locations NMS1 since they are the planned NSR and still under the construction.
- 5.2.2 In addition, a Work Instruction was issued from AECOM to AUES in November 2018 for installing three additional noise monitoring stations, i.e., CN1, CN2 and CN3 for Contract 3. Impact noise monitoring was performed at the three additional noise monitoring locations since December 2018. Additional noise monitoring location was terminated by RE as the construction work at E8 was completed in September 2022. The last monitoring for CN1&CN2 was on 15 September 2022.
- 5.2.3 The noise monitoring schedule is presented in *Appendix G* and the monitoring results are summarized in the following sub-sections.

5.3 NOISE MONITORING RESULTS IN REPORTING MONTH

- 5.3.1 In the Reporting Period, a total of **35** events noise measurements were carried out at the designated locations under Contract 1. The noise monitoring results at the designated locations are summarized in *Tables 5-1*. The detailed noise monitoring data are presented in *Appendix H* and the relevant graphical plots are shown in *Appendix I*.

Table 5-1 Summary of Construction Noise Monitoring Results for Contract 1

Construction Noise Level ($L_{eq30min}$), dB(A)						
Date	NMS2	NMS3	NMS4a	NMS5	NMS6	NMS7
1-Sep-22	64	62	71	69	65	67
7-Sep-22	66	61	70	71	65	68
13-Sep-22	64	63	70	71	67	68
19-Sep-22	65	61	65	64	64	65
29-Sep-22	65	61	66	68	66	66
Limit Level	70 dB(A) / 65 dB(A)^{Note 1}		75 dB(A)			

Note 1: Noise Limit Levels for school is 70dB(A) and should be reduced to 65dB(A) during examination period;

Table 5-1a Summary of Construction Noise Monitoring Results for Contract 1

Construction Noise Level ($L_{eq30min}$), dB(A)	
Date	NMS8
1-Sep-22	60
9-Sep-22	59
15-Sep-22	61
24-Sep-22	64
29-Sep-22	60
Limit Level	75 dB(A)

- 5.3.2 For the additional noise monitoring under Contract 3, a total of **12** events noise measurements were performed for the Contract. The noise monitoring results are summarized in *Tables 5-2*. The detailed noise monitoring data are presented in *Appendix H* and the relevant graphical plots are shown in *Appendix I*.

Table 5-2 Summary of Construction Noise Monitoring Results for Contract 3

Construction Noise Level ($L_{eq30min}$), dB(A)			
Date	CN1	CN2	CN3
1-Sep-22	62	64	64

Construction Noise Level ($L_{eq30min}$), dB(A)			
Date	CN1	CN2	CN3
9-Sep-22	61	63	65
15-Sep-22	62	63	65
24-Sep-22	NA	NA	64
29-Sep-22	NA	NA	65
Limit Level	70 dB(A) / 65 dB(A)^{Note 1}	70 dB(A)^{Note 1} / 65 dB(A)^{Note 1}	75 dB(A)

Note 1: Noise Limit Levels for school is 70dB(A) and should be reduced to 65dB(A) during examination period.

- 5.3.3 As shown in **Tables 5-1 and 5-2**, no Limit Level exceedance was recorded in this Reporting Period. No noise complaint (which triggered Action level exceedance) was received under the Project.

6. WASTE MANAGEMENT**6.1 GENERAL WASTE MANAGEMENT**

6.2.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

6.3 RECORDS OF WASTE QUANTITIES

6.3.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

6.3.2 The quantities of waste for disposal in this Reporting Period are summarized in **Tables 6-1** and **6-2** and the Monthly Summary Waste Flow Table is shown in **Appendix K**. Whenever possible, materials were reused on-site as far as practicable.

Table 6-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Contract 1		Contract 2		Contract 3		Contract 4		Contract 5	
	Quantity	Disposal Location	Quantity	Disposal Location	Quantity	Disposal Location	Quantity	Disposal Location	Quantity	Disposal Location
Total generated Inert C&D Materials ('000m ³) (#)	15.716	-	0.06	-	2.045	-	389.520	-	0.665	-
Hard Rock and Large Broken Concrete ('000m ³)	0	-	0	-	0	-	0	-	0.665	-
Reused in this Contract (Inert) ('000m ³)	0	-	0	-	0.570	-	0	-	0	-
Reused in other Projects (Inert) ('000m ³)	14.996	*	0	-	0.221	-	0	*	0	-
Disposal as Public Fill (Inert) ('000m ³)	0.720	TKO 137	0.06	TKO 137	1.254	TKO 137	389.520	-	0.665	-

Remark (#): The total generated inert C&D materials will not take account for the hard rock and large broken concrete.

(*) Approved alternative disposal ground.

Table 6-2 Summary of Quantities of C&D Wastes

Type of Waste	Contract 1		Contract 2		Contract 3		Contract 4		Contract 5	
	Quantity	Disposal Location	Quantity	Disposal Location	Quantity	Disposal Location	Quantity	Disposal Location	Quantity	Disposal Location
Recycled Metal ('000kg)	0.003	Licensed collector	0	-	0	-	0	-	0	-
Recycled Paper / Cardboard Packing ('000kg)	0	-	0	-	0	-	0	-	0	-
Recycled Plastic ('000kg)	0.009	Licensed collector	0	-	0	-	0	-	0	-
Chemical Wastes ('000kg)	0	-	0	-	0	-	0	-	0	-
General Refuses ('000m ³)	0.192	SENT	0.06	SENT	0.041	SENT	0	-	0	-

7. SITE INSPECTION**7.1 REQUIREMENTS**

- 7.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should be carried out to confirm the environmental performance.

7.2 FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH**Contract 1**

- 7.2.1 In the Reporting Period, joint site inspections for Contract 1 to evaluate site environmental performance were carried out by the RE, ET and the Contractor on **8, 14, 20 and 27 September 2022** in which IEC joined the site inspection with SSEMC on **8 September 2022**. No non-compliance was noted. The findings / deficiencies of **Contract 1** that observed during the weekly site inspection are listed in **Table 7-1**.

Table 7-1 Site Observations of Contract 1

Date	Findings / Deficiencies	Follow-Up Status
8 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to provide dust mitigation measures at G2. 	<ul style="list-style-type: none"> Reminder only
14 September 2022	<ul style="list-style-type: none"> No adverse environmental issue was observed during site inspection. 	<ul style="list-style-type: none"> NA
20 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to treat muddy water prior to discharge. The Contractor was reminded to implement dust mitigation measures regularly in upcoming wind seasons 	<ul style="list-style-type: none"> Reminder only Reminder only
27 September 2022	<ul style="list-style-type: none"> Free standing chemical containers were observed in G2. The Contractor was advised to provide drip trays to prevent leakage. 	<ul style="list-style-type: none"> Chemical containers have been placed on drip tray.

Contract 2

- 7.2.2 In the Reporting Period, joint site inspections for Contract 2 to evaluate site environmental performance were carried out by the RE, ET and the Contractor on **7, 14, 20 and 28 September 2022** in which IEC joined the site inspection with SSEMC on **20 September 2022**. No non-compliance was noted. The findings / deficiencies of **Contract 2** that observed during the weekly site inspection are listed in **Table 7-2**.

Table 7-2 Site Observations of Contract 2

Date	Findings / Deficiencies	Follow-Up Status
7 September 2022	<ul style="list-style-type: none"> The Contractor was advised to implement tree protection zone properly at Portion 2. The Contractor was reminded to clean accumulated water at Portion 3. 	<ul style="list-style-type: none"> Tree protection zone is properly implemented. Reminder only
14 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to remove or dispose general refuse regularly at Portion 2 and E1. 	<ul style="list-style-type: none"> Reminder only
20 September 2022	<ul style="list-style-type: none"> Chemical leakage is observed under generator at E3. The Contractor was advised to clean leaked chemical. The Contractor was reminded to remove or dispose general refuse regularly at Portion 2. 	<ul style="list-style-type: none"> Oil was cleaned under generator at E3. Reminder only.

Date	Findings / Deficiencies	Follow-Up Status
28 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to clean u-channel regularly at Portion 2. 	<ul style="list-style-type: none"> Reminder only.

Contract 3

- 7.2.3 In the Reporting Period, joint site inspections for Contract 3 to evaluate site environmental performance were carried out by the RE, ET and the Contractor on **2, 9, 16, 23 and 30 September 2022** in which IEC joined the site inspection with SSEMC on **16 September 2022**. No non-compliance was noted. The findings / deficiencies of **Contract 3** that observed during the weekly site inspection are listed in **Table 7-3**

Table 7-3 Site Observations of Contract 3

Date	Findings / Deficiencies	Follow-Up Status
2 September 2022	<ul style="list-style-type: none"> No adverse environmental issue was observed. 	<ul style="list-style-type: none"> NA
9 September 2022	<ul style="list-style-type: none"> No adverse environmental issue was observed. 	<ul style="list-style-type: none"> NA
16 September 2022	<ul style="list-style-type: none"> No adverse environmental issue was observed. 	<ul style="list-style-type: none"> NA
23 September 2022	<ul style="list-style-type: none"> Open cement bag should be covered with impervious sheet to avoid dust generation. (System A) 	<ul style="list-style-type: none"> Cement bag is properly covered.
30 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to clean stagnant water regularly. 	<ul style="list-style-type: none"> Reminder only

Contract 4

- 7.2.4 In the Reporting Period, joint site inspections for Contract 4 to evaluate site environmental performance were carried out by the RE, ET and the Contractor on **7, 14, 22 and 28 September 2022** in which IEC joined the site inspection with SSEMC on **22 September 2022**. No non-compliance was noted. The findings / deficiencies of **Contract 4** that observed during the weekly site inspection are listed in **Table 7-4**

Table 7-4 Site Observations of Contract 4

Date	Findings / Deficiencies	Follow-Up Status
7 September 2022	<ul style="list-style-type: none"> Free standing chemical container was observed. The Contractor was advised to remove or provide drip tray. 	<ul style="list-style-type: none"> Chemical container is removed.
14 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to spray water regularly at Portion 12 for dust mitigation measures. 	<ul style="list-style-type: none"> Reminder only
22 September 2022	<ul style="list-style-type: none"> Free-standing chemical containers were observed at Portion 12. The Contractor was advised to provide drip tray or remove them. Generator without NRMM label was observed at Portion 12. The Contractor was advised to provide NRMM label. 	<ul style="list-style-type: none"> Chemical containers have been removed. The use of generator is suspended.
28 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to spray water at Portion 12 for dust mitigation. 	<ul style="list-style-type: none"> Reminder only

Contract 5

- 7.2.5 In the Reporting Period, joint site inspections for Contract 5 to evaluate site environmental performance were carried out by the RE, ET and the Contractor on **1, 8, 15, 22 and 27 September 2022** in which IEC joined the site inspection on **27 September 2022**. No non-compliance was noted. The findings / deficiencies of **Contract 5** that observed during the

weekly site inspection are listed in *Table 7-5*

Table 7-5 Site Observations of Contract 5

Date	Findings / Deficiencies	Follow-Up Status
1 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to keep u-channels clean in wet seasons. 	<ul style="list-style-type: none"> Reminder only
8 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to maintain good housekeeping on site. (Portion E10, E7) The Contractor was reminded to remove stagnant water on site regularly. 	<ul style="list-style-type: none"> Reminder only Reminder only
15 September 2022	<ul style="list-style-type: none"> No adverse environmental issue was observed during site inspection. 	<ul style="list-style-type: none"> NA
22 September 2022	<ul style="list-style-type: none"> The Contractor was reminded to provide water spraying on site regularly to reduce dust generation. The Contractor was reminded to remove stagnant water on site after rainy days. (E7) 	<ul style="list-style-type: none"> Reminder only Reminder only
27 September 2022	<ul style="list-style-type: none"> - The Contractor was reminded to spray water regularly at E6 for dust mitigation. 	<ul style="list-style-type: none"> Reminder only

8. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

8.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

- 8.1.1 In the Reporting Period, one (1) environmental complaint was received regarding to Water Quality for Contract 1 and Contract 4. Besides, no summons and prosecution under the EM&A Programme was lodged for the project. Investigation for the complaint was undertaken and presented in following sections.

Complaint received by ET on 29 September 2022 & 3 October 2022

- 8.1.2 EPD received complaint from DSD concerning muddy water observed at Tin Hau Temple and Po Lam Road in the morning of 29 and 30 September 2022.
- 8.1.3 The case was then referred from EPD to CEDD to follow up. Handling procedure by Environmental Team (ET) in accordance with the Environmental Monitoring & Audit Manual was triggered to investigate if it is related to the Development of Anderson Road Quarry Site Project.
- 8.1.4 With reference to the weather information from the Hong Kong Observatory, there was heavy rainstorm in Hong Kong on 29 and 30 September 2022, in which Amber Rainstorm Warning Signal was issued on 10:25am on 30 September 2022. Due to the heavy rainstorm, large amount of storm runoff from roads and landscape would be flushed into the public drainage, which deteriorated the water quality in the drainage system.
- 8.1.5 Upon receipt of the complaint, on-site checking was immediately conducted by the representatives of Resident Site Staff (RSS) and the Contractors on 30 September and 3 October 2022. It is noted that the majority areas of the ARQ Site have been handed over to other contractors for further development. Each of these interfacing contractors should have been granted a licence for discharge under the Water Pollution Control Ordinance. The findings during the on-site checking are presented below:
- 8.1.6 Muddy water discharge from Site R2-9 to downstream manhole D310 was observed in the mornings of 29 and 30 Sep 2022. Such discharge would enter Q3 and cause muddy outflow at the stepped channel off Po Lam Road.
- 8.1.7 As observed at Q2 cascade, the discharge at Q2 was visually clear in the in the mornings of 29 and 30 Sep 2022. The clear discharge came mainly from the Q2 AquaSeds.
- 8.1.8 Furthermore, wastewater treatment facilities were implemented by C4 for the wastewater generated at various portions under the Contract. The discharge from C4 would enter the drainage system of C1 to further discharge off ARQ Site.
- 8.1.9 Joint site inspection among the RSS, Contractor and ET was carried out on weekly basis to audit the environmental performance. The wastewater mitigation measures were found implemented properly and functioning well. In general, the haul roads within the ARQ Site were hard paved and no water quality impact was observed.
- 8.1.10 As a matter of fact, heavy rain led to large amount of storm runoff from roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. No muddy water discharge from ARQ Site was evident in the morning of 29 and 30 September 2022. It is therefore considered that the muddy water discharge observed by DSD in the morning of 29 and 30 September was unlikely to have been caused by the ARQ contracts of C1 or C4.
- 8.1.11 During wet season, the Contractor was strongly reminded to implement adequate water quality mitigation measures to minimise the impact arising from the construction site. The Contractor should closely monitor the discharge quality from the Site to avoid non-compliance. The ET will pay special attention on water quality mitigation measures implementation on site through regular site inspection, and give advice on remedial action when necessary.
- 8.1.12 Incidentally, it is noted that Site R2-9 has kept discharging muddy water to downstream manhole D310. Record photos of the manhole dated 6, 7 and 8 October 2022 are enclosed for reference.

8.1.13 The complaint log and Investigation Reports issued in the Reporting Period are shown in [Appendix M](#).

8.1.14 The statistical summary table of environmental complaint, summons and prosecution is presented in **Tables 8-1, 8-2 and 8-3**.

Table 8-1 Statistical Summary of Environmental Complaints

Reporting Period	Contract no.	Environmental Complaint Statistics		
		Frequency	Cumulative	Complaint Nature
1 Apr 2017 – 31 August 2022	1	0	61	Dust, Noise, Water and light nuisance
21 Mar 2017 – 31 August 2022	2	0	10	Noise
31 May 2018 – 31 August 2022	3	0	8	Waste Management, Noise, Water Quality
27 Sep 2021 – 31 August 2022	4	0	2	Water Quality
30 Mar 2021 – 31 August 2022	5	0	0	NA
1 – 30 September 2022	1	1	62	Water Quality
	2	0	10	NA
	3	0	8	NA
	4	1	3	Water Quality
	5	0	0	NA

Table 8-2 Statistical Summary of Environmental Summons

Reporting Period	Contract no.	Environmental Summons Statistics		
		Frequency	Cumulative	Summons Nature
1 Apr 2017 – 31 August 2022	1	0	0	NA
21 Mar 2017 – 31 August 2022	2	0	0	NA
31 May 2018 – 31 August 2022	3	0	0	NA
27 Sep 2021 – 31 August 2022	4	0	0	NA
30 Mar 2021 – 31 August 2022	5	0	0	NA
1 – 30 September 2022	1	0	0	NA
	2	0	0	NA
	3	0	0	NA
	4	0	0	NA
	5	0	0	NA

Table 8-3 Statistical Summary of Environmental Prosecution

Reporting Period	Contract no.	Environmental Prosecution Statistics		
		Frequency	Cumulative	Prosecution Nature
1 Apr 2017 – 31 August 2022	1	0	0	NA
21 Mar 2017 – 31 August 2022	2	0	0	NA
31 May 2018 – 31 August 2022	3	0	0	NA

Reporting Period	Contract no.	Environmental Prosecution Statistics		
		Frequency	Cumulative	Prosecution Nature
27 Sep 2021 – 31 August 2022	4	0	0	NA
30 Mar 2021 – 31 August 2022	5	0	0	NA
1 – 30 September 2022	1	0	0	NA
	2	0	0	NA
	3	0	0	NA
	4	0	0	NA
	5	0	0	NA

9. IMPLEMENTATION STATUS OF MITIGATION MEASURES

9.1 GENERAL REQUIREMENTS

- 9.1.1 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the approved EM&A Manual covered the issues of dust, noise, water and waste and they are summarized presented in [Appendix L](#).
- 9.1.2 All contracts under the Project shall be implementing the required environmental mitigation measures according to the approved EM&A Manual as subject to the site condition. Environmental mitigation measures generally implemented in this Reporting Period are summarized in **Table 9-1**.

Table 9-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> Wastewater to be treated by filtration system; such as, silt curtain or sedimentation tank before discharge. Replace silt curtain materials if necessary
Air Quality	<ul style="list-style-type: none"> Maintain damp / wet surface on access road Keep slow speed in the sites All vehicles must use wheel washing facility before off site All vehicles must use wheel washing facility before off site Sprayed water during breaking works
Noise	<ul style="list-style-type: none"> Restrain operation time of plants from 07:00 to 19:00 on any working day except for Public Holiday and Sunday. Keep good maintenance of plants Place noisy plants away from residence or school Provide noise barriers or hoarding to enclose the noisy plants or works Shut down the plants when not in used.
Waste and Chemical Management	<ul style="list-style-type: none"> On-site sorting prior to disposal Follow requirements and procedures of the “Trip-ticket System” Predict required quantity of concrete accurately Collect the unused fresh concrete at designated locations in the sites for subsequent disposal
General	<ul style="list-style-type: none"> The site was generally kept tidy and clean.

9.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 9.2.1 Construction activities for Contract 1 in the coming month are listed below:

Fresh Water Pumping Station:

- Pumping Station E&M Works.
- Draw pits and cabling works

Salt Water Reservoir:

- Salt water Reservoir E&M works
- Draw pits and cabling works

Fresh Water Reservoir:

- To continue the construction works of WSD Access.
- To continue the road works.
- To commence the green roof (Landscape) works.
- To commence the excavation works for retaining wall of Hiking Trail.

RWS Access Road & External Works:

- CLP Power supply duct
- Road Works & Fencing

PTT:

- Lighting system and PMMA panel installation to continue, concrete pavement construction, kerb laying and noise barrier works would continue.

Underpass Tunnel:

- Tunnel backfill to east portal, VE Panels, Road Works and E&M

Road L4 (RWA18, Noise Barrier, RWA12, utilities & Road Works):

- Demolish existing retaining wall R10,
- Road Works – Drainage
- Watermain & Utilities
- Road Formation

Road Improvement Works at Po Lam Road

- Construction of permanent footpath and surface drainage system complete
- Excavation works to facilitate installation of the E&M/ACT/Earth pit and construction of permanent footpath and surface drainage system complete
- Construct concrete carriageway and footpath complete
- Install beam barrier complete
- Construct Island complete
- Implementation of stage 4 TTA

Hiking Trail connecting to Wison Trail (Portion B5):

- Construction works at Hiking Trail

9.2.2 Construction activities for Contract 2 in the coming month are listed below:

- Temporary Traffic Arrangement (TTA)
- Mass Concrete construction
- Formwork and Falsework installation and dismantling
- Lifting Tower Construction and lift installation
- Rebar fixing

9.2.3 Construction activities for Contract 3 in the coming month are listed below:

Pedestrian Connectivity Facility E8 (PC-E8)

- Touch-up outstanding works are in progress.

Pedestrian Connectivity Facility E11 (PC-E11)

- ABWF works and E&M works at LT2 & ST2 are in-progress.
- Backfilling works at PC6 area is in-progress.
- ABWF works and E&M works at LT1 & ST1 are in-progress.
- ABWF work and E&M works inside the footbridge steel frame are in-progress.

Pedestrian Connectivity Facilities Systems A (PC-SYA)

- ABWF works and E&M works at LT1, LT2 & ST1 are in-progress.
- Erect steel works inside RC structure is in-progress.
- Erect footbridge steel frame is in-progress.

Pedestrian Connectivity Facilities Systems B (PC-SYB)

- RC works at SyB-LT1 & ST1 is in-progress.
- Erect footbridge steel frame is in-progress.
- Install sheet-pile and excavation works at PC1 are in-progress.

Tseung Kwan O Bus-Bus Interchange New Public Toilet (BBI-Toilet)

- The completed toilet was handed over to Food and Environmental Hygiene Department on 30 September 2020; Additional works under an instruction is in-progress.

9.2.4 Construction activities for Contract 4 in the coming month are listed below:

- Tree Survey
- Drainage Works
- Footing
- Formation Works
- Hydroseeding

9.2.5 Construction activities for Contract 5 in the coming month are listed below:

Portion 1

- Piling Works at E5-PC1 lower Platform
- Form Piling Platform at E5-PC3
- Implement TTA at EVA and mobilization of crawler crane
- Piling Works at E5-PC2 upper platform
- Remove existing soil nail at E5-PC3

Portion 2

- Piling Works
- Loading test for compression & tension piles
- Install sheet pile and excavation at E6-PC1&PC2

Portion 3

- Lower down slope to form piling platform
- Install mini-piles

Portion 4

- Construction of E10-F3 abutment
- Excavation of lift tower footing E10-FT1

9.3 KEY ISSUES FOR THE COMING MONTH

9.3.1 Key issues to be considered in the coming month include:

- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Discharge of site effluent to the nearby wetland, stockpiling or disposal of materials, and any dredging or construction area at this area are prohibited;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures

9.3.2 During wet season, the Contractors should pay special attention on water quality mitigation measures and fully implement according to the ISEMM of the EM&A Manual, in particular to prevent muddy water or other water pollutants from site surface overflow to public area should be properly maintained. The implementation of water quality mitigation measures conducted by the Contractor is shown in [Appendix N](#).

10. CONCLUSIONS AND RECOMMENDATIONS

10.1 CONCLUSIONS

- 10.1.1 This is 66th monthly EM&A report presenting the monitoring results and inspection findings for the Reporting Period from 1 to 30 September 2022.
- 10.1.2 No 24-hour or 1-hour TSP monitoring and noise monitoring results that triggered the Action or Limit Levels were recorded. No NOEs or the associated corrective actions were therefore issued.
- 10.1.3 In the Reporting Period, no exceedance was recorded and no Notification of Exceedance was issued. Moreover, no noise complaints (which triggered Action Level) were received for the Project.
- 10.1.4 In the Reporting Period, one (1) environmental complaints were received regarding to Water Quality for Contract 1 and Contract 4.
- 10.1.5 No notification of summons or successful prosecution was received under the Project.
- 10.1.6 During the Reporting Period, weekly joint site inspection by the RE, ET with the relevant Main-contractor was carried out for Contracts 1, 2, 3, 4 and 5 in accordance with the EM&A Manual stipulation whereas IEC performed monthly site inspection for both contracts. No non-compliance observed during the site inspection.


10.2 RECOMMENDATIONS

- 10.2.1 During wet season, the Contractors are reminded to pay special attention on water quality mitigation measures and should fully implement the measures as recommended in the EM&A Manual, in particular to prevent muddy water or other water pollutants from site surface overflow to public area should be properly maintained.
- 10.2.2 Since construction site is highly visible to the resident at nearby estates, the Contractors should pay special attention on potential environmental impact generated by the site activities and adhere implement adequate air quality and noise mitigation measures as far as practicable to reduce the impact to the public.
- 10.2.3 Construction noise is one of the key environmental issues during construction work of the Project. Noise mitigation measures such as using quiet plants and noise barriers shall be implemented where practicable according to the EM&A manual.
- 10.2.4 In addition, the Contractors should ensure all effluent discharge shall be fulfilled the Technical Memorandum of Effluent Discharged into Drainage and Sewerage Systems, inland and Coastal Waters criteria or relevant discharge license requirement.
- 10.2.5 Mosquito control measures should be continued to prevent mosquito breeding on site.


Appendix A

Layout plan of the Project

Contract Packages

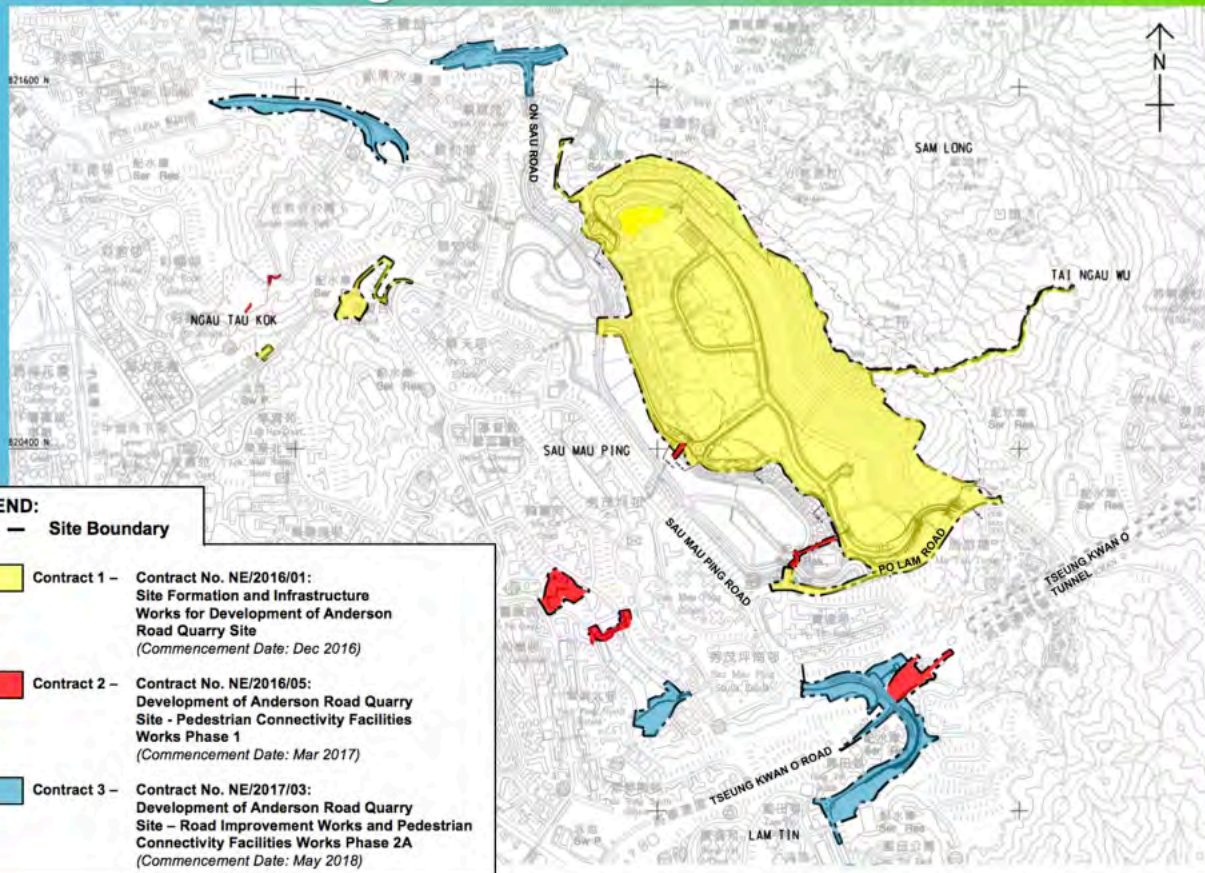

Layout plan of Contract 1 (N/2016/01)

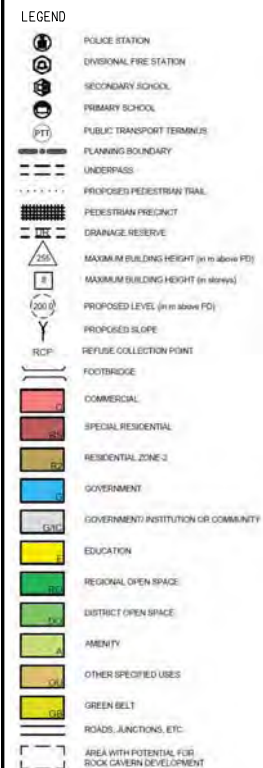

Consultant

ARUP


Drawing title

Recommended Outline
Development Plan

COPYRIGHT RESERVED

 土木工程拓展署
Civil Engineering and
Development Department


Layout plan of Contract 2 (NE/2016/05)

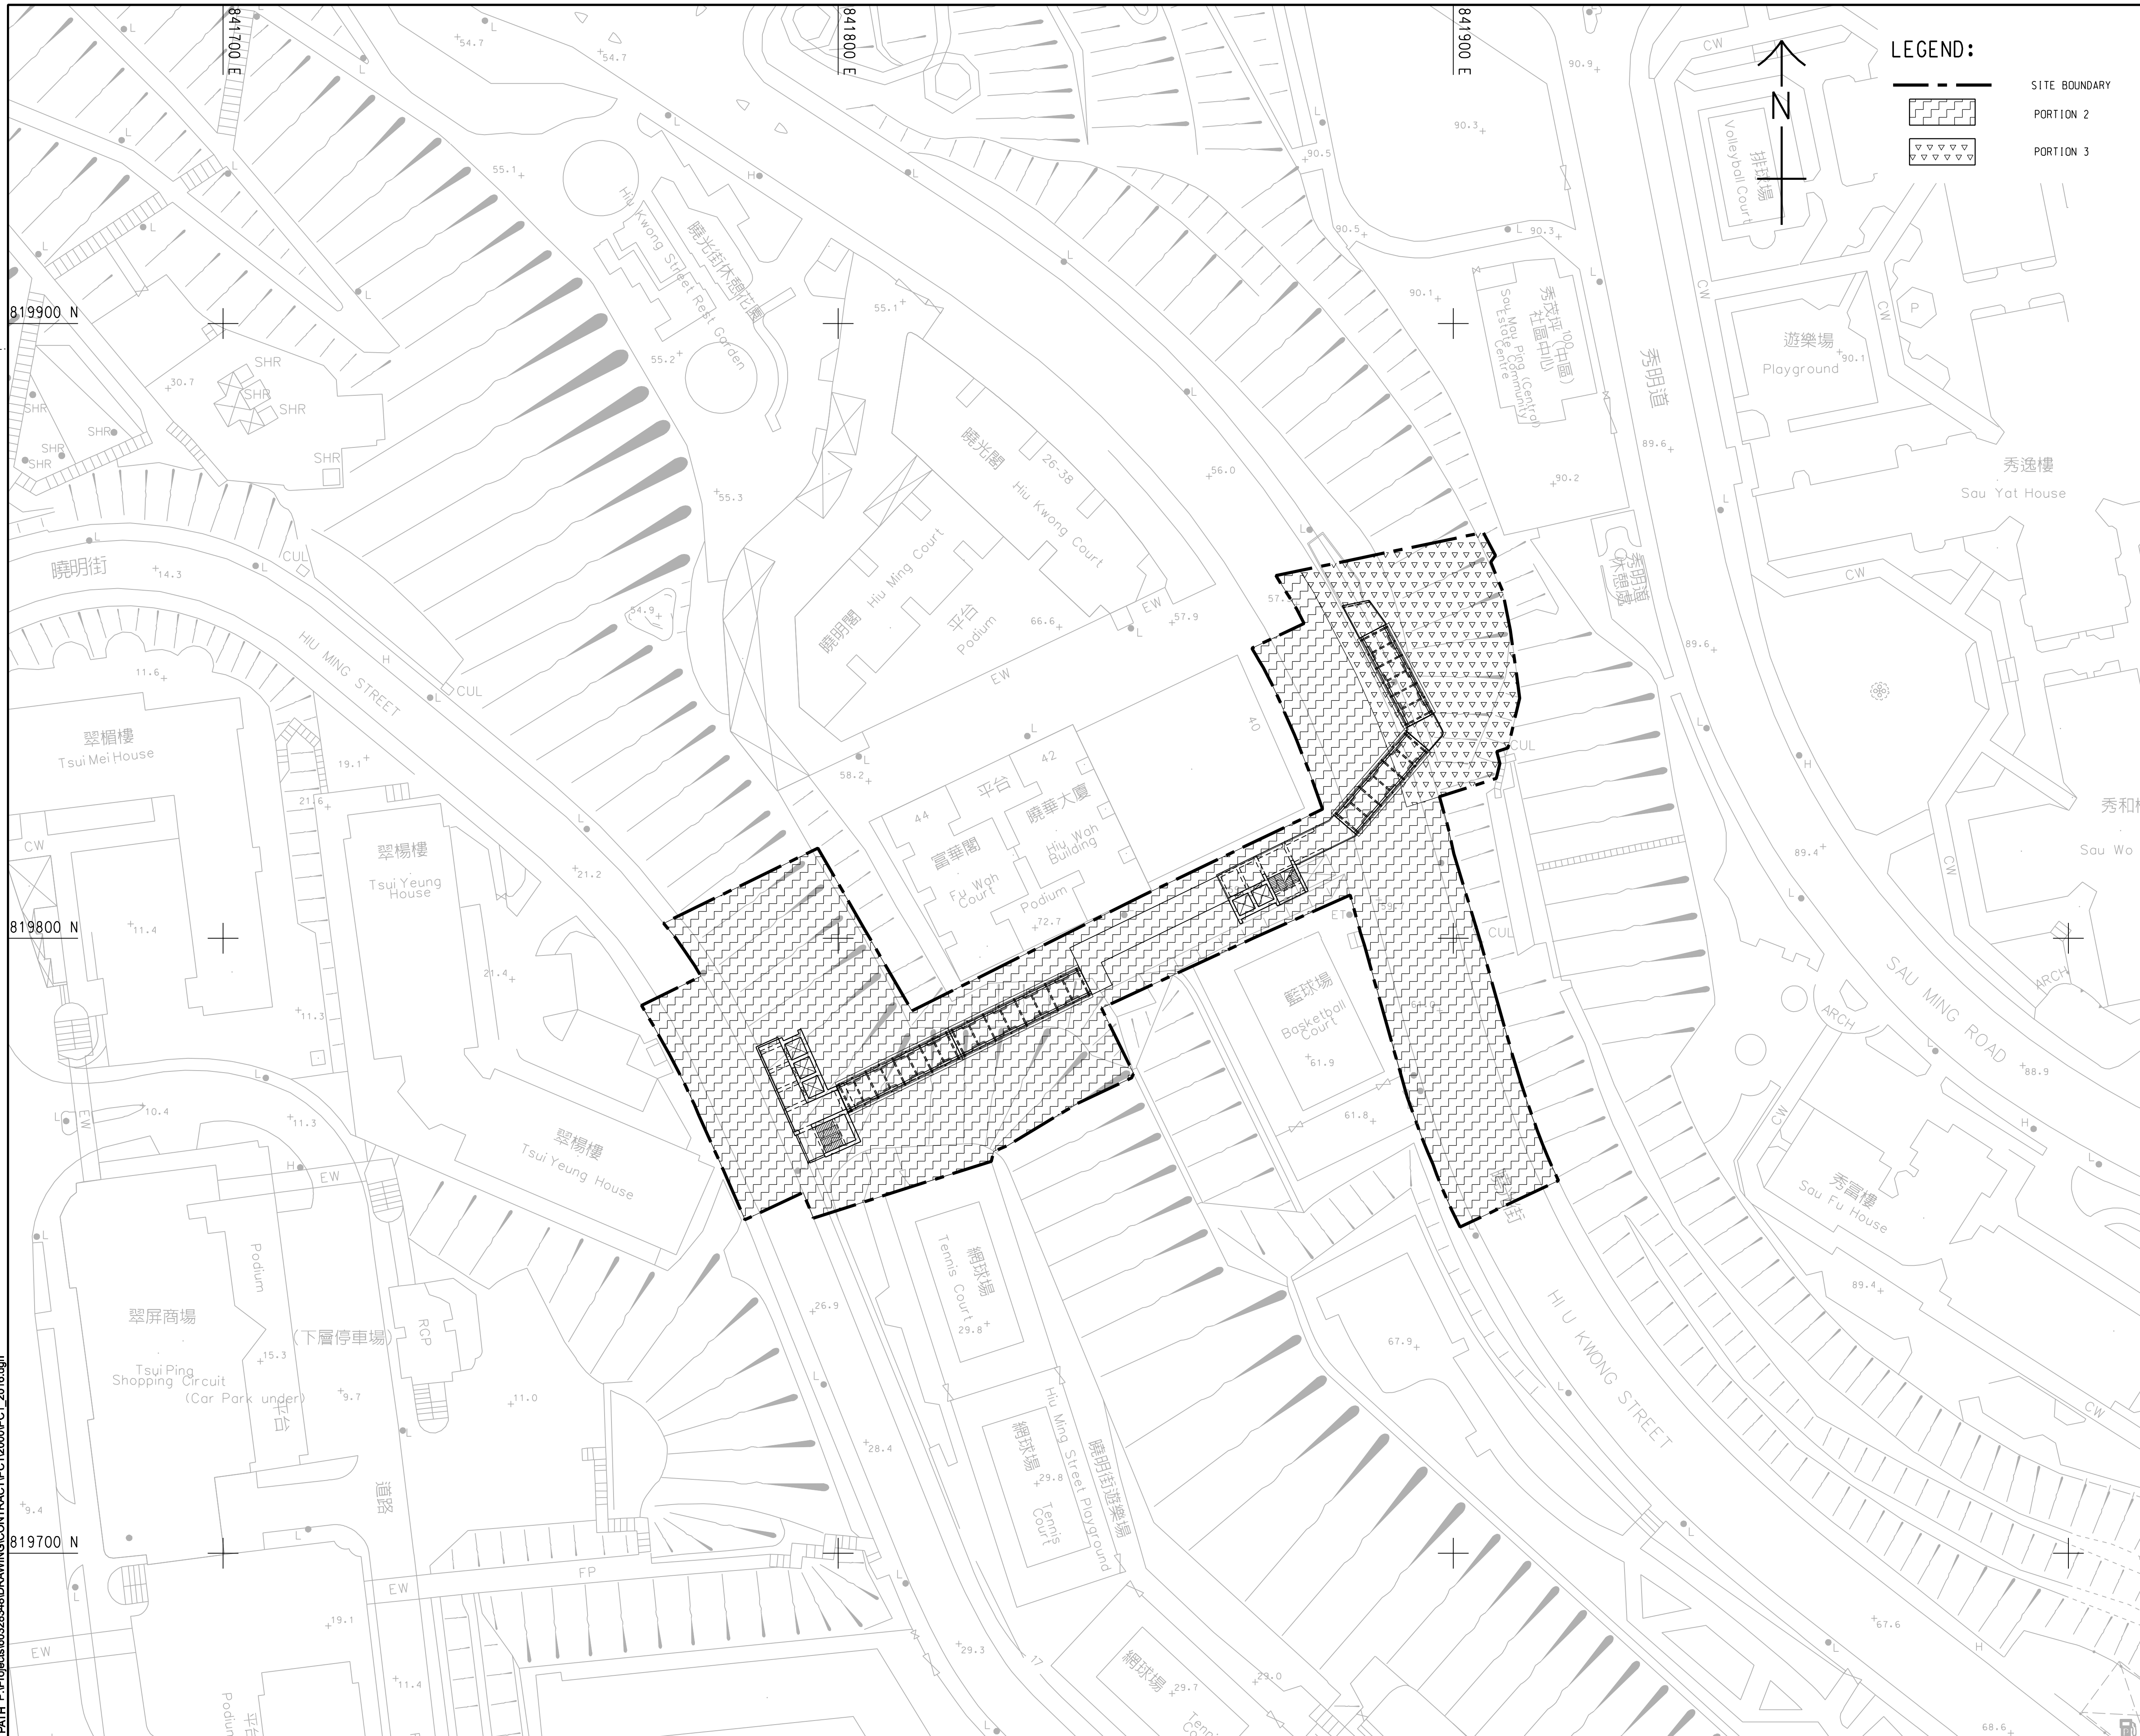[illegible]

60328348/PC1/2016

Pld File by: WANGGLW_2016/10/25
PATH: P:\Projects\60328348\Drawing\contract\pc1\3000\PC1_3016.dgn

Project Management Initials:
Designer:
PCTK Checked:
Approved:
BWCW ISO A1 594mm x 841mm

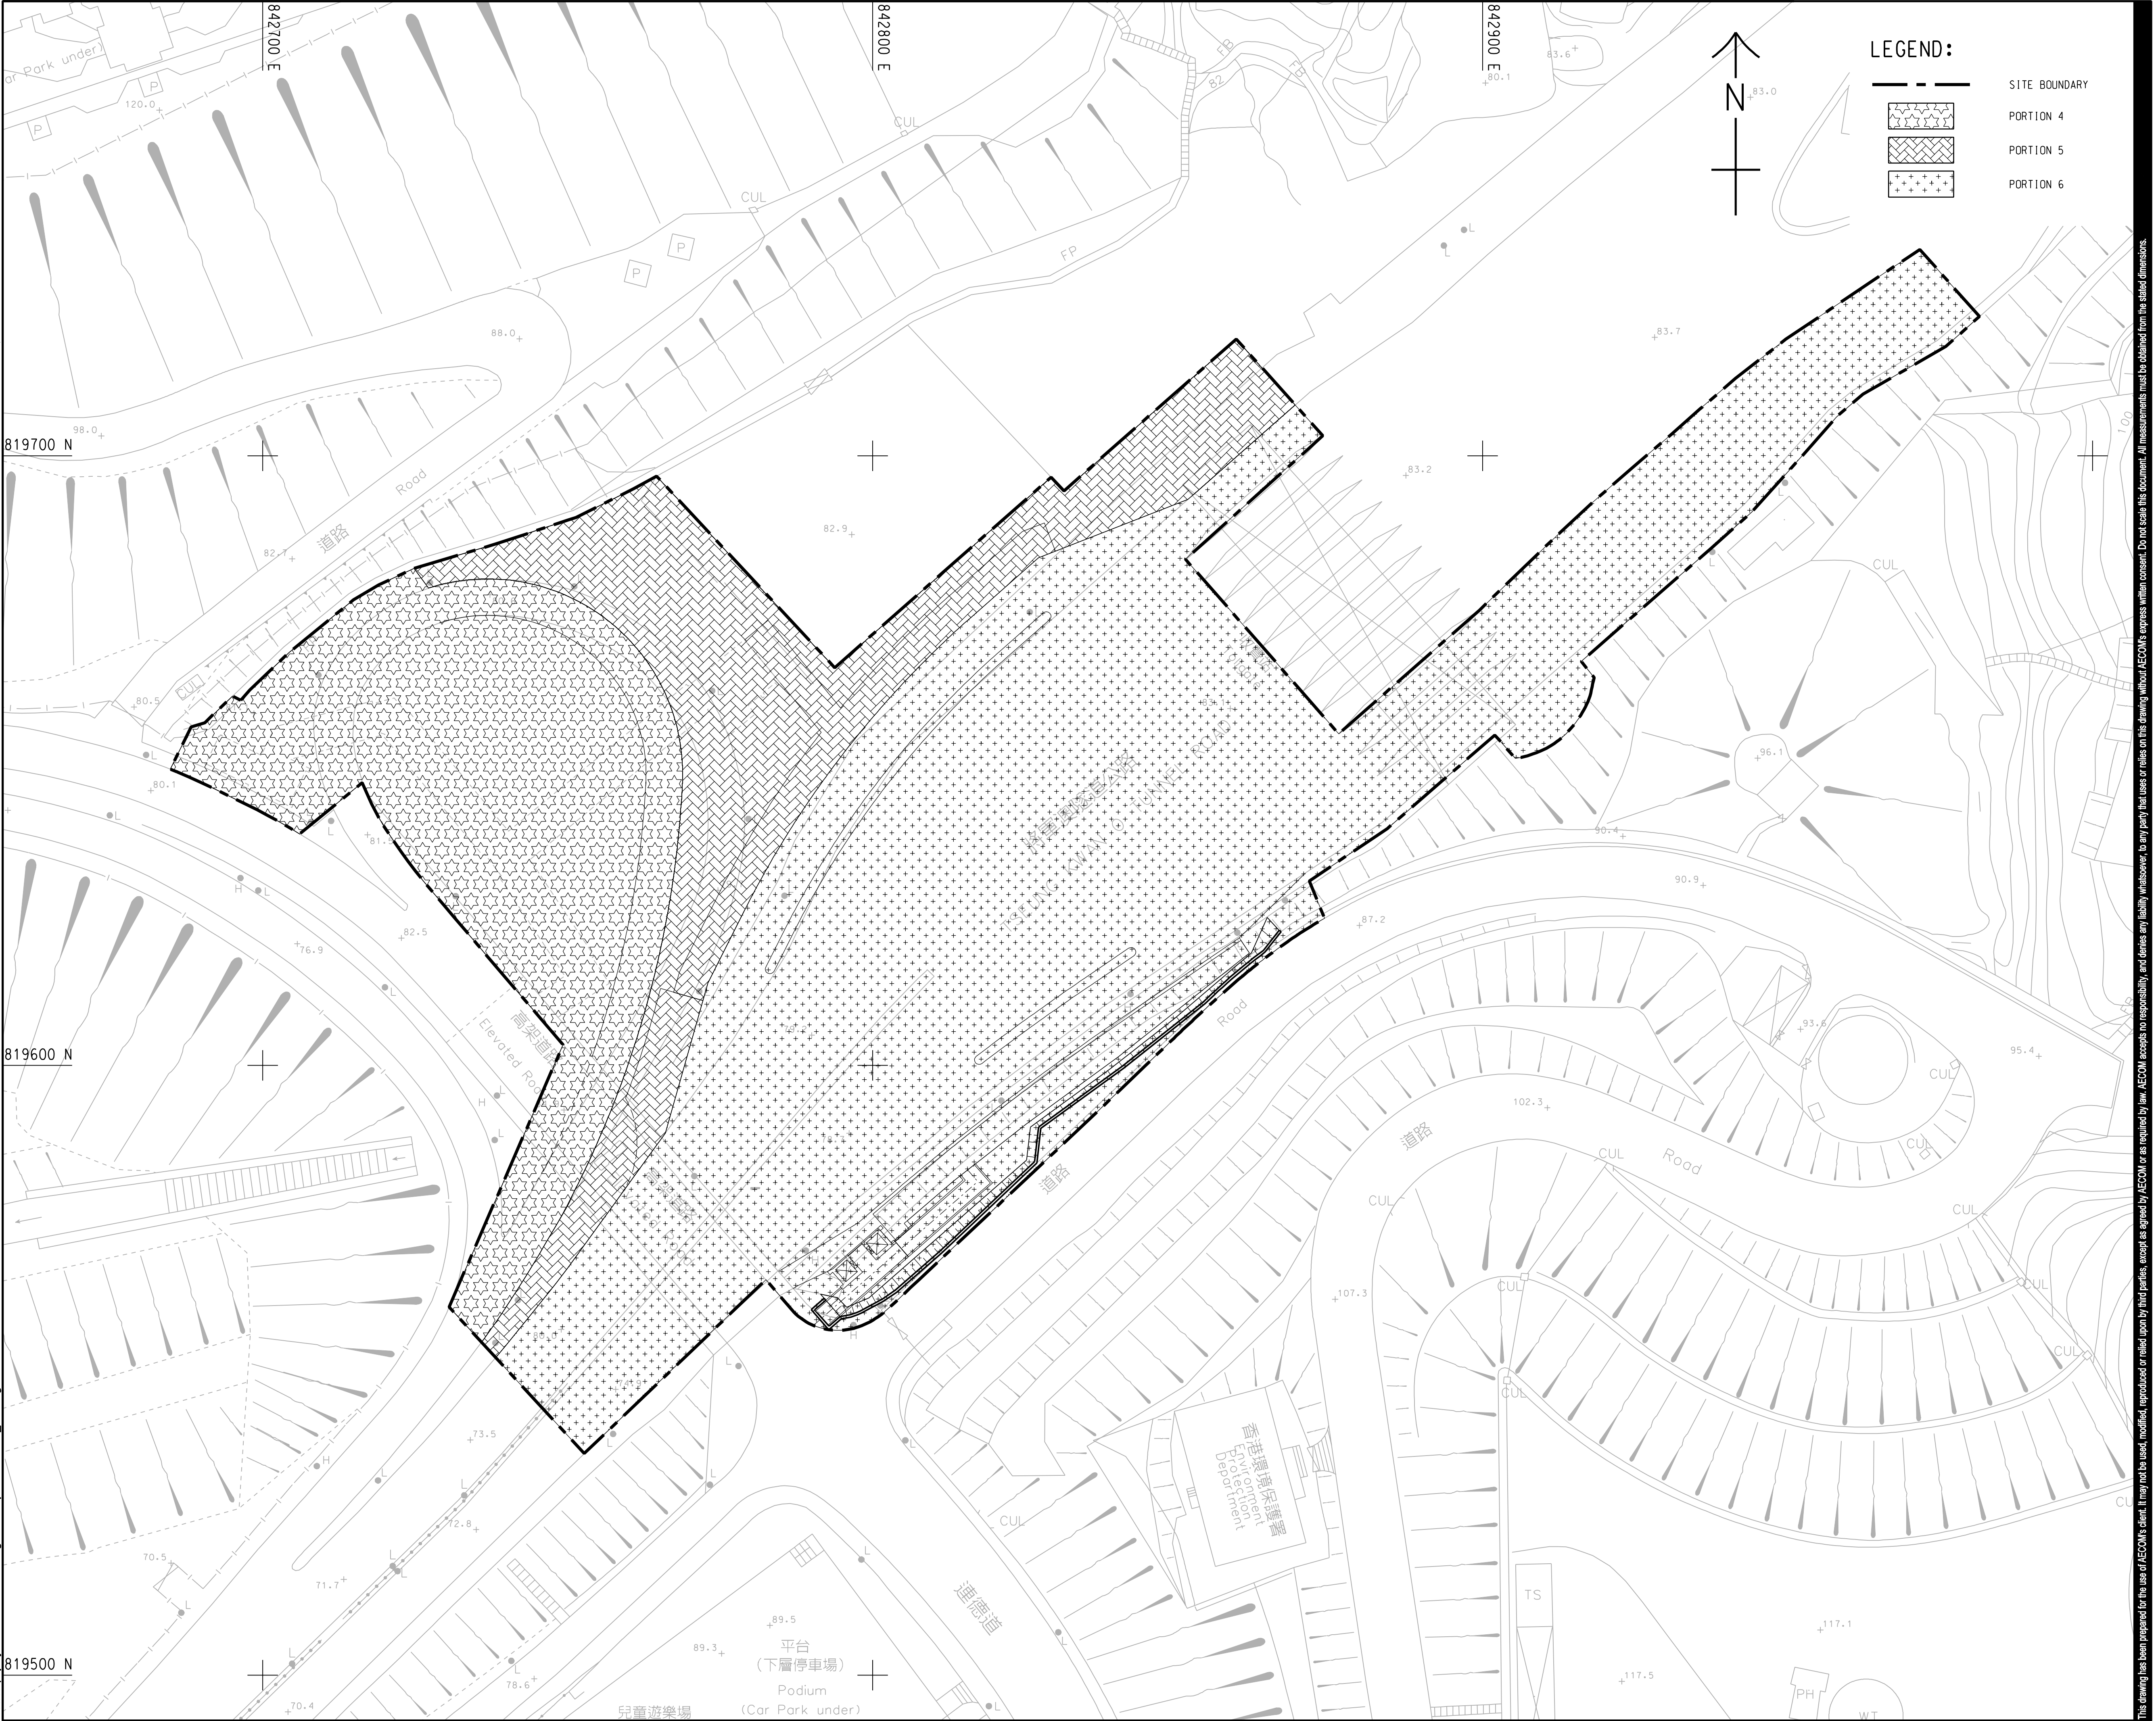


AECOM

PROJECT
項目

**DEVELOPMENT OF
ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION**

CONTRACT TITLE
PEDESTRIAN CONNECTIVITY
FACILITIES WORKS PHASE 1

CLIENT
業主

 **土木工程拓展署**
Civil Engineering and
Development Department

CONSULTANT
工程顧問公司

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION
修訂

I/R 修訂	DATE 日期	DESCRIPTION 內容摘要	CHK. 覆核
-	OCT. 16	TENDER DRAWING	AC

STATUS
階段

SCALE
比例


A1 1 : 500

DIMENSION UNIT
尺寸單位

METRES

KEY PLAN
索引圖

A1 1 : 60000

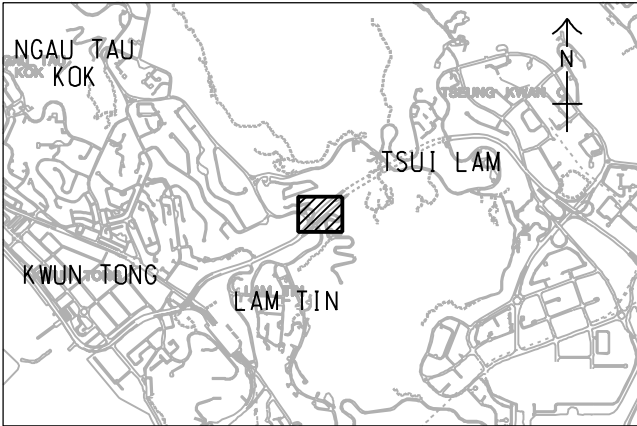

PROJECT NO.
項目編號

60328348

CONTRACT NO.
合約編號

NE/2016/05


SHEET TITLE
圖紙名稱

E12 AND BBI - PORTION OF SITE

SHEET NUMBER
圖紙編號

60328348/PC1/3016

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the related dimensions.

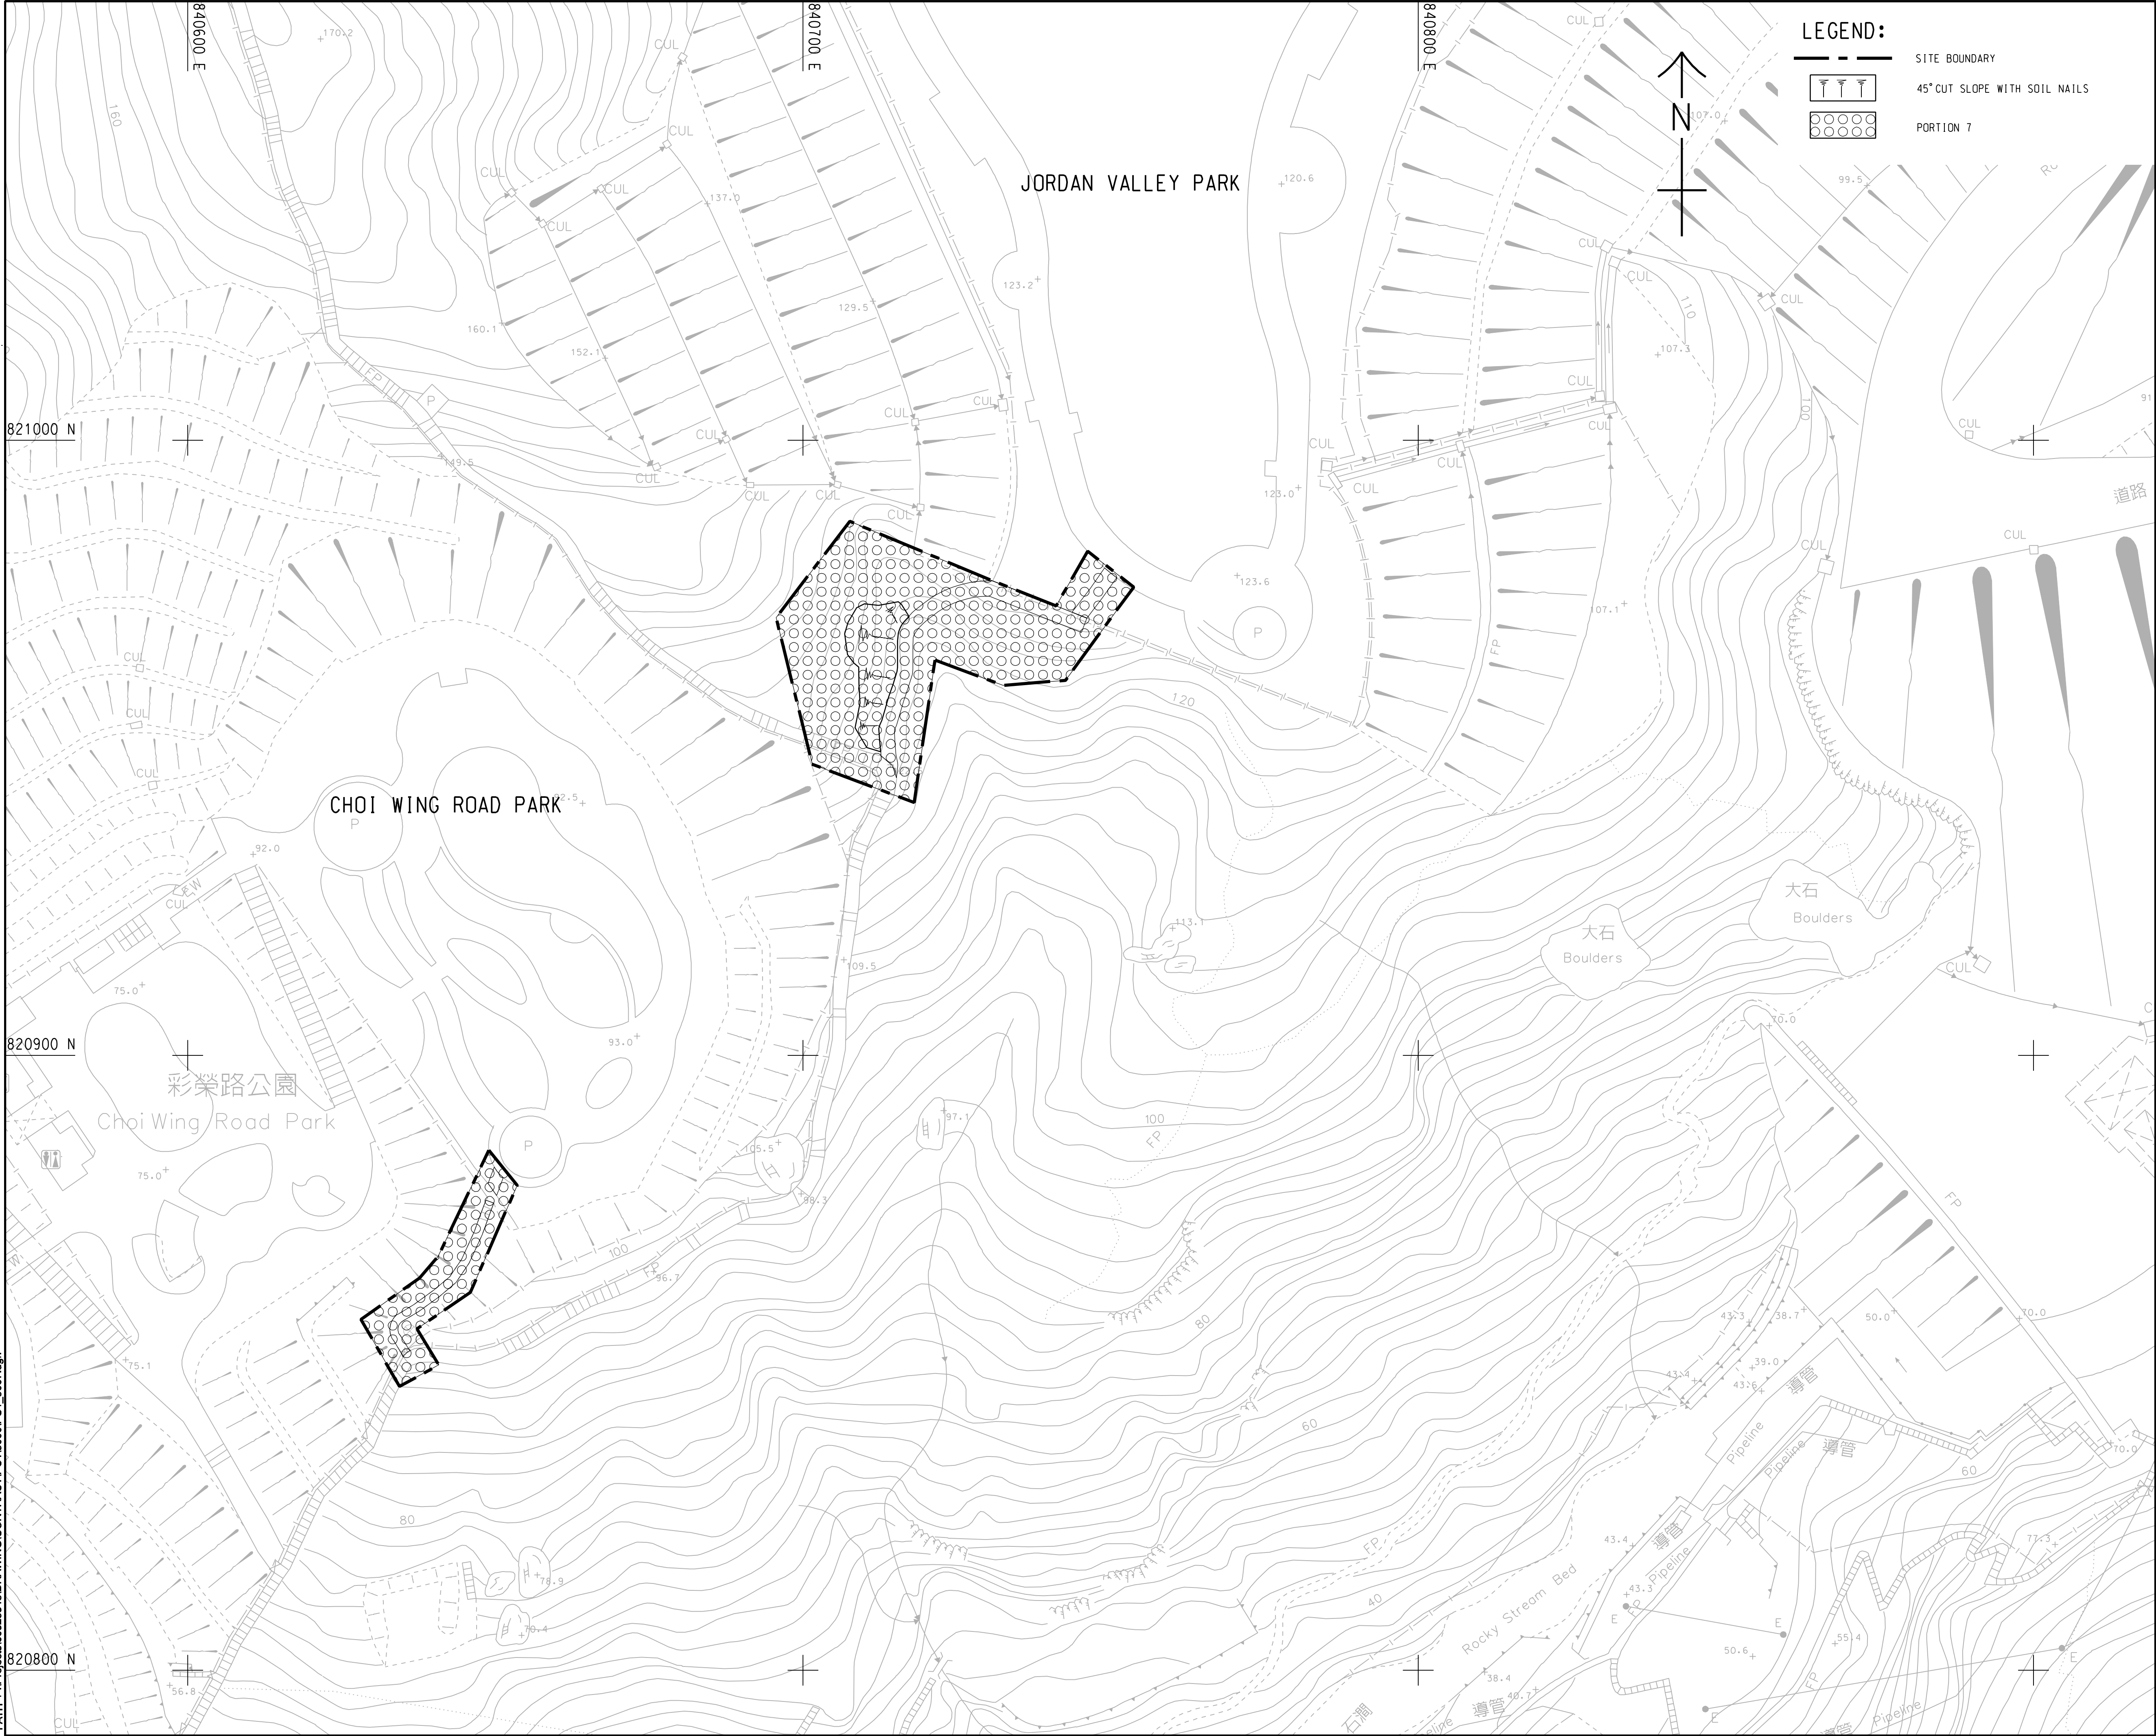

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the related dimensions.

AECOM

PROJECT

DEVELOPMENT OF
ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION

CONTRACT TITLE
PEDESTRIAN CONNECTIVITY
FACILITIES WORKS PHASE 1

CLIENT

土木工程拓展署
Civil Engineering and
Development Department

CONSULTANT

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS

分判工程顧問公司

ISSUE/REVISION

I/R	DATE	DESCRIPTION	CHK.
-	OCT. 16	TENDER DRAWING	AC
1/R	16/10/2016	1/R 16/10/2016	AC

STATUS

備註

SCALE


比例 1:500

DIMENSION UNIT

尺寸單位 METRES

KEY PLAN

索引圖 1:60000

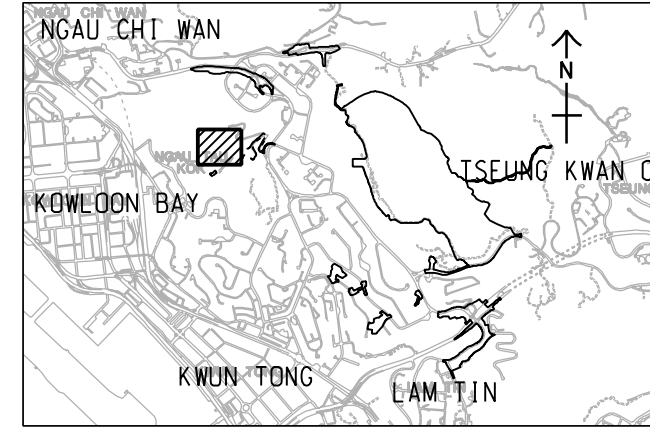

PROJECT NO.

項目編號 60328348

CONTRACT NO.

合約編號 NE/2016/05


SHEET TITLE

圖紙名稱 GREEN ROUTE - PORTION OF SITE

SHEET NUMBER

圖紙編號 60328348/PC1/5007

Pld File by: WANGGLW 2016/11/16
PATH P:\Projects\8626363\DRAWING\CONTRACT\PC1\8000\PC1_8501.dgn
Project Management Initials: Designer: PCTK Checked: AC Approved: BWCW ISO A1 594mm x 841mm

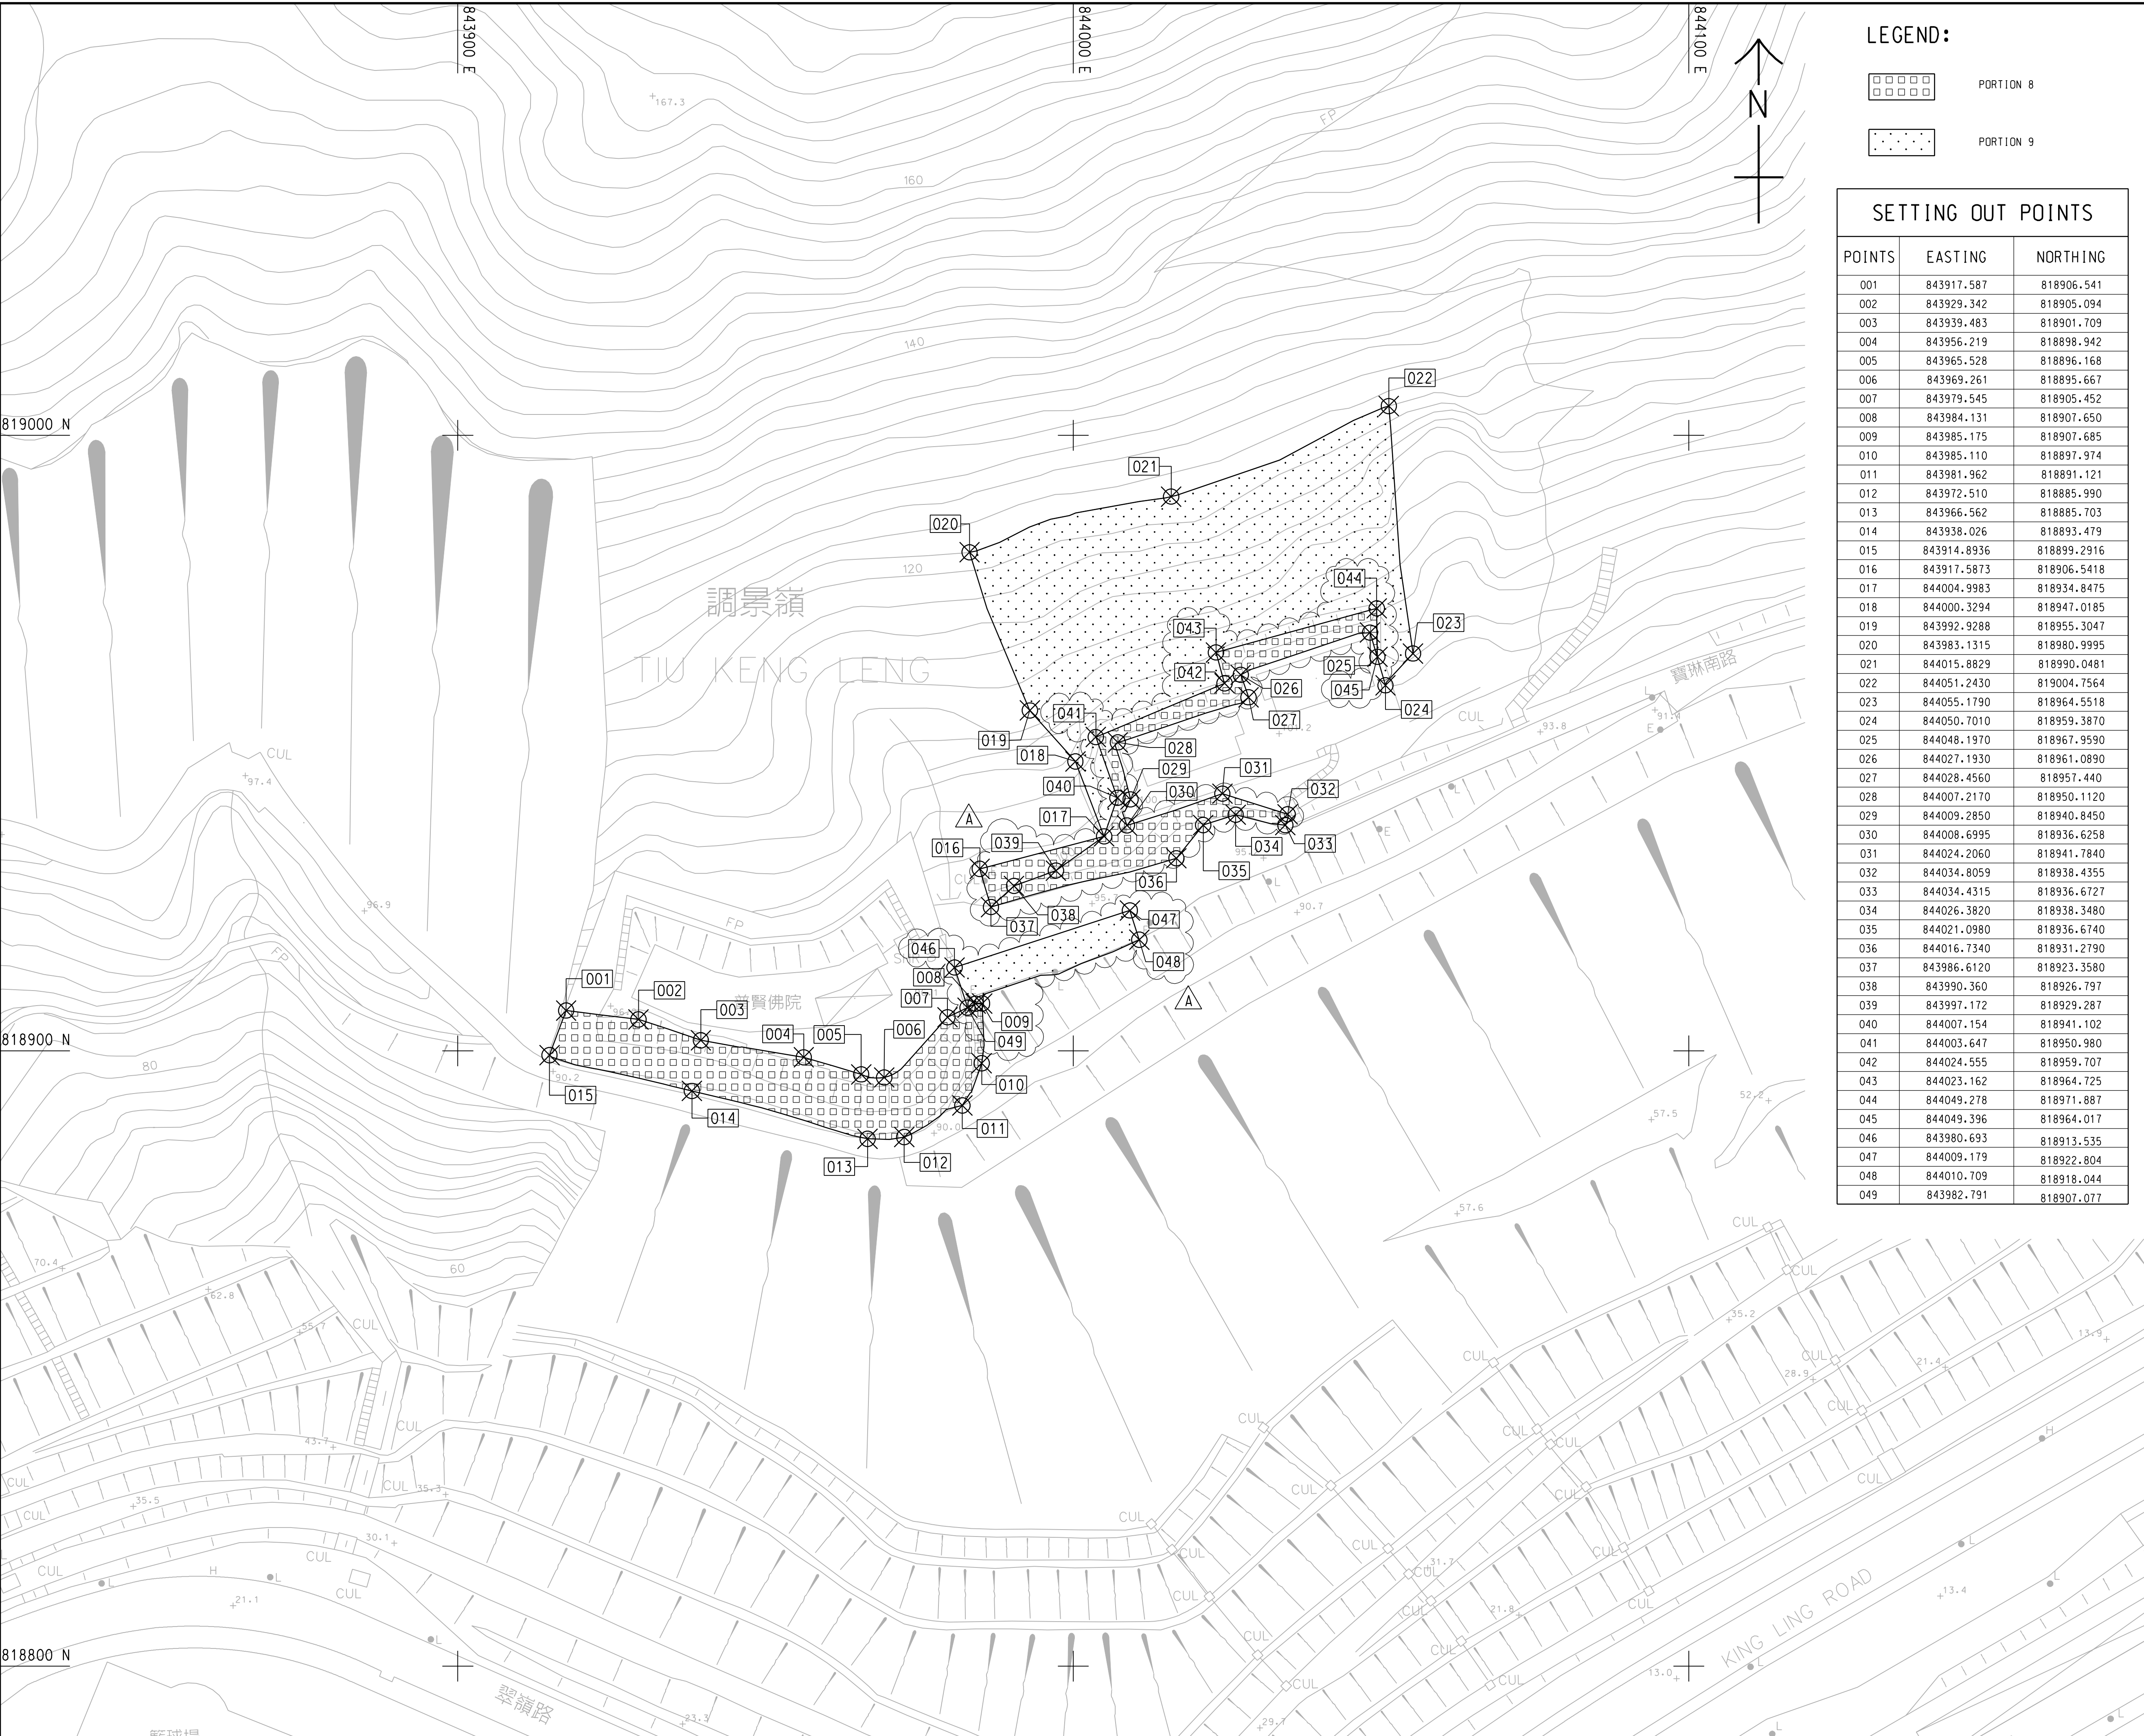

LEGEND:

- PORTION 8
- PORTION 9

SETTING OUT POINTS

POINTS	EASTING	NORTHING
001	843917.587	818906.541
002	843929.342	818905.094
003	843939.483	818901.709
004	843956.219	818898.942
005	843965.528	818896.168
006	843969.261	818895.667
007	843979.545	818905.452
008	843984.131	818907.650
009	843985.175	818907.685
010	843985.110	818897.974
011	843981.962	818891.121
012	843972.510	818885.990
013	843966.562	818885.703
014	843938.026	818893.479
015	843914.8936	818899.2916
016	843917.5873	818906.5418
017	844004.9983	818934.8475
018	844000.3294	818947.0185
019	843992.9288	818955.3047
020	843983.1315	818980.9995
021	844015.8829	818990.0481
022	844051.2430	819004.7564
023	844055.1790	818964.5518
024	844050.7010	818959.3870
025	844048.1970	818967.9590
026	844027.1930	818961.0890
027	844028.4560	818957.440
028	844007.2170	818950.1120
029	844009.2850	818940.8450
030	844008.6995	818936.6258
031	844024.2060	818941.7840
032	844034.8059	818938.4355
033	844034.4315	818936.6727
034	844026.3820	818938.3480
035	844021.0980	818936.6740
036	844016.7340	818931.2790
037	843986.6120	818923.3580
038	843990.360	818926.797
039	843997.172	818929.287
040	844007.154	818941.102
041	844003.647	818950.980
042	844024.555	818959.707
043	844023.162	818964.725
044	844049.278	818971.887
045	844049.396	818964.017
046	843980.693	818913.535
047	844009.179	818922.804
048	844010.709	818918.044
049	843982.791	818907.077

AECOM

PROJECT

DEVELOPMENT OF
ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION

CONTRACT TITLE
PEDESTRIAN CONNECTIVITY
FACILITIES WORKS PHASE 1

CLIENT

CEDD 土木工程拓展署
Civil Engineering and
Development Department

CONSULTANT

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS

分判工程顧問公司

ISSUE/REVISION

REV	DATE	DESCRIPTION	CHK.
A	NOV. 16	TENDER ADDENDUM NO. 1	AC
-	OCT. 16	TENDER DRAWING	AC
I/R	DATE	DESCRIPTION	CHK.
修訂	日期	內容摘要	校核

STATUS

備版

SCALE

比例

A1 1: 500

DIMENSION UNIT


尺寸單位

METRES

KEY PLAN

索引圖

A1 1: 60000

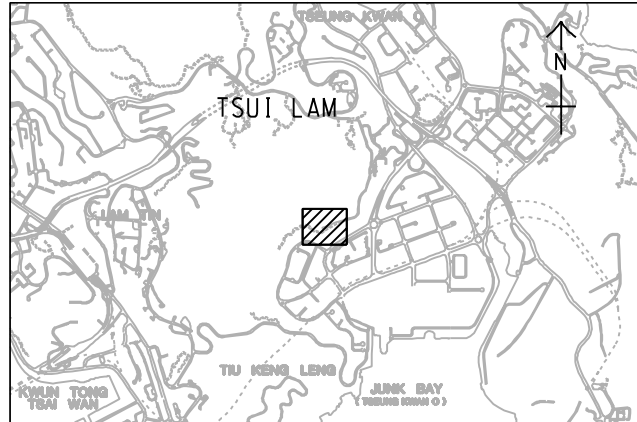

PROJECT NO.

項目編號

60328348

CONTRACT NO.

合約編號

NE/2016/05

SHEET TITLE

圖紙名稱

INFRASTRUCTURAL WORKS AT
PO LAM ROAD SOUTH TIU KENG
LENG – PORTION OF SITE


SHEET NUMBER

圖紙編號

60328348/PC1/9501A

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the stated dimensions.

**Layout plan of Contract 3 (NE/2017/03)
(Non-Designated Area)**

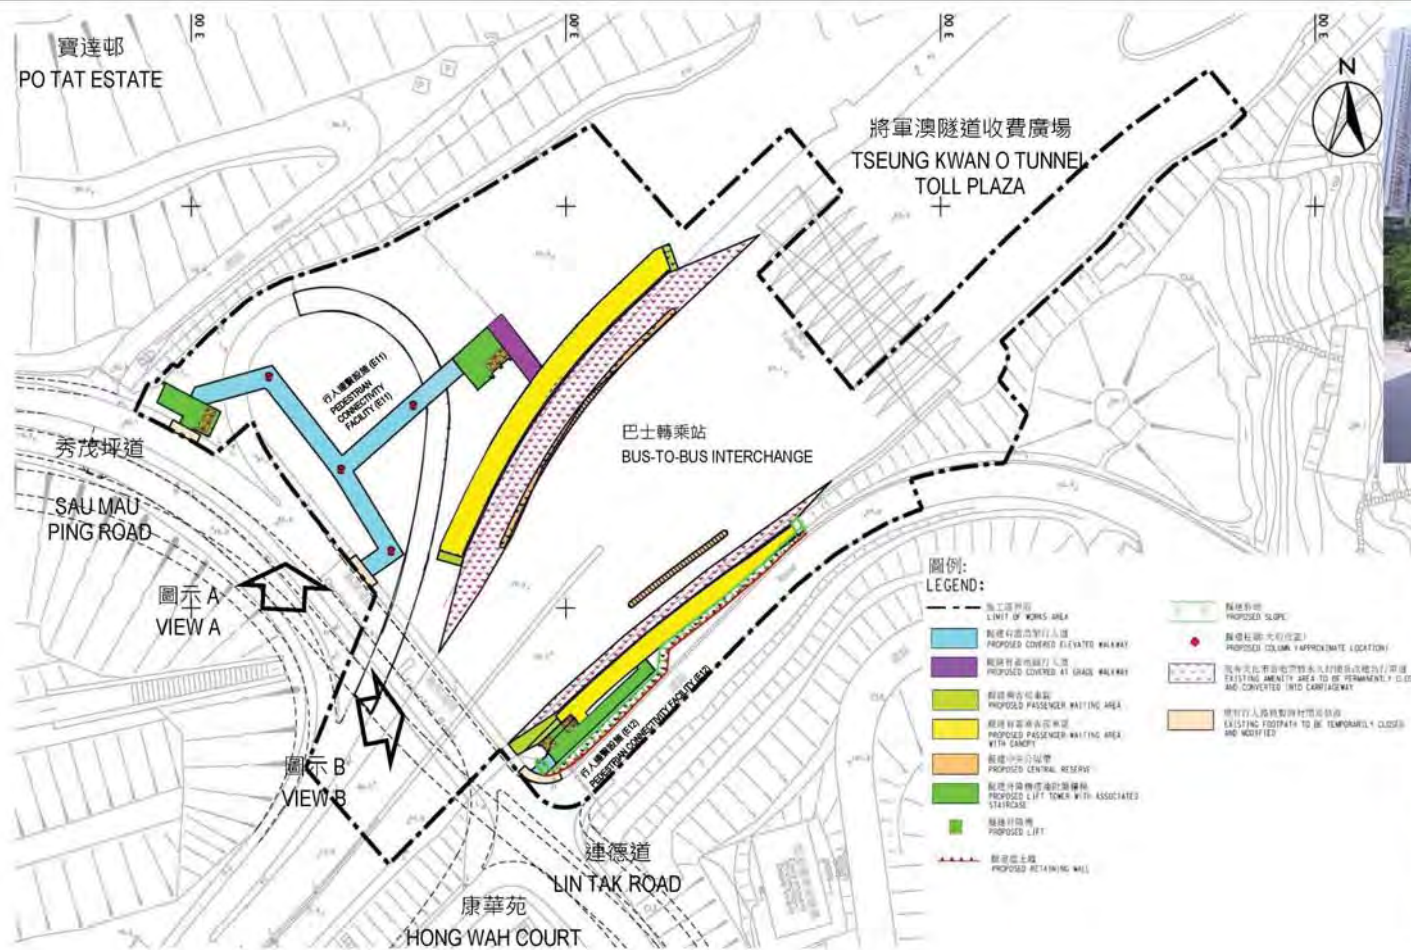

圖示 A

VIEW A



圖示 B

VIEW B

圖則名稱 Drawing Title

行人連繫設施(巴士轉乘站、E11及E12) - 平面圖及構思圖
Pedestrian Connectivity Facilities (Bus-to-Bus Interchange, E11 and E12)
- Layout Plan and Artist's Impression

項目編號 Item No.

765CL

比例 Scale

圖則編號 Drawing No.

附件五 Appendix 5

辦事處 Office

新界東拓展處
NEW TERRITORIES EAST
DEVELOPMENT OFFICE



土木工程拓展署
CIVIL ENGINEERING
AND DEVELOPMENT
DEPARTMENT



- NOTES:
- FOR NOTES AND LEGEND REFER TO DRAWING NO. 60328348/R&P/1001.
 - THIS DRAWING TO BE READ IN CONJUNCTION WITH DRAWING NOS. 60328348/R&P/1001 TO 1008.

AECOM

PROJECT
項目

DEVELOPMENT OF
ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION

CONTRACT TITLE
DEVELOPMENT OF ANDERSON ROAD
QUARRY SITE - ROAD IMPROVEMENT
WORKS AND PEDESTRIAN CONNECTIVITY
FACILITIES WORKS PHASE 2A

CLIENT
業主

CEDD 土木工程拓展署
Civil Engineering and
Development Department

CONSULTANT
工程顧問公司

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION 修訂				
A	NOV. 17	TENDER ADDENDUM NO. 1	AWYC	Y/C
-	OCT. 17	TENDER DRAWING	AWYC	AWYC
I/R	DATE	DESCRIPTION	CHK.	CHK.
修訂	日期	內容摘要	校核	校核

STATUS
階段


SCALE
比例

DIMENSION UNIT
尺寸單位

A1 1 : 500 METRES

KEY PLAN
索引圖

A1 1 : 60000

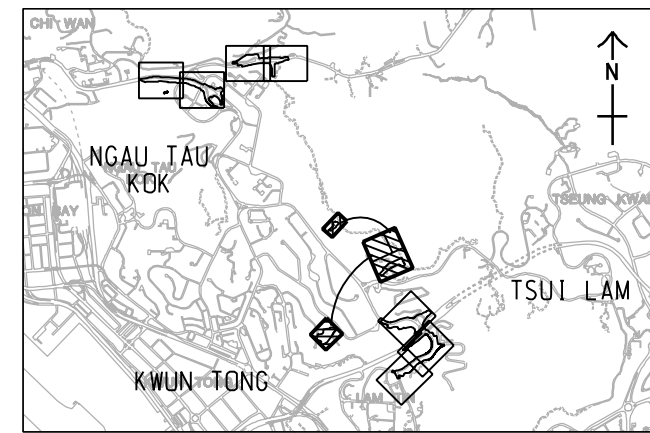

PROJECT NO.
項目編號

CONTRACT NO.
合約編號

60328348 NE/2017/03

SHEET TITLE
圖紙名稱

GENERAL LAYOUT

SHEET NUMBER
圖紙編號

60328348/R&P/1008A

Layout plan of Contract 4 (ED/2020/02)

Plot File by: YangRO 3/19/2021
PATH P:\PROJECT\1560328348\Drawing\CONTRACT\LS1000\LS_1000.dgn
ISO A1 594mm x 841mm
Designer: DKMW Checked: AWYC Approved: HKT
Project Management Initials:



LEGEND:
--- SITE BOUNDARY



AECOM

PROJECT
項目
DEVELOPMENT OF
ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION

CONTRACT TITLE
DEVELOPMENT OF ANDERSON ROAD
QUARRY SITE - INFRASTRUCTURE,
GREENING AND LANDSCAPE WORKS

CLIENT
業主
 土木工程拓展署
Civil Engineering and
Development Department

CONSULTANT
工程顧問公司
AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS
分判工程顧問公司

ISSUE/REVISION			
修訂			
-	MAR. 21	TENDER DRAWING	Y.C.
I/R	DATE	DESCRIPTION	CHK.
修訂	日期	內容簡要	校核

STATUS
階段

SCALE
比例
A1 1 : 6000

DIMENSION UNIT
尺寸單位
METRES

KEY PLAN
索引圖

PROJECT NO.
項目編號
60328348


CONTRACT NO.
合約編號
ED/2020/02

SHEET TITLE
圖紙名稱
KEY PLAN

SHEET NUMBER
圖紙編號
60328348/LS/1000

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the stated dimensions.

Layout plan of Contract 5 (ED/2019/02)

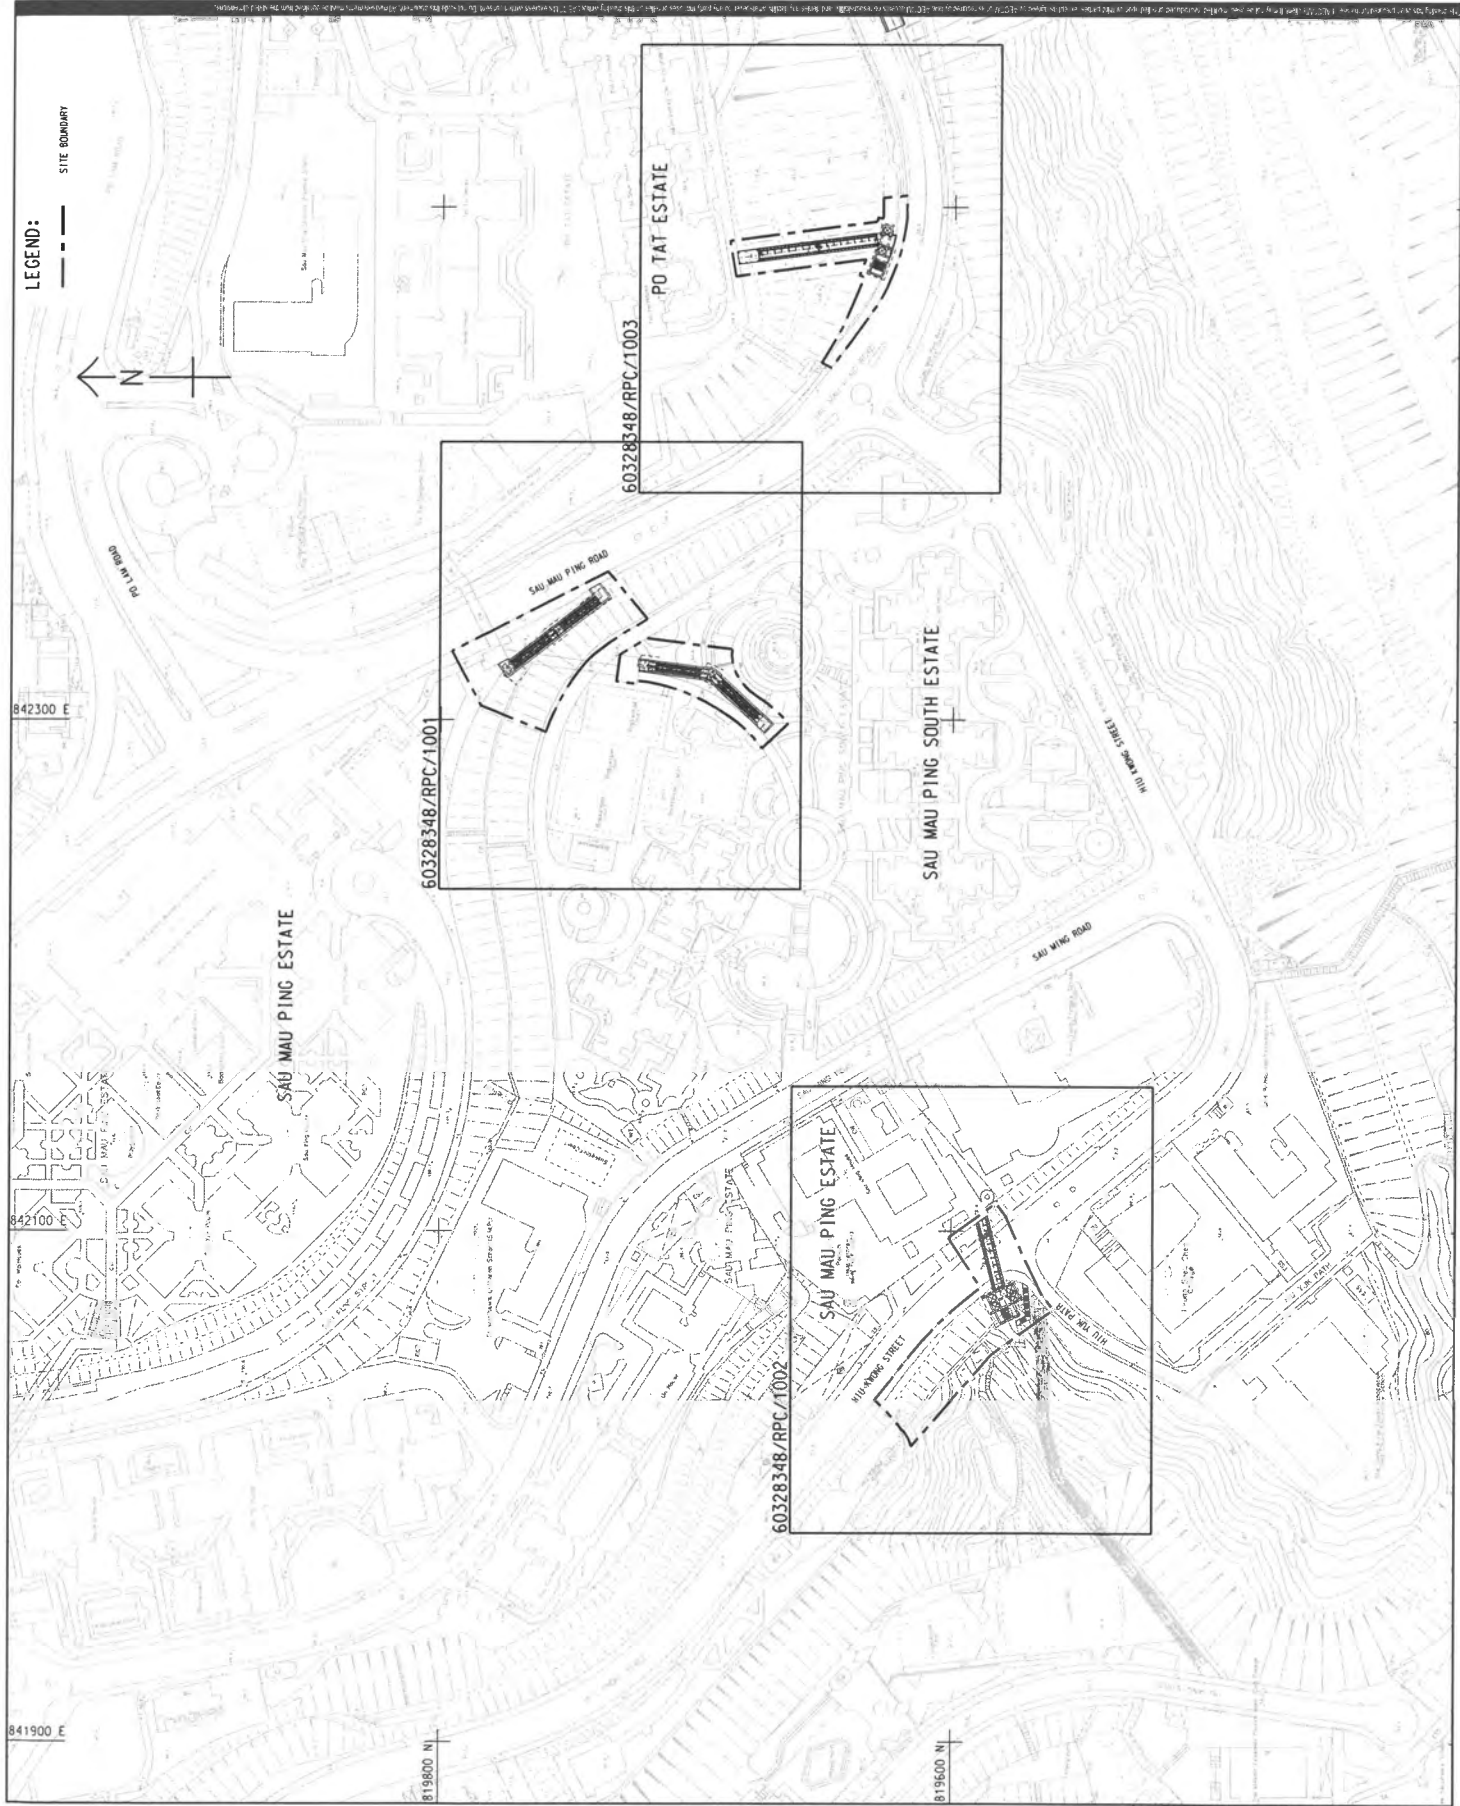

AECOM

PROJECT

DEVELOPMENT OF
ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION
CONTRACT TITLE
DEVELOPMENT OF ANDERSON ROAD
QUARRY SITE - INVESTIGATION,
DESIGN AND CONSTRUCTION
CONNECTIVITY FACILITIES WORKS

CLIENT

CEDD
Civil Engineering and
Development Department

土木工務發展部
Civil Engineering and
Development Department

CONSULTANT

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS

5/1/2021

ISSUE/REVISION

NO.	DATE	DESCRIPTION	BY	CHK.
1	NOV. 20	TENDER DRAWING	AMYC	
2				
3				
4				
5				
6				
7				
8				
9				
10				

STATUS

SCALE

AT 1:1000

KEY PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PLAN

SECTION

PROJECT NO.

60328348

CONTRACT NO.

ED/2019/02

SHEET TITLE

KEY PLAN





SHEET NUMBER


60328348/RPC/1000

NOTES:

1. FOUNDATION INDICATIVE ONLY.
2. ALL LEVELS INDICATED ARE STRUCTURAL FLOOR LEVEL UNLESS NOTED OTHERWISE.

END:

-  SITE BOUNDARY
 EXISTING GROUND LEVEL
 414.30
 EXISTING COVERED WALKWAY TO BE MAINTAINED

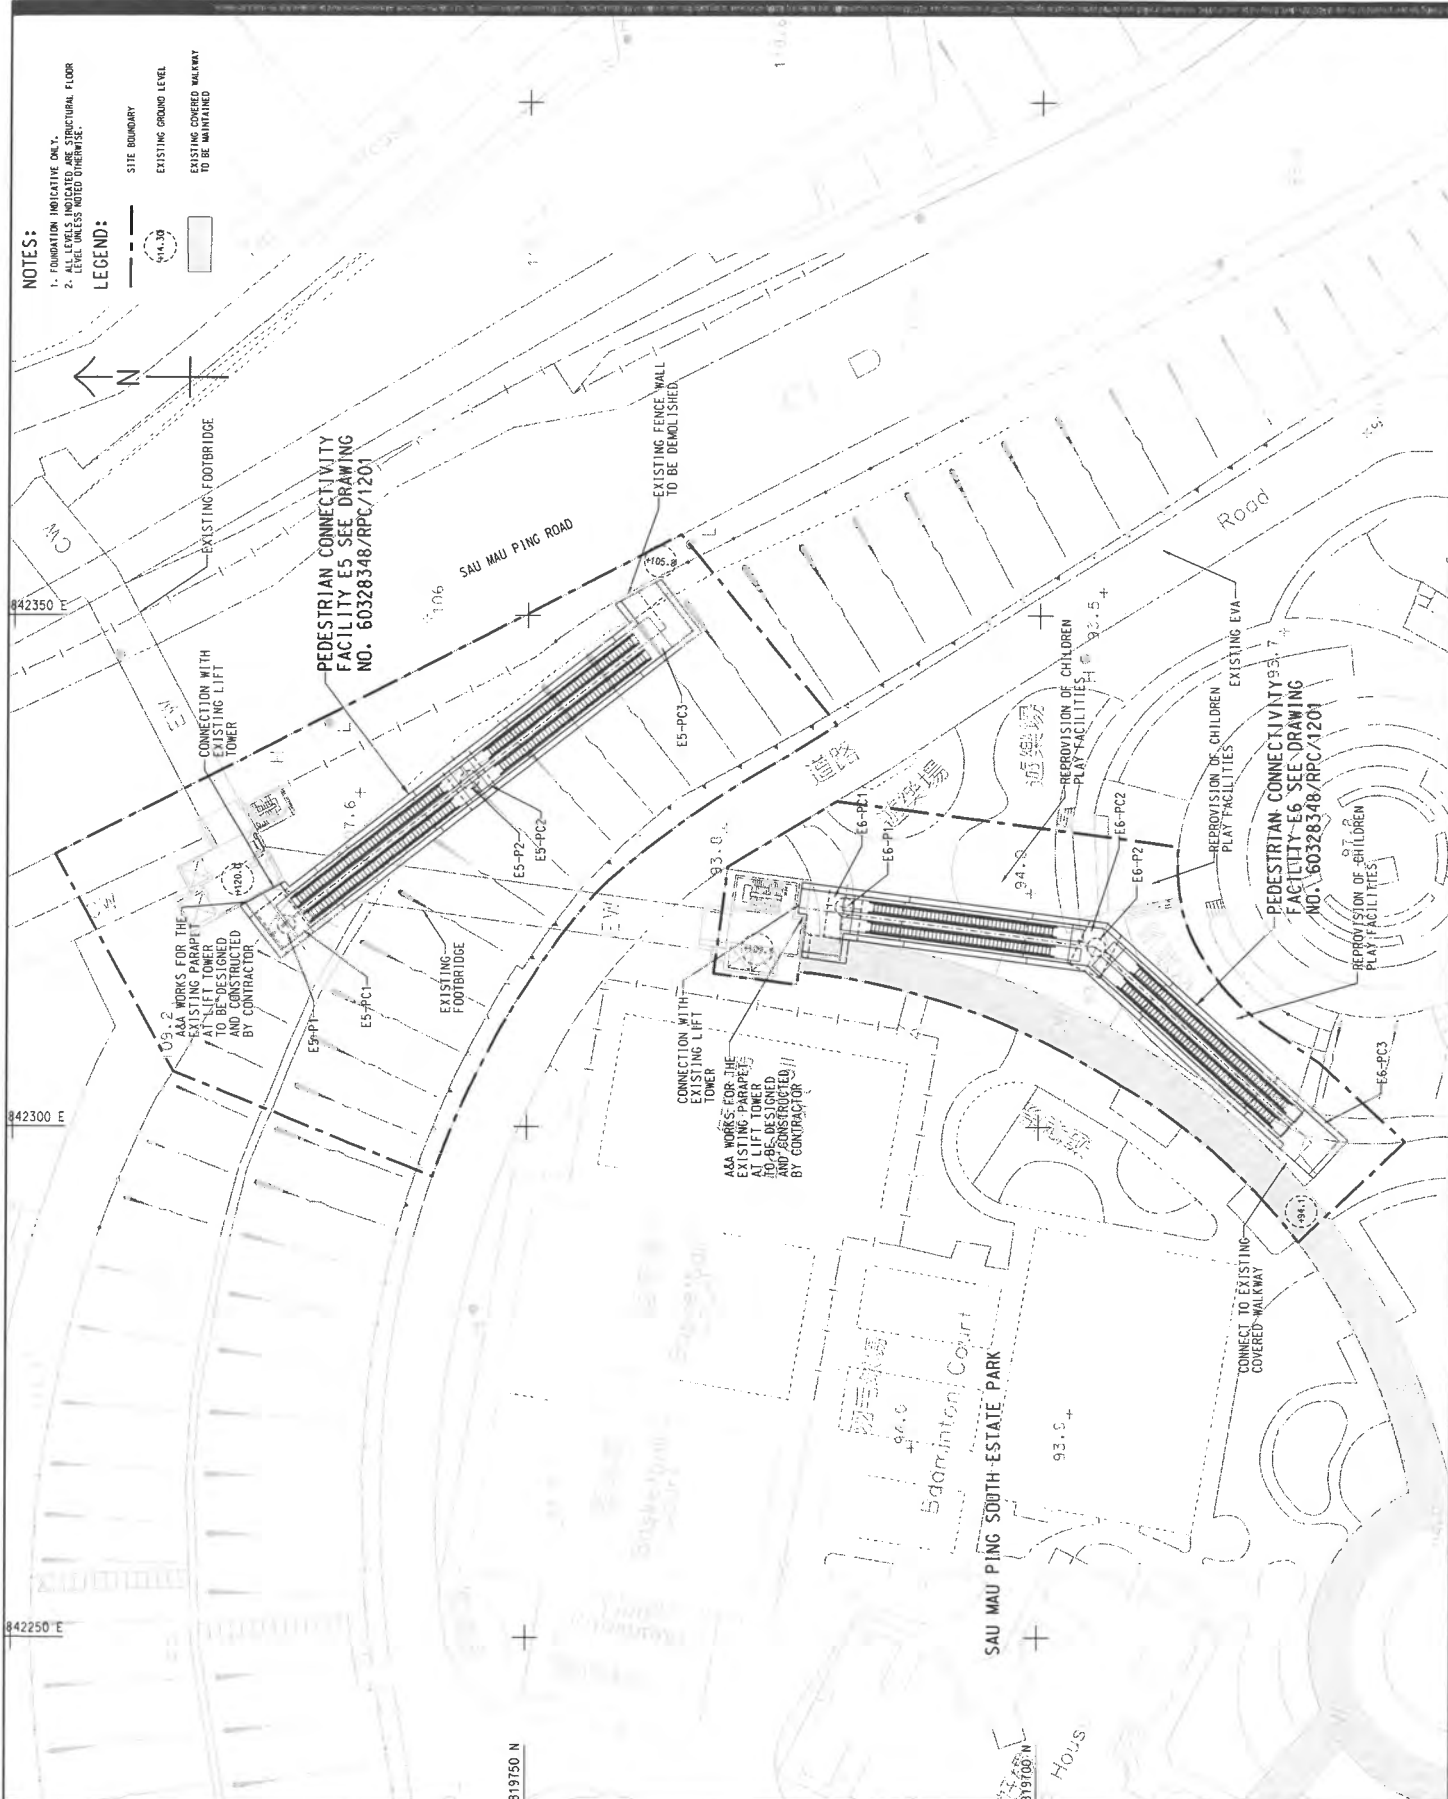


NO.	DATE	DESCRIPTION	CHK.
1	DEC. 20	TENDER ADDENDUM NO.1	AWVC
2	NOV. 20	TENDER DRAWING	AWVC
3	DEC. 20	DESIGN	CHK.
4	DEC. 20	DESIGN	CHK.
5	DEC. 20	DESIGN	CHK.
6	DEC. 20	DESIGN	CHK.
7	DEC. 20	DESIGN	CHK.
8	DEC. 20	DESIGN	CHK.
9	DEC. 20	DESIGN	CHK.
10	DEC. 20	DESIGN	CHK.
11	DEC. 20	DESIGN	CHK.
12	DEC. 20	DESIGN	CHK.
13	DEC. 20	DESIGN	CHK.
14	DEC. 20	DESIGN	CHK.
15	DEC. 20	DESIGN	CHK.
16	DEC. 20	DESIGN	CHK.
17	DEC. 20	DESIGN	CHK.
18	DEC. 20	DESIGN	CHK.
19	DEC. 20	DESIGN	CHK.
20	DEC. 20	DESIGN	CHK.
21	DEC. 20	DESIGN	CHK.
22	DEC. 20	DESIGN	CHK.
23	DEC. 20	DESIGN	CHK.
24	DEC. 20	DESIGN	CHK.
25	DEC. 20	DESIGN	CHK.
26	DEC. 20	DESIGN	CHK.
27	DEC. 20	DESIGN	CHK.
28	DEC. 20	DESIGN	CHK.
29	DEC. 20	DESIGN	CHK.
30	DEC. 20	DESIGN	CHK.
31	DEC. 20	DESIGN	CHK.
32	DEC. 20	DESIGN	CHK.
33	DEC. 20	DESIGN	CHK.
34	DEC. 20	DESIGN	CHK.
35	DEC. 20	DESIGN	CHK.
36	DEC. 20	DESIGN	CHK.
37	DEC. 20	DESIGN	CHK.
38	DEC. 20	DESIGN	CHK.
39	DEC. 20	DESIGN	CHK.
40	DEC. 20	DESIGN	CHK.
41	DEC. 20	DESIGN	CHK.
42	DEC. 20	DESIGN	CHK.
43	DEC. 20	DESIGN	CHK.
44	DEC. 20	DESIGN	CHK.
45	DEC. 20	DESIGN	CHK.
46	DEC. 20	DESIGN	CHK.
47	DEC. 20	DESIGN	CHK.
48	DEC. 20	DESIGN	CHK.
49	DEC. 20	DESIGN	CHK.
50	DEC. 20	DESIGN	CHK.
51	DEC. 20	DESIGN	CHK.
52	DEC. 20	DESIGN	CHK.
53	DEC. 20	DESIGN	CHK.
54	DEC. 20	DESIGN	CHK.
55	DEC. 20	DESIGN	CHK.
56	DEC. 20	DESIGN	CHK.
57	DEC. 20	DESIGN	CHK.
58	DEC. 20	DESIGN	CHK.
59	DEC. 20	DESIGN	CHK.
60	DEC. 20	DESIGN	CHK.
61	DEC. 20	DESIGN	CHK.
62	DEC. 20	DESIGN	CHK.
63	DEC. 20	DESIGN	CHK.
64	DEC. 20	DESIGN	CHK.
65	DEC. 20	DESIGN	CHK.
66	DEC. 20	DESIGN	CHK.
67	DEC. 20	DESIGN	CHK.
68	DEC. 20	DESIGN	CHK.
69	DEC. 20	DESIGN	CHK.
70	DEC. 20	DESIGN	CHK.
71	DEC. 20	DESIGN	CHK.
72	DEC. 20	DESIGN	CHK.
73	DEC. 20	DESIGN	CHK.
74	DEC. 20	DESIGN	CHK.
75	DEC. 20	DESIGN	CHK.
76	DEC. 20	DESIGN	CHK.
77	DEC. 20	DESIGN	CHK.
78	DEC. 20	DESIGN	CHK.
79	DEC. 20	DESIGN	CHK.
80	DEC. 20	DESIGN	CHK.
81	DEC. 20	DESIGN	CHK.
82	DEC. 20	DESIGN	CHK.
83	DEC. 20	DESIGN	CHK.
84	DEC. 20	DESIGN	CHK.
85	DEC. 20	DESIGN	CHK.
86	DEC. 20	DESIGN	CHK.
87	DEC. 20	DESIGN	CHK.
88	DEC. 20	DESIGN	CHK.
89	DEC. 20	DESIGN	CHK.
90	DEC. 20	DESIGN	CHK.
91	DEC. 20	DESIGN	CHK.
92	DEC. 20	DESIGN	CHK.
93	DEC. 20	DESIGN	CHK.
94	DEC. 20	DESIGN	CHK.
95	DEC. 20	DESIGN	CHK.
96	DEC. 20	DESIGN	CHK.
97	DEC. 20	DESIGN	CHK.
98	DEC. 20	DESIGN	CHK.
99	DEC. 20	DESIGN	CHK.
100	DEC. 20	DESIGN	CHK.


NOTES:

1. STAIRCASE AND FOUNDATION INDICATIVE ONLY.
2. DOOR OPENING TO BE IN THE SAME DIRECTION ON DIFFERENT FLOORS UNLESS NOTED OTHERWISE.
3. LEVEL UNLESS NOTED OTHERWISE.

LEGEND:

- SITE BOUNDARY
- LIFT
- STAIRCASE
- DOOR OPENING DIRECTION OF LIFT
- EXISTING GROUND LEVEL
- PROPOSED LEVEL

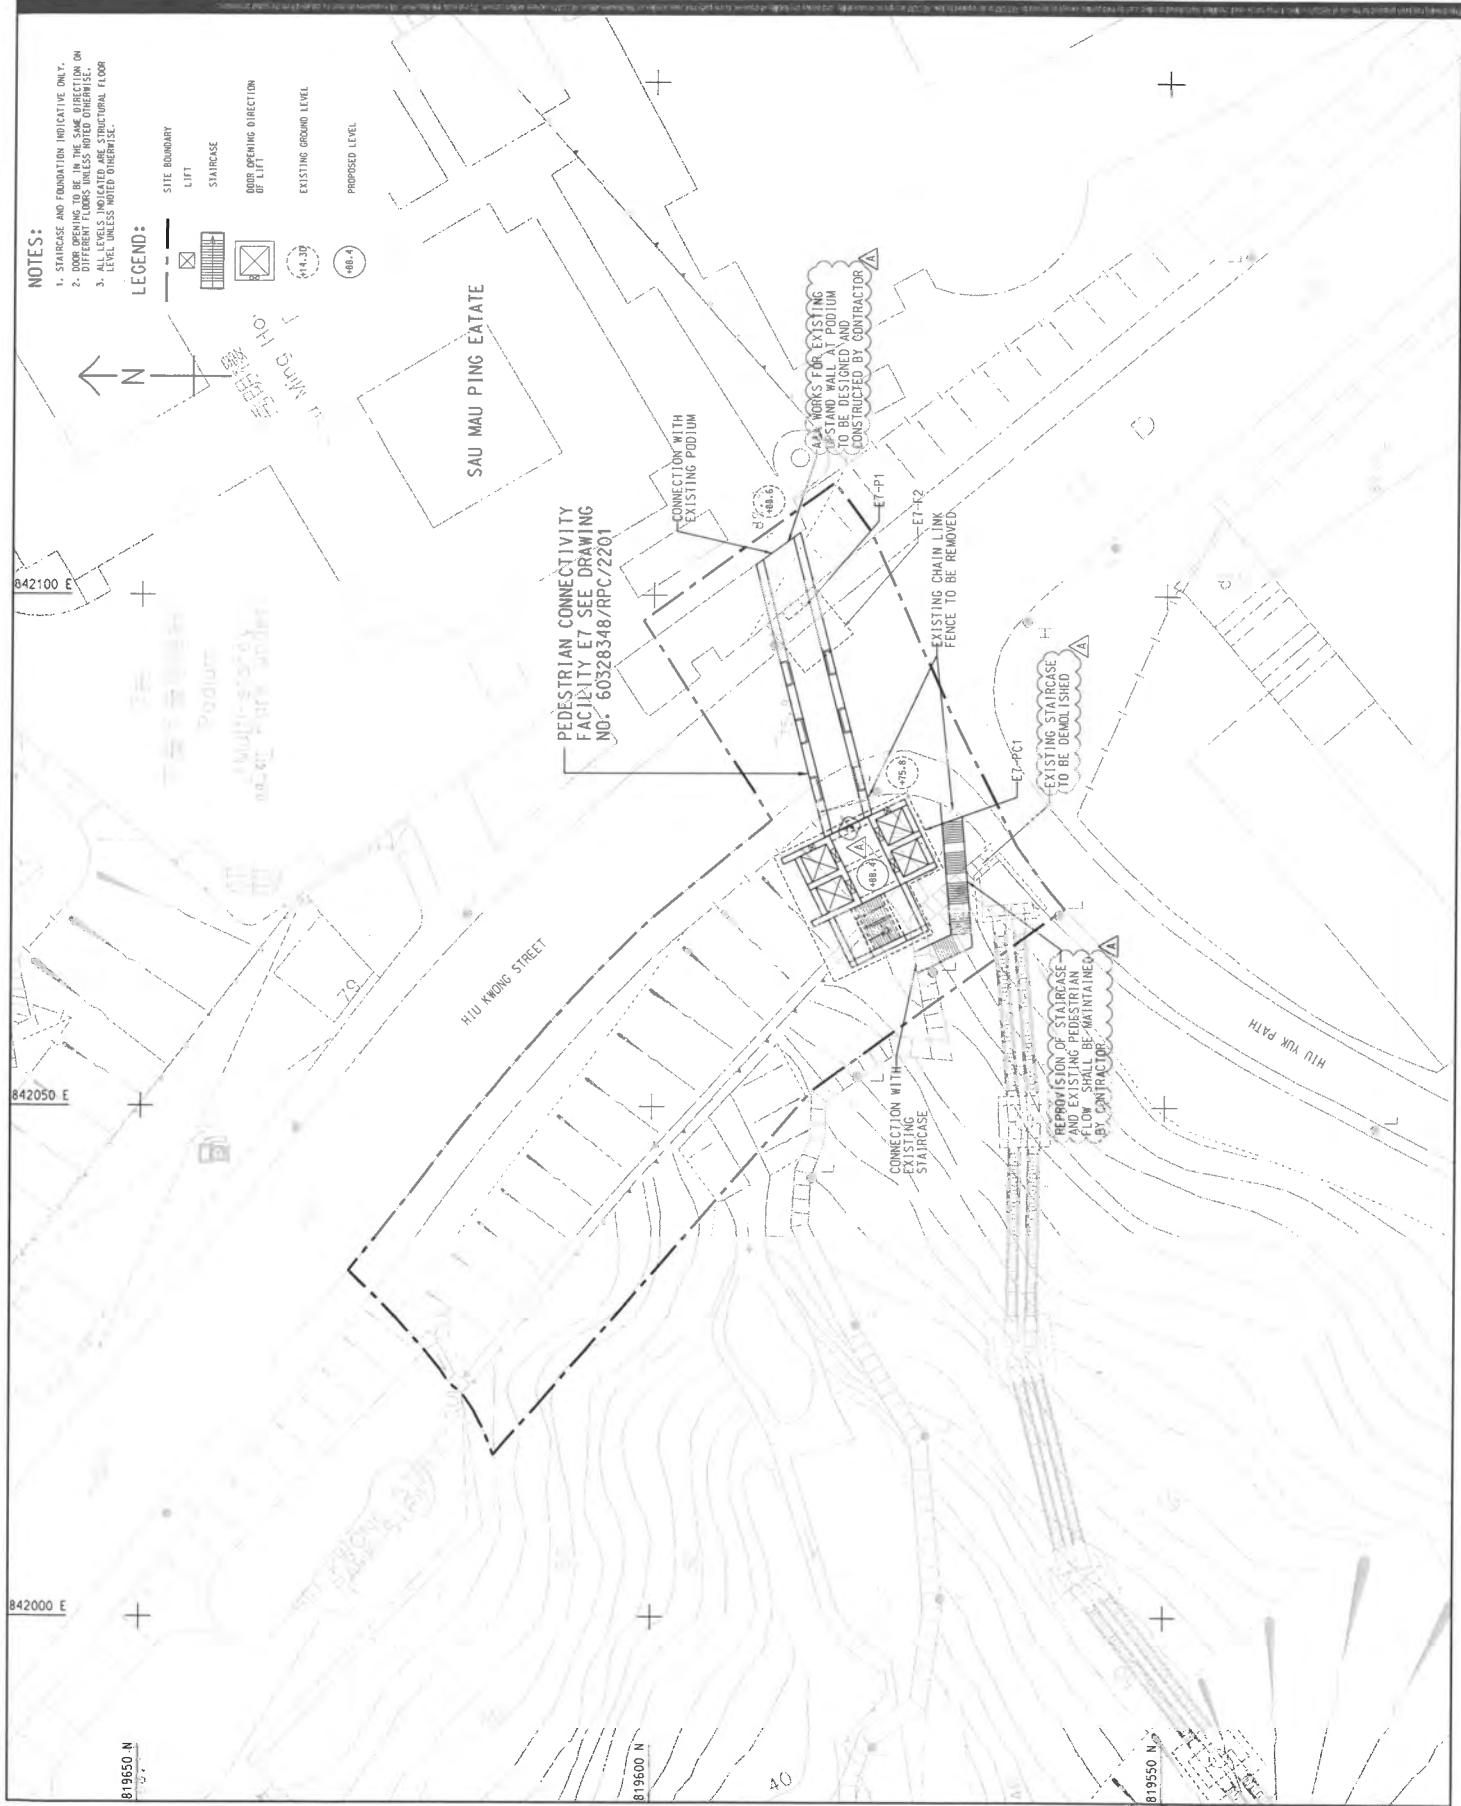

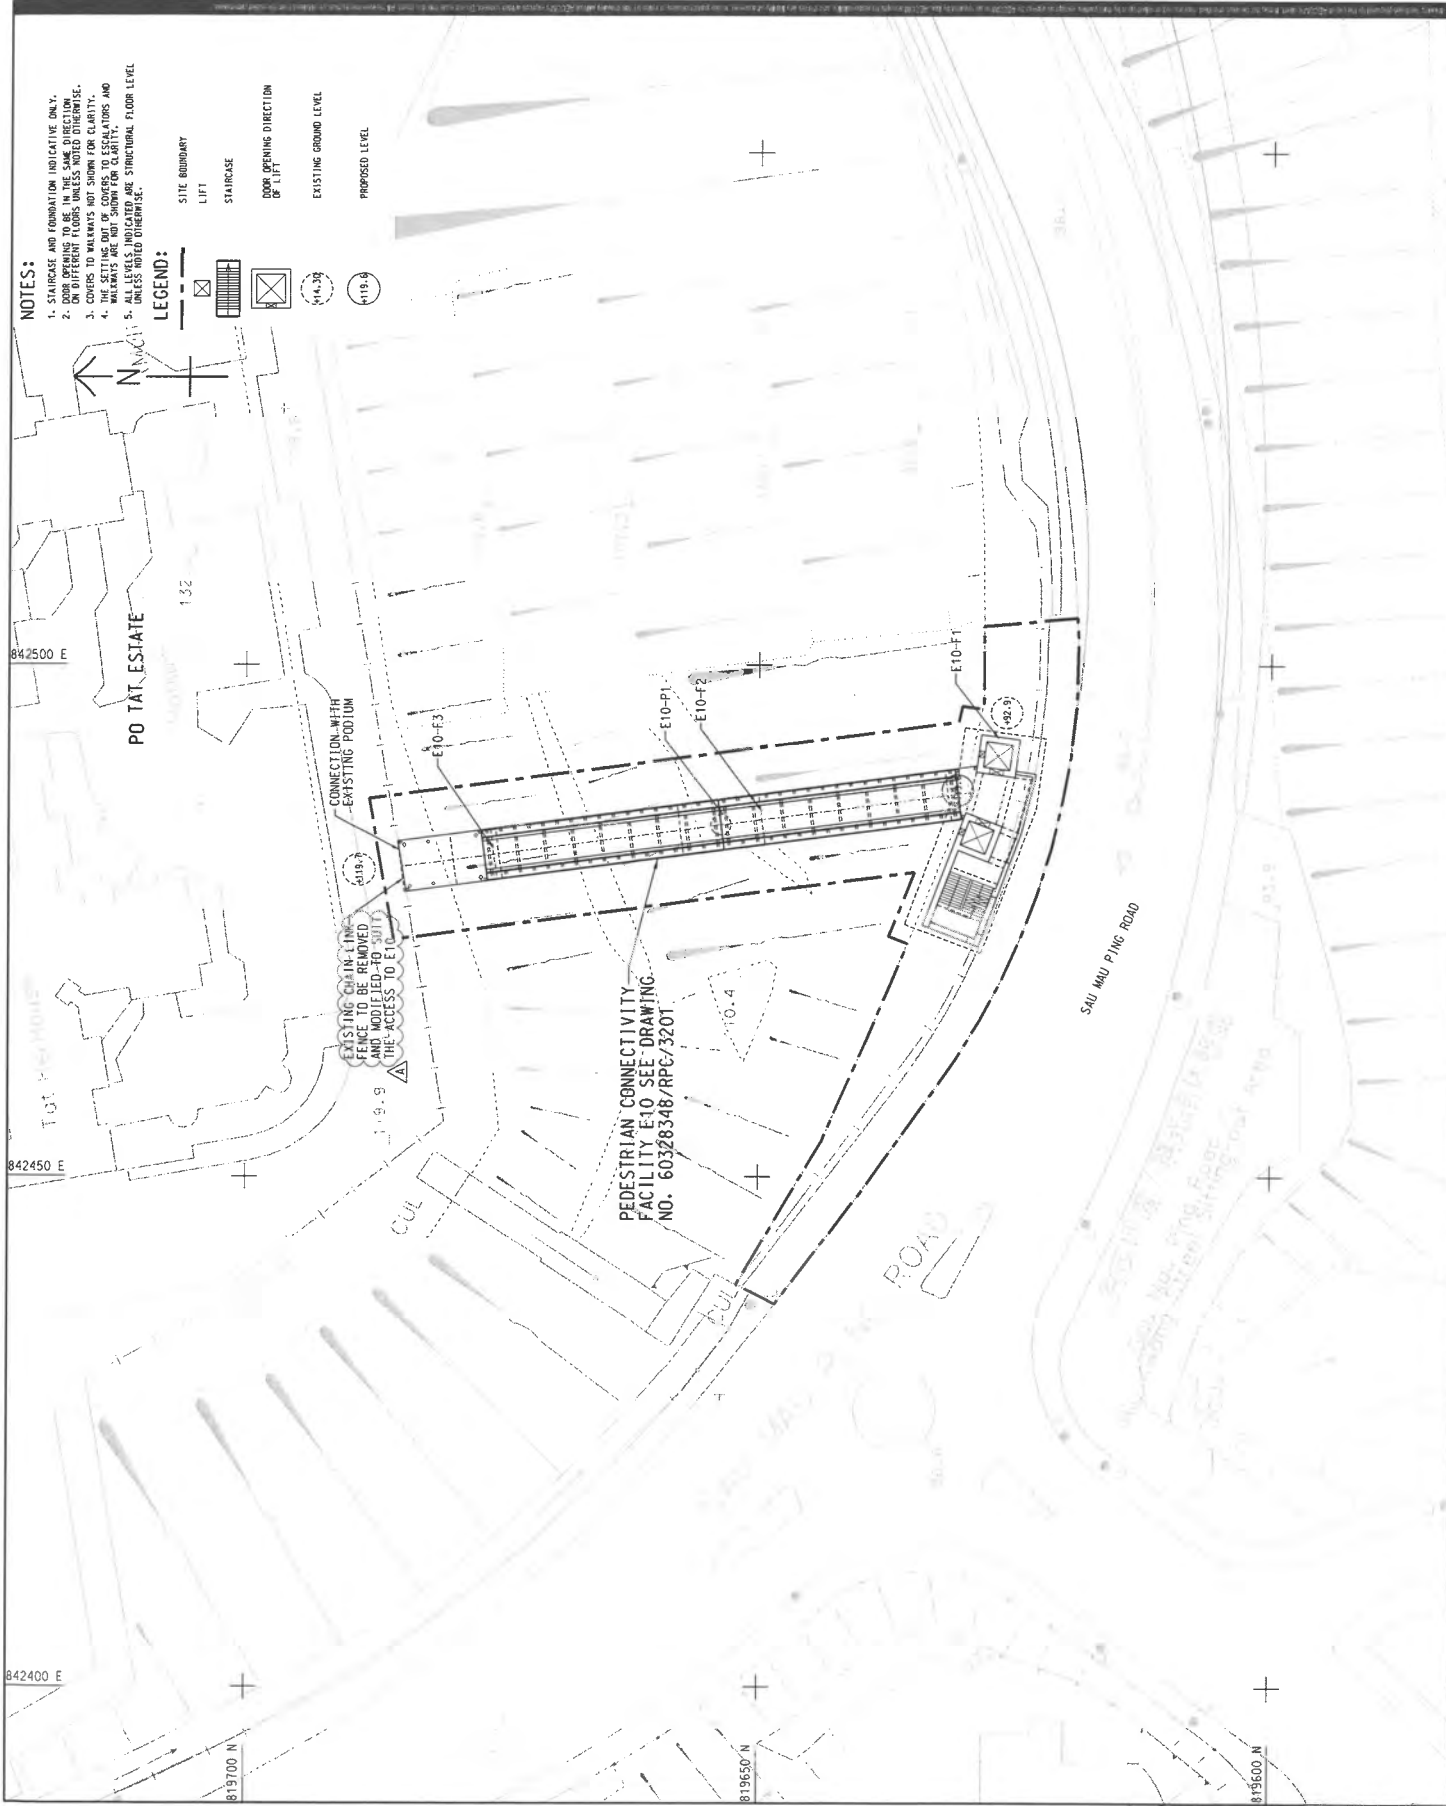

- NOTES:**
1. STAIRCASE AND FOUNDATION INDICATIVE ONLY.
 2. DOOR OPENING TO BE IN THE SAME DIRECTION AS THE STAIRCASE.
 3. COVERS TO WALKWAYS NOT SHOWN FOR CLARITY.
 4. THE SETTING OUT OF COVERS TO ESCALATORS AND WALKWAYS ARE NOT SHOWN FOR CLARITY.
 5. ALL LEVELS INDICATED ARE STRUCTURAL FLOOR LEVEL UNLESS OTHERWISE SPECIFIED.

LEGEND:

- SITE BOUNDARY
- LIFT
- STAIRCASE
- DOOR OPENING DIRECTION OR LIFT
- EXISTING GROUND LEVEL
- PROPOSED LEVEL

PO TAT ESTATE

842500 E

842450 E

842400 E

CONNECTION WITH EXISTING PODIUM

EXISTING GROUND LEVEL TO BE REMOVED AND MODIFIED TO SUIT THE ACCESS TO E10

PEDESTRIAN CONNECTIVITY FACILITY E10 SEE DRAWING NO. 60328348/RPC/3201

E10-F1

E10-F2

E10-F3

SAU MAU PING ROAD

819650 N

819600 N



PROJECT

DEVELOPMENT OF ANDERSON ROAD QUARRY SITE - INVESTIGATION, DESIGN AND CONSTRUCTION

CLIENT

CEPD
Civil Engineering and Development Department

CONSULTANT

AECOM Asia Company Ltd.
www.aecom.com

SUB-CONSULTANTS

211-100-000

ISSUE/REVISION

NO.	DATE	DESCRIPTION	BY	CHK
1	11/11/20	ISSUED FOR TENDER	AWYC	
2	11/11/20	ISSUED FOR TENDER	AWYC	
3	11/11/20	ISSUED FOR TENDER	AWYC	
4	11/11/20	ISSUED FOR TENDER	AWYC	

STATUS


NOT FOR CONSTRUCTION

SCALE

AT 1:250

KEY PLAN

AT 1:5000



PROJECT NO.

60328348

CONTRACT NO.

ED/2019/02

SHEET TITLE


GENERAL LAYOUT - E10

SHEET NUMBER

60328348/RPC/0001A

Appendix B

Project Organization Structure

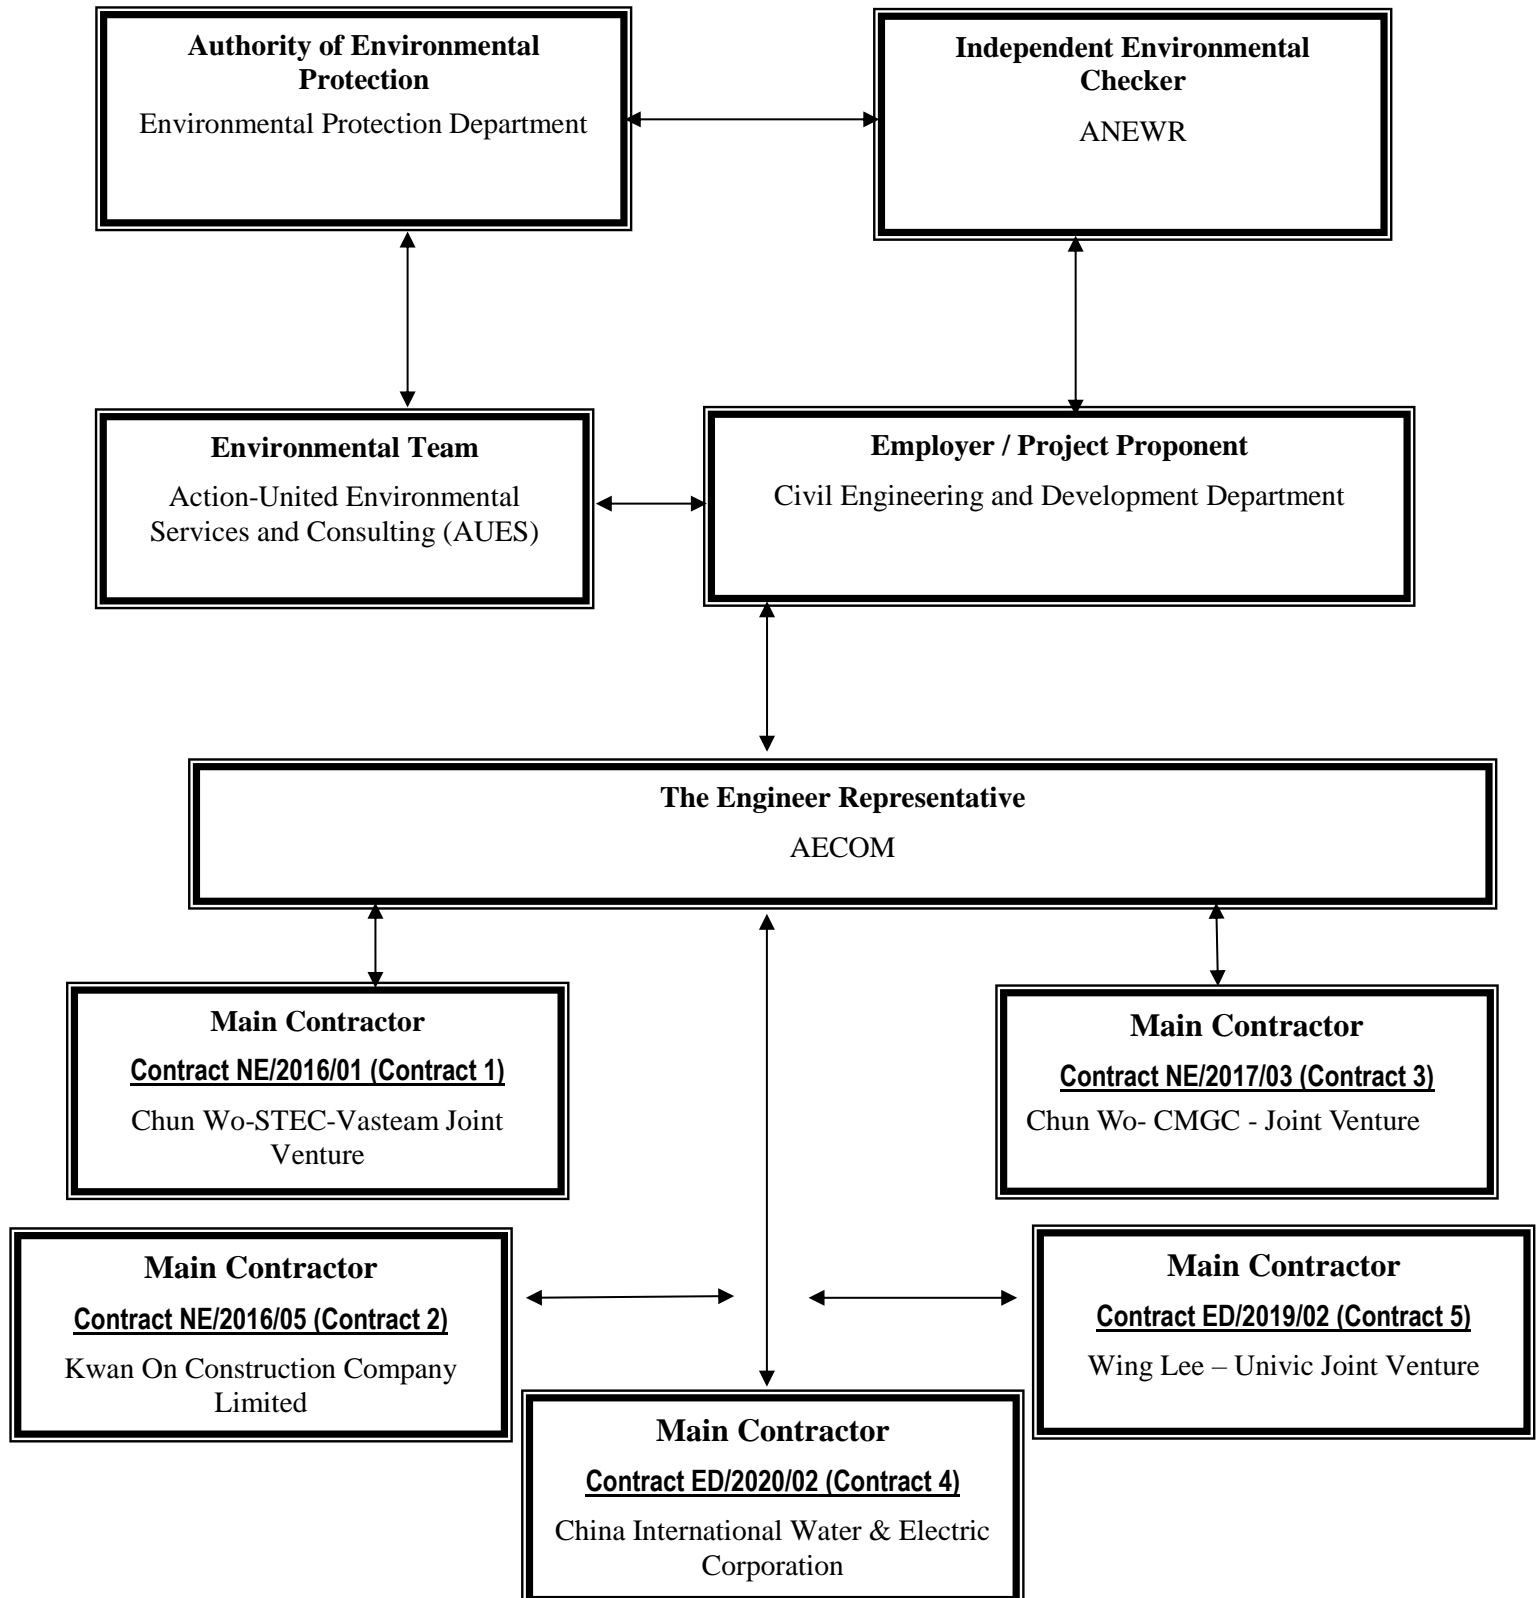Project Organization Structure

Contact Details of Key Personnel for Contract 1 – NE/2016/01

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Mr Leung Chi Foon	3842 7087	2739 0076
AECOM	Chief Resident Engineer	Lee, Yu Ching Paul	5723 6880	2473 3221
AECOM	Senior Resident Engineer	Li, Ling Tommy	9389 8792	2473 3221
ANWR	Independent Environmental Checker	James Choi	2618 2836	3007 8648
CSVJV	Project Manager	William Leung	2638 7181	2744 6937
CSVJV	Site Agent	TY Leung	2638 7181	2744 6937
CSVJV	Project Environmental Manager	Jimmy Cheng	2638 7181	2744 6937
CSVJV	Environmental Officer	Ken Chu	2638 7181	2744 6937
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:*CEDD (Employer) – Civil Engineering and Development Department**AECOM (Engineer) – AECOM Asia Co. Ltd.**CSVJV (Main Contractor) – Chun Wo-STECC-Vasteam Joint Venture**ANWR (IEC) – ANewR Consulting Limited**AUES (ET) – Action-United Environmental Services & Consulting*

Contact Details of Key Personnel for Contract 2 – NE/2016/05

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Mr Leung Chi Foon	3842 7087	2739 0076
AECOM	Chief Resident Engineer	Lee, Yu Ching Paul	5723 6880	2473 3221
AECOM	Senior Resident Engineer	Bill Hon	5599 1466	2473 3221
ANWR	Independent Environmental Checker	James Choi	2618 2836	3007 8648
KOCCL	Project Director	Ambrose Kwong	2889 2675	2558 6900
KOCCL	Site Agent	Mr. Albert PK Ng	9150 1523	2558 6900
KOCCL	Safety and Environmental Manager	Joly C K Kwong	6111 5711	2558 6900
KOCCL	Environmental Officer	Kenny Chan	5542 4335	2558 6900
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:*CEDD (Employer) – Civil Engineering and Development Department**AECOM (Engineer) – AECOM Asia Co. Ltd.**KOCCL (Main Contractor) –Kwan On Construction Company Limited**ANWR (IEC) –ANewR Consulting Limited**AUES (ET) – Action-United Environmental Services & Consulting*

Contact Details of Key Personnel for Contract 3 –NE/2017/03

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Mr Leung Chi Foon	3842 7087	2739 0076
AECOM	Chief Resident Engineer	Lee, Yu Ching Paul	5723 6880	2473 3221
AECOM	Senior Resident Engineer	Brad Chan	5506 0068	2473 3221
ANWR	Independent Environmental Checker	James Choi	2618 2836	3007 8648
CW – CMGC - JV	Construction Manager	William Leung	9464 1392	3965 9900
CW – CMGC - JV	Site Agent	Yu, Chi Kuen Paul	9456 9819	3965 9900
CW – CMGC - JV	Environmental Officer	King Lam	9570 6187	3965 9900
CW – CMGC - JV	Environmental Supervisor	Anna Tsang	9333 8499	3965 9900
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:*CEDD (Employer) – Civil Engineering and Development Department**AECOM (Engineer) – AECOM Asia Co. Ltd.**CW – CMGC - JV (Main Contractor) – Chun Wo- CMGC - Joint Venture**ANWR (IEC) –ANewR Consulting Limited**AUES (ET) – Action-United Environmental Services & Consulting*

Contact Details of Key Personnel for Contract 4 –ED/2020/02

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Mr Leung Chi Foon	3842 7087	2739 0076
AECOM	Chief Resident Engineer	Lee, Yu Ching Paul	5723 6880	2473 3221
AECOM	Senior Resident Engineer	Li, Ling Tommy	9389 8792	2473 3221
ANEWR	Independent Environmental Checker	James Choi	2618 2836	3007 8648
CIWEC	Project Director	Leung, Siu Ming Wilson	5135 6590	2508 0987
CIWEC	Site Agent	Tam. Wing San Wilson	9031 5600	2508 0987
CIWEC	Environmental Officer	Cat Ng	6162 4944	2508 0987
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:*CEDD (Employer) – Civil Engineering and Development Department**AECOM (Engineer) – AECOM Asia Co. Ltd.**CIWEC (Main Contractor) –China International Water & Electric Corporation**ANEWR (IEC) –ANewR Consulting Limited**AUES (ET) – Action-United Environmental Services & Consulting*

Contact Details of Key Personnel for Contract 5 –ED/2019/02

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
CEDD	Engineer	Mr Leung Chi Foon	3842 7087	2739 0076
AECOM	Chief Resident Engineer	Lee, Yu Ching Paul	9824 7016	2473 3221
AECOM	Senior Resident Engineer	Bill Hon	5599 1486	2473 3221
ANWR	Independent Environmental Checker	James Choi	2618 2836	3007 8648
WL-UJV	Construction Manager	PH Ho	9464 1392	2983 6640
WL-UJV	Site Agent	Lee Chi Wai	9255 7014	2983 6640
WL-UJV	Environmental Officer	Guo Liming	5723 9883	2983 6640
AUES	Environmental Team Leader	T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Ben Tam	2959 6059	2959 6079

Legend:*CEDD (Employer) – Civil Engineering and Development Department**AECOM (Engineer) – AECOM Asia Co. Ltd.**WL–UJV (Main Contractor) – Wing Lee – Univac Joint Venture**ANWR (IEC) – ANewR Consulting Limited**AUES (ET) – Action-United Environmental Services & Consulting*

Appendix C

Construction Programme

- (a) Contract 1 (NE/2016/01)**
- (b) Contract 2 (NE/2016/05)**
- (c) Contract 3 (NE/2017/03)**
- (d) Contract 4 (ED/2020/02)**
- (e) Contract 5 (ED/2019/02)**

Contract 1 (NE/2016/01)

Anderson Rd Sub-programme (September 2022 _0) _ccn _220913							
Fresh Water Pumping Station							
Stage 5 - ABWF, Finishing & E&M							
FWP-1320	Pumping Station E&M works	0			667	29-Jun-20 A	23-Sep-22
FWP-1322	Draw pits and cabling works (Pumping Station)	0			600	16-Sep-20 A	23-Sep-22
FWP-1330	E&M T&C works (Pumping Station)	0			26	08-Oct-22	07-Nov-22
Salt Water Reservoir							
ABWF, Finishing & E&M							
SWR-1420	Saltwater Reservoir E&M works	0			692	29-May-20 A	23-Sep-22
SWR-1422	Draw pits and cabling works (Saltwater Reservoir)	0			600	16-Sep-20 A	23-Sep-22
Fresh Water Reservoir							
ABWF, Finishing & E&M							
FWR-2000	Freshwater Reservoir E&M works	0			591	12-Oct-20 A	08-Oct-22
Temporary DN450 Water Pipe at Anderson No.3 Reservoir							
FWR-2020	Pipe works	0			170	01-Mar-22 A	23-Sep-22
FWR-2040	Pipe testing	0			8	24-Sep-22	05-Oct-22
FWR-2060	Pipe sterilization & water supply from Anderson Road to Reservoir	0			11	06-Oct-22	18-Oct-22
RWS Access Road & External Works							
FWP-1430	CLP power supply duct	0			601	16-Sep-20 A	24-Sep-22
FWP-1440	Road Works & Fencing	0			103	26-Sep-22	31-Jan-23
FWP-1450	Green Roof & Paving Area	0			88	21-Oct-22	06-Feb-23
Pedestrian Connection System A & B							
PC system B							
PCB-1090	System B - Backfill south tower	81	19-Aug-19	23-Nov-19	768	16-Feb-20 A	16-Sep-22
PCB-1100	System B - Backfill north tower	81	19-Aug-19	23-Nov-19	768	16-Feb-20 A	16-Sep-22
PCB-1120	System B - E&M	22	23-Sep-19	19-Oct-19	694	05-Jun-20 A	05-Oct-22
PCB-1122	System B - energizing (by CLP)	0			19	22-Oct-22	12-Nov-22
PCB-1130	System B - E&M T&C	24	21-Oct-19	16-Nov-19	513	02-Mar-21 A	19-Nov-22
PCB-1140	System B - Lift installation	75	21-Oct-19	18-Jan-20	513	02-Mar-21 A	19-Nov-22
PCB-1150	System B - Lift T&C	27	20-Jan-20	22-Feb-20	27	21-Nov-22	21-Dec-22
PC system A							
PCA-1060	B5 - E&M and BS Works	0			373	02-Jul-21 A	29-Sep-22
PCA-1070	B5 - ABWF Works	0			260	20-Dec-21 A	05-Nov-22
PCA-1080	B5 - Testing & Commissioning	0			90	07-Nov-22	24-Feb-23
PCA-1160	C1a - Back Fill Lift Tower (South) upwards Formation Level	0			278	18-Oct-21 A	22-Sep-22
PCA-1170	C1a - E&M and BS Works	0			262	22-Nov-21 A	11-Oct-22
PCA-1180	C1a - ABWF Works	0			229	03-Jan-22 A	11-Oct-22
PCA-1190	C1a - Testing & Commissioning	0			90	12-Oct-22	30-Jan-23
Underpass Tunnel							
East Portal							
TUN-3620	Tunnel - backfill to east portal	0			191	01-Apr-22 A	21-Nov-22
VE Panels, Road Works, E&M							
TUN-3530A	(NOC(TBA)) 5th wave COVID19 affected to works in Tunnel	0			165	28-Feb-22 A	16-Sep-22

<h3>3-month Rolling Programme</h3> <p>Anderson Rd Sub-programme</p> <p>15 Sep 22</p>	Date	Revision	Checked	Approved
	15-Sep-22	C1-MPU202209		

Page 2 of 3

 Planned Bar (WP)  Planned Milestone (WP)  Actual Bar  Milestone  Forecast Bar	<div> <div>3-month Rolling Programme</div> <div>Anderson Rd Sub-programme</div> <div>15-Sep-22</div> </div>	Date	Revision	Checked	Approved
		15-Sep-22	C1-MPU202209		

		CONTRACT NO.NE/2016/01 SITE FORMATION AND INFRASTRUCTURE WORKS FOR DEVELOPMENT OF ANDERSON ROAD QUARRY SITE 3-MONTH ROLLING PROGRAMME						Page 3 of 3					
Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	At Completion Duration	Start	Finish	Qtr 3, 2022		Qtr 4, 2022			
								Aug	Sep	Oct	Nov	Dec	
RL3-2010	Carriageway works (Road L3)	0			179	03-May-22 A	02-Dec-22						Carriageway works (R
RL3-2030	Footpath & cycle track (Road L3)	0			66	17-Nov-22	07-Feb-23						
RL4-2010	Carriageway works (Road L4)	0			50	04-Nov-22	03-Jan-23						
RL4-2030	Footpath & cycle track (Road L4)	0			52	03-Dec-22	07-Feb-23						
Hiking Trail Connecting to Wison Trail (Portion B5)													
Construction works at Hiking Trail													
HIK10130	(NOC215) Delay due to Design review on Hiking Trail	0			383	06-Jul-21 A	17-Oct-22						(NOC215) Delay due to Design review on Hiking Trail
HIK10150	Resume work - Construction of Dwarf Walls for Hiking Trail (SP001 to SP001A)	0			78	18-Oct-22	18-Jan-23						
HIK10250	Slope works at Portion B5	0			497	14-Jun-21 A	13-Feb-23						

Contract 2 (NE/2016/05)

ID	Task Name	Duration	Start	Finish	Predecessors	Successors	Timeline																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
							August	September	October	November	December	1st Half	January	February	March	April	May	June	2nd Half	July	August	September	October	November	December	1st Half	January	February																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
1	NE/2016/05	457 days	Tue 3/8/21	Mon 6/2/23																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

ID	Task Name	Duration	Start	Finish	Predecessors	Successors	Calendar																																	
							1st Half							2nd Half							1st Half							2nd Half												
							August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February			
							E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E

174	Excavation of Sump Pit	69 days	Sat 9/10/21	Fri 31/12/21	136	175
175	Construction of Sump Pit	28 days	Mon 3/1/22	Mon 7/2/22	174	184
176	Construction of Footing of Covered Walkway	40 days	Mon 20/6/22	Fri 5/8/22	155	177
177	Backfilling and Compaction Test	6 days	Sat 6/8/22	Fri 12/8/22	176	192,206,180
178	Installation of Steel Frame (Covered Walkway)	28 days	Wed 21/9/22	Sat 22/10/22	193	179
179	Installation of Roofing (Covered Walkway)	28 days	Mon 24/10/22	Thu 24/11/22	178	183,185,186,184
180	Construction of E2 Pillar Box (Civil)	28 days	Sat 13/8/22	Wed 14/9/22	177	181,182
181	Construction of E2 Pillar Box (E&M)	12 days	Thu 15/9/22	Wed 28/9/22	180	182,257
182	E2 Pillar Energized from E3 Pillar	1 day	Fri 30/9/22	Fri 30/9/22	257,180,181	202
183	Construction of Pavement	28 days	Fri 25/11/22	Tue 27/12/22	179	
184	Installation of E&M Works (Pump & Lighting)	21 days	Fri 25/11/22	Mon 19/12/22	175,179	
185	Installation of Irrigation Pipe	6 days	Fri 25/11/22	Thu 1/12/22	179	
186	Fall Arrest System	6 days	Fri 25/11/22	Thu 1/12/22	179	
187	E2 Lift Tower	342 days	Tue 14/9/21	Sat 5/11/22		
188	Scaffolding Modification	6 days	Tue 14/9/21	Mon 20/9/21		189,190,191
189	Window and Louvre Installation	28 days	Tue 21/9/21	Tue 26/10/21	188	199
190	Tiling Works on Wall	28 days	Fri 15/10/21	Tue 16/11/21	188	
191	Waterproofing Works	5 days	Fri 15/10/21	Wed 20/10/21	188	
192	Erect Falseworks for E2-LT1 RC Decking at +66.3mPD	12 days	Sat 13/8/22	Fri 26/8/22	177	193,208
193	Construction of E2-LT1 RC Decking at +66.3mPD	21 days	Sat 27/8/22	Tue 20/9/22	192	196,178,194
194	Erect Falseworks for E2-LT1 Staircase Landing at +62.85mPD	12 days	Wed 21/9/22	Tue 4/10/22	193	195
195	Construction of E2-LT1 Staircase Landing at +62.85mPD	12 days	Wed 5/10/22	Tue 18/10/22	194	
196	Installation of Steel Frame (E2-LT1 Canopy)	12 days	Wed 21/9/22	Tue 4/10/22	193	197,198
197	Installation of Railing	12 days	Wed 5/10/22	Tue 18/10/22	196	203
198	Tiling Works	28 days	Wed 5/10/22	Sat 5/11/22	196	
199	E&M Works	28 days	Wed 27/10/21	Sat 27/11/21	189	200,201
200	Cabling for Permanent Power	12 days	Mon 29/11/21	Sat 11/12/21	199	203
201	Lift Installation	85 days	Fri 28/1/22	Tue 17/5/22	199	203,202
202	Lift T&C	12 days	Sat 1/10/22	Fri 14/10/22	201,257,182	203
203	LES Submission to EMSD	1 day	Wed 19/10/22	Wed 19/10/22	201,200,197,257,202	204
204	Use Permit for E2-LT1	14 days	Thu 20/10/22	Fri 4/11/22	203	310
205	E2-PC2 Pile Cap	47 days	Sat 13/8/22	Thu 6/10/22		
206	Excavation for Column Construction	3 days	Sat 13/8/22	Tue 16/8/22	177	207
207	Construction of Column	12 days	Wed 17/8/22	Tue 30/8/22	206	208
208	Construction of Pier Head and Corbal	18 days	Wed 31/8/22	Tue 20/9/22	207,192	211,209,210
209	Concrete Curing for Pier Head and Corbal	14 days	Wed 21/9/22	Thu 6/10/22	208	
210	Bearing Installation	3 days	Wed 21/9/22	Fri 23/9/22	208	
211	Drainage	28 days	Wed 21/9/22	Sat 22/10/22	208	212
212	Reinstatement	12 days	Mon 24/10/22	Sat 5/11/22	211	
213	E3-LT1 Lift TowerPortion 2	433 days	Tue 31/8/21	Mon 6/2/23		
214	E3-LT1 Lift tower structure	57 days	Tue 31/8/21	Mon 8/11/21		
219	E3-ST1 Staircase (landing & stairs)	201 days	Fri 4/3/22	Wed 2/11/22		
220	1st pour (+25.0 - +28.6mPD)	7 days	Fri 4/3/22	Fri 11/3/22	218	221
221	2nd pour (+28.6 - +32.2mPD)	10 days	Thu 14/4/22	Thu 28/4/22	220	222
222	3rd pour (+32.2 - +35.8mPD)	14 days	Fri 29/4/22	Tue 17/5/22	221	223
223	4th pour (+35.8 - +38.8mPD)	14 days	Wed 18/5/22	Thu 2/6/22	222	224
224	5th pour (+38.8 - +41.8mPD)	14 days	Sat 4/6/22	Mon 20/6/22	223	225
225	6th pour (+41.8 - +45.4mPD)	14 days	Tue 21/6/22	Thu 7/7/22	224	226
226	7th pour (+45.4 - +49.0mPD)	14 days	Wed 13/7/22	Thu 28/7/22	225	227
227	8th pour (+49.0 - +52.6mPD)	14 days	Fri 29/7/22	Sat 13/8/22	226	228
228	9th pour (+52.6 - +56.2mPD)	14 days	Mon 15/8/22	Tue 30/8/22	227	229
229	10th pour (+56.2 - +59.7mPD)	15 days	Wed 31/8/22	Fri 16/9/22	228	230
230	11th pour (+59.7 - +63.3mPD)	16 days	Sat 17/9/22	Wed 5/10/22	229	231
231	12th pour (+63.3mPD)	8 days	Thu 6/10/22	Fri 14/10/22	230	232,252
232	13th pour (+66.5mPD)	8 days	Sat 15/10/22	Mon 24/10/22	231	233
233	14th pour (+70.45mPD)	8 days	Tue 25/10/22	Wed 2/11/22	232	266,239
234	Erection of small crane at roof	7 days	Mon 22/8/22	Mon 29/8/22	156	235
235	Removal of tower crane & footing	7 days	Tue 30/8/22	Tue 6/9/22	234,161	237
236	Reinstatement works for tower crane slab	63 days	Wed 7/9/22	Fri 18/11/22		
237	Slab Opening Reinstatement	56 days	Wed 7/9/22	Thu 10/11/22	235	238,266
238	Parapet Wall (Remaining)	7 days	Fri 11/11/22	Fri 18/11/22	237	246,247,239
239	Removal of small crane	14 days	Sat 19/11/22	Mon 5/12/22	238,233	
240	Steel truss - welding works & welding test	31 days	Thu 23/9/21	Sun 31/10/21		241,242
241	Window installation	45 days	Tue 10/5/22	Sat 2/7/22	240	243
242	Louvre installation	45 days	Tue 10/5/22	Sat 2/7/22	240	243
243	Water tightness test for E3-LT1 louvre / windows	12 days	Mon 4/7/22	Sat 16/7/22	241,242	244SS,245SS,251,268
244	Tiles (Wall/Staircase/Floor)	90 days	Mon 4/7/22	Sat 15/10/22	243SS	249

Project: NE201605_Programme_20

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

Page 2

ID	Task Name	Duration	Start	Finish	Predecessors	Successors	Calendar																											
							1st Half						2nd Half						1st Half						2nd Half									
							August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July				
							E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E			
245	Paint	90 days	Mon 4/7/22	Sat 15/10/22	243SS	249																												
246	Fall Arrest System (Roof)	6 days	Sat 19/11/22	Fri 25/11/22	238																													
247	Waterproof (Roof)	6 days	Sat 19/11/22	Fri 25/11/22	238																													
248	Water tightness test for E3-LT1 roof	4 days	Sat 26/11/22	Wed 30/11/22	247	249																												
249	Dismantle of scaffolding working platform	30 days	Thu 1/12/22	Wed 4/1/23	248,244,245	250																												
250	Glass canopy at G/F	15 days	Thu 5/1/23	Sat 21/1/23	249																													
251	Install inclined plate at the recess of Windows & Louvres	59 days	Mon 18/7/22	Fri 23/9/22	243																													
252	Railing (GMS) on staircase	59 days	Sat 15/10/22	Thu 22/12/22	231																													
253	E&M works	317 days	Mon 18/10/21	Mon 7/11/22																														
254	Excavation and Laying Cable by CLP (Next to HD Site)	30 days	Mon 4/7/22	Sat 6/8/22		255,257																												
255	Excavation by KO and Laying Cable by CLP (Outside E3-LT1)	14 days	Mon 8/8/22	Tue 23/8/22	254	257																												
256	E3 Pillar Box (Civil)	65 days	Mon 18/10/21	Tue 4/1/22		263																												
257	E3 Pillar Energized by CLP	1 day	Thu 29/9/22	Thu 29/9/22	181,254,255	270,203,202,182,271																												
258	Telemetry Duct	47 days	Mon 4/7/22	Fri 26/8/22		259SS																												
259	Drainage Manhole	109 days	Mon 4/7/22	Mon 7/11/22	258SS																													
260	Electrical installation	329 days	Tue 9/11/21	Tue 13/12/22																														
261	Lift Shafts	90 days	Tue 9/11/21	Mon 28/2/22	218	264																												
262	Sump Pit (E&M)	30 days	Thu 26/5/22	Thu 30/6/22																														
263	Pillar Box (E&M)	82 days	Wed 5/1/22	Thu 14/4/22	256																													
264	Lighting	31 days	Mon 4/7/22	Mon 8/8/22	261																													
265	Machine room (Above Lift Shaft)	28 days	Mon 25/4/22	Sat 28/5/22		266																												
266	Machine room (Above E3-ST1 Staircase & Tower Crane)	28 days	Fri 11/11/22	Tue 13/12/22	237,265,233	271,270																												
267	Lift installation	159 days	Mon 18/7/22	Wed 18/1/23																														
268	Lift Car Installation	90 days	Mon 18/7/22	Sat 29/10/22	243	269SS,270,271																												
269	Door frames / Misc.	90 days	Mon 18/7/22	Sat 29/10/22	268SS	270,271																												
270	Self test	30 days	Wed 14/12/22	Tue 17/1/23	257,268,269,266																													
271	T&C	30 days	Wed 14/12/22	Tue 17/1/23	266,257,268,269	272																												
272	Submit LE5 to EMSD	1 day	Wed 18/1/23	Wed 18/1/23	271	273																												
273	Pre-handing over inspection (E3-LT1 & E3-FB1) by HyD/Structure	15 days	Thu 19/1/23	Sat 4/2/23	272	274																												
274	Ready to open Lift Tower E3-LT1 / Footbridge E3-FB1 to public	1 day	Mon 6/2/23	Mon 6/2/23	273																													
275																																		
276	Portion 3	414 days	Mon 20/9/21	Fri 3/2/23																														
277	E2-FB1 Bridge	414 days	Mon 20/9/21	Fri 3/2/23																														
278	Shop Drawing Approval of E3-FB1	7 days	Mon 20/9/21	Tue 28/9/21		279																												
279	Procurement of Material for E3-FB1	45 days	Mon 4/10/21	Thu 25/11/21	278	281																												
280	E2-FB1 - 1st Span (Housing Lift Tower to E2-P2)	215 days	Fri 21/1/22	Tue 11/10/22																														
281	Bridge Erection (Only allow on Sat to Sun / Public Holiday)	2 days	Fri 21/1/22	Sun 23/1/22	279	282																												
282	Remaining Steelworks before Bridge Deck Casting	6 days	Mon 24/1/22	Sat 29/1/22	281	283																												
283	Concreting Bridge Deck	12 days	Tue 2/8/22	Mon 15/8/22	282,311	284,286,285																												
284	Construction of RC Planter	28 days	Tue 16/8/22	Fri 16/9/22	283	292,291,285																												
285	Floor Tiling	21 days	Sat 17/9/22	Tue 11/10/22	283,284																													
286	Erection of Scaffolding	10 days	Tue 16/8/22	Fri 26/8/22	283	287,288,289,290																												
287	Installation of Corrugated Roof Panel & Gutter	21 days	Sat 27/8/22	Tue 20/9/22	286	290,293,294,288																												
288	Installation of GRP Feature	12 days	Wed 21/9/22	Tue 4/10/22	286,287	294																												
289	Installation of E&M Works incl. Unistruct & Lighting	28 days	Sat 27/8/22	Wed 28/9/22	286	294																												
290	Installation of Downpipe	6 days	Wed 21/9/22	Tue 27/9/22	287,286	294																												
291	Installation of Railing	12 days	Sat 17/9/22	Fri 30/9/22	284																													
292	Installation of Irrigation System	6 days	Sat 17/9/22	Fri 23/9/22	284	294																												
293	Fall Arrest System	6 days	Wed 21/9/22	Tue 27/9/22	287	294																												
294	Dismantling of Scaffolding	6 days	Wed 5/10/22	Tue 11/10/22	288,289,290,292,287,293																													
295	E2-FB1 - 2nd Span (E2-P2 to E2-LT1)	102 days	Sat 8/10/22	Fri 3/2/23																														
296	Bridge Lifting (Only allow on Sat to Sun / Public Holiday)	2 days	Sat 8/10/22	Mon 10/10/22		297																												
297	Remaining Steelworks before Bridge Deck Casting	6 days	Tue 11/10/22	Mon 17/10/22	296	299,298																												
298	Erection of Scaffolding	10 days	Tue 18/10/22	Fri 28/10/22	297	299																												
299	Concreting Bridge Deck	12 days	Sat 29/10/22	Fri 11/11/22	297,298	300,301																												
300	Construction of RC Planter	28 days	Sat 12/11/22	Wed 14/12/22	299	306,307,301,302																												
301	Floor Tiling	21 days	Thu 15/12/22	Sat 7/1/23	299,300																													
302	Installation of Corrugated Roof Panel & Gutter	21 days	Thu 15/12/22	Sat 7/1/23	300	308,305,303,309,304SS+10 day																												
303	Installation of GRP Feature	12 days	Mon 9/1/23	Sat 21/1/23	302	309																												
304	Installation of E&M Works incl. Unistruct & Lighting	28 days	Tue 27/12/22	Fri 27/1/23	302SS+10 days	309,310																												
305	Installation of Downpipe	6 days	Mon 9/1/23	Sat 14/1/23	302	309																												
306	Installation of Irrigation System	6 days	Thu 15/12/22	Wed 21/12/22	300	309																												
307	Installation of Railing	12 days	Thu 15/12/22	Wed 28/12/22	300	310																												
308	Fall Arrest System	6 days	Mon 9/1/23	Sat 14/1/23	302	309																												
309	Dismantling of Scaffolding	6 days	Sat 28/1/23	Fri 3/2/23	303,304,305,306,308,302																													
310	Ready to open Lift Tower E2-LT1 & E2-FB1	1 day	Sat 28/1/23	Sat 28/1/23	307,304,204																													
311	Underground Drainage	60 days	Sat 21/5/22	Mon 1/8/22		312,283																												

Project: NE201605_Programme_20

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress


Manual Progress

Page 3

Contract 3 (NE/2017/03)

Activity ID	Activity Name	Duration	Start	Finish	2022				
					Sep 57	Oct 58	Nov 59	Dec 60	
NE2017/03 - ARQ PHASE 2A - Monthly Programme Update (202209)-0 _220921		1156	04-Nov-20 A	20-Oct-23					
Road Improvement Works Location 1 (RIW1)		738	04-Nov-20 A	05-May-23					
Construction Works		738	04-Nov-20 A	05-May-23					
CON10650	Construct RW wall (RWC2 type 1a & 1 [Bay 2 to Bay 1])	225	04-Nov-20 A	28-Sep-22					
CON10268	(NCE178) Trial pit excavation (RWC2 type 5)	60	21-Sep-21 A	20-Oct-22					
CON12650	Prepare TTA scheme & TMLG procedure for TTA setup at CT6 PC1 to PC3	120	10-May-22 A	29-Sep-22					
CON10650A	(NCE148) Inclement weather 21/5/2021 to 20/6/2021 RWC2 type 1a, 1 & 2	12	19-Jul-22 A	12-Oct-22					
CON12372	ELS works (KS27 east side)	60	01-Aug-22 A	12-Oct-22					
CON11550A	Gas Main Diversion Works	29	11-Aug-22 A	31-Oct-22					
CON10231E	(CE358) Watermain diversion due to unforeseen ground condition (by WSD &	30	17-Aug-22 A	02-Nov-22					
CON10271	Further ELS to RWC2 type 5 due to unforeseen ground utilities	54	31-Aug-22 A	05-Jan-23					
CON12356I	(NCE210) Inclement weather (21/7/2022 to 20/8/2022) on KS27 west side	17	05-Sep-22 A	24-Sep-22					
CON10750B	(NCE201) Inclement weather (21/5/2022 to 20/6/2022) on RIW1 RWC2 type :	6	16-Sep-22 A	22-Sep-22					
CON10750D	(NCE202) Inclement weather (21/6/2022 to 20/7/2022) on RIW1 RWC2 type :	6	23-Sep-22	29-Sep-22					
CON12356J	(NCE[TBA]) Inclement weather (21/8/2022 to 20/9/2022) on KS27 west side	9	26-Sep-22	07-Oct-22					
CON12690	Modification existing TTA, Site formation works, construct temporary road, pre-c	96	30-Sep-22*	28-Jan-23					
CON10750F	(NCE210) Inclement weather (21/7/2022 to 20/8/2022) on RIW1 RWC2 type :	17	30-Sep-22	21-Oct-22					
CON10650B	(NCE153) Inclement weather 21/6/2021 to 20/7/2021 RWC2 type 1a, 1 & 2	12	12-Oct-22	26-Oct-22					
CON12372A	(NCE[TBA]) Inclement weather (21/8/2022 to 20/9/2022) on KS27 east side	9	13-Oct-22	22-Oct-22					
CON10390	Construct pile cap (RWC2 type 5 [bay 46])	77	21-Oct-22	21-Jan-23					
CON10750H	(NCE[TBA]) Inclement weather (21/8/2022 to 20/9/2022) on RIW1 RWC2 type	9	22-Oct-22	01-Nov-22					
CON12410	Application for power supply & energization (KS27)	156	24-Oct-22	05-May-23					
CON12390	ELS works & construct subway footing (KS27 east side)	90	24-Oct-22	11-Feb-23					
CON10650C	(NCE157) Inclement weather 21/7/2021 to 20/8/2021 RWC2 type 1a, 1 & 2	11	26-Oct-22	08-Nov-22					
CON11552	Install sheet pile for pile cap construction (FE1-PC1b, 32m, 1m/d)	14	01-Nov-22	16-Nov-22					
CON10752	Install sheet pile & ELS to RW pile cap (RWC2 type 3, stage 1)	72	02-Nov-22	31-Jan-23					
CON10240	Existing sewage drainage pipe diversion (lower stream)	28	03-Nov-22	05-Dec-22					
CON10652	Construct RW footing (RWC2 type 2)	60	08-Nov-22	20-Jan-23					
CON11554	ELS works for pile cap construction (FE1-PC1b, 32m, 1m/d)	36	17-Nov-22	30-Dec-22					
Road Improvement Works Location 2 (RIW2)		466	23-Aug-22 A	15-Jul-23					
Construction Works in Slope C3 (Portion B)		109	10-Sep-22 A	27-Dec-22					
CON20790D	(NCE[TBA]) Inclement weather 21/8/2022 to 20/9/2022 at RWC3	9	10-Sep-22 A	21-Sep-22					
CON20170	Fabrication of NB steel post - along slope side	70	19-Oct-22	27-Dec-22					
Construction Noise Semi-Enclosure SE2 (Portion C)		379	23-Aug-22 A	15-Jul-23					
CON219671A	(NCE208) Excavation & Install additional sheet pile for exposed 132kV cable p	60	23-Aug-22 A	28-Nov-22					
CON21774	Install pipe pile wall at CT4 road side (46nos, 2no/d 1 team + setup)	36	27-Aug-22 A	11-Oct-22					
CON21968	(NCE208) Construct piling fdn SE2 Bay13 to Bay21 (95nos, 2d/no. 1 team + s	200	30-Aug-22 A	14-Jul-23					
CON21660	(CE332) Excavate trial trench, SLG meeting & UU portection works	24	03-Sep-22 A	03-Oct-22					
CON219662C	(NCE210) Inclement weather 21/7/2022 to 20/8/2022 at SE2 (Bay13 to Bay11	17	15-Sep-22 A	06-Oct-22					
CON22590	Road lighting, irrigation system & utilities works	240	21-Sep-22	15-Jul-23					
CON22570	Slope impovement Works (pit-by-pit method) (CT4 & SE2 fount part, 250nos f	120	21-Sep-22	16-Feb-23					
CON22610	Application for power supply & energization (RIW2)	156	21-Sep-22	30-Mar-23					
CON21658	(CE332) Construct piling fdn of SE2 (Bay9 to Bay12, stage 2 38nos. 1 team)	30	05-Oct-22	08-Nov-22					
CON219662D	(NCE[TBA]) Inclement weather 21/8/2022 to 20/9/2022 at SE2 (Bay13 to Bay	9	07-Oct-22	17-Oct-22					
CON21776	ELS works at CT4 (12nos. strut, 0.25no/d, 1 team + setup)	48	12-Oct-22	06-Dec-22					
CON21670	Install pipe pile wall at SE2 Bay4 to Bay8 (48m 68no. 1 team + setup)	30	09-Nov-22	13-Dec-22					
Road Improvement Works Location 3 (RIW3)		785	09-Aug-21 A	18-Apr-23					
Construction Works		785	09-Aug-21 A	18-Apr-23					
CON31150	Construct RWD3 (CH60 to CH152)	150	09-Aug-21 A	13-Oct-22					
CON32410	Construct type 2 NB footing (SE1 bay13 to bay8)	150	16-Aug-21 A	10-Nov-22					
CON30170	Slope works & fill no-fine concrete at slope D1 (Level 1/4, 400m3)	72	19-Aug-21 A	27-Oct-22					
CON30410F	JV prepare pipe pile wall design; ICE review & approval; PM review, comment	266	24-Aug-21 A	15-Nov-22					
CON31706A	(RFI295) Design review to footing F1-4	36	15-Feb-22 A	27-Sep-22					
CON30392	Backfill RWD1 (bay10 to bay13)	60	12-Apr-22 A	20-Oct-22					
CON31708B	(NCE200) utility owner design reviewing	42	17-Jun-22 A	20-Oct-22					
CON31424B	(NCE210) Inclement weather (21/7/2022 to 20/8/2022) on RIW3 Slope D4	17	01-Sep-22 A	21-Sep-22					
CON32750	(CE497) Construct footing of RWD2 bay8 & bay9	60	13-Sep-22 A	23-Nov-22					
CON30652B	(NCE202) Inclement weather (21/6/2022 to 20/7/2022) on RIW3 WM	6	15-Sep-22 A	21-Sep-22					
CON32402C	(NCE210) Inclement weather (21/7/2022 to 20/8/2022) on RIW3 SE1 bay8 &	17	16-Sep-22 A	07-Oct-22					
CON30652C	(NCE210) Inclement weather (21/7/2022 to 20/8/2022) on RIW3 WM	17	22-Sep-22	13-Oct-22					
CON31424C	(NCE[TBA]) Inclement weather (21/8/2022 to 20/9/2022) on RIW3 Slope D4	9	22-Sep-22	03-Oct-22					
CON31430	Install safety fencing, from haul road & hoarding (Slope D4, CH275 to CH430)	18	05-Oct-22	25-Oct-22					
CON32402D	(NCE[TBA]) Inclement weather (21/8/2022 to 20/9/2022) on RIW3 SE1 bay8 &	9	08-Oct-22	18-Oct-22					
CON31170	Soil nail works (11NE-D/F246, stage 2)	150	14-Oct-22	18-Apr-23					
CON30652D	(NCE[TBA]) Inclement weather (21/8/2022 to 20/9/2022) on RIW3 WM	9	14-Oct-22	24-Oct-22					
CON32770	(CE497) Construct wall of RWD2 bay8 & bay9	60	20-Oct-22	30-Dec-22					
CON31710	Construct footing, pier & pier head F1-4	144	21-Oct-22	18-Apr-23					
CON30392A	(NCE201) Inclement weather (21/5/2022 to 20/6/2022) on RIW3 WM	6	21-Oct-22	27-Oct-22					
CON30670	Application of TTA/ discussion with WSD for fresh watermain B and salt waterm	60	25-Oct-22	05-Jan-23					
CON31450	Trees felling (Sbpe D4, CH275 to CH430)	24	26-Oct-22	22-Nov-22					

- Actual Work
- Remaining Work
- Milestone

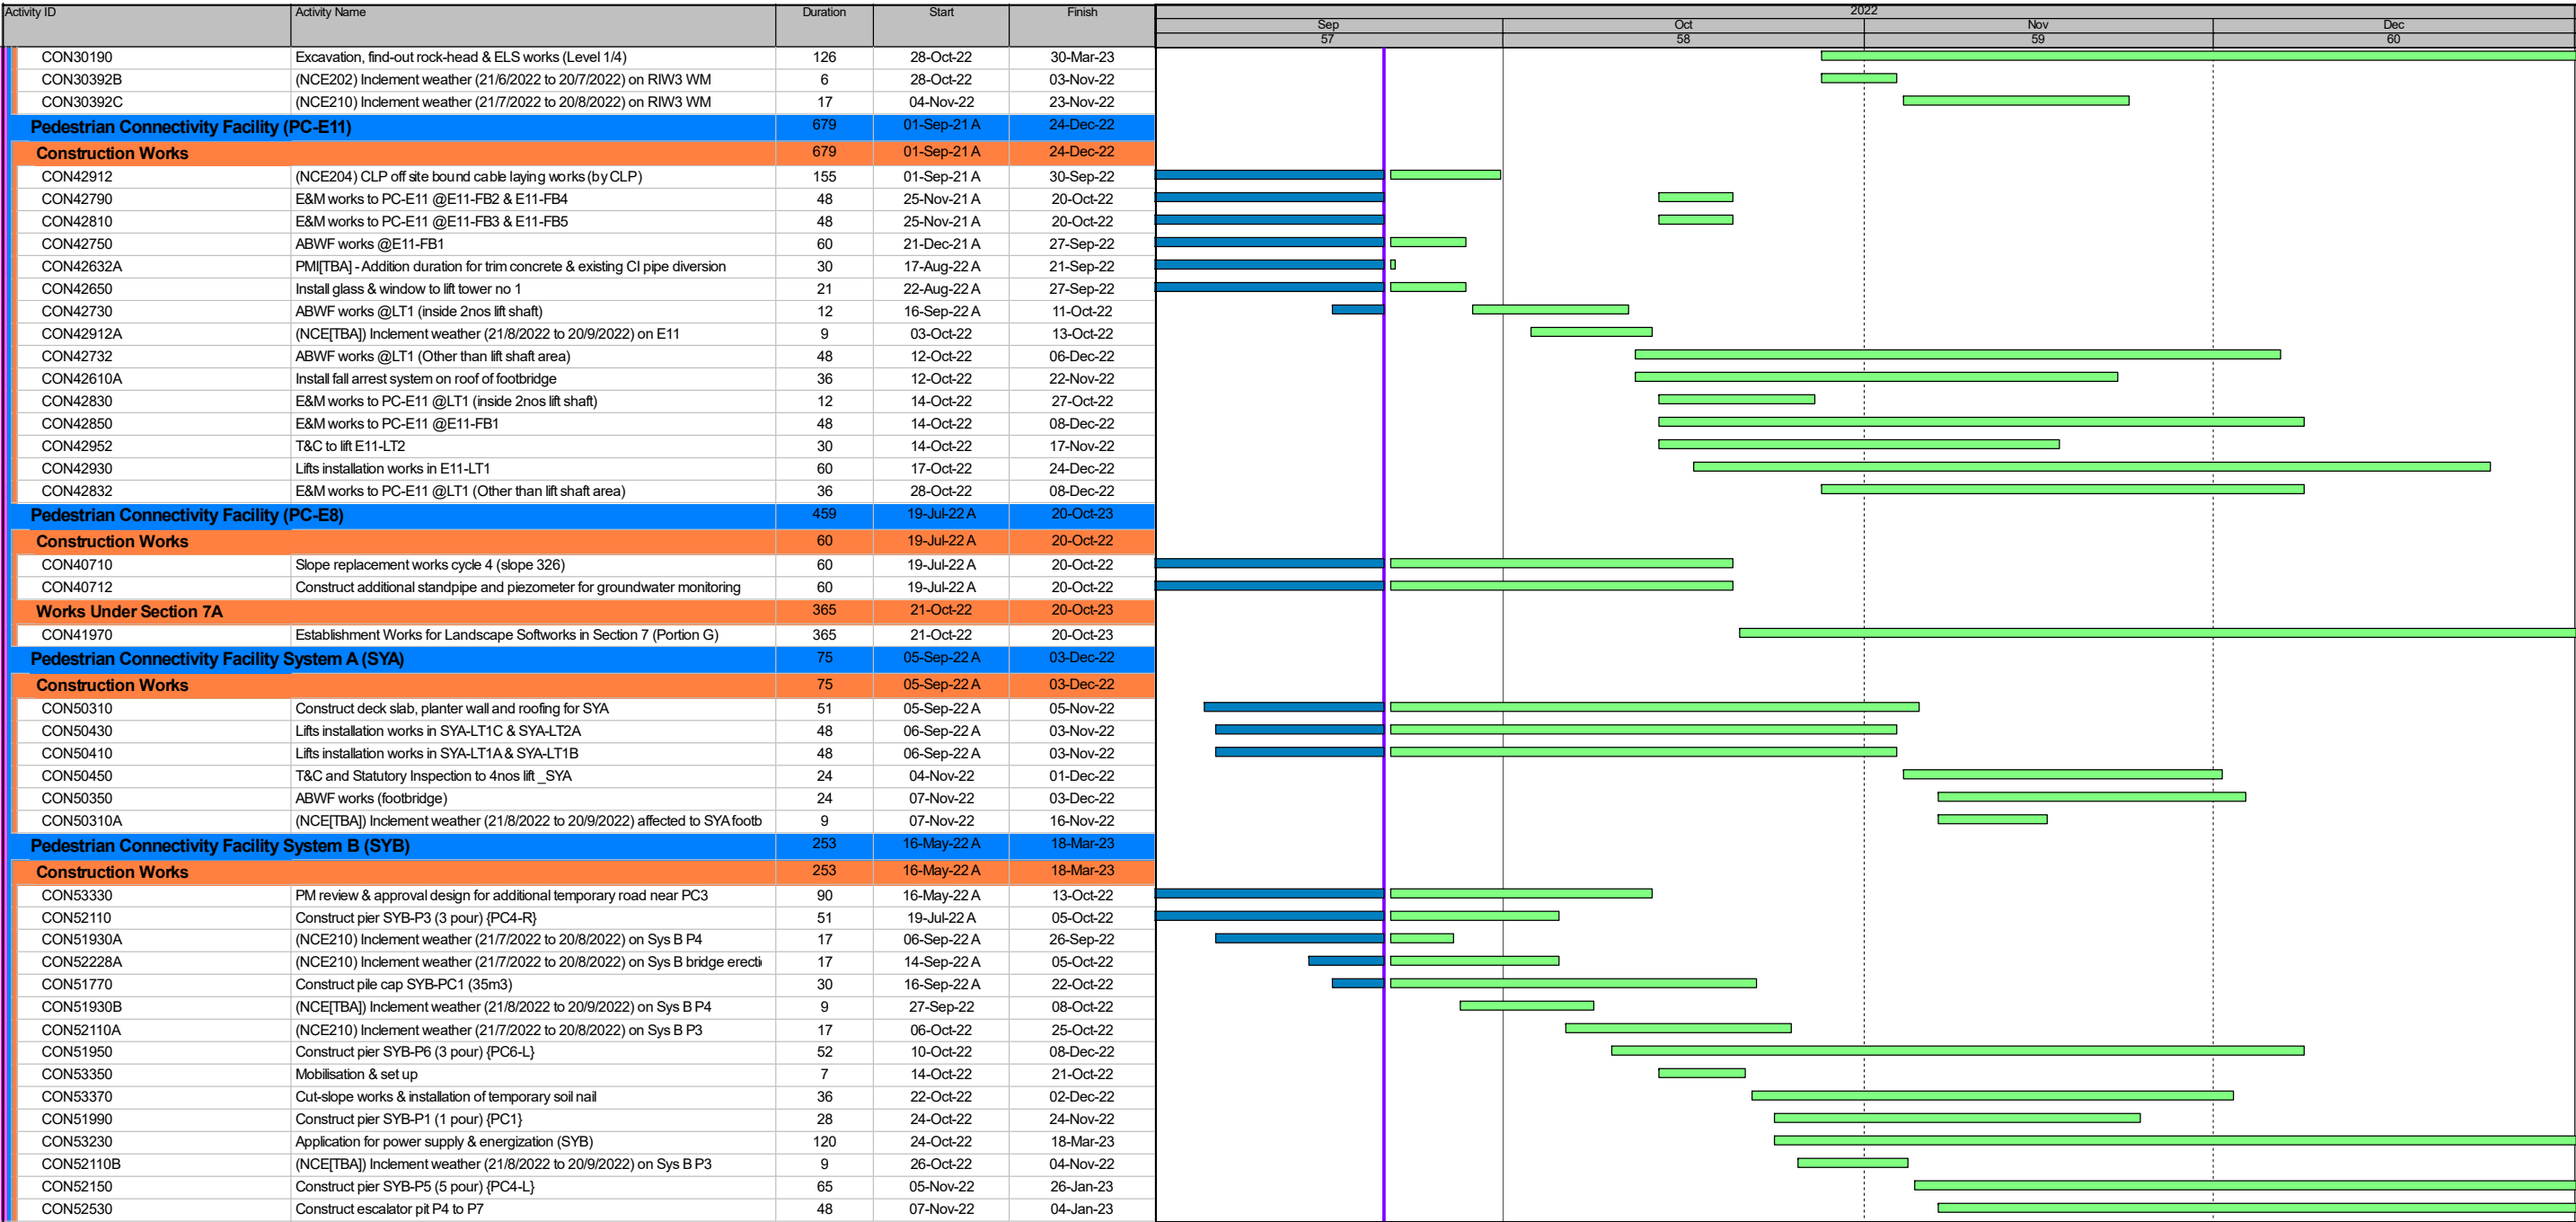

Contract 4 (ED/2020/02)

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负	9月	10月	11月
1 Contract Period	1,341 天	週五 30/7/21	週一 31/3/25	週五 30/7/21	週一 31/3/25				
2 Contract Starting Date [Contract Award Date 21 Jul 2021]	0 天	週五 30/7/21	週五 30/7/21	週五 30/7/21	週五 30/7/21				
3 Contract Duration	1,247 天	週六 31/7/21	週六 28/12/24	週六 31/7/21	週六 28/12/24	2FS+1 天			
4 Original Completion Date	0 天	週六 28/12/24	週六 28/12/24	週日 29/12/24	週日 29/12/24	3			
5 Potential EOT due to CEs and Inclement weather	93 天	週日 29/12/24	週一 31/3/25	週日 29/12/24	週一 31/3/25	4			
6 Completion of the Whole of the Works	0 天	週一 31/3/25	週一 31/3/25	週一 31/3/25	週一 31/3/25	28,39,63,79,94,110,121,138,			
7 Section of Works and Relevant Portions of Work	1,341 天	週五 30/7/21	週一 31/3/25	週五 30/7/21	週一 31/3/25				
8 Section of Works 1 - Portions 1a, 2a & 2b	945 天	週五 30/7/21	週一 31/3/25	週五 30/7/21	週一 31/3/25				
9 Original Completion Date	0 天	週三 13/12/23	週三 13/12/23	週一 14/24	週一 14/24	11FF,16FF,21FF			
10 Access date for Portion 1a	0 天	週五 29/4/22	週五 29/4/22	週五 29/4/22	週五 29/4/22	2			
11 Construction Duration for Portion 1a	594 天	週五 29/4/22	週三 13/12/23	週五 29/4/22	週三 13/12/23	10			
12 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週四 14/12/23	週日 21/1/24	週四 14/12/23	週日 21/1/24	11			
13 Potential EOT due to CEs	70 天	週一 22/1/24	週日 31/3/24	週一 22/1/24	週日 31/3/24	12			
14 Completion of Works in Portion 1a	0 天	週日 31/3/24	週日 31/3/24	週一 14/24	週一 14/24	360,356,352,361,359,13,377FF			
15 Access date for Portion 2a	0 天	週一 30/8/21	週一 30/8/21	週一 30/8/21	週一 30/8/21	2			
16 Construction Duration for Portion 2a	836 天	週一 30/8/21	週三 13/12/23	週一 30/8/21	週三 13/12/23	15			
17 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週四 14/12/23	週日 21/1/24	週四 14/12/23	週日 21/1/24	16			
18 Potential EOT due to CEs	70 天	週一 22/1/24	週日 31/3/24	週一 22/1/24	週日 31/3/24	17			
19 Completion of Works in Portion 2a	0 天	週日 31/3/24	週日 31/3/24	週一 14/24	週一 14/24	18,416FF,420FF,421FF,422FF			
20 Access date for Portion 2b	0 天	週二 14/12/21	週二 14/12/21	週二 22/2/22	週二 22/2/22	2			
21 Construction Duration for Portion 2b	730 天	週二 14/12/21	週三 13/12/23	週二 22/2/22	週三 21/2/22	20			
22 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週四 14/12/23	週日 21/1/24	週四 22/2/22	週日 31/3/22	21			
23 Completion of Works in Portion 2b	0 天	週日 21/1/24	週日 21/1/24	週一 14/24	週一 14/24	445,448,451,452,450,449,22			
24 Section of Works 1A - Establishment Works for all Landscape Softworks in Section 1 of the Works	365 天	週日 31/3/24	週一 31/3/25	週一 14/24	週一 31/3/25				
25 Original Completion Date	0 天	週四 12/12/24	週四 12/12/24	週一 31/3/25	週一 31/3/25	9FS-365 天			
26 Commencement of Establishment Work for Section 1	0 天	週日 31/3/24	週日 31/3/24	週一 14/24	週一 14/24	14,19,23			
27 Establishment Work Duration for Section 1	365 天	週一 14/24	週一 31/3/25	週一 14/24	週一 31/3/25	26			
28 Completion of Works in Section 1	0 天	週一 31/3/25	週一 31/3/25	週一 31/3/25	週一 31/3/25	27,456			
29 Section of Works 2 - Portion 8	769 天	週五 30/7/21	週三 6/9/23	週一 22/2/22	週一 14/24				
30 Access date for Portion 8	0 天	週五 30/7/21	週五 30/7/21	週二 22/2/22	週二 22/2/22	2			
31 Construction Duration for Portion 8	730 天	週五 30/7/21	週六 29/7/23	週二 22/2/22	週三 21/2/22	30			
32 Original Completion Date	0 天	週六 29/7/23	週六 29/7/23	週四 22/2/22	週四 22/2/22	31			
33 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週日 30/7/23	週三 6/9/23	週四 22/2/22	週日 31/3/22	32			
34 Completion of Works in Portion 8	0 天	週三 6/9/23	週三 6/9/23	週一 14/24	週一 14/24	478,481,468,470,472,474,476,			
35 Section of Works 2A - Establishment Works for all Landscape Softworks in Section 2 of the Works	365 天	週二 6/9/23	週四 5/9/24	週一 14/24	週一 31/3/25				
36 Original Completion Date	0 天	週日 28/7/24	週日 28/7/24	週一 31/3/25	週一 31/3/25	32FS-365 天			
37 Commencement of Establishment Work for Section 2	0 天	週三 6/9/23	週三 6/9/23	週一 14/24	週一 14/24	34			
38 Establishment Work Duration for Section 2	365 天	週四 7/9/23	週四 5/9/24	週一 14/24	週一 31/3/25	37			
39 Completion of Works in Section 2	0 天	週四 5/9/24	週四 5/9/24	週一 31/3/25	週一 31/3/25	38,485			
40 Section of Works 3 - Portions 1b, 3, 4, 5	770 天	週五 30/7/21	週四 7/9/23	週六 23/4/22	週一 14/24				
41 Original Completion Date	0 天	週三 31/5/23	週三 31/5/23	週一 14/24	週一 14/24	43FF,48FF-60 天,52FF,56FF			
42 Access date for Portion 1b	0 天	週二 29/11/22	週二 29/11/22	週三 23/8/22	週三 23/8/22	2			
43 Construction Duration for Portion 1b	183 天	週二 29/11/22	週二 30/5/23	週三 23/8/22	週三 21/2/22	42			
44 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週三 31/5/23	週六 8/7/23	週四 22/2/22	週日 31/3/22	43			
45 Completion of Works in Portion 1b	0 天	週六 8/7/23	週六 8/7/23	週一 14/24	週一 14/24	499,498,496,44			
46 Access date for Portion 3	0 天	週三 29/9/21	週三 29/9/21	週六 23/4/22	週六 23/4/22	2			
47 PMI 003 & 004 issued	61 天	週三 29/9/21	週日 28/11/21	週六 23/4/22	週三 22/6/22	46			
48 Construction Duration for Portion 3	609 天	週日 28/11/21	週六 29/7/23	週四 23/6/22	週三 21/2/22	47FS-1 天			
49 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週日 30/7/23	週三 6/9/23	週四 22/2/22	週日 31/3/22	48			
50 Completion of Works in Portion 3	0 天	週四 7/9/23	週四 7/9/23	週一 14/24	週一 14/24	507,49			
51 Access date for Portion 4	0 天	週五 30/7/21	週五 30/7/21	週六 23/4/22	週六 23/4/22	2			
52 Construction Duration for Portion 4	670 天	週五 30/7/21	週二 30/5/23	週六 23/4/22	週三 21/2/22	51			
53 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週三 31/5/23	週六 8/7/23	週四 22/2/22	週日 31/3/22	52			
54 Completion of Works in Portion 4	0 天	週日 9/7/23	週日 9/7/23	週一 14/24	週一 14/24	512,53			
55	0 天	週日 9/7/23	週日 9/7/23	週一 14/24	週一 14/24	514,53			

China International Water

Task

Critical Task

Milestone

◆

Summary

◆

Updated on: 22 Aug 2022

Page 1/18

29/11

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负	9月	10月	11月
56 Construction Duration for Portion 5	458 天	週二 27/2/22	週二 30/5/23	週一 21/11/22	週三 21/2/23	55			
57 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週三 31/5/23	週六 8/7/23	週四 22/2/23	週日 31/3/23	56			
58 Completion of Works in Portion 5	0 天	週六 8/7/23	週六 8/7/23	週一 1/4/24	週一 1/4/24	2,517.57			
59 Section of Works 3A - Establishment Works for all Landscape Softworks in Section 3 of the Works	365 天	週四 7/9/23	週六 6/9/24	週一 1/4/24	週一 31/3/23				
60 Original Completion Date	0 天	週三 29/5/24	週三 29/5/24	週一 31/3/23	週一 31/3/23	41FS+365 天			
61 Commencement of Establishment Work for Section 3	0 天	週四 7/9/23	週四 7/9/23	週一 1/4/24	週一 1/4/24	50,45,54,58			
62 Establishment Work Duration for Section 3	365 天	週五 8/9/23	週五 6/9/24	週一 1/4/24	週一 31/3/23	61			
63 Completion of Works in Section 3	0 天	週五 6/9/24	週五 6/9/24	週一 31/3/23	週一 31/3/23	62,521			
64 Section of Works 4 - Portions 6, 12	804 天	週五 30/7/21	週三 11/10/22	週一 18/1/23	週一 1/4/24				
65 Original Completion Date	0 天	週三 14/6/23	週三 14/6/23	週一 1/4/24	週一 1/4/24	68FF-81 天,72FF			
66 Access date for Portion 6	0 天	週六 29/1/22	週六 29/1/22	週三 20/7/22	週三 20/7/22	2			
67 Deferred possession	81 天	週六 29/1/22	週二 19/4/22	週三 20/7/22	週六 8/10/22	66			
68 Construction Duration for Portion 6	501 天	週三 20/4/22	週六 2/9/23	週日 9/10/22	週三 21/2/23	67			
69 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週日 3/9/23	週三 11/10/23	週四 22/2/23	週日 31/3/23	68			
70 Completion of Works in Portion 6	0 天	週三 11/10/23	週三 11/10/23	週一 1/4/24	週一 1/4/24	539,540,538,69			
71 Access date for Portion 12	0 天	週五 30/7/21	週五 30/7/21	週二 18/1/22	週二 18/1/22	2			
72 Construction Duration for Portion 12	684 天	週五 30/7/21	週三 13/6/23	週六 9/4/22	週三 21/2/23	71			
73 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週三 14/6/23	週六 22/7/23	週四 22/2/23	週日 31/3/23	72			
74 Completion of Works in Portion 12	0 天	週三 11/10/23	週三 11/10/23	週一 1/4/24	週一 1/4/24	556,558,560,553,559,73			
75 Section of Works 4A - Establishment Works for all Landscape Softworks in Section 4 of the Works	365 天	週三 11/10/23	週四 10/10/24	週一 1/4/24	週一 31/3/23				
76 Original Completion Date	0 天	週四 13/6/24	週四 13/6/24	週一 31/3/23	週一 31/3/23	65FS+365 天			
77 Commencement of Establishment Work for Section 4	0 天	週三 11/10/23	週三 11/10/23	週一 1/4/24	週一 1/4/24	70,74			
78 Establishment Work Duration for Section 4	365 天	週四 12/10/23	週四 10/10/24	週一 1/4/24	週一 31/3/23	77			
79 Completion of Works in Section 4	0 天	週四 10/10/24	週四 10/10/24	週一 31/3/23	週一 31/3/23	78,565			
80 Section of Works 5A - Portions 9, 10	738 天	週五 30/7/21	週日 6/8/23	週五 25/3/23	週一 1/4/24				
81 Original Completion Date	0 天	週三 28/6/23	週三 28/6/23	週一 1/4/24	週一 1/4/24	83FF,87FF			
82 Access date for Portion 9	0 天	週三 29/9/21	週三 29/9/21	週三 25/5/22	週三 25/5/22	2			
83 Construction Duration for Portion 9	638 天	週三 29/9/21	週三 28/6/23	週三 25/5/22	週三 21/2/23	82			
84 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週四 29/6/23	週日 6/8/23	週四 22/2/23	週日 31/3/23	83			
85 Completion of Works in Portion 9	0 天	週日 6/8/23	週日 6/8/23	週一 1/4/24	週一 1/4/24	583,581,584,84			
86 Access date for Portion 10	0 天	週五 30/7/21	週五 30/7/21	週五 25/3/22	週五 25/3/22	2			
87 Construction Duration for Portion 10	699 天	週五 30/7/21	週三 28/6/23	週五 25/3/22	週三 21/2/23	86			
88 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週四 29/6/23	週日 6/8/23	週四 22/2/23	週日 31/3/23	87			
89 Completion of Works in Portion 10	0 天	週日 6/8/23	週日 6/8/23	週一 1/4/24	週一 1/4/24	687,636,629,617,611,606,601,			
90 Section of Works 5AII - Establishment Works for all Landscape Softworks in Section 5A of the Works	365 天	週日 6/8/23	週一 5/8/24	週一 1/4/24	週一 31/3/23				
91 Original Completion Date	0 天	週五 28/6/24	週五 28/6/24	週一 31/3/23	週一 31/3/23	81FS+365 天			
92 Commencement of Establishment Work for Section 5A	0 天	週日 6/8/23	週日 6/8/23	週一 1/4/24	週一 1/4/24	85,89			
93 Establishment Work Duration for Section 5A	365 天	週一 7/8/23	週一 5/8/24	週一 1/4/24	週一 31/3/23	92			
94 Completion of Works in Section 5A	0 天	週一 5/8/24	週一 5/8/24	週一 31/3/23	週一 31/3/23	93,691			
95 Section of Works 5B - Portion 11	558 天	週日 27/2/22	週四 7/9/23	週一 23/10/22	週一 31/3/23				
96 Original Completion Date	0 天	週三 28/6/23	週三 28/6/23	週一 31/3/23	週一 31/3/23	98FF			
97 Access date for Portion 11	0 天	週日 27/2/22	週日 27/2/22	週一 23/10/22	週一 23/10/22	2			
98 Construction Duration for Portion 11	487 天	週日 27/2/22	週三 28/6/23	週一 23/10/22	週四 20/2/23	97			
99 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週四 29/6/23	週日 6/8/23	週五 21/2/22	週一 31/3/23	98			
100 Completion of Works in Portion 11	0 天	週四 7/9/23	週四 7/9/23	週一 31/3/23	週一 31/3/23	695,99			
101 Section of Works 6 - Portion 7	365 天	週一 29/11/22	週一 28/11/23	週日 2/4/23	週一 1/4/24				
102 Original Completion Date	0 天	週二 28/11/23	週二 28/11/23	週一 1/4/24	週一 1/4/24	104FF			
103 Access date for Portion 7	0 天	週二 29/11/22	週二 29/11/22	週日 2/4/23	週日 2/4/23	2			
104 Construction Duration for Portion 7	365 天	週二 29/11/22	週二 28/11/23	週日 2/4/23	週日 31/3/23	103			
105 Completion of Works in Portion 7	0 天	週二 28/11/23	週二 28/11/23	週一 1/4/24	週一 1/4/24	104,706,707			
106 Section of Works 6A - Establishment Works for all Landscape Softworks in Section 6 of the Works	365 天	週一 28/11/22	週三 27/11/24	週一 1/4/24	週一 31/3/23				
107 Original Completion Date	0 天	週三 27/11/24	週三 27/11/24	週一 31/3/23	週一 31/3/23	102FS+365 天			

29/11

China International Water

Task

Critical Task

Milestone

Summary

Updated on: 22 Aug 2022

Page 2 /18

China International Water & Electric Corp. CEDD Contract No. ED/2020/02
Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works
Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负	9月	10月	11月
109 Establishment Work Duration for Section 6	365 天	週三 29/11/23	週三 27/11/24	週一 1/4/24	週一 31/3/2	108			
110 Completion of Works in Section 6	0 天	週三 27/11/24	週三 27/11/24	週一 31/3/2	週一 31/3/2	109,711			
111 Section of Works 7A - Portions 13a, 14 (DELETED)	706 天	週五 30/7/21	週六 5/7/23 1	週四 2/6/22	週三 31/3/2				
112 Access date for Portion 13a	0 天	週六 29/1/22	週六 29/1/22	週五 2/12/2	週五 2/12/2 2				
113 Construction Duration for Portion 13a	486 天	週六 29/1/22	週一 29/5/23	週六 2/12/2	週一 31/3/2	112			
114 Completion of Works in Portion 13a	0 天	週三 5/7/23 1	週三 5/7/23 1	週一 31/3/2	週一 31/3/2	113,722			
115 Access date for Portion 14	0 天	週五 30/7/21	週五 30/7/21	週四 2/6/22	週四 2/6/22 2				
116 Construction Duration for Portion 14	669 天	週五 30/7/21	週一 29/5/23	週四 2/6/22	週日 31/3/2	115			
117 Completion of Works in Portion 14	0 天	週一 29/5/23	週一 29/5/23	週一 1/4/24	週一 1/4/24	116,734,733			
118 Section of Works 7Ai - Establishment Works for all Landscape Softworks in Section 7A of the Works (DELETED)	402 天	週一 29/5/23	週四 4/7/24 1	週一 1/4/24	週一 31/3/2				
119 Commencement of Establishment Work for Section 7A	0 天	週一 29/5/23	週一 29/5/23	週一 1/4/24	週一 1/4/24	117			
120 Establishment Work Duration for Section 7A	365 天	週二 30/5/23	週二 28/5/24	週一 1/4/24	週一 31/3/2	119			
121 Completion of Works in Section 7A	0 天	週四 4/7/24 1	週四 4/7/24 1	週一 31/3/2	週一 31/3/2	120,739			
122 Section of Works 7B - Portions 13b, 15	752 天	週日 27/2/22	週一 19/3/24	週五 11/3/2	週一 1/4/24				
123 Original Completion Date	0 天	週六 30/12/23	週六 30/12/23	週一 1/4/24	週一 1/4/24	126FF-52 天,131FF-52 天			
124 Access date for Portion 13b	0 天	週日 27/2/22	週日 27/2/22	週五 11/3/2	週五 11/3/2 2				
125 Deferred possession	52 天	週日 27/2/22	週二 19/4/22	週五 11/3/2	週日 1/5/22	124			
126 Construction Duration for Portion 13b	671 天	週三 20/4/22	週一 19/2/24	週一 2/5/22	週六 2/3/24	125			
127 Potential EOT due to Inclement weather up to 31 July 2022	29 天	週二 20/2/24	週二 19/3/24	週日 3/3/24	週日 31/3/2	126			
128 Completion of Works in Portion 13b	0 天	週二 19/3/24	週二 19/3/24	週一 1/4/24	週一 1/4/24	759,766,762,764,763,763,765,			
129 Access date for Portion 15	0 天	週日 27/2/22	週日 27/2/22	週五 11/3/2	週五 11/3/2 2				
130 Deferred possession	52 天	週日 27/2/22	週二 19/4/22	週五 11/3/2	週日 1/5/22	129			
131 Construction Duration for Portion 15	671 天	週三 20/4/22	週一 19/2/24	週一 2/5/22	週六 2/3/24	130			
132 Potential EOT due to Inclement weather up to 31 July 2022	29 天	週二 20/2/24	週二 19/3/24	週日 3/3/24	週日 31/3/2	131			
133 Completion of Works in Portion 15	0 天	週二 19/3/24	週二 19/3/24	週一 1/4/24	週一 1/4/24	132			
134 Section of Works 7Bi - Establishment Works for all Landscape Softworks in Section 7B of the Works	365 天	週一 19/3/24	週二 19/3/25	週一 1/4/24	週一 31/3/2				
135 Original Completion Date	0 天	週六 28/12/24	週六 28/12/24	週一 31/3/2	週一 31/3/2	123FS+365 天			
136 Commencement of Establishment Work for Section 7B	0 天	週二 19/3/24	週二 19/3/24	週一 1/4/24	週一 1/4/24	128,133			
137 Establishment Work Duration for Section 7B	365 天	週三 20/3/24	週三 19/3/25	週一 1/4/24	週一 31/3/2	136			
138 Completion of Works in Section 7B	0 天	週三 19/3/25	週三 19/3/25	週一 31/3/2	週一 31/3/2	137,770			
139 Section of Works 8 - Portion 16	402 天	週四 16/6/22	週六 22/7/23	週五 24/2/2	週一 1/4/24				
140 Original Completion Date	0 天	週三 28/6/23	週三 28/6/23	週一 1/4/24	週一 1/4/24	142			
141 Access date for Portion 16	0 天	週四 16/6/22	週四 16/6/22	週五 24/2/2	週五 24/2/2 2				
142 Construction Duration for Portion 16	378 天	週四 16/6/22	週三 28/6/23	週一 1/3/2	週日 24/3/2	141			
143 Potential EOT due to Inclement weather up to 31 July 2022	7 天	週四 29/6/23	週三 5/7/23 1	週一 2/5/22	週日 31/3/2	142			
144 Completion of Works in Portion 16	0 天	週六 22/7/23	週六 22/7/23	週一 1/4/24	週一 1/4/24	780,143			
145 Section of Works 8A - Establishment Works for all Landscape Softworks in Section 8 of the Works	365 天	週六 22/7/23	週日 21/7/24	週一 1/4/24	週一 31/3/2				
146 Original Completion Date	0 天	週五 28/6/24	週五 28/6/24	週一 31/3/2	週一 31/3/2	140FS+365 天			
147 Commencement of Establishment Work for Section 8	0 天	週六 22/7/23	週六 22/7/23	週一 1/4/24	週一 1/4/24	144			
148 Establishment Work Duration for Section 8	365 天	週日 23/7/23	週日 21/7/24	週一 1/4/24	週一 31/3/2	147			
149 Completion of Works in Section 8	0 天	週日 21/7/24	週日 21/7/24	週一 31/3/2	週一 31/3/2	148,784			
150 Section of Works 9 - Portion 17	740 天	週日 27/2/22	週四 7/3/24 1	週一 23/3/2	週一 1/4/24				
151 Original Completion Date	0 天	週六 30/12/23	週六 30/12/23	週一 1/4/24	週一 1/4/24	154FF-30 天			
152 Access date for Portion 17	0 天	週日 27/2/22	週日 27/2/22	週三 23/3/2	週三 23/3/2 2				
153 Deferred possession	30 天	週日 27/2/22	週一 28/3/22	週六 2/4/22	週日 1/5/22	152			
154 Construction Duration for Portion 17	671 天	週二 29/3/22	週日 28/1/24	週一 2/5/22	週六 2/3/24	153			
155 Potential EOT due to Inclement weather up to 31 July 2022	29 天	週一 29/1/24	週一 26/2/24	週日 3/3/24	週日 31/3/2	154			
156 Completion of Works in Portion 17	0 天	週四 7/3/24 1	週四 7/3/24 1	週一 1/4/24	週一 1/4/24	843,875,155			
157 Section of Works 9A - Establishment Works for all Landscape Softworks in Section 9 of the Works	365 天	週四 7/3/24 1	週五 7/3/25 1	週一 1/4/24	週一 31/3/2				
158 Original Completion Date	0 天	週日 29/12/24	週日 29/12/24	週一 31/3/2	週一 31/3/2	151FS+365 天			
159 Commencement of Establishment Work for Section 9	0 天	週四 7/3/24 1	週四 7/3/24 1	週一 1/4/24	週一 1/4/24	156			
160 Establishment Work Duration for Section 9	365 天	週五 8/3/24 8	週五 7/3/25 1	週一 1/4/24	週一 31/3/2	159			

China International Water

Task

Critical Task

Milestone

◆

Summary

◆

Updated on: 22 Aug 2022

Page 3 / 18

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负	9月	10月	11月
162 Section of Works 10 - All Tree Protection and Preservation Works	922 天	週五 30/7/21	週一 6/2/24 1	週四 22/9/2	週一 31/3/2				
163 Original Completion Date	0 天	週五 29/12/23	週五 29/12/23	週一 31/3/2	週一 31/3/2	165			
164 Commencement of All Tree Protection and Preservation Work	0 天	週五 30/7/21	週五 30/7/21	週四 22/9/2	週四 22/9/2	2			
165 All Tree Protection and Preservation Work Duration for Section 10	883 天	週五 30/7/21	週五 29/12/23	週四 22/9/2	週四 20/2/2	164			
166 Potential EOT due to Inclement weather up to 31 July 2022	39 天	週六 30/12/23	週二 6/2/24 1	週五 21/2/2	週一 31/3/2	165			
167 Completion of All Tree Protection and Preservation Work	0 天	週二 6/2/24 1	週二 6/2/24 1	週一 31/3/2	週一 31/3/2	883, 166			
168 Preliminaries	1,341 天	週五 30/7/21	週一 31/3/25	週五 30/7/2	週一 31/3/2				
169 Establishment of Commercial Organization	226 天	週五 30/7/21	週六 12/3/22	週四 31/10/2	週一 31/3/2				
170 Inform Contractor of the name and delegated authorities of the PMD (E	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
171 Confirmation and arrangement of the method of payment	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
172 Issue forms to CIC& PCFB	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/2	週一 31/3/2	2			
173 Submission of MPF form to MPFSA	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
174 Notification to Labour Department/Marine Department of the commencement date and other details of the contract	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
175 Submission of Summary Details of Contract to the Departmental Safety and Environmental	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/2	週一 31/3/2	2			
176 Nominate a Labour Officer	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
177 Set up Site Liaison Group (SLG)	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
178 Professional video production company and a competent video director	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
179 Surveyor, Key People	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
180 Traffic Consultant, Traffic Engineer	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
181 Particulars of Independent service provider for Digital Works Supervision System	7 天	週五 30/7/21	週四 5/8/21 1	週二 25/3/2	週一 31/3/2	2			
182 Contractor's Management Team	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/2	週一 31/3/2	2			
183 BIM team	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/2	週一 31/3/2	2			
184 Competent member of the sites supervisory staff to oversee and supervise tree works related to arboricultural operations and preservation of trees within the Site	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/2	週一 31/3/2	2			
185 Content of Contract Webpage (Monthly update afterwards)	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/2	週一 31/3/2	2			
186 Particulars of the assigned person (competent member with arboriculture knowledge of the site supervisory for tree preservation)	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/2	週一 31/3/2	2			
187 Details of Geotechnical monitoring team	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/2	週一 31/3/2	2			
188 Design of the CRE Site Office certified by an accepted ICE	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/2	2			
189 Design Architect	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/2	2			
190 Specially required staff	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/2	2			
191 Public Relation Officer	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/2	2			
192 Site Safety Committee (SSC) Meeting (monthly afterwards)	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/2	2			
193 Meeting of the SSMC (monthly afterwards)	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/2	2			
194 Professional Indemnity Insurance in respect of Contractor's Design	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/2	週一 31/3/2	2			
195 Proposed gasket material for waterworks	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/2	週一 31/3/2	2			
196 7 days advance notice of the date on which workers begin to wear Site uniform; Provide uniforms within 5 days after the design is accepted by PM	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/2	週一 31/3/2	2			
197 2 Engineering Graduates 3 Technician apprentices	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2			
198 Commissioning of DWSS	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2			
199 Agree on the content and presentation of the dashboard of DWSS	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2			
200 Monthly collaboration and information exchange of BIM	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2			
201 Combined Services Drawing (CSD) and CBWD generated from BIM model	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2			
202 Video script for Project Video Film	180 天	週五 30/7/21	週二 25/1/22	週四 3/10/2	週一 31/3/2	2			
203 Employment of Construction Industry Council's Graduates (min. 4 graduates)	180 天	週五 30/7/21	週二 25/1/22	週四 3/10/2	週一 31/3/2	2			
204 Nomination of Treatment process specialist, Design Engineer, and Independent Checking Engineer (ICE)	34 天	週一 7/2/22 8	週六 12/3/22	週二 29/10/2	週日 1/12/2	283SS			
205 Plan & Proposals	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/2	週一 31/3/2				

China International Water

Task

Critical Task

Milestone

◆

Summary

◆

Updated on: 22 Aug 2022

Page 4 / 18

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负	9月	10月	11月
206 Preparation and submission of Noise Mitigation Plan (3 hard copies, 2 electronic copies)	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
207 Preparation and submission of Waste Management Plan (WMP)	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
208 Preparation and submission of Draft Construction Health and Safety Plan (3 copies)	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2			
209 Preparation and submission of Quality Policy statement and quality plan	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2			
210 Preparation and submission of Draft Environmental Management Plan (EMP) 3 copies	4 天	週五 30/7/21	週一 2/8/21	週五 28/3/22	週一 31/3/22	2			
211 Tender requirements for suppliers of Plant and Materials, Equipment and Insurance Proposal	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/22	週一 31/3/22	2			
212 Preparation of Proposal for arrangement for placement of storage compartments/ drinking water facilities/ toilet/ hand-wash facilities/ showering/ rubbishbin/ working shelter on Site	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/22	週一 31/3/22	2			
213 Preparation Proposal for security system	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/22	週一 31/3/22	2			
214 Preparation and submission of DWSS proposal	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/22	週一 31/3/22	2			
215 Preparation and submission of Subcontractor Management Plan (SMP)	21 天	週五 30/7/21	週四 19/8/21	週二 11/3/22	週一 31/3/22	2			
216 Preparation and submission of Construction Health and Safety Plan (6 copies)	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
217 Weather protection scheme	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
218 Proposal of COBe information requirements	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
219 Preparation and submission of Final Environmental Management Plan (EMP) 3 copies	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
220 Preparation of Proposed Plans for submission of each Release of construction and Project Video Films	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2			
221 Preparation and submission of Site Traffic Safety Management Plan (STSMP), (monthly update)	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2			
222 Preparation and submission of Site Management Plan for TTS	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2			
223 Preparation and submission of BIM Execution Plan accordance with the PSA 1.14D	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2			
224 Public Relation (PR) Company, PR plan	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2			
225 Preparation and submission of Temporary drainage management plan	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2			
226 Procurements of Major Materials	430 天	週一 15/2/22	週四 20/4/23	週三 19/4/22	週三 31/3/22				
227 Procurement & material submission of bearing for elevated walkway	90 天	週四 26/5/22	週二 23/8/22	週三 14/6/22	週一 11/9/22	2SS+300 天			
228 Design, manufacturing and FAT of bearing for elevated walkway	90 天	週三 24/8/22	週一 21/11/22	週二 12/9/22	週日 10/12/22	227			
229 Deliveries and site inspection of bearing for elevated walkway etc.	60 天	週二 22/11/22	週五 20/1/23	週一 11/1/22	週四 8/2/24	228			
230 Procurement & material submission of movement joint for elevated walkway	90 天	週三 24/8/22	週一 21/11/22	週三 14/6/22	週一 11/9/22	2SS+390 天			
231 Design, manufacturing and FAT of movement joint for elevated walkway	90 天	週二 22/11/22	週日 19/2/23	週二 12/9/22	週日 10/12/22	230			
232 Deliveries and site inspection of movement joint for elevated walkway etc.	60 天	週一 20/2/23	週四 20/4/23	週一 11/1/22	週四 8/2/24	231			
233 Procurement of Raise Planter Type A&B	90 天	週二 15/2/22	週日 15/5/22	週四 3/10/22	週二 31/12/22	2SS+200 天			
234 Manufacturing, FAT & delivery of Raise Planter Type A&B	90 天	週一 16/5/22	週六 13/8/22	週三 1/1/25	週一 31/3/22	233			
235 Procurement of Balustrade Wall BW1-2	90 天	週六 3/9/22	週四 1/12/22	週四 3/10/22	週二 31/12/22	2SS+400 天			
236 Manufacturing, FAT & delivery of Balustrade Wall BW1-2	90 天	週五 2/12/22	週三 1/3/23	週三 1/1/25	週一 31/3/22	235			
237 Procurement of Children Play Areas & water play area Park Facilities	90 天	週四 26/5/22	週二 23/8/22	週三 19/4/22	週一 17/7/22	2SS+300 天			
238 Design, Manufacturing, FAT & delivery of Children Play Areas & water play area Park Facilities	90 天	週三 24/8/22	週一 21/11/22	週二 18/7/22	週日 15/10/22	237			
239 Procurement of Adult fitness Area Park Facilities	90 天	週四 26/5/22	週二 23/8/22	週三 19/4/22	週一 17/7/22	2SS+300 天			
240 Design Manufacturing, FAT & delivery of Adult fitness Area Park Facilities	90 天	週三 24/8/22	週一 21/11/22	週二 18/7/22	週日 15/10/22	239			
241 Procurement of Elderly fitness Area Park Facilities	90 天	週四 26/5/22	週二 23/8/22	週三 19/4/22	週一 17/7/22	2SS+300 天			
242 Design, Manufacturing, FAT & delivery of Elderly fitness Area Park Facilities	90 天	週三 24/8/22	週一 21/11/22	週二 18/7/22	週日 15/10/22	241			
243 Programme	1,332 天	週五 30/7/21	週六 22/3/25	週四 8/8/21	週一 31/3/22				
244 Preparation & Submission of First Works Program	6 天	週五 30/7/21	週三 4/8/21	週日 8/8/21	週五 13/8/22	2			

China International Water

Task

Critical Task

Milestone

◆

Summary

Updated on: 22 Aug 2022

Page 5 / 18

China International Water & Electric Corp. CEDD Contract No. ED/2020/02
Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works
Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负		9月	10月	11月
246 Program Review and Acceptance of First Program	14 天	週四 5/8/21	週三 18/8/21	週六 14/8/21	週五 27/8/21	244				
247 Preparation and Submission of Detailed Works Program	60 天	週四 19/8/21	週日 17/10/21	週六 28/8/21	週二 26/10/21	246,245				
248 Program Review and Acceptance of Works Program	14 天	週一 18/10/21	週日 31/10/21	週三 27/10/21	週二 9/11/21	247				
249 Implementation of Programme Management and Monthly Reporting	1,238 天	週一 1/11/21	週六 22/3/25	週三 10/11/21	週一 31/3/25	248				
250 Permit and Licences	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22					
251 Detailed construction sequences with associated traffic diversion schemes and obtain endorsement in principle from the relevant authorities and the Supervisor	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2				
252 Risk Assessment for slope works	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
253 Welfare facilities for workers in accordance with requirements in PS Clause 1.69B	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
254 UU detection equipment brand/model	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
255 Certified calibration certificates	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
256 Contract Computer Facilities, Electronic Document Management System, Site Record Information System, Digital Works Supervision System and other software	6 天	週五 30/7/21	週三 4/8/21	週三 26/3/22	週一 31/3/22	2				
257 Name of the designated bank and all related arrangement details for payment of wages to all the Site Workers	6 天	週五 30/7/21	週三 4/8/21	週三 26/3/22	週一 31/3/22	2				
258 Site Cleanliness and Tidiness	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
259 3 sets of coloured record photos in SR size (recording existing building/ street furniture.....)	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
260 Contract Cars	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
261 Design of uniform for site workers	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
262 Survey Equipment for Initial survey	7 天	週五 30/7/21	週四 5/8/21	週二 25/3/22	週一 31/3/22	2				
263 Inclinator access tubes - suppliers, material specification and samples of the tubes and couplings	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/22	週一 31/3/22	2				
264 Payment of Wages System for Site Workers	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/22	週一 31/3/22	2				
265 Tree survey record	14 天	週五 30/7/21	週四 12/8/21	週二 18/3/22	週一 31/3/22	2				
266 Supply of Survey Equipment for PM use	30 天	週五 30/7/21	週六 28/8/21	週日 2/3/25	週一 31/3/22	2				
267 Complete setting up and begin to operate the Security System	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2				
268 Initial Survey	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2				
269 Assessment for the risk resulting from working in hot weather	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/22	週一 31/3/22	2				
270 Contractor's Design	659 天	週五 30/7/21	週五 19/5/23	週六 22/1/22	週一 31/3/22					
271 Prepare & Submission Contractor's Design - Architectural & Structural	90 天	週五 30/7/21	週三 27/10/21	週六 22/1/22	週四 21/4/22	2				
272 Internal Review & Submission Contractor's Design - Architectural & Structural	30 天	週四 28/10/21	週五 26/11/21	週五 22/4/22	週六 21/5/22	271				
273 PM Review & AIP Contractor's Design - Architectural	30 天	週六 27/11/21	週日 26/12/21	週日 22/5/22	週一 20/6/22	271,272				
274 Re-submission Contractor's Design - Architectural & Structural	90 天	週一 27/12/21	週六 26/3/22	週二 21/6/22	週日 18/9/22	273				
275 Design Checker Review & Endorsement of Contractor's Design - Architectural	60 天	週日 27/3/22	週三 25/5/22	週一 19/9/22	週四 17/11/22	274				
276 DDA Submission (circulation to Government Authorities)	7 天	週四 26/5/22	週三 1/6/22	週五 18/11/21	週四 24/11/21	275				
277 Time risk allowance for DDA processing	30 天	週四 26/6/22	週五 17/7/22	週五 24/2/22	週六 25/3/22	276				
278 Vetting Process and Approval by Government Authorities and PM	45 天	週六 27/7/22	週一 15/8/22	週二 14/5/22	週四 27/6/22	277,276				
279 Design Checker issue certificate of Approved Design	7 天	週二 16/8/22	週一 22/8/22	週五 28/6/22	週四 4/7/24	278,277				
280 Prepare Contractor's Design - Toilet, Management office & Store room	90 天	週六 27/7/22	週四 29/9/22	週日 26/3/22	週五 23/6/22	277				
281 Internal review, ICE, CSD and submission Contractor's Design - Toilet, Management office & Store room	60 天	週五 30/9/22	週一 28/11/22	週六 24/6/22	週二 22/8/22	280				
282 AIP Contractor's Design - Toilet, Management office & Store room	30 天	週二 29/11/22	週三 28/12/22	週三 23/8/22	週四 21/9/22	280,281				
283 Prepare Contractor's Design - Underground Water Treatment Plant	90 天	週一 7/2/22	週六 7/5/22	週二 3/9/24	週日 1/12/22	283+192 天				
284 Internal review, ICE, CSD and submission Contractor's Design - Underground Water Treatment Plant	90 天	週日 8/5/22	週五 5/8/22	週一 21/2/22	週六 1/3/25	283,204				
285 AIP Contractor's Design - Underground Water Treatment Plant	30 天	週六 6/8/22	週日 4/9/22	週日 23/3/25	週一 31/3/22	283,284				
286 Prepare Contractor's Design - Entry Portal, Shelters, Signage, Solar Panels & Associated System etc.	150 天	週二 23/8/22	週四 19/1/23	週五 5/7/24	週日 1/12/22	279				
287 Internal review, ICE, CSD and submission Contractor's Design - Entry Portal, Shelters, Signage, Solar Panels & Associated System	90 天	週五 20/1/23	週三 19/4/23	週一 21/2/22	週六 1/3/25	286				

China International Water

Task

Critical Task

Milestone

◆

Summary

◆

Updated on: 22 Aug 2022

Page 6 /18

China International Water & Electric Corp.

CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负		9月	10月	11月
288 AIP Contractor's Design - Entry Portal, Shelters, Signage, Solar Panels & Associated System etc.	30 天	週四 20/4/23	週五 19/5/23	週日 2/3/25	週一 31/3/2	286,287				
289 Prepare Contractor's Design - Park lighting, irrigation system, smart system etc.	70 天	週日 29/5/22	週六 6/8/22	週一 21/11/2	週日 29/1/2	276SS+3 天				
290 Internal review, ICE, CSD and submission Contractor's Design - Park lighting, irrigation system, smart system etc.	40 天	週日 7/8/22	週四 15/9/22	週二 21/1/2	週六 1/3/25	289		15/9		
291 AIP Contractor's Design- Park lighting, irrigation system, smart system etc.	30 天	週五 16/9/22	週六 15/10/22	週日 2/3/25	週一 31/3/2	289,290		16/9	15/10	
292 Contractor's Design [Enhancement on Architectural Design & Associated Works]	450 天	週五 30/7/21	週六 22/10/22	週五 19/11/2	週六 11/2/2					
293 Proposal of proposed architects firm & quotation for acceptance of the Project Manager	60 天	週五 30/7/21	週一 27/9/21	週五 19/11/2	週一 17/1/2	2				
294 Prepare & Submission Preliminary Arch., Design	90 天	週二 28/9/21	週日 26/12/2	週二 18/1/2	週日 17/4/2	293				
295 PM Review & AIP Preliminary Architectural Design	30 天	週一 27/12/21	週二 25/1/22	週一 18/4/2	週二 17/5/2	294				
296 Vetting of design through public engagement activities	60 天	週三 26/1/22	週六 26/3/22	週三 18/5/2	週六 16/7/2	295				
297 Submission of design to DSD, LCSD and other authorities for vetting and acceptance	60 天	週日 27/3/22	週三 25/5/22	週日 17/7/2	週三 14/9/2	296				
298 Preparation & submission of detailed design for approval	90 天	週四 26/5/22	週二 23/8/22	週四 15/9/2	週二 13/12/2	297				
299 Time risk allowance for DDA processing	30 天	週三 24/8/22	週四 22/9/22	週三 14/12/2	週四 12/1/2	297,298		22/9		
300 Approval of detailed design	30 天	週五 23/9/22	週六 22/10/22	週五 13/1/2	週六 11/2/2	297,298,299		23/9	22/10	
301 Method Statements & Temporary Works	120 天	週五 30/7/21	週六 26/11/2	週四 24/3/2	週一 31/3/2					
302 Preparation & submission of generic method statement for site formation work	60 天	週五 30/7/21	週一 27/9/21	週三 18/1/2	週六 18/3/2	2				
303 Preparation & submission of generic method statement for earth slope works	60 天	週五 30/7/21	週一 27/9/21	週三 18/1/2	週六 18/3/2	2				
304 Preparation & submission of generic method statement for retaining wall construction	60 天	週五 30/7/21	週一 27/9/21	週四 24/3/2	週日 22/5/2	2				
305 Preparation & submission of generic method statement for G.I works	60 天	週五 30/7/21	週一 27/9/21	週一 31/10/2	週四 11/2/2	2				
306 Preparation & Submission of generic method statement for drainage works	60 天	週五 30/7/21	週一 27/9/21	週五 31/1/2	週一 31/3/2	2				
307 Preparation and submission of generic method statement of road works	60 天	週五 30/7/21	週一 27/9/21	週五 28/4/2	週一 26/6/2	2				
308 Preparation & submission of generic method statement of elevated walkway construction	120 天	週五 30/7/21	週五 26/11/2	週三 13/7/2	週三 9/11/2	2				
309 Temporary Work for cutfill slope works	60 天	週五 30/7/21	週一 27/9/21	週日 11/9/2	週三 9/11/2	2				
310 Temporary Work for retaining wall construction	60 天	週五 30/7/21	週一 27/9/21	週日 11/9/2	週三 9/11/2	2				
311 Temporary Work for elevated walkway construction	60 天	週五 30/7/21	週一 27/9/21	週日 11/9/2	週三 9/11/2	2				
312 Temporary Work for road and drainage works	60 天	週五 30/7/21	週一 27/9/21	週五 28/4/2	週一 26/6/2	2				
313 BIM Deliverable	1,341 天	週五 30/7/21	週一 31/3/25	週五 30/7/2	週一 31/3/2					
314 Submission of COBie Information Requirements for Asset Management	30 天	週五 30/7/21	週六 28/8/21	週五 30/7/2	週六 28/8/2	2				
315 Submission of BIM Execution Plan in accordance with the PS Appendix 1.14D	60 天	週五 30/7/21	週一 27/9/21	週五 30/7/2	週一 27/9/2	2,314FF+30 天				
316 Submission of Combined Services Drawings	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2				
317 Submission of proposal for BIM training plan	90 天	週五 30/7/21	週三 27/10/21	週三 1/1/25	週一 31/3/2	2				
318 Nomination of staff or subcontractor to attend BIM skill training courses under the pre approved list of the CITF managed by the	120 天	週五 30/7/21	週五 26/11/2	週一 21/2/2	週一 31/3/2	2				
319 Collaboration and Model Sharing	60 天	週四 28/10/21	週日 26/12/2	週四 28/10/2	週日 26/12/2	315FS+30 天				
320 Monthly Coordination meeting& Submission of monthly BIM progress reports & Submission of 4D Simulation	1,191 天	週一 27/12/21	週一 31/3/25	週一 27/12/2	週一 31/3/2	319				
321 Submission of COBie data deliverables	30 天	週五 31/1/25	週六 1/3/25	週五 31/1/2	週六 1/3/25	320FS-60 天				
322 Submission of a Fully Coordinated BIM Model with field verified in LOD 500	30 天	週二 18/2/25	週三 19/3/25	週日 2/3/25	週一 31/3/2	320FS-42 天				
323 Submission of O&M Manuals, Product Catalogues and Operating Data	30 天	週二 18/2/25	週三 19/3/25	週日 2/3/25	週一 31/3/2	320FS-42 天				
324 Submission of As-built drawings	30 天	週二 18/2/25	週三 19/3/25	週日 2/3/25	週一 31/3/2	320FS-42 天				
325 Submission of Asset Data	30 天	週二 18/2/25	週三 19/3/25	週日 2/3/25	週一 31/3/2	320FS-42 天				
326 Work Area	1,341 天	週五 30/7/21	週一 31/3/25	週五 30/7/2	週一 31/3/2					
327 CRE Site Office Design & ICE Endorsement	30 天	週五 30/7/21	週六 28/8/21	週四 16/9/2	週五 15/10/2					

China International Water

Task Critical Task Milestone Summary


Updated on: 22 Aug 2022

Page 7 / 18

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

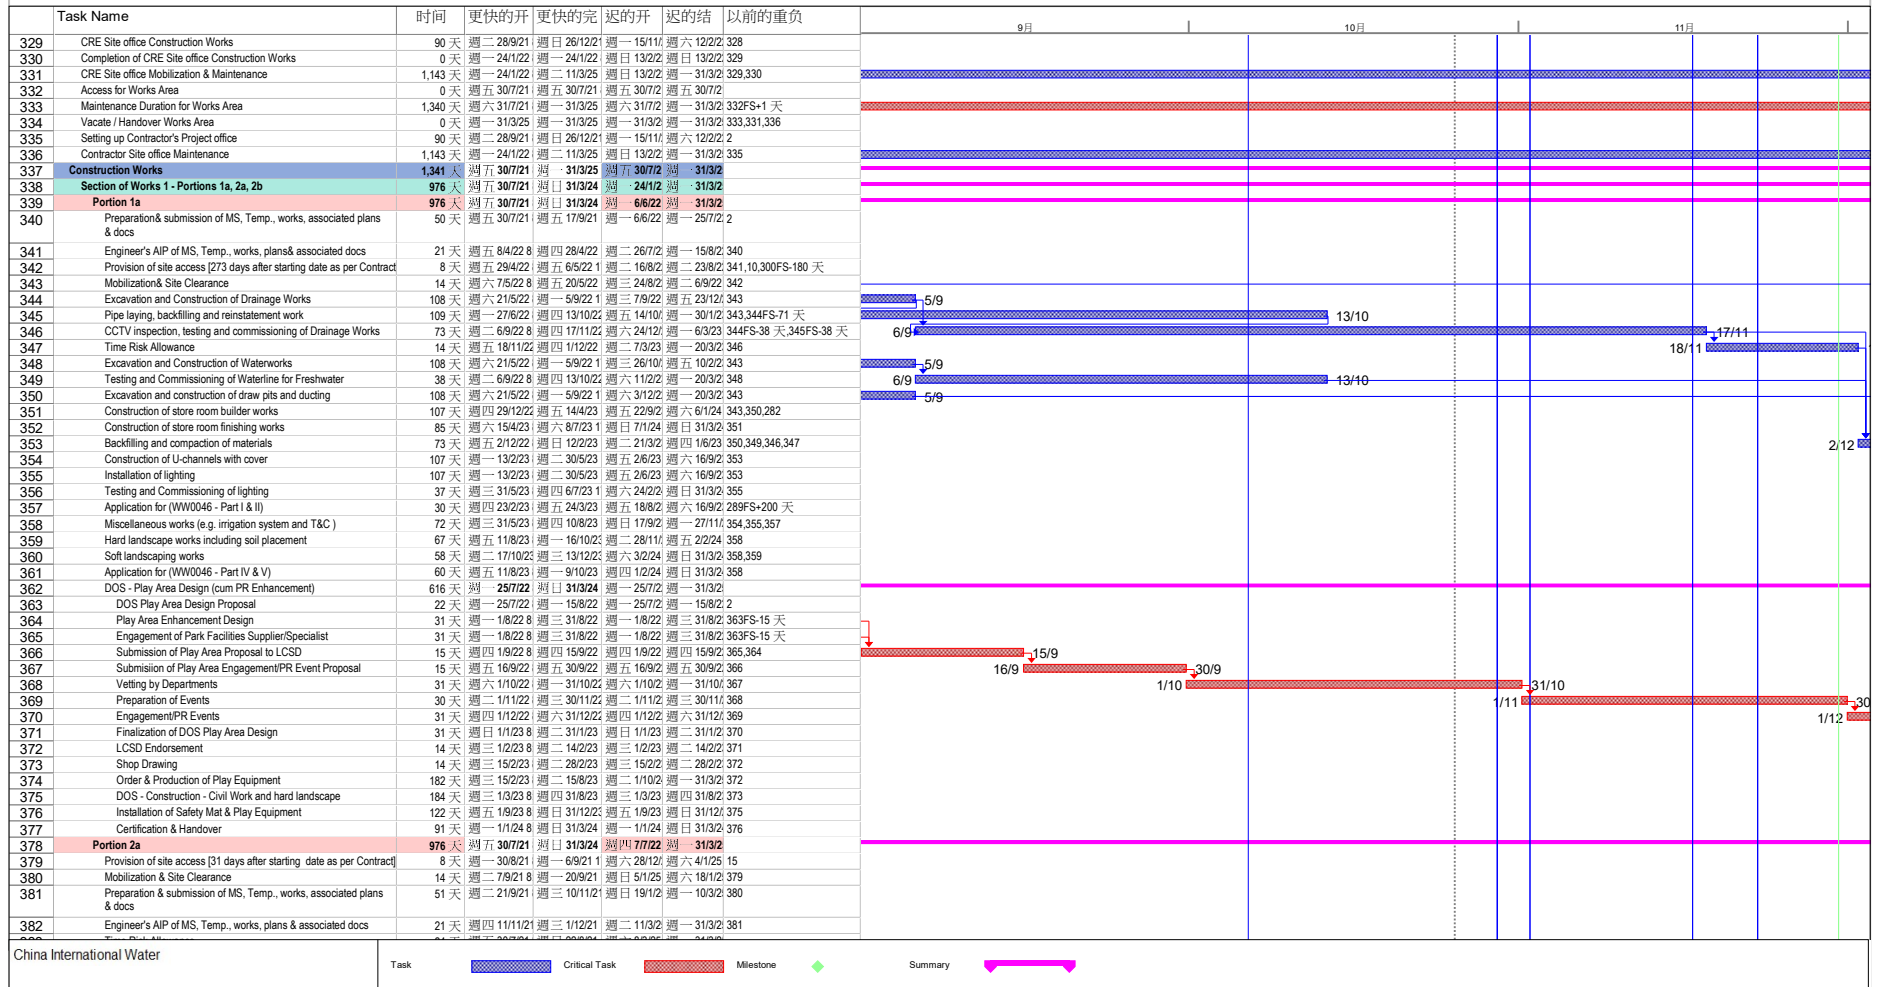


Updated on: 22 Aug 2022

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

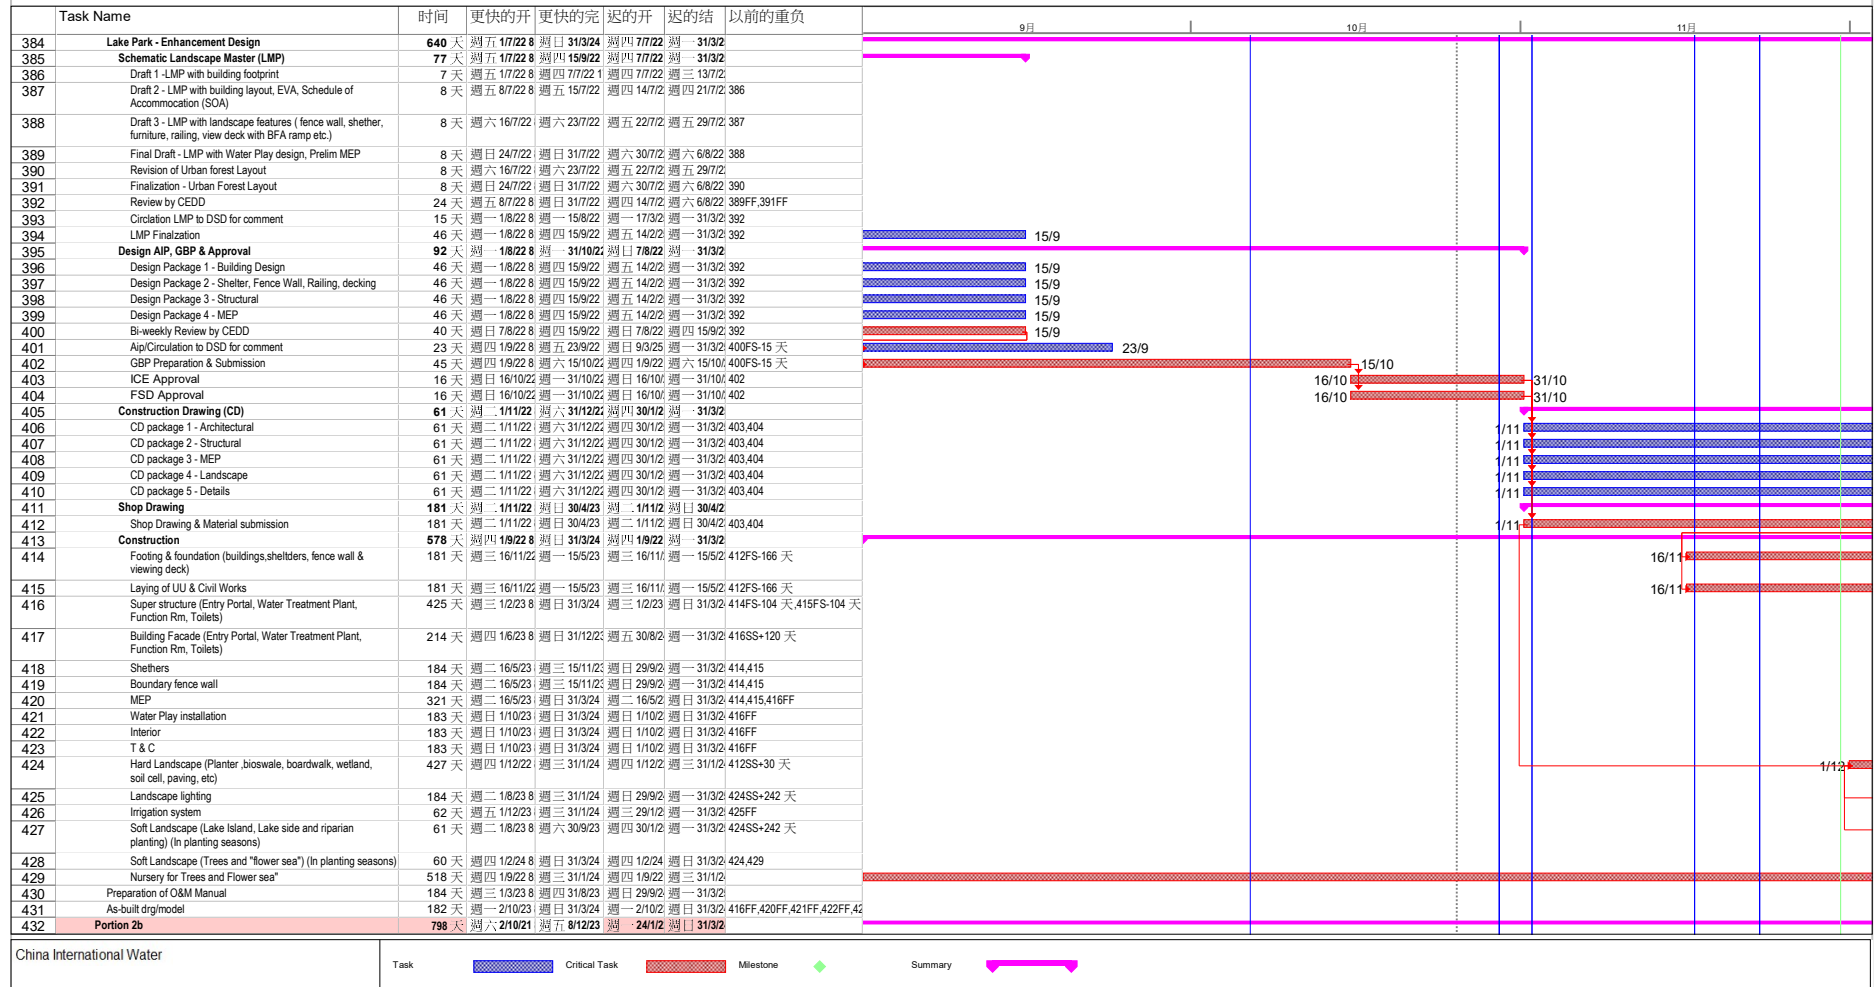


Updated on: 22 Aug 2022

China International Water & Electric Corp.

CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

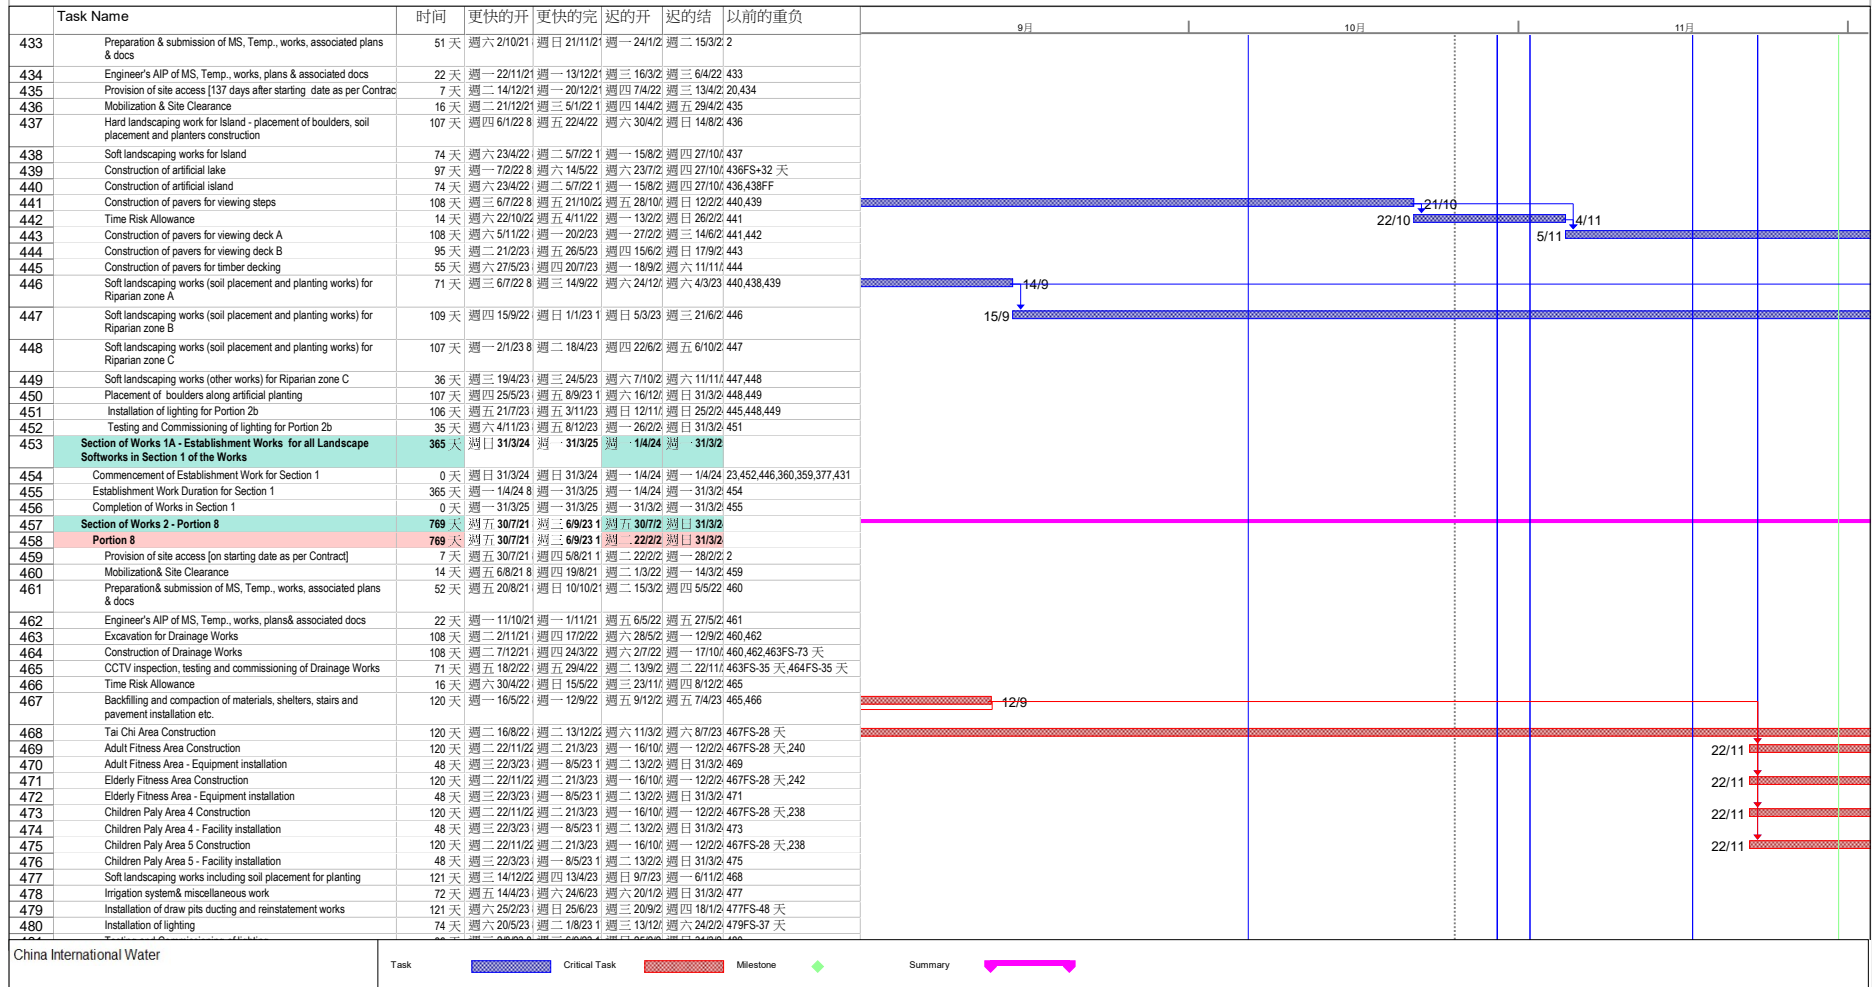


Updated on: 22 Aug 2022


China International Water & Electric Corp. CEDD Contract No. ED/2020/02


Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works


Revised Works Programme : August 2022

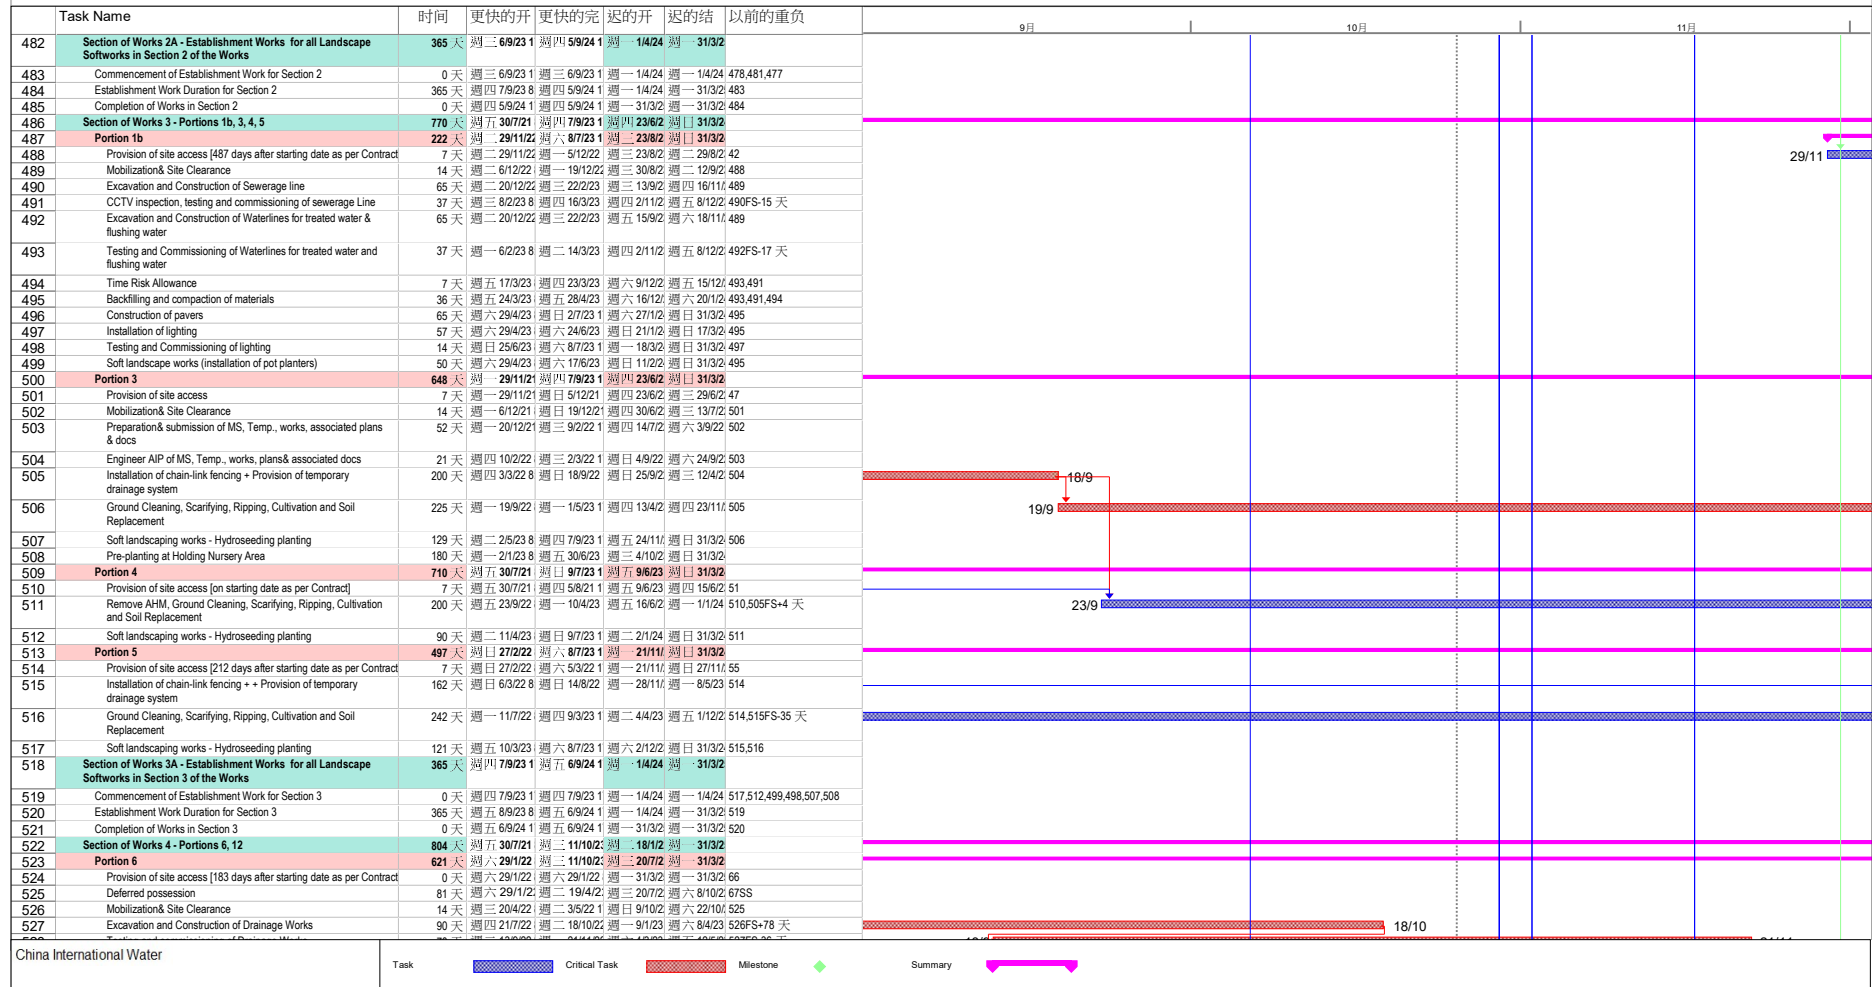

Updated on: 22 Aug 2022

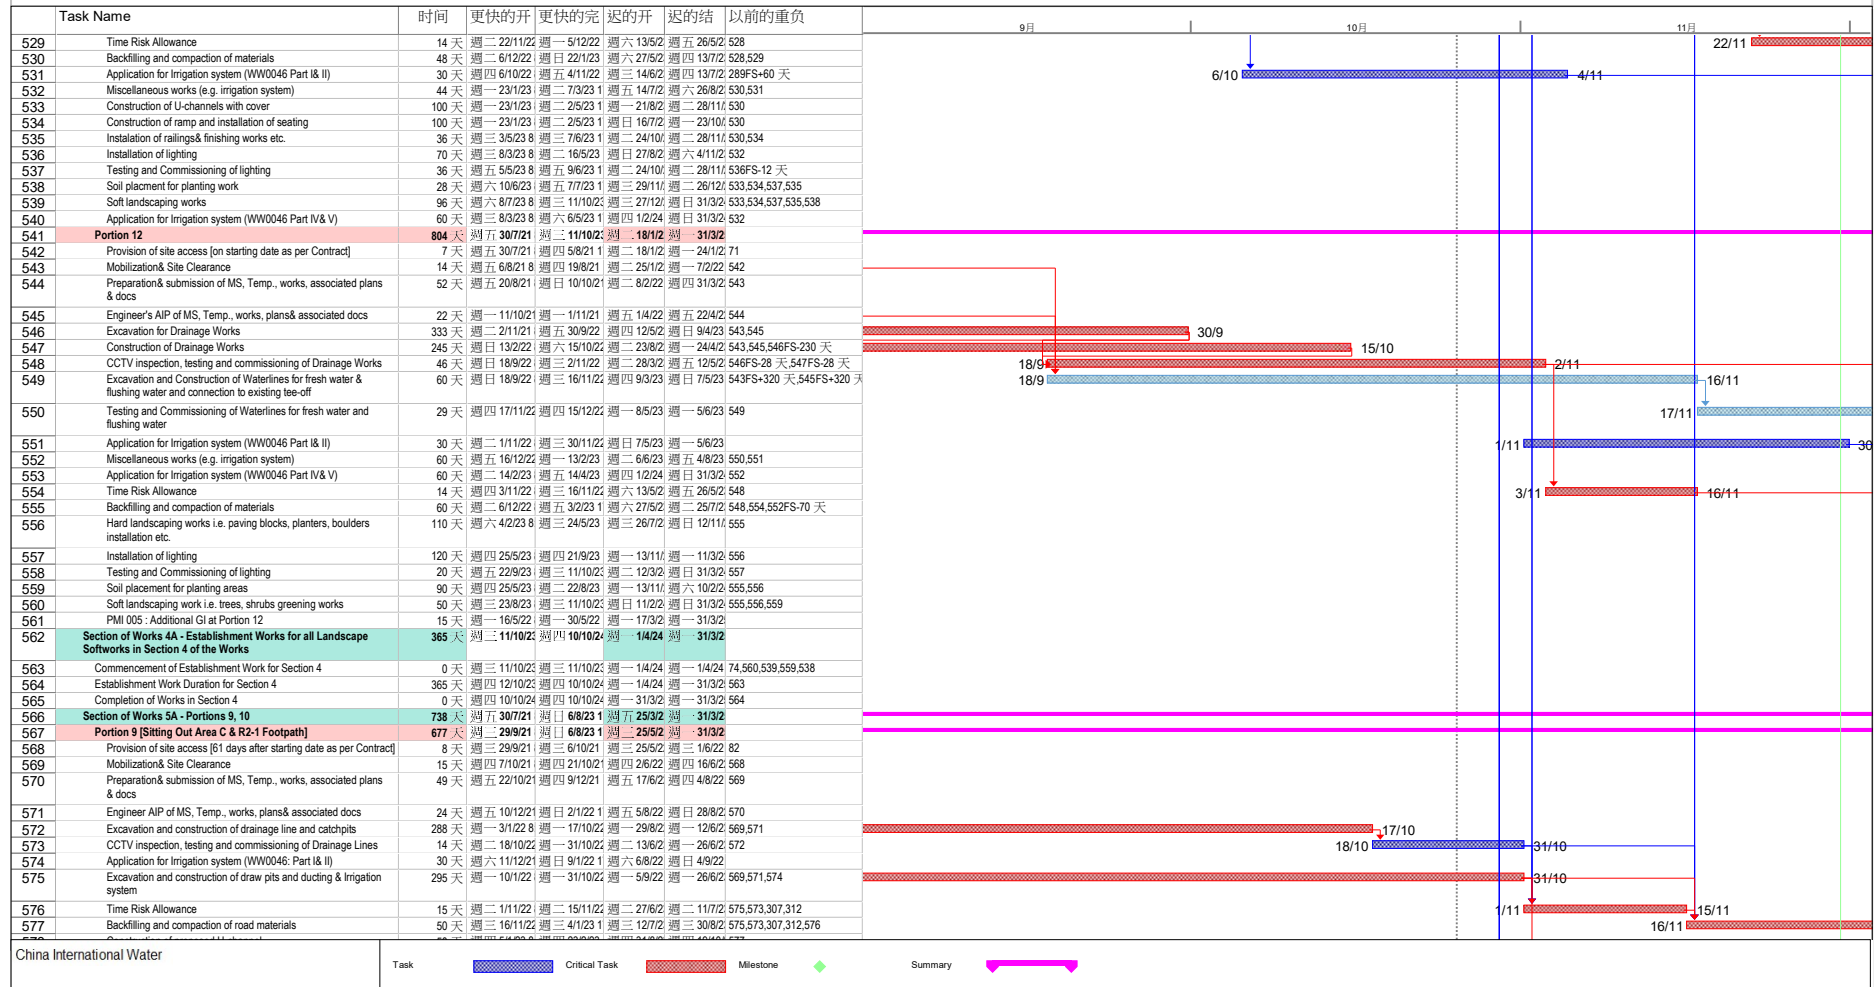

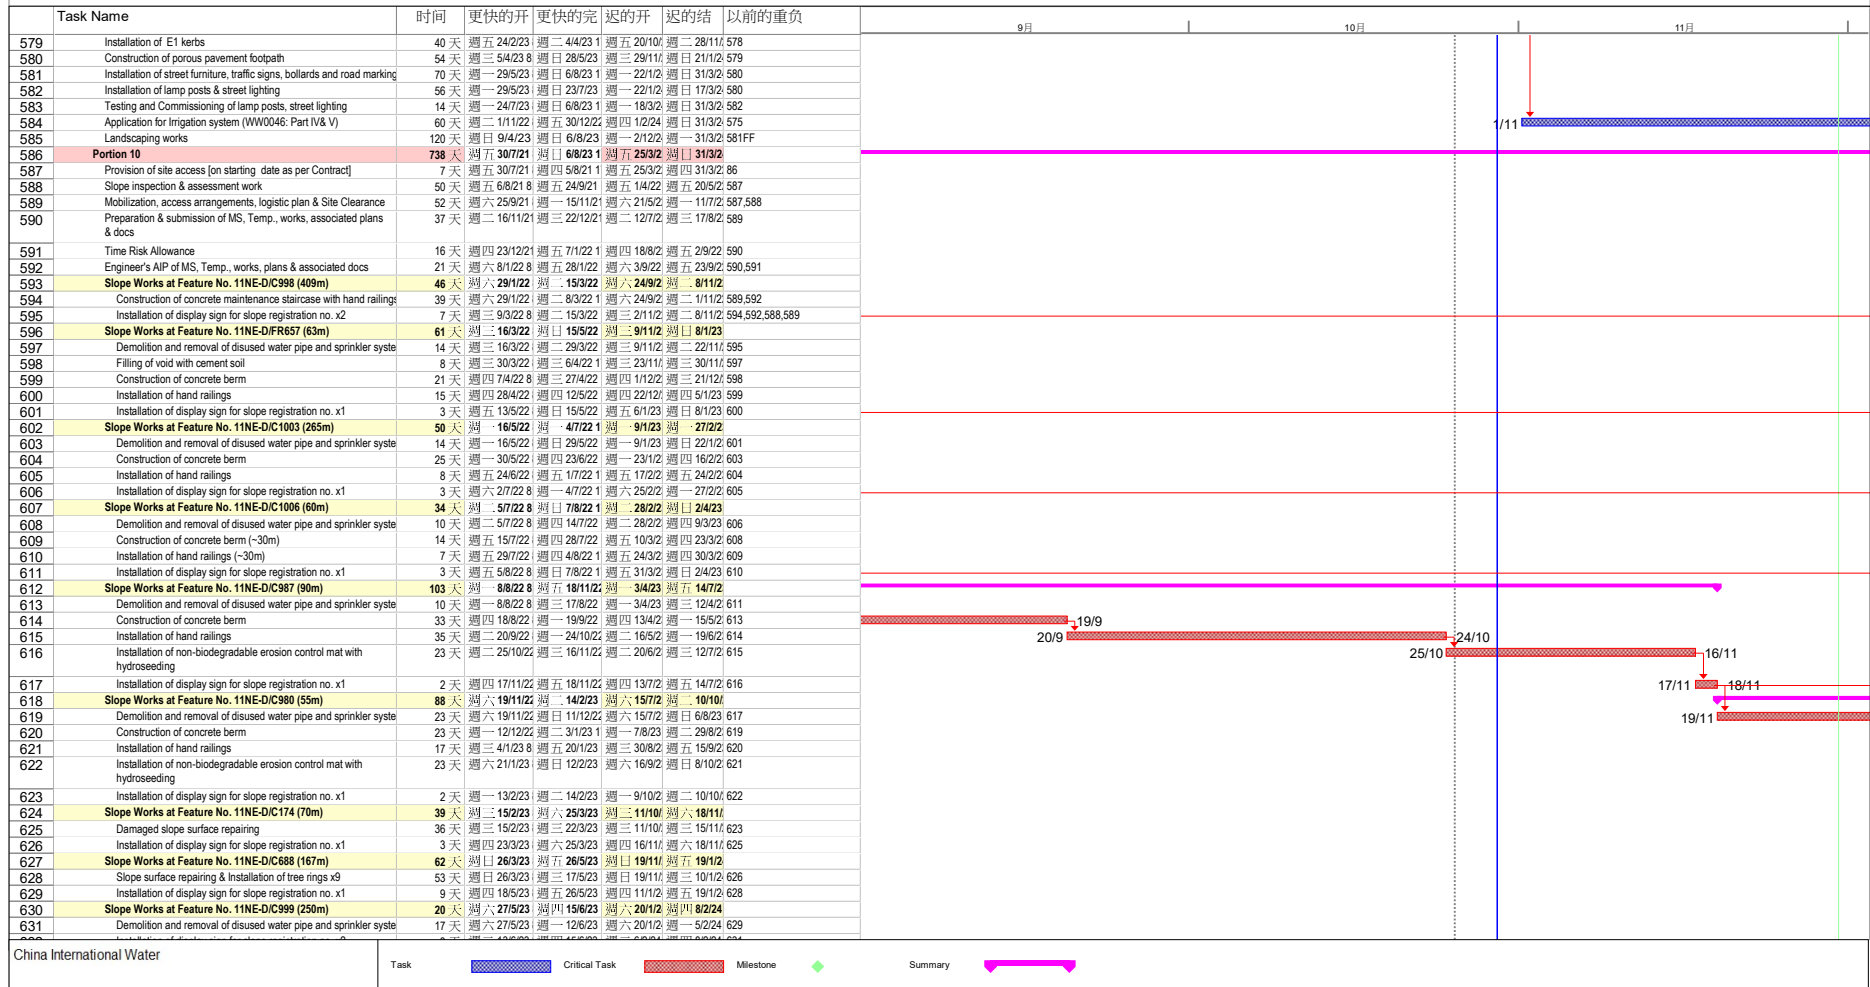


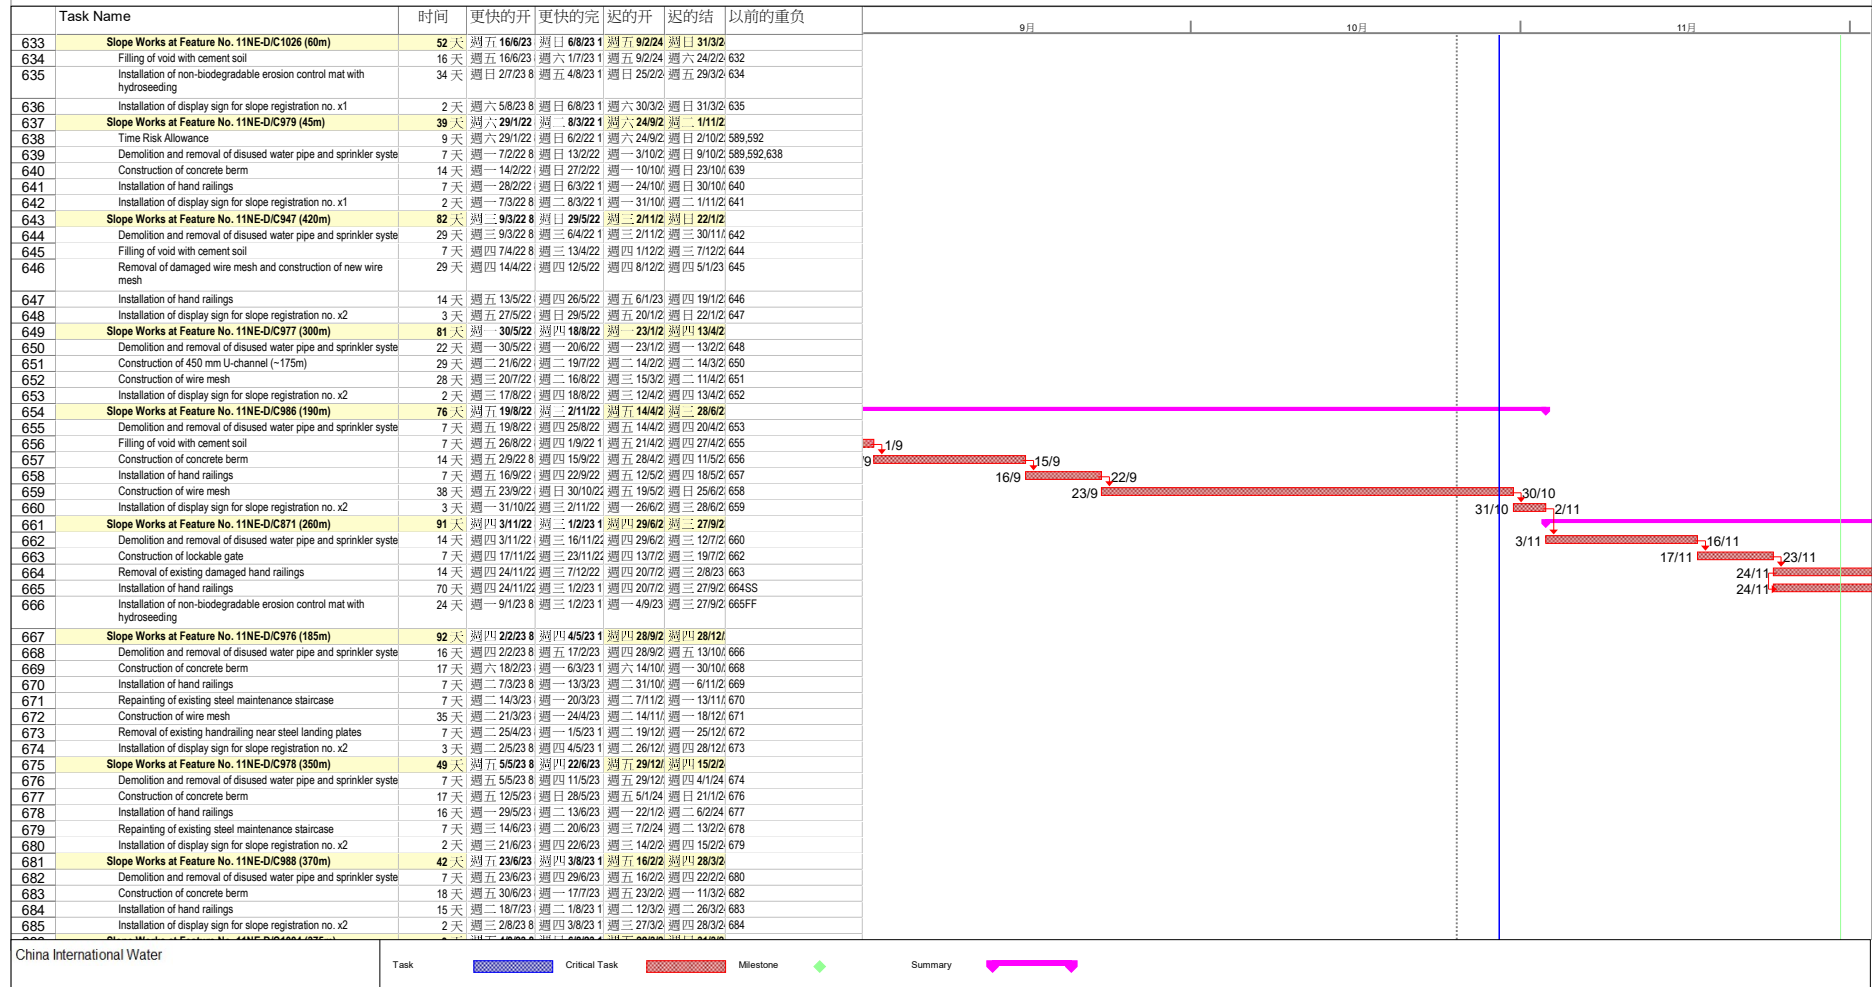

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

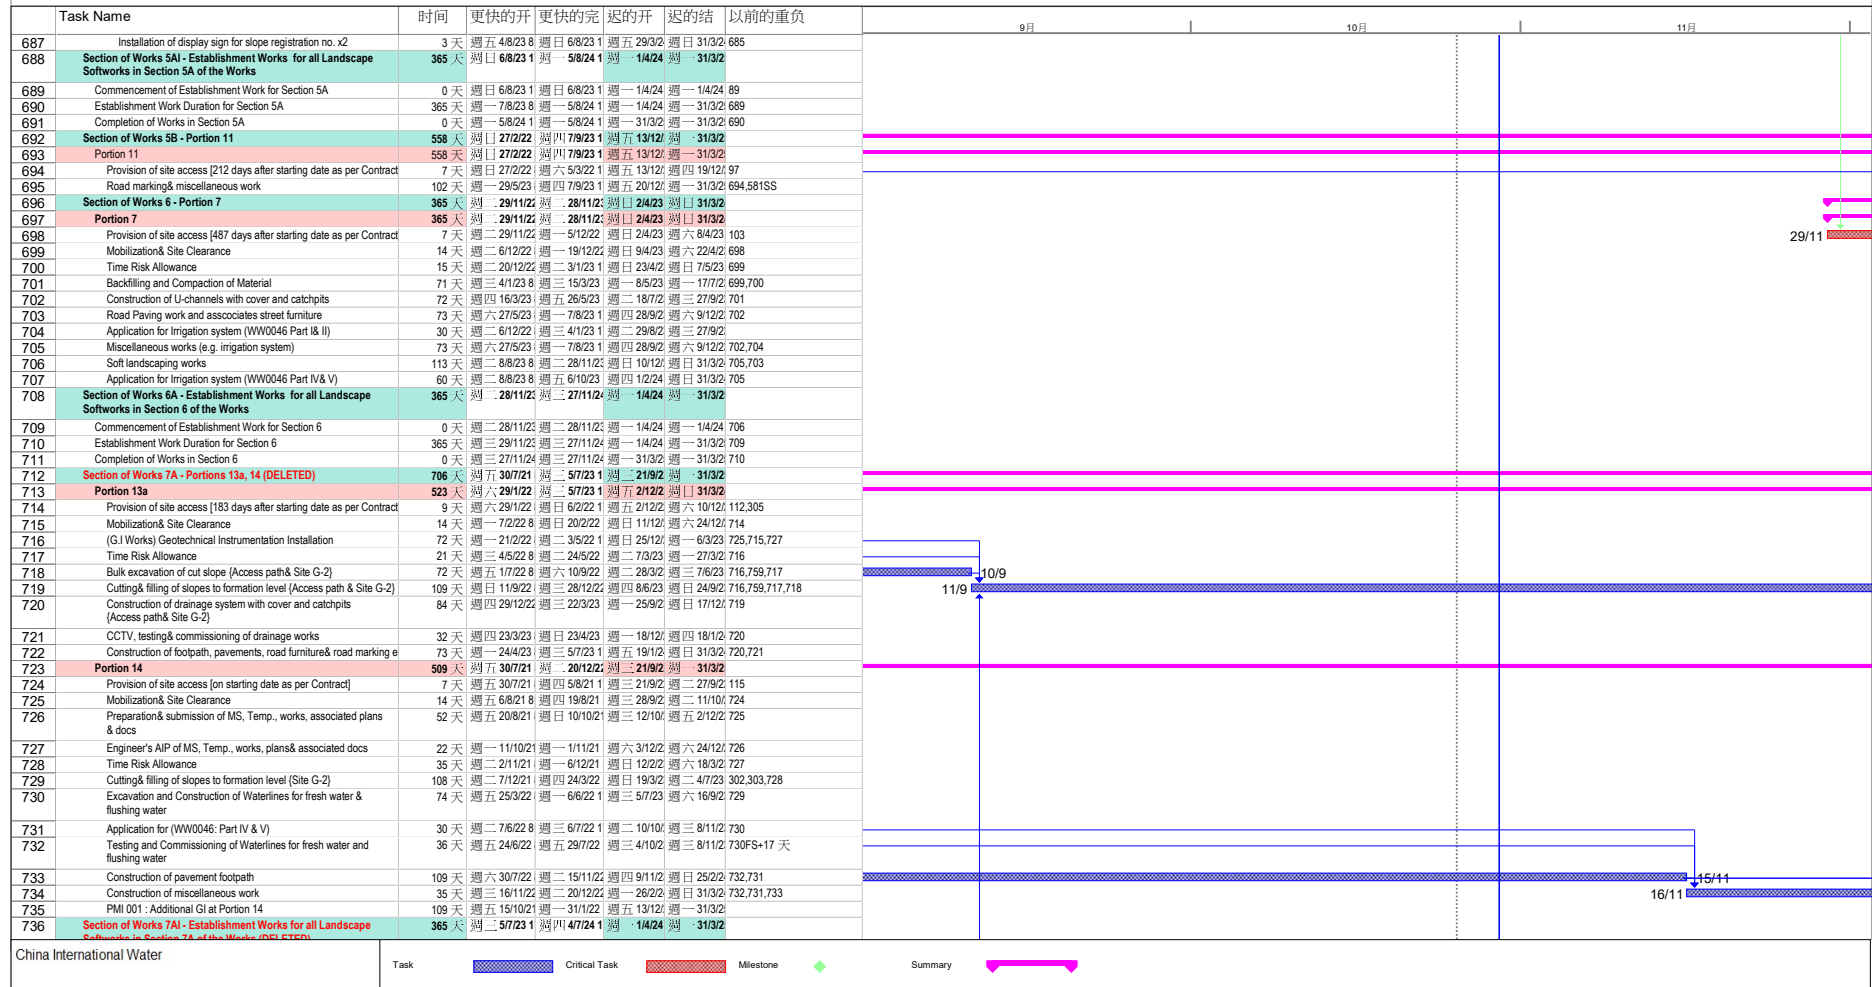


Updated on: 22 Aug 2022

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

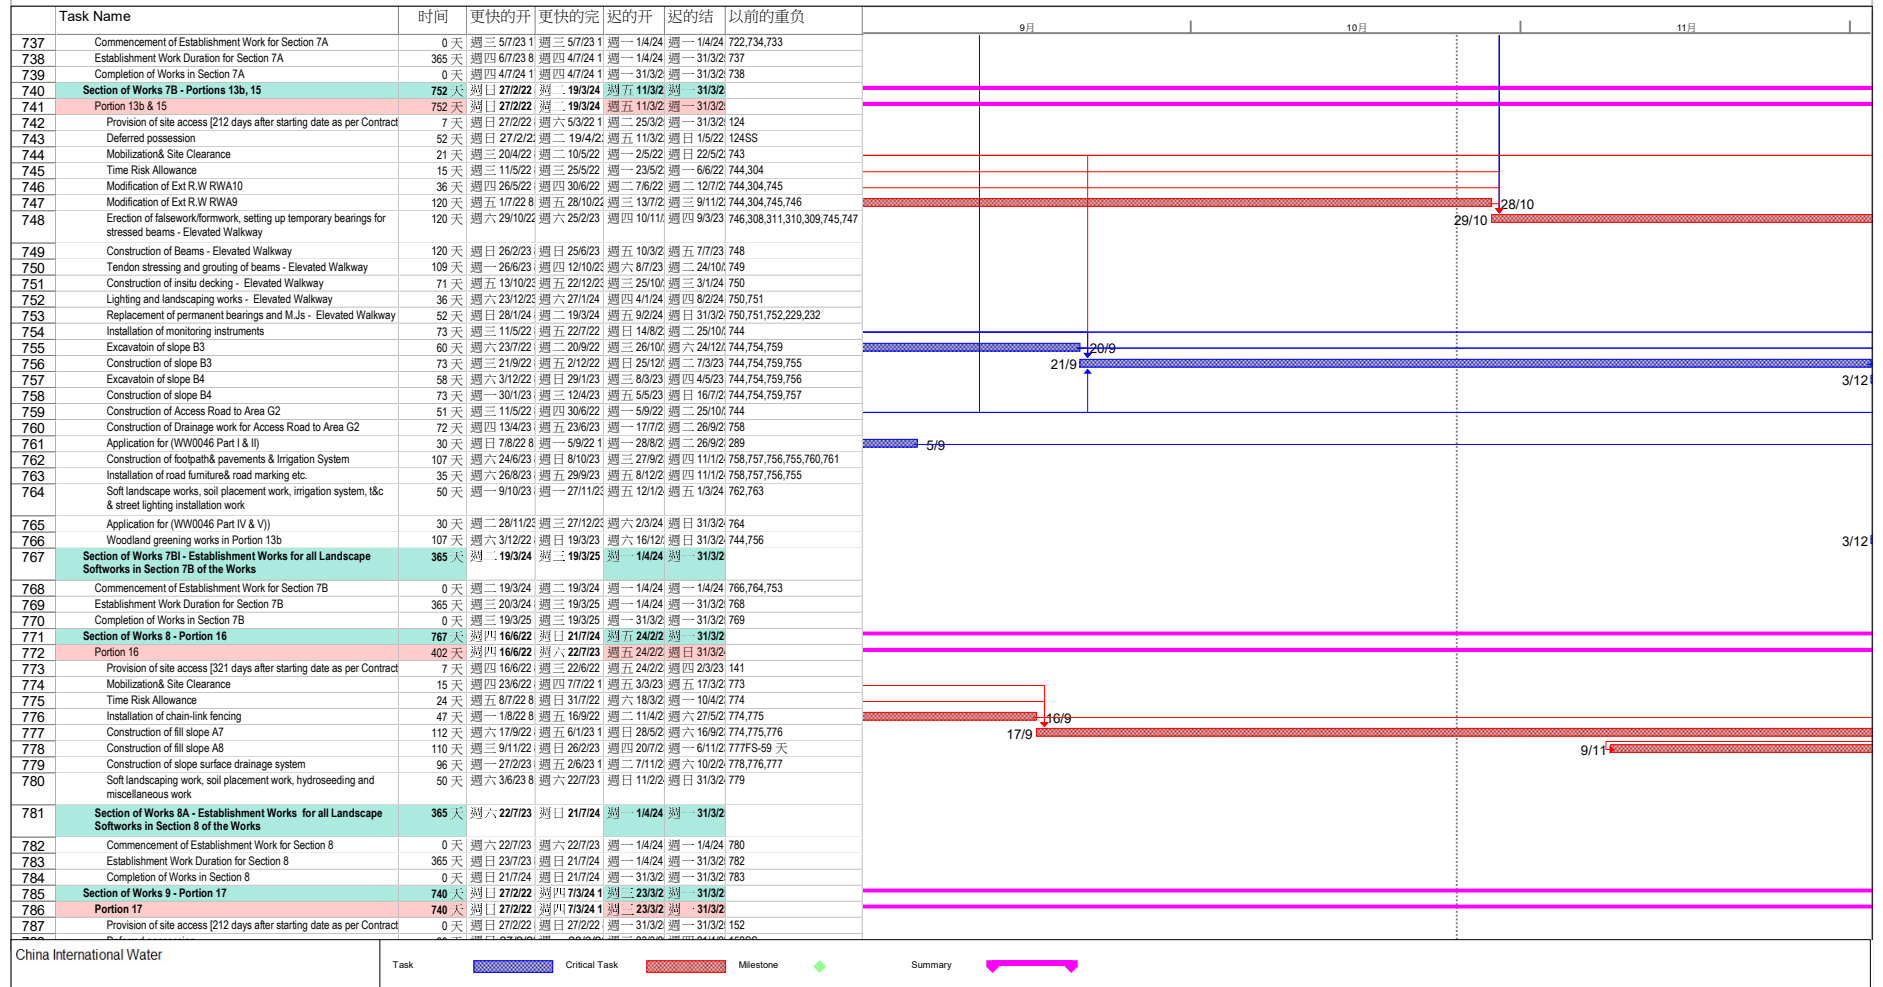


Updated on: 22 Aug 2022

China International Water & Electric Corp. CEDD Contract No. ED/2020/02

Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works

Revised Works Programme : August 2022

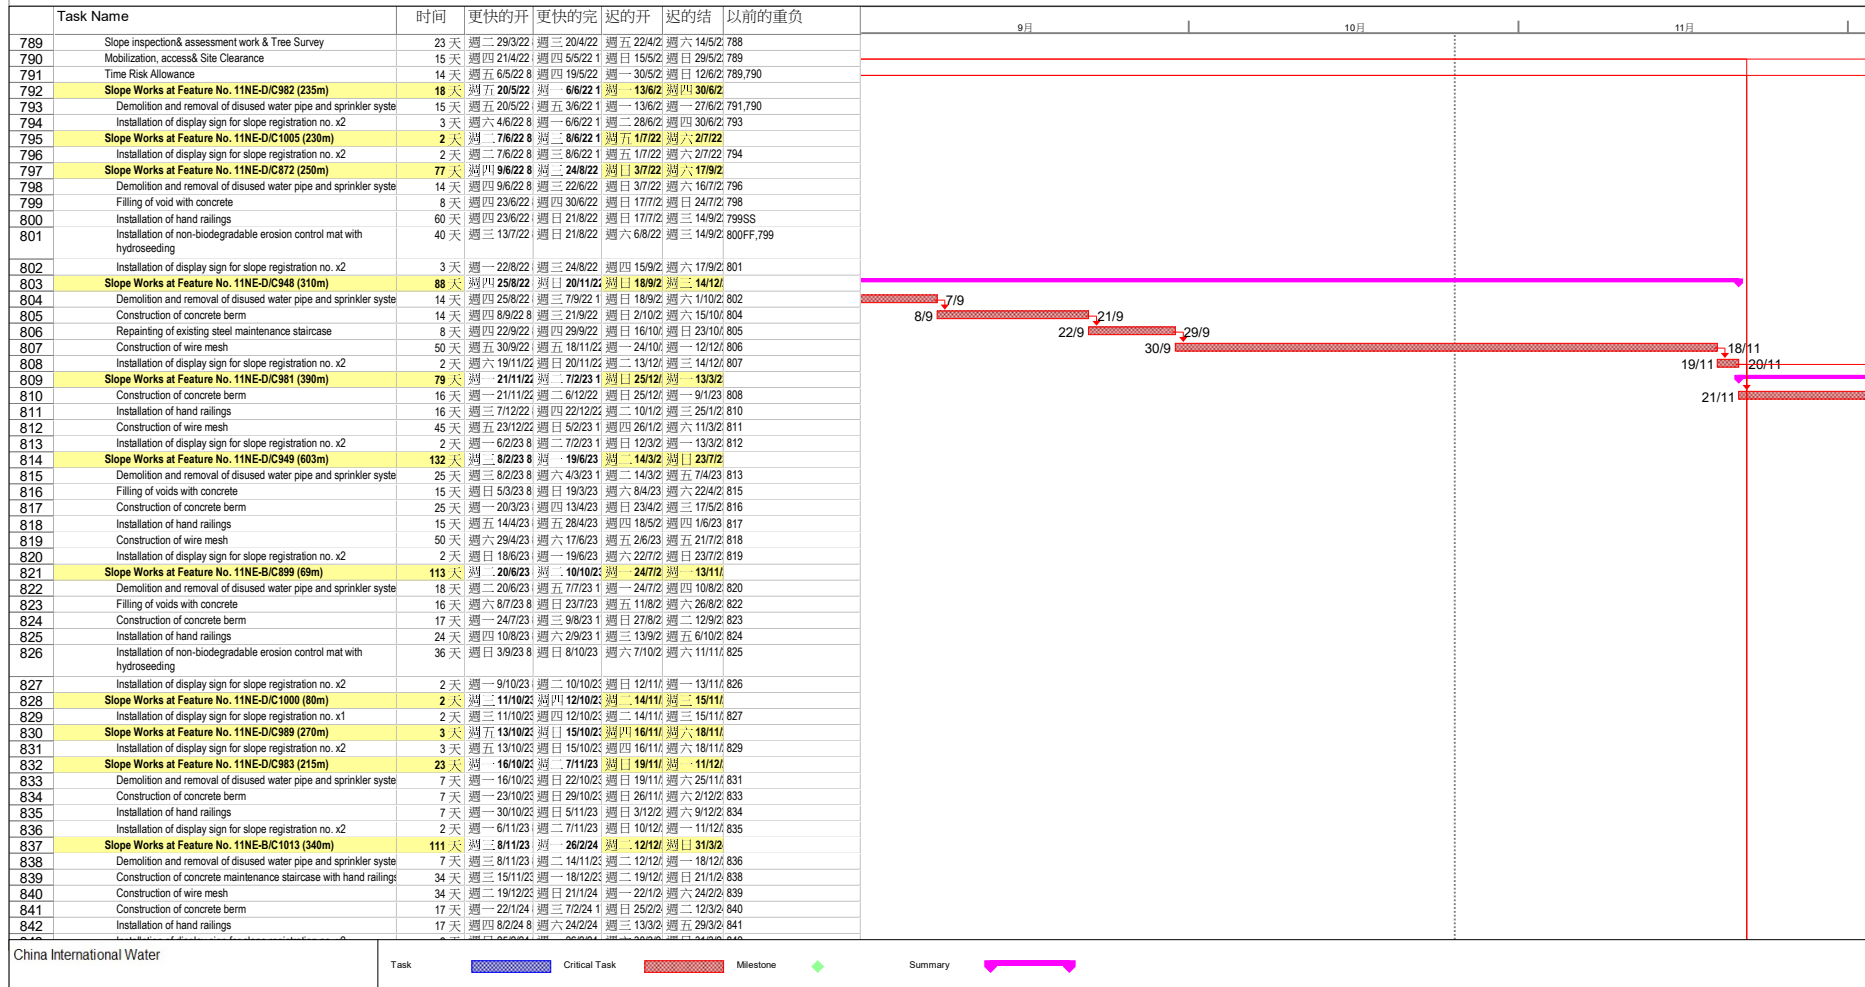

Updated on: 22 Aug 2022

China International Water & Electric Corp. CEDD Contract No. ED/2020/02
Development of Anderson Road Quarry Site - Infrastructure, Greening and Landscape Works
Revised Works Programme : August 2022

Task Name	时间	更快的开	更快的完	迟的开	迟的结	以前的重负				
844 Slope Works at Feature No. 11NE-B/C1014 (95m)	38 天	週一 21/11/22	週三 28/12/22	週四 15/12/22	週六 21/1/23			9月	10月	11月
845 Time Risk Allowance	21 天	週一 21/11/22	週日 11/12/22	週四 15/12/22	週三 4/1/23	791,808,790				
846 Demolition and removal of disused water pipe and sprinkler syste	7 天	週一 12/12/22	週日 18/12/22	週四 5/1/23	週三 11/1/23	791,808,790,845				
847 Removal of disused water pump and electricity box	7 天	週一 19/12/22	週日 25/12/22	週四 12/1/23	週三 18/1/23	846				
848 Installation of display sign for slope registration no. x1	3 天	週一 26/12/22	週三 28/12/22	週四 19/1/23	週六 21/1/23	847				
849 Slope Works at Feature No. 11NE-B/C900 (335m)	111 天	週四 29/12/22	週一 18/4/23	週一 22/1/23	週五 12/5/23					
850 Demolition and removal of disused water pipe and sprinkler syste	17 天	週四 29/12/22	週六 14/1/23	週日 22/1/23	週二 7/2/23	848				
851 Installation of non-biodegradable erosion control mat with hydroseeding	56 天	週日 15/1/23	週六 11/3/23	週三 8/2/23	週二 4/4/23	850				
852 Installation of hand railings	36 天	週日 12/3/23	週日 16/4/23	週三 5/4/23	週三 10/5/23	851				
853 Installation of display sign for slope registration no. x2	2 天	週一 17/4/23	週二 18/4/23	週四 11/5/23	週五 12/5/23	852				
854 Slope Works at Feature No. 11NE-B/C901 (290m)	107 天	週三 19/4/23	週四 3/8/23	週六 13/5/23	週一 27/8/23					
855 Filling of void with concrete	16 天	週三 19/4/23	週四 4/5/23	週六 13/5/23	週日 28/5/23	853				
856 Installation of non-biodegradable erosion control mat with hydroseeding	46 天	週五 5/5/23	週一 19/6/23	週一 29/5/23	週四 13/7/23	855				
857 Construction of lockable gate	7 天	週二 20/6/23	週一 26/6/23	週五 14/7/23	週四 20/7/23	856				
858 Installation of hand railings	36 天	週二 27/6/23	週二 1/8/23	週五 21/7/23	週五 25/8/23	857				
859 Installation of display sign for slope registration no. x1	2 天	週三 2/8/23	週四 3/8/23	週六 26/8/23	週日 27/8/23	858				
860 Slope Works at Feature No. 11NE-B/C902 (360m)	217 天	週五 4/8/23	週四 7/3/24	週一 28/8/23	週一 31/3/24					
861 Filling of void with cement soil	28 天	週五 4/8/23	週四 31/8/23	週一 28/8/23	週日 24/9/23	859				
862 Filling of void with concrete	18 天	週五 1/9/23	週一 18/9/23	週一 25/9/23	週四 12/10/23	861				
863 Construction of concrete berm	18 天	週二 19/9/23	週五 6/10/23	週五 13/10/23	週一 30/10/23	862				
864 Installation of hand railings	18 天	週六 7/10/23	週二 24/10/23	週二 31/10/23	週五 17/11/23	863				
865 Repainting of existing steel maintenance staircase	14 天	週三 25/10/23	週二 7/11/23	週六 18/11/23	週五 1/12/23	864				
866 Installation of display sign for slope registration no. x2	3 天	週三 8/11/23	週五 10/11/23	週六 21/12/23	週一 4/1/24	865				
867 Slope Works at Feature No. 11NE-B/C903 (105m)	32 天	週六 11/11/23	週一 12/12/23	週一 5/1/24	週五 5/1/24					
868 Installation of non-biodegradable erosion control mat with hydroseeding	30 天	週六 11/11/23	週日 10/12/23	週二 5/1/24	週三 31/1/24	866				
869 Installation of display sign for slope registration no. x1	2 天	週一 11/12/23	週二 12/12/23	週四 4/1/24	週五 5/1/24	868				
870 Slope Works at Feature No. 11NE-B/C224 (40m)	2 天	週三 13/12/23	週四 14/12/23	週六 6/1/24	週日 7/1/24					
871 Installation of display sign for slope registration no. x1	2 天	週三 13/12/23	週四 14/12/23	週六 6/1/24	週日 7/1/24	869				
872 Slope Works at Feature No. 11NE-B/C225 (60m)	84 天	週五 15/12/23	週四 7/3/24	週一 8/1/24	週一 31/3/24					
873 Demolition and removal of existing damaged U-channel	22 天	週五 15/12/23	週五 5/1/24	週一 8/1/24	週一 29/1/24	871				
874 Construction of 225 mm U-channel (-60m)	60 天	週六 6/1/24	週二 5/3/24	週二 30/1/24	週五 29/3/24	873				
875 Installation of display sign for slope registration no. x1	2 天	週三 6/3/24	週四 7/3/24	週六 30/3/24	週日 31/3/24	874				
876 Section of Works 9A - Establishment Works for all Landscape Softworks in Section 9 of the Works	365 天	週四 7/3/24	週五 7/3/25	週一 1/4/24	週一 31/3/24					
877 Commencement of Establishment Work for Section 9	0 天	週四 7/3/24	週四 7/3/24	週一 1/4/24	週一 1/4/24	875				
878 Establishment Work Duration for Section 9	365 天	週五 8/3/24	週五 7/3/25	週一 1/4/24	週一 31/3/24	877				
879 Completion of Works in Section 9	0 天	週五 7/3/25	週五 7/3/25	週一 31/3/24	週一 31/3/24	878				
880 Section of Works 10 - All Tree Protection and Preservation Works	922 天	週五 30/7/21	週一 6/2/24	週四 22/9/22	週一 31/3/24					
881 Commencement of All Tree Protection and Preservation Work	0 天	週五 30/7/21	週五 30/7/21	週四 22/9/22	週四 22/9/22					
882 All Tree Protection and Preservation Work, Duration for Section 8	922 天	週五 30/7/21	週二 6/2/24	週四 22/9/22	週一 31/3/24	881				
883 Completion of All Tree Protection and Preservation Work	0 天	週二 6/2/24	週二 6/2/24	週一 31/3/24	週一 31/3/24	882				

China International Water

Task

Critical Task

Milestone

◆


Summary

Updated on: 22 Aug 2022

Page 18 /18

Contract 5 (NE/2019/02)

Major Activities in Coming 3 Months

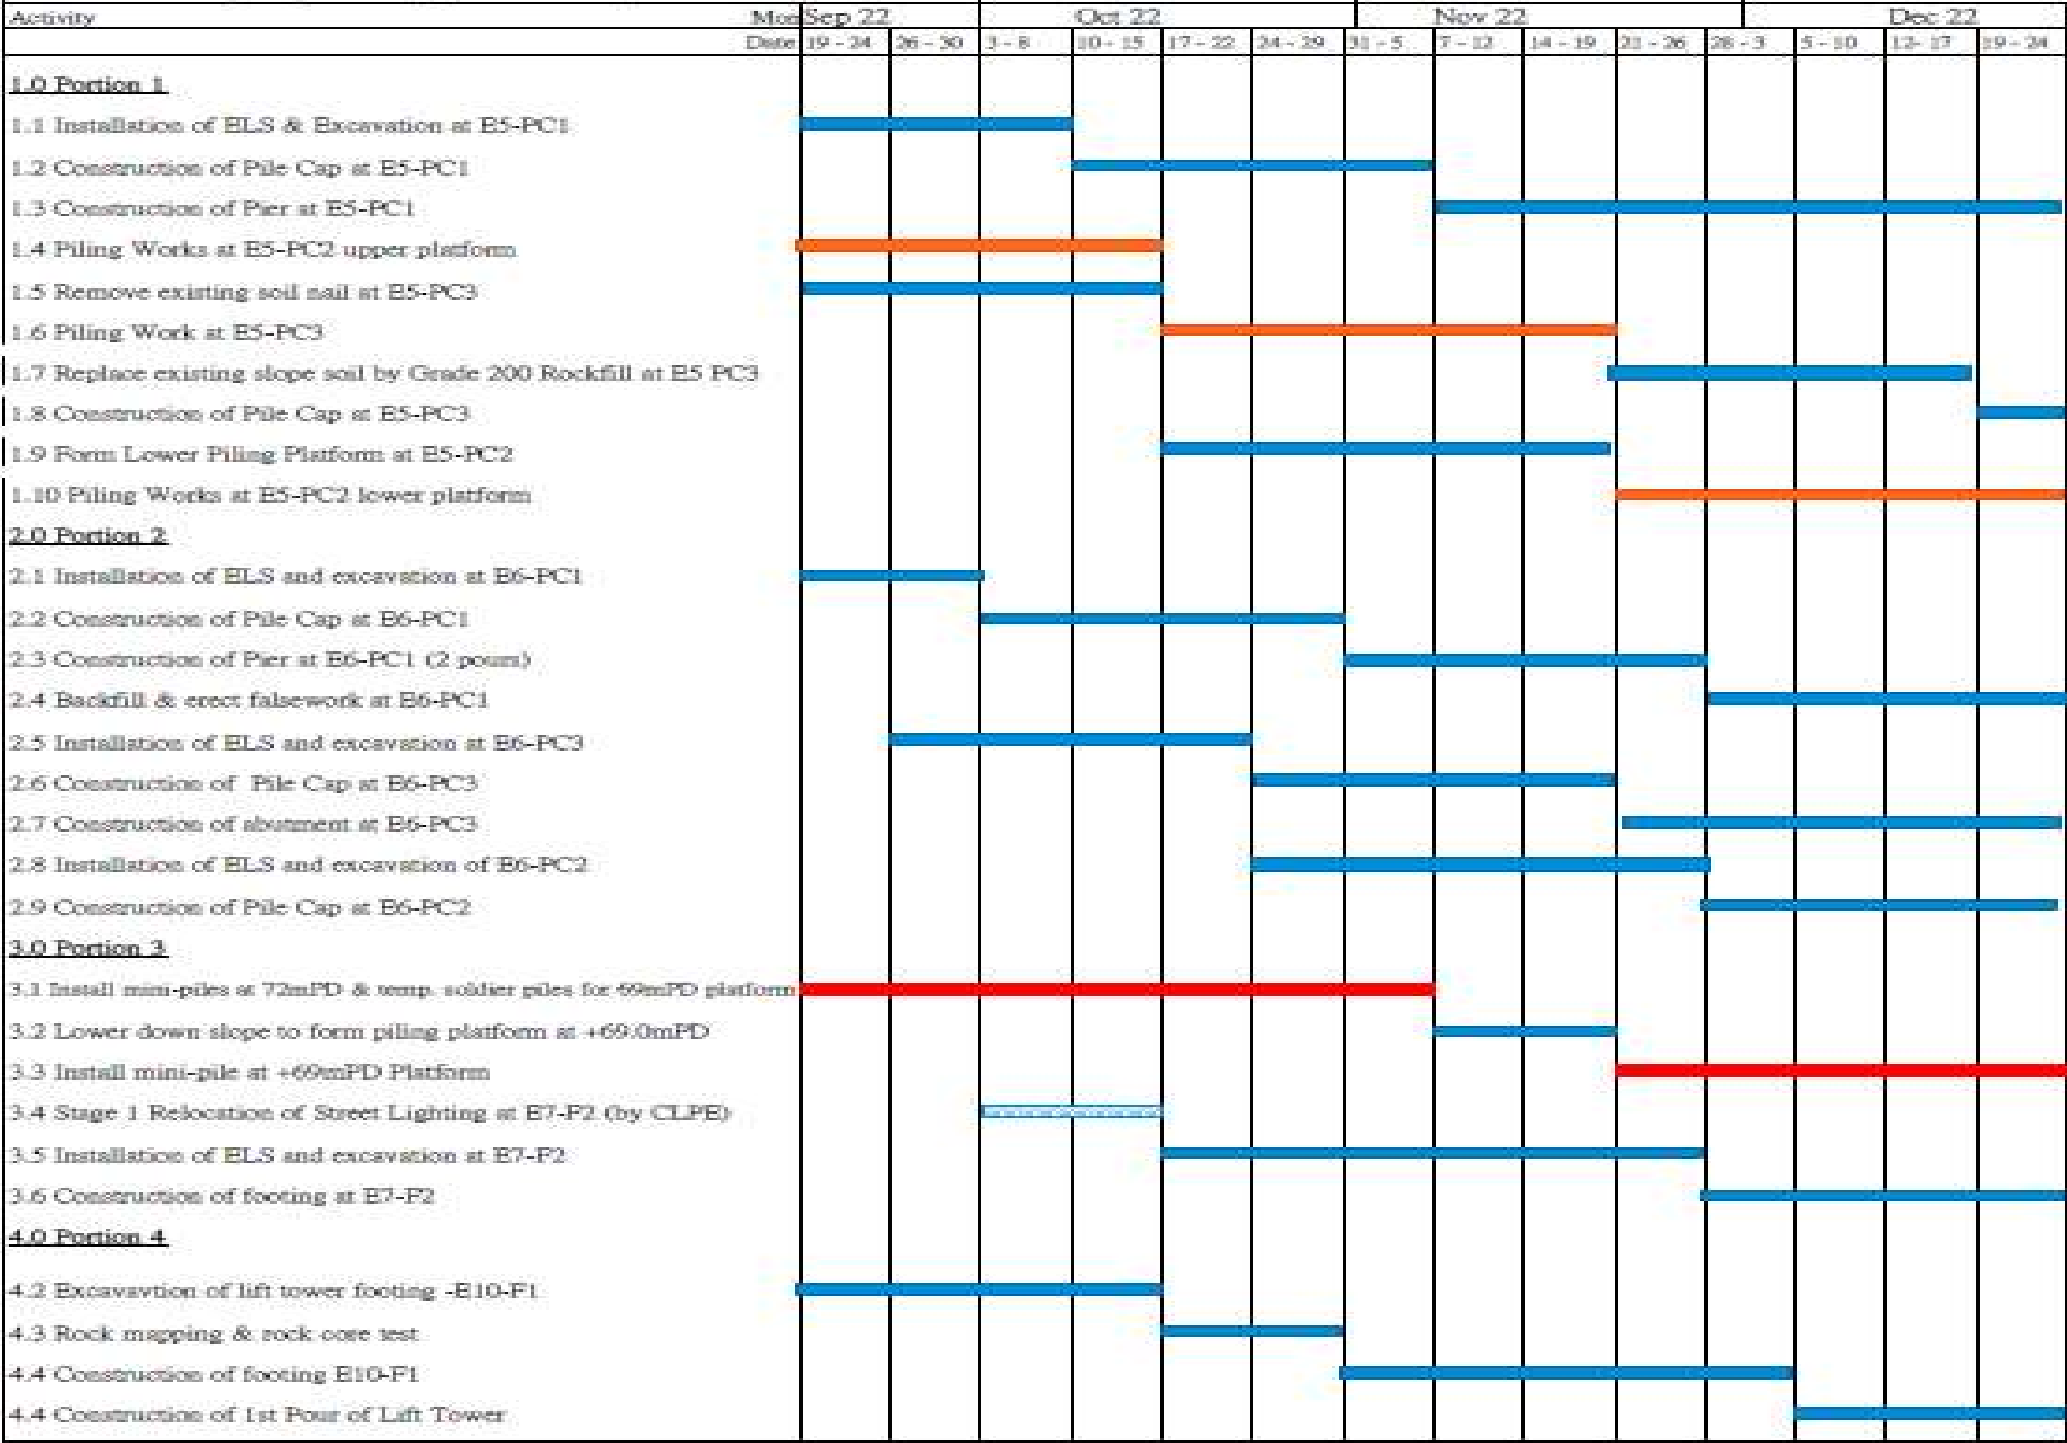

Appendix D

Monitoring Locations for Impact Monitoring

**Monitoring Locations
for
Contract 1 (NE/2016/01)**


DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED
© DYE ARUP



HVS in AMS-1 for 24-Hour TSP



- Legend
- Study Area
 - 500m Assessment Area
 - Dust Monitoring Locations

B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Construction Dust Monitoring (Sheet 1 of 3)			
Drawing no.		Rev.	
227724/E/1045		B	
Drawn GL	Date 03/14	Checked TC	Approved ST
Scale 1:5000 @A3		Status PRELIMINARY	
COPYRIGHT RESERVED			
			
土木工程拓展署 Civil Engineering and Development Department			

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© THE ARUP & PARTNERS HONG KONG LIMITED

Legend

-  Study Area
-  500m Assessment Area
-  Dust Monitoring Locations

B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Construction Dust Monitoring (Sheet 2 of 3)			
Drawing no.		Rev.	
227724/E/1046		B	
Drawn GL	Date 03/14	Checked TC	Approved ST
Scale 1:5000 @A3		Status PRELIMINARY	



HVS in AMS-5 for 24-Hour TSP



HVS in AMS-6 for 24-Hour TSP




DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED
© DYE ARUP



HVS in AMS-1 for 24-Hour TSP



- Legend
- Study Area
 - 500m Assessment Area
 - Dust Monitoring Locations

B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Construction Dust Monitoring (Sheet 1 of 3)			
Drawing no.		Rev.	
227724/E/1045		B	
Drawn GL	Date 03/14	Checked TC	Approved ST
Scale 1:5000 @A3		Status PRELIMINARY	
COPYRIGHT RESERVED			
			
土木工程拓展署 Civil Engineering and Development Department			

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© THE ARUP & PARTNERS HONG KONG LIMITED

NMS-7 (Chi Tai House of On Tai Estate)

Building layout is assumed for assessment purpose

NMS-6 (Yung Tai House of On Tai Estate)

Building layout is assumed for assessment purpose

NMS-3 (Site C2 - R102)

NMS-1 (Site C2 + School 05)

NMS-5 (Hau Tat House of On Tat Estate)

NMS-4 / NMS-4a (On Tat House of On Tat Estate)

Building layout is assumed for assessment purpose

NMS-2 (Site E - School)
(Site E - School)

Legend

- Study Area
- Construction Noise Monitoring Location
- Construction and Operational Road Traffic Noise Monitoring Location
- Review Noise monitoring Location

C	THIRD ISSUE	GL	05/14
B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date

Consultant

ARUP

Contract No. and Title

Agreement No. CE 18/2012(CE)

Development of
Anderson Road Quarry -
Investigation

Drawing title

Locations of Noise
Monitoring

Drawing no.	227724/E/2400	Rev.	C
Drawn	Date	Checked	Approved
GL	05/14	TC	ST
Scale	1:5000	Status	PRELIMINARY

COPYRIGHT RESERVED



土木工程拓展署
Civil Engineering and
Development Department

DO NOT SCALE DRAWING/ CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© THE ARUP & PARTNERS HONG KONG LIMITED

Legend

-  Study Area
-  500m Assessment Area
-  Dust Monitoring Locations



HVS in AMS-5 for 24-Hour TSP



HVS in AMS-6 for 24-Hour TSP



B SECOND ISSUE		GL	03/14
A FIRST ISSUE		GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Construction Dust Monitoring (Sheet 2 of 3)			
Drawing no. 227724/E/1046		Rev. B	
Drawn	Date	Checked	Approved
GL	03/14	TC	ST
Scale 1:5000		Status PRELIMINARY	

COPYRIGHT RESERVED



土木工程發展署
Civil Engineering and
Development Department



- Legend**
- Study Area
 - 500m Assessment Area
 - Dust Monitoring Locations
 - Noise Monitoring Location

Rev	Description	By	Date
B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13

Consultant

Contract No. and Title


Agreement No. CE 18/2012(CE)
Development of
Anderson Road Quarry -
Investigation

Drawing Title
Locations of Construction Dust
and Noise Monitoring


COPYRIGHT RESERVED


**Monitoring Locations
for
Contract 3 (NE/2017/03)**

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© THE ARUP & PARTNERS HONG KONG LIMITED

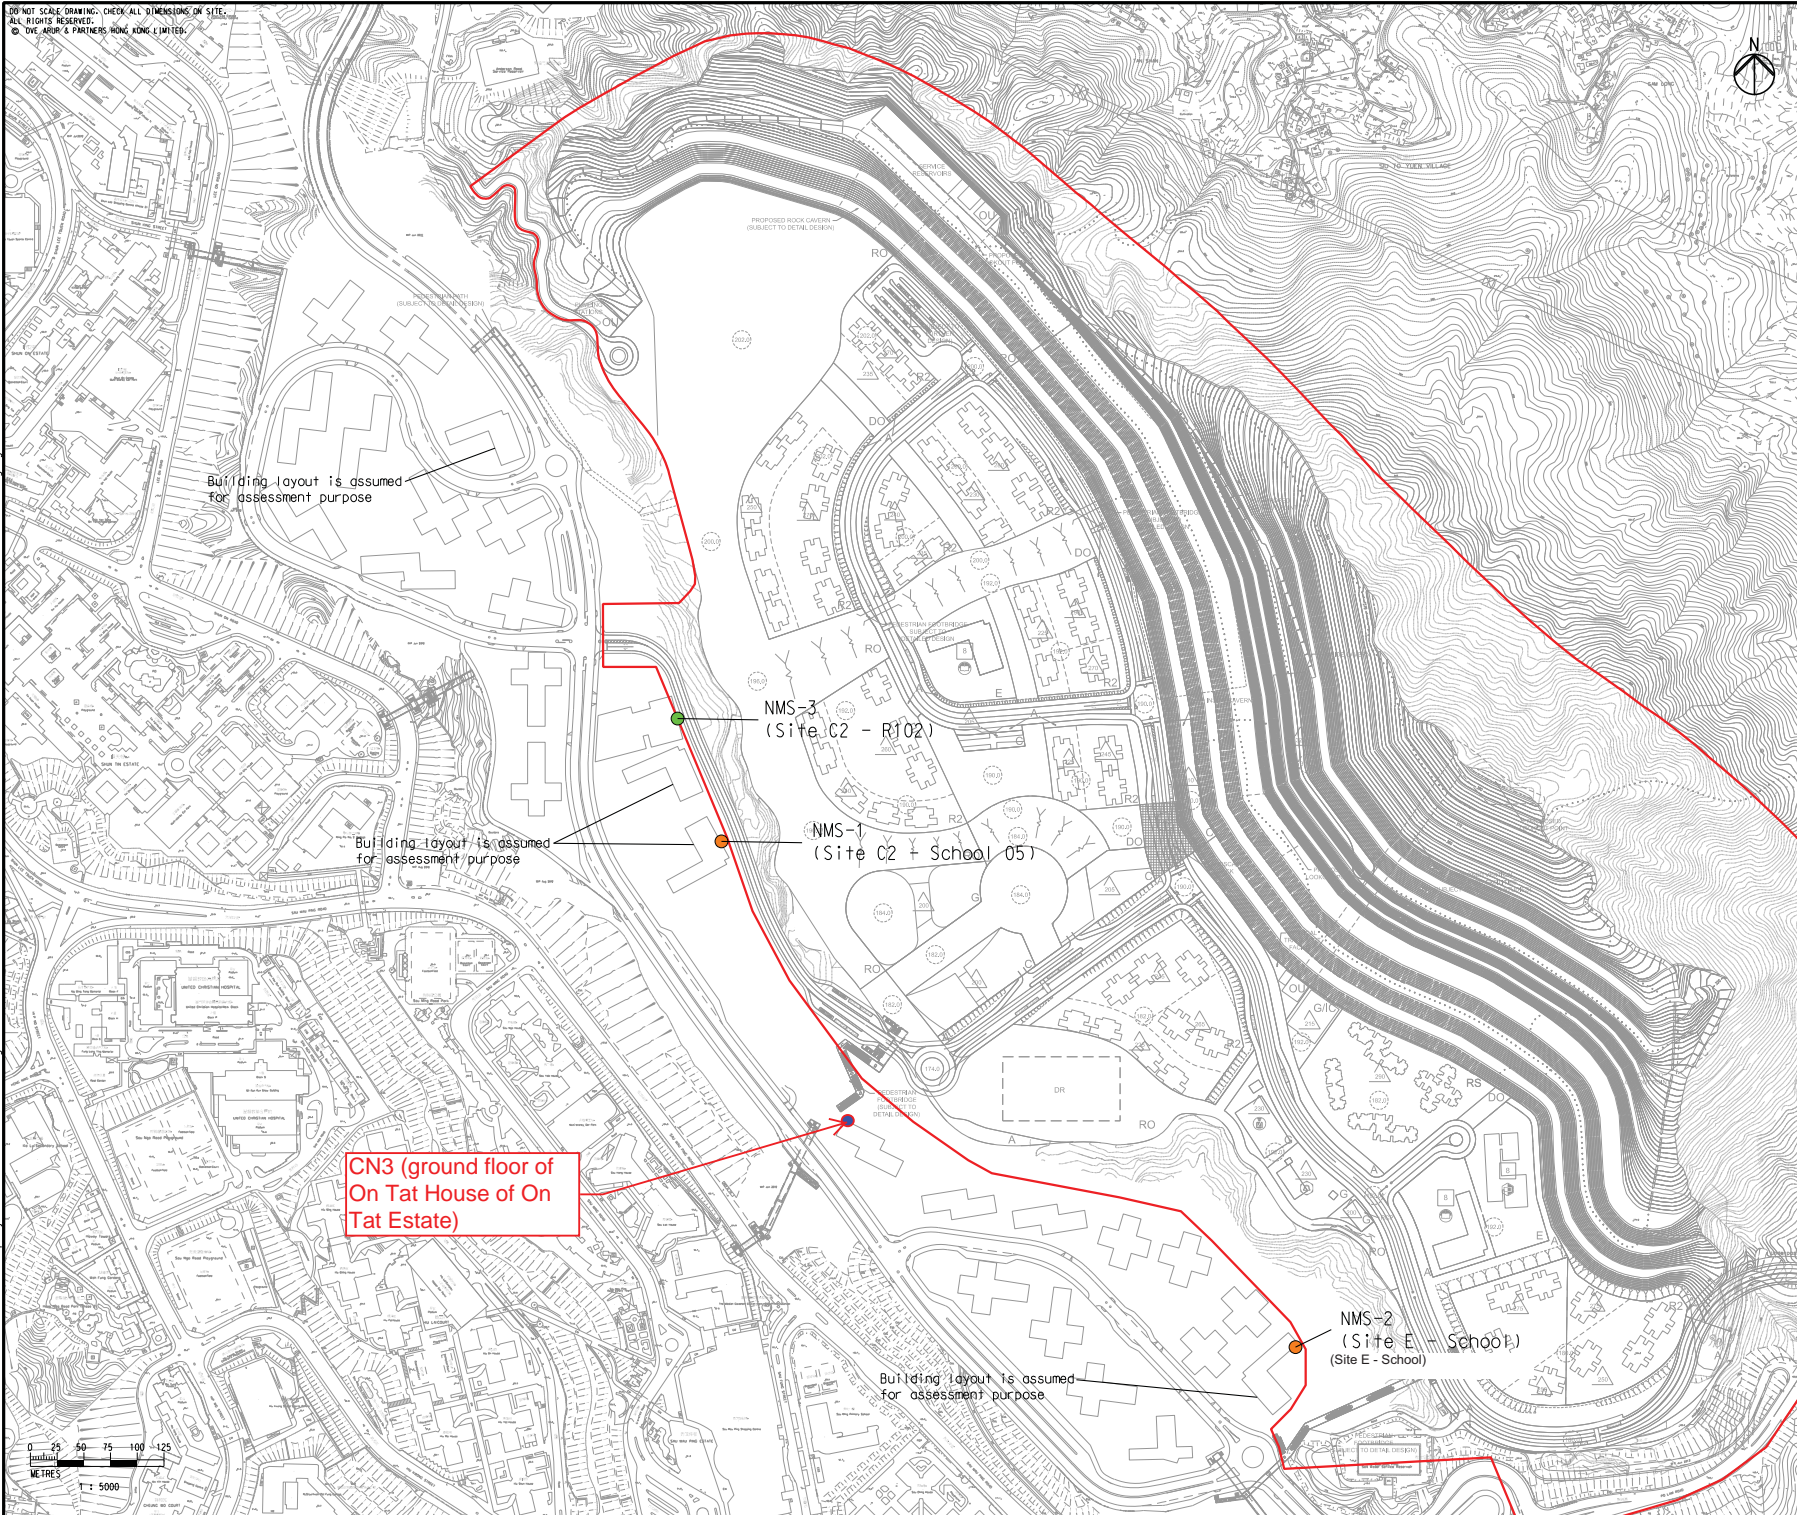

- Legend
- Study Area
 - Construction Noise Monitoring Location
 - Construction and Operational Road Traffic Noise Monitoring Location
 - Noise monitoring Location

C	THIRD ISSUE	GL	05/14
B	SECOND ISSUE	GL	03/14
A	FIRST ISSUE	GL	10/13
Rev	Description	By	Date
Consultant			
ARUP			
Contract No. and Title			
Agreement No. CE 18/2012(CE)			
Development of Anderson Road Quarry - Investigation			
Drawing title			
Locations of Noise Monitoring			
Drawing no.		Rev.	
227724/E/2400		C	
Drawn	Date	Checked	Approved
GL	05/14	TC	ST
Scale	1:5000	Status	PRELIMINARY
COPYRIGHT RESERVED			
 土木工程拓展署 Civil Engineering and Development Department			

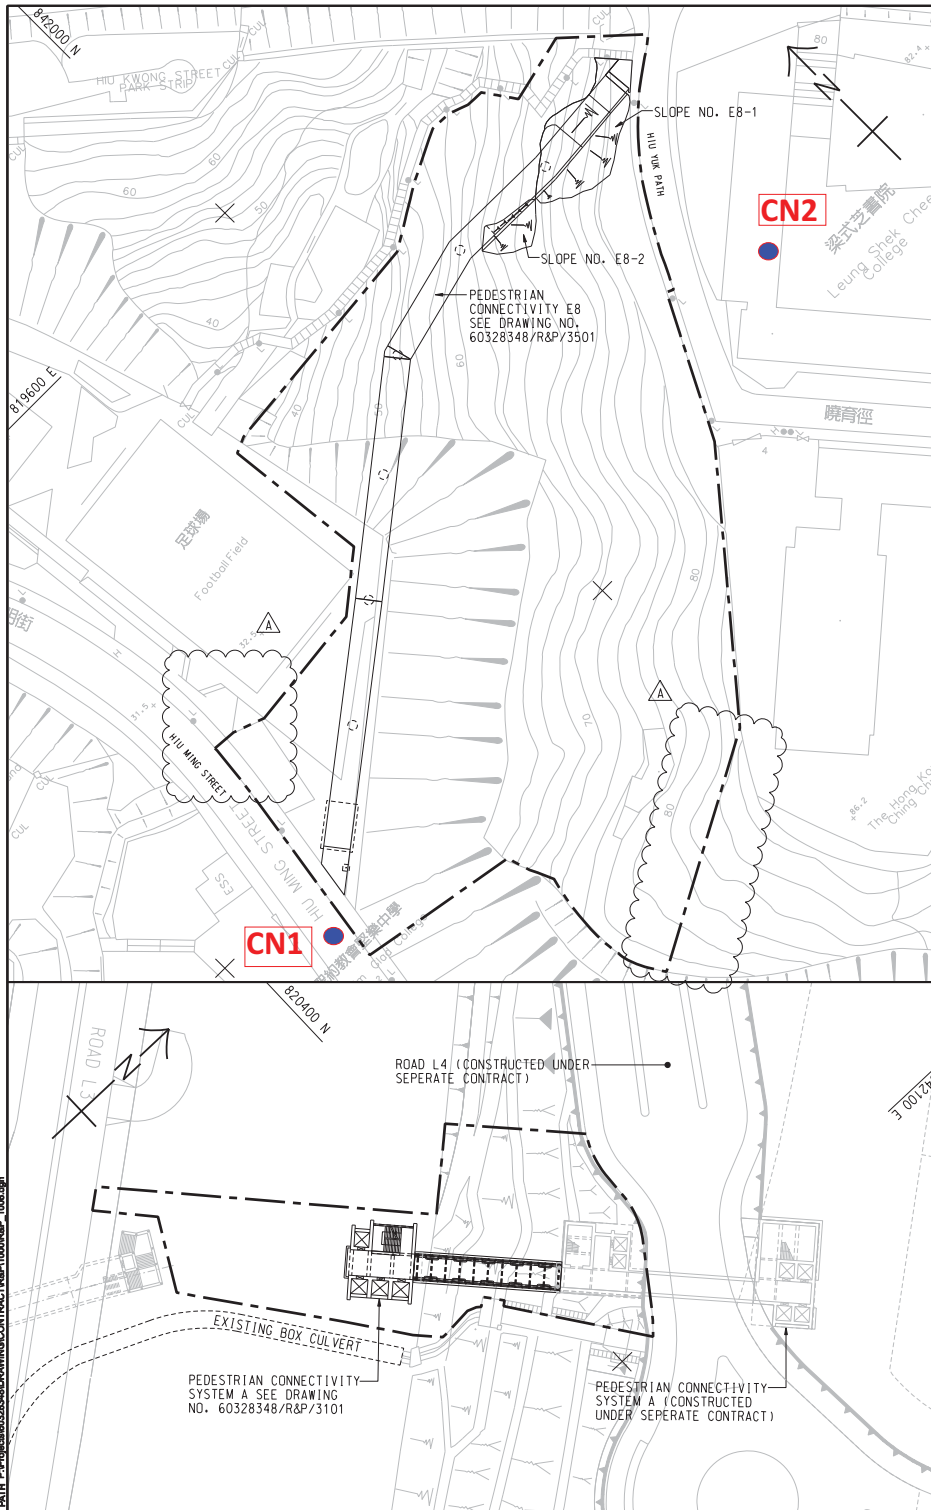

NOTES:
1. FOR NOTES AND LEGEND REFER TO DRAWING NO. 60328348/R&P/1001.
2. THIS DRAWING TO BE READ IN CONJUNCTION WITH DRAWING NOS. 60328348/R&P/1001 TO 1008.

AECOM
PROJECT NO. 60328348
CONTRACT NO. NE/2017/03
SHEET TITLE GENERAL LAYOUT
SHEET NUMBER 60328348/R&P/1008A

DEVELOPMENT OF ANDERSON ROAD QUARRY SITE - INVESTIGATION, DESIGN AND CONSTRUCTION
CONTRACT TITLE DEVELOPMENT OF ANDERSON ROAD QUARRY SITE - ROAD IMPROVEMENT WORKS AND PEDESTRIAN CONNECTIVITY FACILITIES WORKS PHASE 2A
CLIENT AECOM
CONSULTANT AECOM Asia Company Ltd.
SUB-CONSULTANTS

Issue/Revision
A NOV. 17 TENDER ADDENDUM NO. 1
OCT. 17 TENDER DRAWING
MR. DATE DESCRIPTION CHK.
STATUS
SCALE A1: 500 DIMENSION UNIT METRES
KEY PLAN
PROJECT NO. 60328348
CONTRACT NO. NE/2017/03
SHEET TITLE GENERAL LAYOUT
SHEET NUMBER 60328348/R&P/1008A

noise monitoring location

Appendix E

Calibration Certificate of Monitoring Equipment and HOKLAS-accreditation Certificate of the Testing Laboratory

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Tan Shan Village No. 5 - 6				Date of Calibration: 29-Jul-22			
Location ID : AMS1a				Next Calibration Date: 30-Oct-22			
Model: TISCH High Volume Air Sampler TE-5170				Technician: Mr. Fai So			
CONDITIONS							
Sea Level Pressure (hPa)		<div style="border: 1px solid black; padding: 2px;">1005.9</div>		Corrected Pressure (mm Hg)		<div style="border: 1px solid black; padding: 2px;">754.425</div>	
Temperature (°C)		<div style="border: 1px solid black; padding: 2px;">29.2</div>		Temperature (K)		<div style="border: 1px solid black; padding: 2px;">302</div>	
CALIBRATION ORIFICE							
Make->		<div style="border: 1px solid black; padding: 2px;">TISCH</div>		Qstd Slope ->		<div style="border: 1px solid black; padding: 2px;">1.99838</div>	
Model->		<div style="border: 1px solid black; padding: 2px;">TE-5025A</div>		Qstd Intercept ->		<div style="border: 1px solid black; padding: 2px;">-0.00903</div>	
Serial # ->		<div style="border: 1px solid black; padding: 2px;">1941</div>					
CALIBRATION							
Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.4	6.4	12.8	1.776	51	50.46	Slope = 36.5599 Intercept = -14.8015 Corr. coeff. = 0.9967
13	5.2	5.2	10.4	1.601	45	44.52	
10	4	4	8	1.405	35	34.63	
7	2.4	2.4	4.8	1.089	26	25.72	
5	1.5	1.5	3	0.862	17	16.82	
<p>Calculations :</p> <p>Qstd = 1/m[Sqrt(H2O(Pa/Pstd)(Tstd/Ta))-b]</p> <p>IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]</p> <p>Qstd = standard flow rate</p> <p>IC = corrected chart responses</p> <p>I = actual chart response</p> <p>m = calibrator Qstd slope</p> <p>b = calibrator Qstd intercept</p> <p>Ta = actual temperature during calibration (deg K)</p> <p>Pstd = actual pressure during calibration (mm Hg)</p> <p>For subsequent calculation of sampler flow:</p> <p>1/m((I) [Sqrt(298/Tav)(Pav/760)]-b)</p> <p>m = sampler slope</p> <p>b = sampler intercept</p> <p>I = chart response</p> <p>Tav = daily average temperature</p> <p>Pav = daily average pressure</p>							

FLOW RATE CHART

Standard Flow Rate (m3/min)	Actual chart response (IC)
0.862	16.82
1.089	25.72
1.405	34.63
1.601	44.52
1.776	50.46

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Oi Tat House	Date of Calibration: 29-Jul-22
Location ID : AMS 5	Next Calibration Date: 30-Oct-22
Model: TISCH High Volume Air Sampler TE-5170	Technician: Mr. Fai So

CONDITIONS

Sea Level Pressure (hPa)	1005.9	Corrected Pressure (mm Hg)	754.425
Temperature (°C)	29.2	Temperature (K)	302

CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope -> 1.99838
Model-> TE-5025A	Qstd Intercept -> -0.00903
Serial # -> 1941	

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.4	6.4	12.8	1.776	56	55.41	Slope = 40.7127 Intercept = -18.6613 Corr. coeff. = 0.9912
13	5.2	5.2	10.4	1.601	47	46.50	
10	4.2	4.2	8.4	1.439	37	36.61	
7	2.6	2.6	5.2	1.133	29	28.69	
5	1.5	1.5	3	0.862	17	16.82	

Calculations :

$Qstd = 1/m[\text{Sqrt}(H20(Pa/Pstd)(Tstd/Ta)) - b]$
 $IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:

$1/m((I) [\text{Sqrt}(298/Tav)(Pav/760)] - b)$

m = sampler slope


b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

FLOW RATE CHART

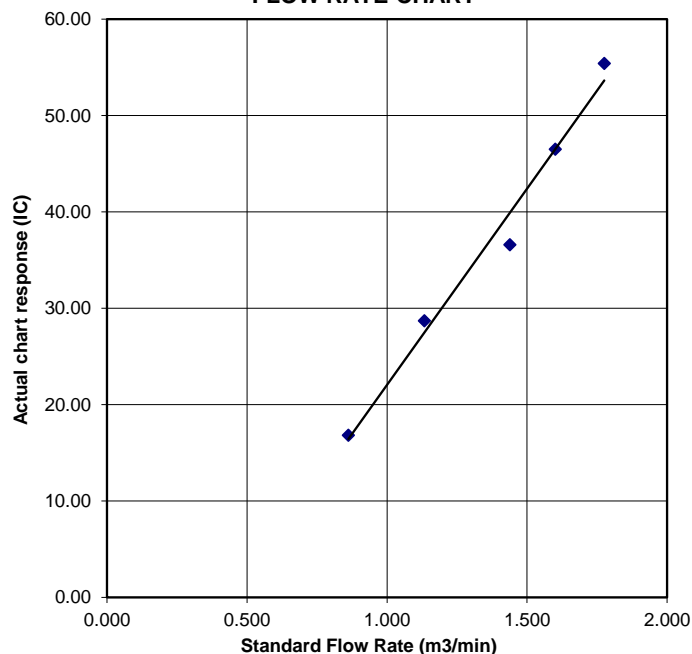

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Date of Calibration: 29-Jul-22

Next Calibration Date: 30-Oct-22

Technician: Mr. Fai So

CONDITIONS

1005.9

29.2

754.425

302

CALIBRATION ORIFICE

TISCH

TE-5025A

1941

1.99838

-0.00903

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.3	6.3	12.6	1.762	53	52.44	Slope = 41.9587
13	5.4	5.4	10.8	1.632	45	46.00	Intercept = -21.6530
10	3.7	3.7	7.4	1.351	35	34.63	Corr. coeff. = 0.9943
7	2.5	2.5	5	1.112	28	27.70	
5	1.5	1.5	3	0.862	13	12.86	

Calculations :

$$Q_{std} = 1/m[\text{Sqrt}(H20(Pa/P_{std})(T_{std}/T_a)) - b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

 $m = \text{calibrator Qstd slope}$

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/T_{av})(P_{av}/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

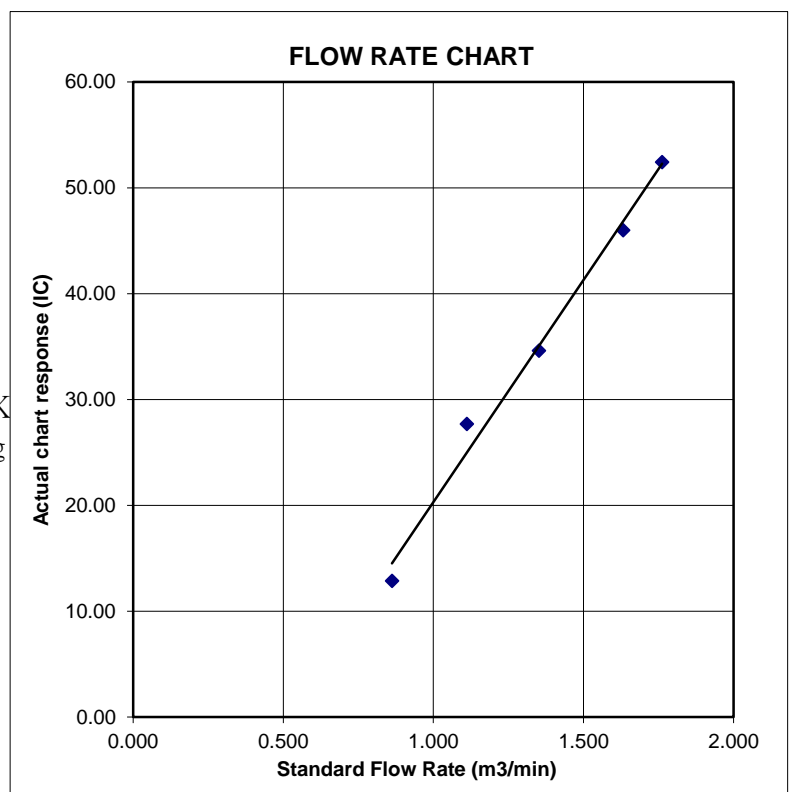

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Ma Yau Tong Village

Date of Calibration: 29-Jul-22

Location ID : AMS 7

Next Calibration Date: 30-Oct-22

Model: TISCH High Volume Air Sampler TE-5170

Technician: Mr. Fai So

CONDITIONS

Sea Level Pressure (hPa)

1005.9

Corrected Pressure (mm Hg)

754.425

Temperature (°C)

29.2

Temperature (K)

302

CALIBRATION ORIFICE

Make-> TISCH

Qstd Slope ->

1.99838

Model-> TE-5025A

Qstd Intercept ->

-0.00903

Serial # -> 1612

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	6.5	6.5	13	1.790	56	55.41	Slope = 43.9346
13	5.5	5.5	11	1.647	48	47.49	Intercept = -23.9309
10	3.7	3.7	7.4	1.351	35	34.63	Corr. coeff. = 0.9965
7	2.7	2.7	5.4	1.155	29	28.69	
5	1.9	1.9	3.8	0.970	18	17.81	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

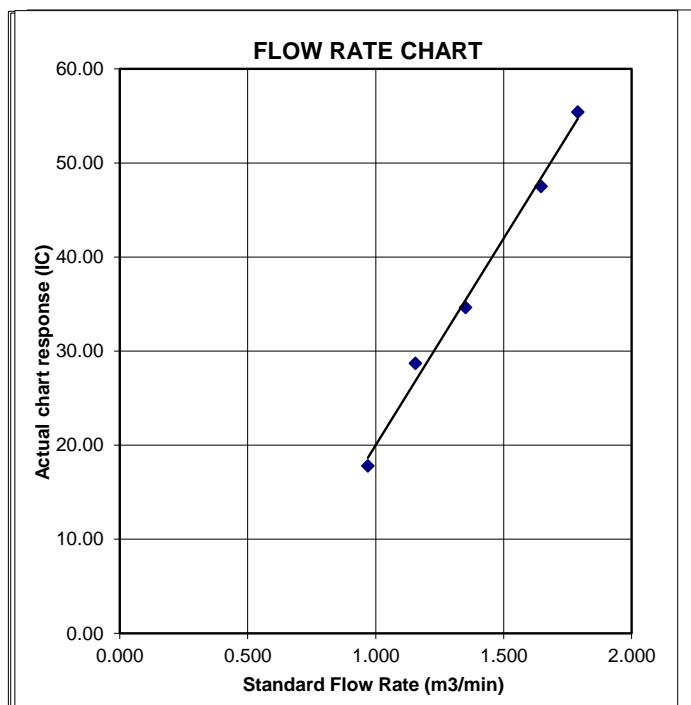



Certificate of Calibration

Calibration Certification Information

Cal. Date:	December 27, 2021	Rootsmeter S/N:	438320	Ta:	295	°K
Operator:	Jim Tisch	Pa:	740.4			mm Hg
Calibration Model #:	TE-5025A	Calibrator S/N:	1612			

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.3890	3.2	2.00
2	3	4	1	0.9760	6.4	4.00
3	5	6	1	0.8740	7.9	5.00
4	7	8	1	0.8320	8.8	5.50
5	9	10	1	0.6870	12.7	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
0.9799	0.7055	1.4029	0.9957	0.7168	0.8927
0.9756	0.9996	1.9841	0.9914	1.0157	1.2624
0.9736	1.1140	2.2183	0.9893	1.1320	1.4114
0.9724	1.1688	2.3265	0.9881	1.1876	1.4803
0.9673	1.4079	2.8059	0.9828	1.4306	1.7853
QSTD	m=	1.99838	QA	m=	1.25135
	b=	-0.00903		b=	-0.00574
	r=	0.99999		r=	0.99999

Calculations

Vstd=	$\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va=	$\Delta Vol((Pa-\Delta P)/Pa)$
Qstd=	Vstd/ΔTime	Qa=	Va/ΔTime
For subsequent flow rate calculations:			
Qstd= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$		Qa= $1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$	

Standard Conditions

Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30

Certificate of Calibration

校正證書

Certificate No. : C221362
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC22-0258) Date of Receipt / 收件日期 : 14 February 2022

Description / 儀器名稱 : Sound Calibrator (EQ089)
Manufacturer / 製造商 : Rion
Model No. / 型號 : NC-75
Serial No. / 編號 : 34680623
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(50 \pm 25)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 12 March 2022

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Fluke Everett Service Center, USA
- Agilent Technologies / Keysight Technologies

Tested By : 
測試 K C Lee
Engineer

Certified By : 
核證 H C Chan
Engineer

Date of Issue : 16 March 2022
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C221362

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C213954
CL281	Multifunction Acoustic Calibrator	AV210017
TST150A	Measuring Amplifier	C201309

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.25	± 0.2

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C221363
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC22-0258) Date of Receipt / 收件日期 : 14 February 2022

Description / 儀器名稱 : Sound Level Meter (EQ067)
Manufacturer / 製造商 : Rion
Model No. / 型號 : NL-31
Serial No. / 編號 : 00410221
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(50 \pm 25)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 12 March 2022

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Fluke Everett Service Center, USA
- Agilent Technologies / Keysight Technologies

Tested By : 
測試 : K C Lee
Engineer

Certified By : 
核證 : H C Chan
Engineer

Date of Issue : 16 March 2022
簽發日期

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C221363

證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID

CL280

CL281

Description

40 MHz Arbitrary Waveform Generator

Multifunction Acoustic Calibrator

Certificate No.

C220381

AV210017

- Test procedure : MA101N.

- Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT	IEC 61672 Class 1
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Spec. (dB)
30 - 120	L _A	A	Fast	94.00	1	93.8	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
30 - 120	L _A	A	Fast	94.00	1	93.8 (Ref.)
				104.00		103.8
				114.00		113.7

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT	IEC 61672 Class 1
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Spec. (dB)
30 - 120	L _A	A	Fast	94.00	1	93.8	Ref.
			Slow			93.7	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C221363
證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT	IEC 61672 Class 1
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
30 - 120	L _A	A	Fast	94.00	63 Hz	67.5	-26.2 ± 1.5
					125 Hz	77.6	-16.1 ± 1.5
					250 Hz	85.1	-8.6 ± 1.4
					500 Hz	90.5	-3.2 ± 1.4
					1 kHz	93.8	Ref.
					2 kHz	95.0	+1.2 ± 1.6
					4 kHz	94.9	+1.0 ± 1.6
					8 kHz	92.7	-1.1 (+2.1 ; -3.1)
					16 kHz	87.4	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT	IEC 61672 Class 1
Range (dB)	Mode	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
30 - 120	L _C	C	Fast	94.00	63 Hz	92.8	-0.8 ± 1.5
					125 Hz	93.5	-0.2 ± 1.5
					250 Hz	93.7	0.0 ± 1.4
					500 Hz	93.8	0.0 ± 1.4
					1 kHz	93.7	Ref.
					2 kHz	93.6	-0.2 ± 1.6
					4 kHz	93.1	-0.8 ± 1.6
					8 kHz	90.8	-3.0 (+2.1 ; -3.1)
					16 kHz	85.4	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C221363

證書編號

Remarks : - UUT Microphone Model No. : UC-53A & S/N : 322551

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 94 dB : 63 Hz - 125 Hz : ± 0.35 dB
250 Hz - 500 Hz : ± 0.30 dB
1 kHz : ± 0.20 dB
2 kHz - 4 kHz : ± 0.35 dB
8 kHz : ± 0.45 dB
16 kHz : ± 0.70 dB
104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C221365

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC22-0258)

Date of Receipt / 收件日期 : 14 February 2022

Description / 儀器名稱 : Sound Level Meter (EQ018)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00809405

Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(50 \pm 25)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 12 March 2022

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.


The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Fluke Everett Service Center, USA
- Agilent Technologies / Keysight Technologies


Tested By

測試


K C Lee
Engineer

Certified By

核證


H C Chan
Engineer

Date of Issue

簽發日期

16 March 2022

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C221365
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration was performed before the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C220381
CL281	Multifunction Acoustic Calibrator	AV210017

- Test procedure : MA101N.

- Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.0	± 1.1

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L _A	A	Fast	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.0	Ref.
			Slow			94.0	± 0.3

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C221365

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _A	A	Fast	94.00	63 Hz	67.8	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.5
					250 Hz	85.4	-8.6 ± 1.4
					500 Hz	90.8	-3.2 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	95.0	+1.2 ± 1.6
					4 kHz	94.7	+1.0 ± 1.6
					8 kHz	92.9	-1.1 (+2.1 ; -3.1)
					16 kHz	85.5	-6.6 (+3.5 ; -17.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT	IEC 61672
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.	Reading (dB)	Class 1 Spec. (dB)
30 - 130	L _C	C	Fast	94.00	63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.5
					250 Hz	94.0	0.0 ± 1.4
					500 Hz	94.1	0.0 ± 1.4
					1 kHz	94.0	Ref.
					2 kHz	93.6	-0.2 ± 1.6
					4 kHz	92.9	-0.8 ± 1.6
					8 kHz	91.0	-3.0 (+2.1 ; -3.1)
					16 kHz	83.5	-8.5 (+3.5 ; -17.0)

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606 Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C221365

證書編號

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 16463

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB	: 63 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	16 kHz	: ± 0.70 dB
104 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	: 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration is traceable to the National Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號四樓

Tel/電話: (852) 2927 2606

Fax/傳真: (852) 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F, Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

*is accredited by the Hong Kong Accreditation Service (HKAS) to ISO/IEC 17025:2017
for performing specific laboratory activities as listed in the scope of accreditation within the test category of*
獲香港認可處根據ISO/IEC 17025:2017認可
進行載於認可範圍內下述測試類別中的指定實驗所活動

Environmental Testing
環境測試

*This accreditation to ISO/IEC 17025:2017 demonstrates technical competence for a defined scope and
the implementation of a management system relevant to laboratory operation
(see joint IAF-ILAC-ISO Communiqué).*
此項 ISO/IEC 17025:2017 的認可資格證明此實驗所具備指定範疇內所須的技術能力並
實施一套與實驗所運作相關的管理體系
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of HKAS is affixed hereto by the authority of the HKAS Executive
現經香港認可處執行機關授權在此蓋上香港認可處的印章

SHUM Wai-leung, Executive Administrator
執行幹事 沈偉良
Issue Date : 28 February 2020
簽發日期：二零二零年二月二十八日

Registration Number : **HOKLAS 066**
註冊號碼：



Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日

Appendix F

Event and Action Plan

Event / Action Plan for construction dust

Event	Action			
	ET	IEC	ER	Contractor
Action Level exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER and Contractor; 3. Repeat measurement to confirm finding; and 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; and 3. Review and advise the ET and ER on the effectiveness of the proposed remedial measures. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Rectify any unacceptable practice and implement remedial measures; and 3. Amend working methods agreed with ER if appropriate.
Action Level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC, ER and Contractor; 3. Advise the ER and Contractor on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC, ER and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET and ER on the effectiveness of the proposed remedial measures; and 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; and 3. Supervise and ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Submit proposals for remedial actions to ER with a copy to ET and IEC within 3 working days of notification; 3. Implement the agreed proposals; and 4. Amend proposal if appropriate.
Limit Level exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor, IEC and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; and 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET, ER and Contractor on possible remedial measures; 4. Advise the ER and ET on the effectiveness of the proposed remedial measures; and 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; and 3. Supervise and ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER with a copy to ET and IEC within 3 working days of notification; 4. Implement the agreed proposals; and 5. Amend proposal if appropriate.
Limit Level exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC, Contractor and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 4. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 5. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the ET and IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise and ensure remedial measures properly implemented; and 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Take immediate action to avoid further exceedance; 3. Submit proposals for remedial actions to ER with a copy to ET and IEC within 3 working days of notification; 4. Implement the agreed proposals; 5. Resubmit proposals if problem still not under control; and 6. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level Exceedance	<ol style="list-style-type: none"> 1. Notify IEC, ER and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; and 5. Increase monitoring frequency to check mitigation effectiveness. 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; and 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; and 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IEC and ER; and 2. Implement noise mitigation proposals.
Limit Level Exceedance	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; and 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; and 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; and 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; and 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Appendix G

Impact Monitoring Schedule

Impact Monitoring Schedule for the Reporting Period

Date		NOISE MONITORING (0700 – 1900)	AIR QUALITY MONITORING	
			1-HOUR TSP	24-HOUR TSP
Thu	1-Sep-22	NMS2, NMS3, NMS-4a, NMS5, NMS6 and NMS7 CN1, CN2, CN3 and NMS8	✓	
Fri	2-Sep-22			
Sat	3-Sep-22			
Sun	4-Sep-22			
Mon	5-Sep-22			
Tue	6-Sep-22			✓
Wed	7-Sep-22	NMS2, NMS3, NMS-4a, NMS5, NMS6 and NMS7	✓	
Thu	8-Sep-22			
Fri	9-Sep-22	CN1, CN2, CN3 and NMS8		
Sat	10-Sep-22			✓
Sun	11-Sep-22			
Mon	12-Sep-22			
Tue	13-Sep-22	NMS2, NMS3, NMS-4a, NMS5, NMS6 and NMS7	✓	
Wed	14-Sep-22			
Thu	15-Sep-22	CN1, CN2, CN3 and NMS8		
Fri	16-Sep-22			✓
Sat	17-Sep-22			
Sun	18-Sep-22			
Mon	19-Sep-22	NMS2, NMS3, NMS-4a, NMS5, NMS6, NMS7, NMS8	✓	
Tue	20-Sep-22			
Wed	21-Sep-22			
Thu	22-Sep-22			✓
Fri	23-Sep-22			
Sat	24-Sep-22		✓	
Sun	25-Sep-22			
Mon	26-Sep-22			
Tue	27-Sep-22			
Wed	28-Sep-22			✓
Thu	29-Sep-22	NMS2, NMS3, NMS-4a, NMS5, NMS6, NMS7, NMS8	✓	
Fri	30-Sep-22			

✓	Monitoring Day
	Sunday or Public Holiday

Impact Monitoring Schedule for next Reporting Period

DATE		NOISE MONITORING (0700 – 1900)	AIR QUALITY MONITORING	
			1-HOUR TSP	24-HOUR TSP
Sat	1-Oct-22			
Sun	2-Oct-22			
Mon	3-Oct-22			✓
Tue	4-Oct-22			
Wed	5-Oct-22	✓	✓	
Thu	6-Oct-22			
Fri	7-Oct-22			
Sat	8-Oct-22			✓
Sun	9-Oct-22			
Mon	10-Oct-22			
Tue	11-Oct-22	✓	✓	
Wed	12-Oct-22			
Thu	13-Oct-22			
Fri	14-Oct-22			✓
Sat	15-Oct-22			
Sun	16-Oct-22			
Mon	17-Oct-22	✓	✓	
Tue	18-Oct-22			
Wed	19-Oct-22			
Thu	20-Oct-22			✓
Fri	21-Oct-22			
Sat	22-Oct-22		✓	
Sun	23-Oct-22			
Mon	24-Oct-22			
Tue	25-Oct-22			
Wed	26-Oct-22			✓
Thu	27-Oct-22			
Fri	28-Oct-22	✓	✓	
Sat	29-Oct-22			
Sun	30-Oct-22			
Mon	31-Oct-22			

✓	Monitoring Day
	Sunday or Public Holiday

Appendix H

Database of Monitoring Result

24-HOUR TSP MONITORING RESULT DATABASE

24-hour TSP Monitoring Data for AMS1a															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-hr TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
6-Sep-22	28658	25153.87	25177.87	1440	40	40	40	30.8	1008.2	1.49	2139	2.6929	2.7745	0.0816	38
10-Sep-22	28662	25177.87	25201.87	1440	40	40	40	28.9	1011.4	1.49	2147	2.6986	2.8028	0.1042	49
16-Sep-22	28582	25201.87	25225.87	1440	40	41	40.5	30.8	1005.1	1.50	2156	2.7378	2.8257	0.0879	41
22-Sep-22	28394	25225.87	25249.87	1440	40	41	40.5	28.5	1011.1	1.50	2167	2.7747	2.8805	0.1058	49
28-Sep-22	28737	25249.87	25273.87	1440	40	41	40.5	28	1010.1	1.51	2168	2.7067	2.7538	0.0471	22
24-hour TSP Monitoring Data for AMS-5															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-hr TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
6-Sep-22	28518	12705.84	12729.84	1440.00	38	38	38.0	30.8	1008.2	1.38	1988	2.6551	2.7376	0.0825	42
10-Sep-22	28663	12729.84	12753.84	1440.00	38	38	38.0	28.9	1011.4	1.38	1994	2.6994	2.8416	0.1422	71
16-Sep-22	28696	12753.84	12777.84	1440.00	38	39	38.5	30.8	1005.1	1.39	2003	2.6975	2.8589	0.1614	81
22-Sep-22	28682	12777.84	12801.84	1440.00	38	39	38.5	28.5	1011.1	1.40	2012	2.7148	2.8638	0.1490	74
28-Sep-22	28738	12801.84	12825.84	1440.00	38	39	38.5	28	1010.1	1.40	2013	2.7204	2.7678	0.0474	24
24-hour TSP Monitoring Data for AMS-6															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-hr TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
6-Sep-22	28517	18028.69	18052.69	1440.00	40	40	40.0	30.8	1008.2	1.46	2099	2.6570	2.7145	0.0575	27
10-Sep-22	28664	18052.69	18076.69	1440.00	40	40	40.0	28.9	1011.4	1.46	2106	2.7070	2.7911	0.0841	40
16-Sep-22	28583	18076.69	18100.69	1440.00	40	41	40.5	30.8	1005.1	1.47	2114	2.7342	2.7855	0.0513	24
22-Sep-22	28683	18100.69	18124.69	1440.00	40	41	40.5	28.5	1011.1	1.47	2123	2.7068	2.8520	0.1452	68
28-Sep-22	28739	18124.69	18148.69	1440.00	40	41	40.5	28	1010.1	1.47	2124	2.7100	2.7347	0.0247	12
24-hour TSP Monitoring Data for AMS-7															
DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (°C)	AVG AIR PRESS (hPa)	STANDARD FLOW RATE (m ³ /min)	AIR VOLUME (std m ³)	FILTER WEIGHT (g)		DUST WEIGHT COLLECTED (g)	24-hr TSP (µg/m ³)
		INITIAL	FINAL	(min)	MIN	MAX	AVG					INITIAL	FINAL		
6-Sep-22	28587	12882.73	12906.73	1440.00	40	40	40.0	30.8	1008.2	1.44	2080	2.7438	2.7883	0.0445	21
10-Sep-22	28695	12906.73	12930.73	1440.00	40	40	40.0	28.9	1011.4	1.45	2086	2.7138	2.8040	0.0902	43
16-Sep-22	28697	12930.73	12954.73	1440.00	40	41	40.5	30.8	1005.1	1.45	2094	2.7107	2.8931	0.1824	87
22-Sep-22	28681	12954.73	12978.73	1440.00	40	41	40.5	28.5	1011.1	1.46	2103	2.7220	2.8778	0.1558	74
28-Sep-22	28740	12978.73	13002.73	1440.00	40	41	40.5	28	1010.1	1.46	2103	2.7169	2.8120	0.0951	45

NOISE MONITORING RESULT DATABASE FOR CONTRACT 1

Noise Measurement Results (dB) of NMS2																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30 min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	11:17	64.3	65.5	56	63.8	66	55.5	63.6	65.5	56	65.2	67	56	63.4	66.5	55.5	62.8	65	55	64	70
7-Sep-22	11:21	65.7	68.5	63	63.6	70	60	63.8	70.5	61	65.6	68.5	63.5	66.2	68.5	64.5	67.4	70	65.5	66	70
13-Sep-22	11:18	65.7	68.5	62	63.4	66	60.5	62.8	65.5	61.5	63.7	65	59	62.2	63.5	58.5	65.2	66	58.5	64	70
19-Sep-22	14:28	64.6	67.5	63.5	65.2	67.5	63.5	66	69.5	64.4	63.2	69.5	61.8	63	68	59.6	65.6	67.9	62.9	65	70
29-Sep-22	10:07	63.8	70.1	62.4	63.6	68.6	60.2	66.2	68.5	63.5	65.2	68.1	64.1	65.8	68.1	64.1	66.6	70.1	65	65	70

Noise Measurement Results (dB) of NMS3																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	9:27	60.9	62.0	57.5	62.2	62.5	67.0	60.3	62.5	57.5	61.1	63.0	57.5	62.0	64.5	56.0	62.2	64.5	55.5	62	75
7-Sep-22	14:50	60.2	63.0	57.0	61.3	63.5	57.5	60.6	62.5	55.5	60.7	62.5	56.5	61.8	63.0	55.5	59.9	62.0	55.5	61	75
13-Sep-22	14:21	63.7	65.0	58.5	62.2	64.5	58.0	61.8	63.0	58.0	62.2	63.5	58.5	63.1	63.5	58.0	62.7	63.5	58.5	63	75
19-Sep-22	10:56	62.1	64.5	59.8	62.0	63.7	60.1	61.4	62.6	59.8	59.9	60.9	59.0	59.2	60.7	57.3	58.2	59.6	56.5	61	75
29-Sep-22	14:32	60.5	61.5	59.6	59.8	61.3	57.9	58.8	60.2	57.1	62.7	65.1	60.4	62.6	64.3	60.7	62.0	63.2	60.4	61	75

Noise Measurement Results (dB) of NMS4a																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min in, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	9:18	69.6	73	66	70.2	73	65.5	68.8	73	66	72.6	73.5	66.5	69.9	73	66	71.7	73.5	66	71	75
7-Sep-22	9:28	70.6	73	68	69.3	72.5	66.5	70.4	72.5	65.5	70.3	73	66	69.8	72	65	68.9	72	65	70	75
13-Sep-22	9:25	68.2	72.5	65	70.4	73	66.5	70.6	73	66	69.4	73	66	68.6	72.5	65.5	70.7	72	66	70	75
19-Sep-22	13:05	64.1	65.5	62.6	64.3	65.6	62.7	64.6	66	63	65	66.2	63.3	65	66	63.5	66.2	68.2	63.2	65	75
29-Sep-22	14:04	65.6	66.8	63.9	65.6	66.6	64.1	66.8	68.8	63.8	64.7	66.1	63.2	64.9	66.2	63.3	65.2	66.6	63.6	66	75

Noise Measurement Results (dB) of NMS5																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	10:35	70.2	73.5	66	68.6	72	65	67.3	72	65	70.2	73	65.5	68.4	72	65	68.2	72	63	69	75
7-Sep-22	10:19	70.6	72.5	66	71.2	73	65.5	71.4	73	67	69.2	71	65.5	70.3	72	65	70.6	72	66	71	75
13-Sep-22	10:15	71.2	72.5	65.5	70.9	73	66	70.2	73	65.5	69.2	71.5	65.5	70.8	73	66.5	72.1	73	66	71	75
19-Sep-22	13:47	62.7	64.2	61	64.6	66.2	62.1	64	66.2	60.4	61	62.3	59.3	65.1	69	60.5	62.7	64.5	60.6	64	75

Noise Measurement Results (dB) of NMS5

Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
29-Sep-22	13:07	62.8	64.1	63.1	62.9	64.8	63.3	69.5	71.3	63.4	70.2	71.5	65.5	70.3	74.2	65.7	67.9	69.7	65.8	68	75

Noise Measurement Results (dB) of NMS6

Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	10:03	66.4	68.9	62.7	65.9	68.7	62.7	65.5	66.8	64.1	64.8	66	63.6	64.9	66.5	62.8	63.4	64.5	62.2	65	75
7-Sep-22	15:43	65.6	68	62	63.7	66	60	62.8	65.5	59.5	65.2	66.5	60.5	63.9	65.5	60	65.6	67	62.5	65	75
13-Sep-22	15:27	65.2	66.5	63	66.4	68	65	63.7	67.5	60.8	69.4	70	65	66.2	69.5	65	67.1	69	63.5	67	75
19-Sep-22	10:16	64.8	67.1	61.3	62.2	63.7	60.4	62.5	65.1	60	66.2	67.9	63.8	62.4	64.6	60.3	64.2	66.2	61.2	64	75
29-Sep-22	15:43	65.7	66.9	64.5	65.8	67.4	63.7	64.3	65.4	63.1	67.3	69.8	63.6	66.8	69.6	63.6	66.4	67.7	65	66	75

Noise Measurement Results (dB) of NMS7

Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	10:42	65.1	66.2	63.9	66.1	67.4	64.3	65.9	67.8	63.9	67.1	68.2	65.5	68.1	70.6	64.4	67.6	70.4	64.4	67	75
7-Sep-22	16:30	68.2	70	63.25	69.6	72	65	70.2	72.5	65.5	65.5	68	63	68.3	70	62	65.8	67.5	62	68	75
13-Sep-22	16:28	70.2	72	63	68.8	71.5	65	67.4	71.5	66	62.7	68	62.5	67.8	69.5	65.5	65.4	67.5	63.5	68	75
19-Sep-22	9:34	69.3	72.8	63.1	64.2	65.9	61.8	64.4	66.6	61.3	62.8	65.1	59.3	60.2	61.7	58.4	60.5	63.1	57	65	75
29-Sep-22	14:42	65.7	69	62	67.2	69.5	62.5	65.4	68.5	62	65.3	70	62	66.7	70.5	63	67.8	71	65.5	66	75

Noise Measurement Results (dB) of NMS8

Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	13:18	61.7	65.1	54.6	60.9	65.1	56.1	60	64.1	57.1	58.3	61.6	55.1	60.8	64.6	57.1	58.9	61.6	55.6	60	75
9-Sep-22	14:12	60.5	63.5	56	57.6	61	49	56.8	59.5	46.5	54.9	58	48.5	61.5	62.5	50	60.2	62.5	55	59	75
15-Sep-22	10:32	60.9	64.2	56.7	62.4	65.2	57.7	59.5	62.2	56.2	62.3	65.7	55.2	61.5	65.7	56.7	60.6	64.7	57.7	61	75
19-Sep-22	9:51	65	66	58	63.7	66.5	58.5	63.4	66	59.5	65.3	67.5	60	62.1	65	60	60.8	63	58	64	75
29-Sep-22	9:06	57.7	61	54.5	60.2	64	56.5	58.3	61	55	61.1	64.5	54	60.3	64.5	55.5	59.4	63.5	56.5	60	75

NOISE MONITORING RESULT DATABASE FOR CONTRACT 3




Noise Measurement Results (dB) of CN1																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	13:42	60.7	62.5	58	62.4	63	58.5	60.3	63.5	58	62.6	63.5	61	61.2	63	59	62.8	63.5	58.5	62	70
9-Sep-22	15:43	61.8	62.5	61	61.4	62	60.5	62.5	62.5	61	61	61	60	60.5	61	59.5	60.2	61	59.5	61	70
15-Sep-22	13:58	63.5	66	58.5	63.8	65.1	58.2	59.4	62.2	57	59.6	62	56.9	58.9	60.7	56.8	61.1	62.3	58.3	62	70




Noise Measurement Results (dB) of CN2																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	13:16	62.8	65.5	59.5	63.4	65	60	65.2	66.5	62	63.7	65	59.5	63.3	64.5	59.5	62.4	65	60	64	70
9-Sep-22	15:08	62	64	56.5	64.6	64.5	56.5	58.2	59	57	60.4	62	57.5	63.6	64.5	60	63.7	64.5	62.5	63	70
15-Sep-22	13:24	62.7	64.8	59.8	63.9	64.8	60.3	62	63.8	59.8	63.6	66.3	60.3	62	65.8	59.8	62.9	65.3	59.3	63	70



Noise Measurement Results (dB) of CN3																					
Date	Start Time	1st Leq (5min)			2nd Leq (5min)			3rd Leq (5min)			4th Leq (5min)			5th Leq (5min)			6th Leq (5min)			Leq30min, dB(A)	Limit Level dB(A)
		Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)	Leq, dB(A)	L10, dB(A)	L90, dB(A)		
1-Sep-22	9:53	63.8	67.5	62	65.2	67	62.5	65.5	68	62.5	63.6	67.5	60	62.3	66	60	65.3	66	61.5	64	75
9-Sep-22	13:18	62.6	67	60	63.7	68	61	65.8	68	62.5	63.9	67	62	65.2	67.5	61.5	65.3	68	62.5	65	75
15-Sep-22	9:41	63.9	66.2	60.2	65.4	66.7	59.7	64.3	66.7	59.2	64.4	66.2	62.2	66.1	67.2	61.7	64.9	66.7	61.2	65	75
19-Sep-22	10:52	65.8	68	63.5	66.1	68	62.5	65.4	67.5	62.5	62.5	66.2	68.5	62.5	65.6	68	63	67.1	68.5	64	75
29-Sep-22	11:14	65.1	68.8	62.1	63.1	66.2	68.6	63.6	67.7	69.1	66.4	68.6	64.1	66.7	68.6	63.1	66	68.1	63.1	65	75



Appendix I



Graphical Plots for Monitoring Result

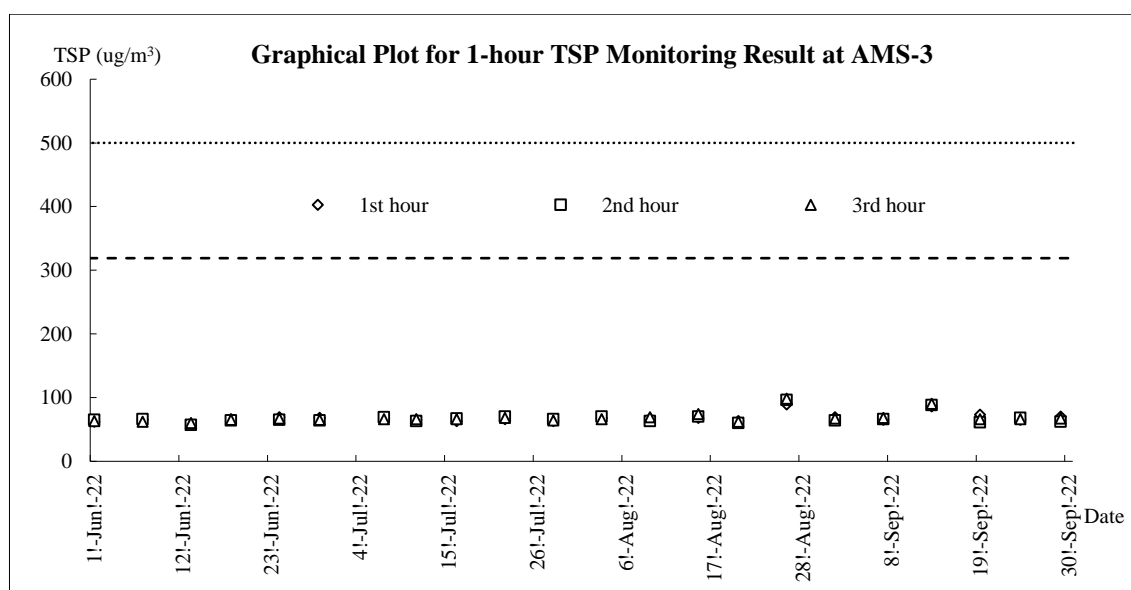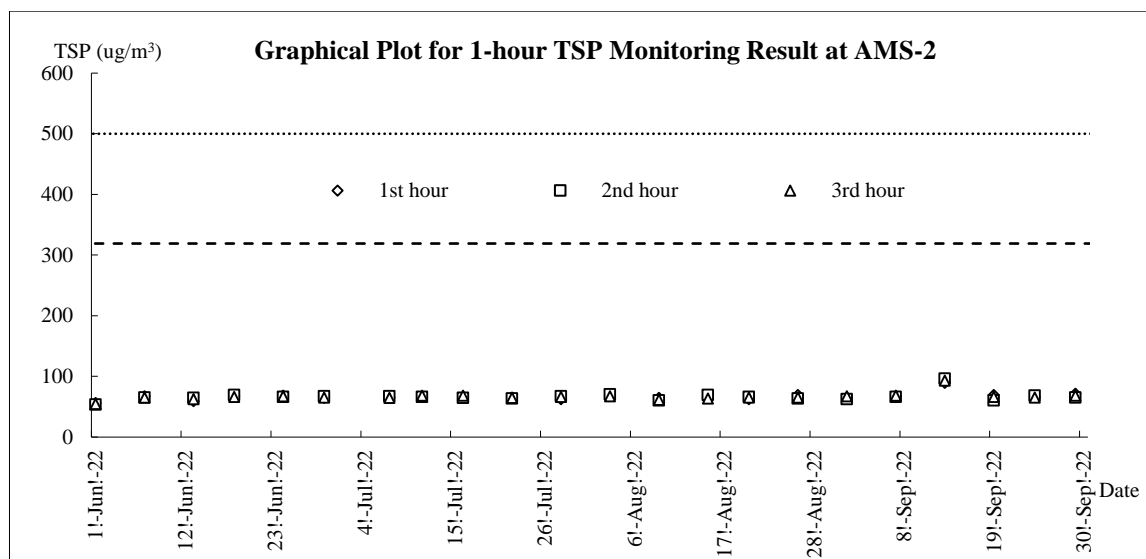
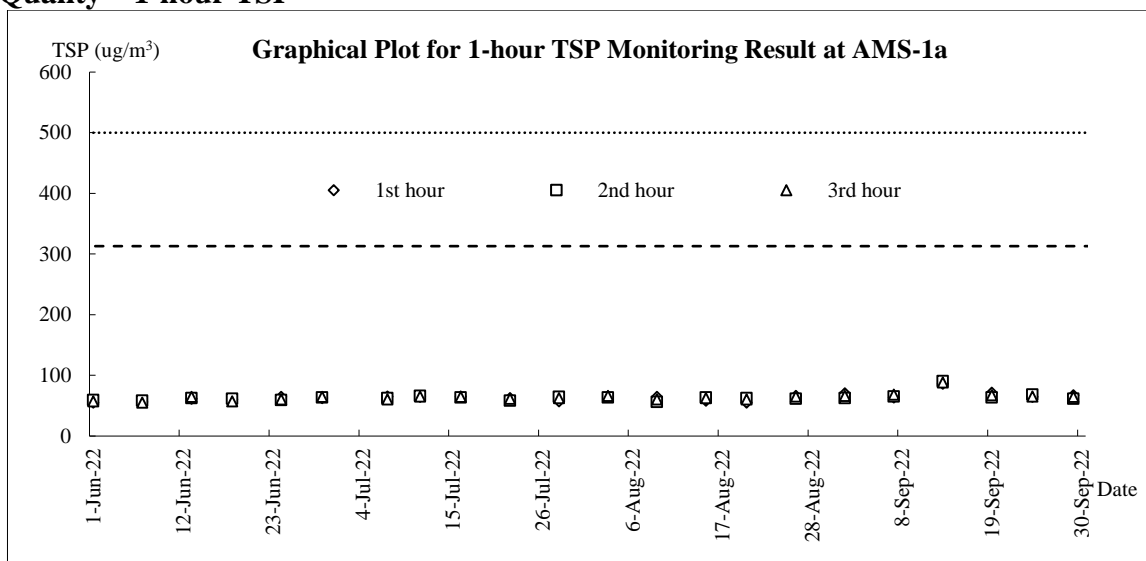
Air Quality – 1-hour TSP

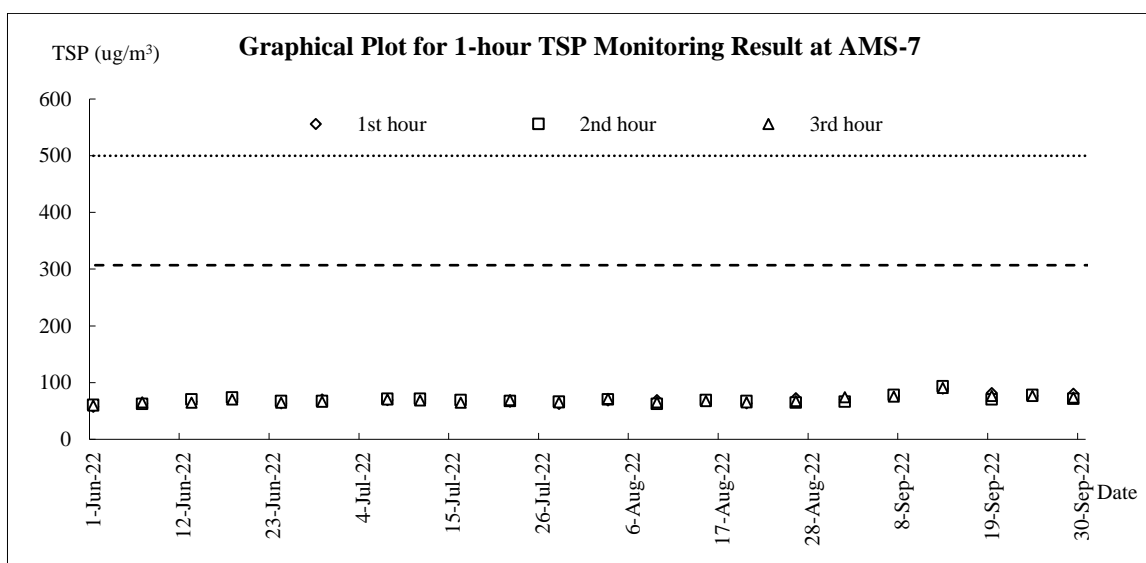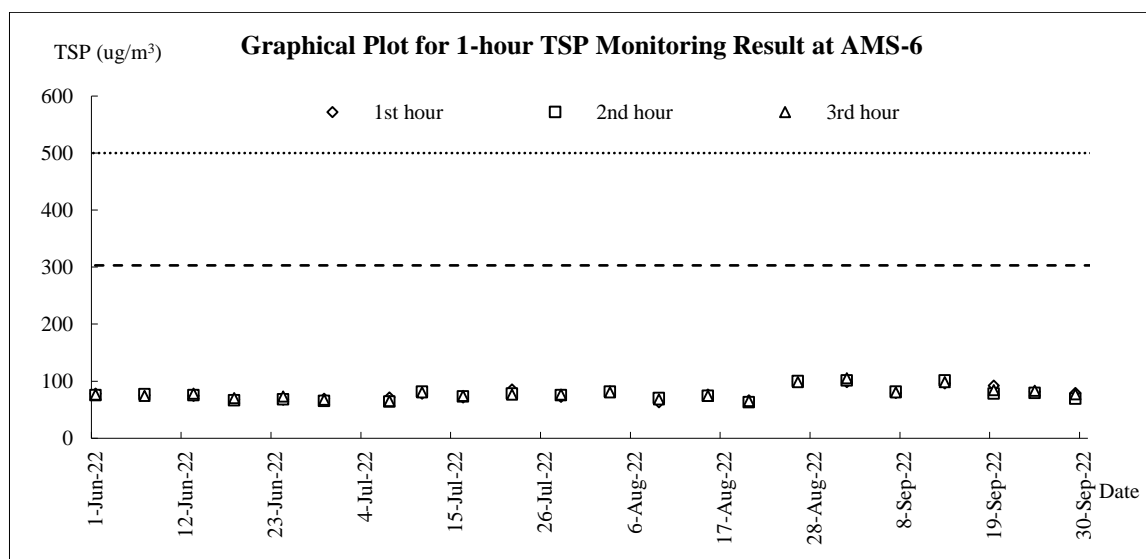
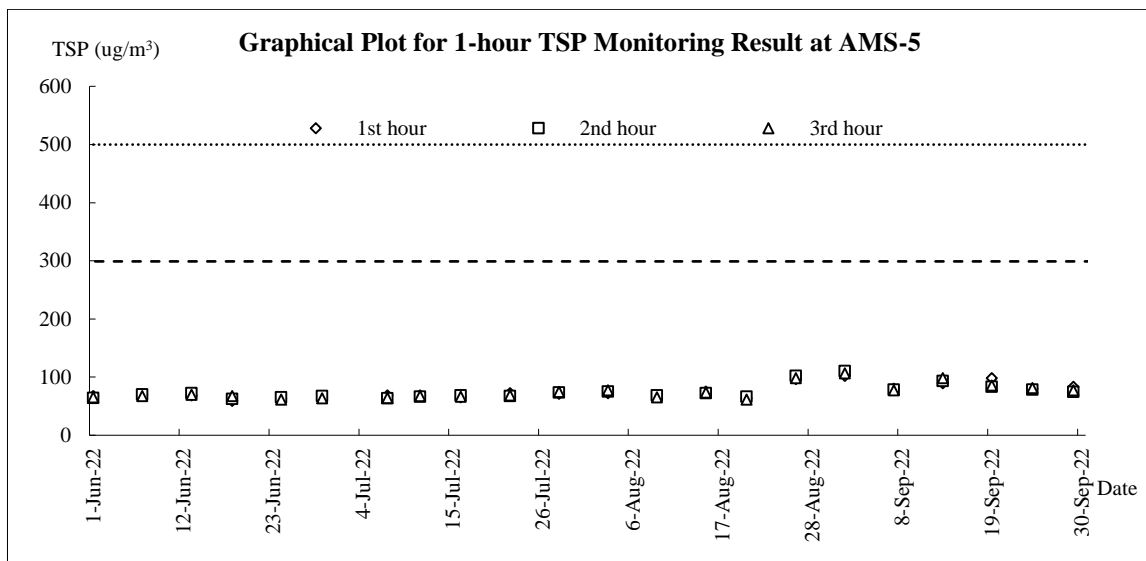


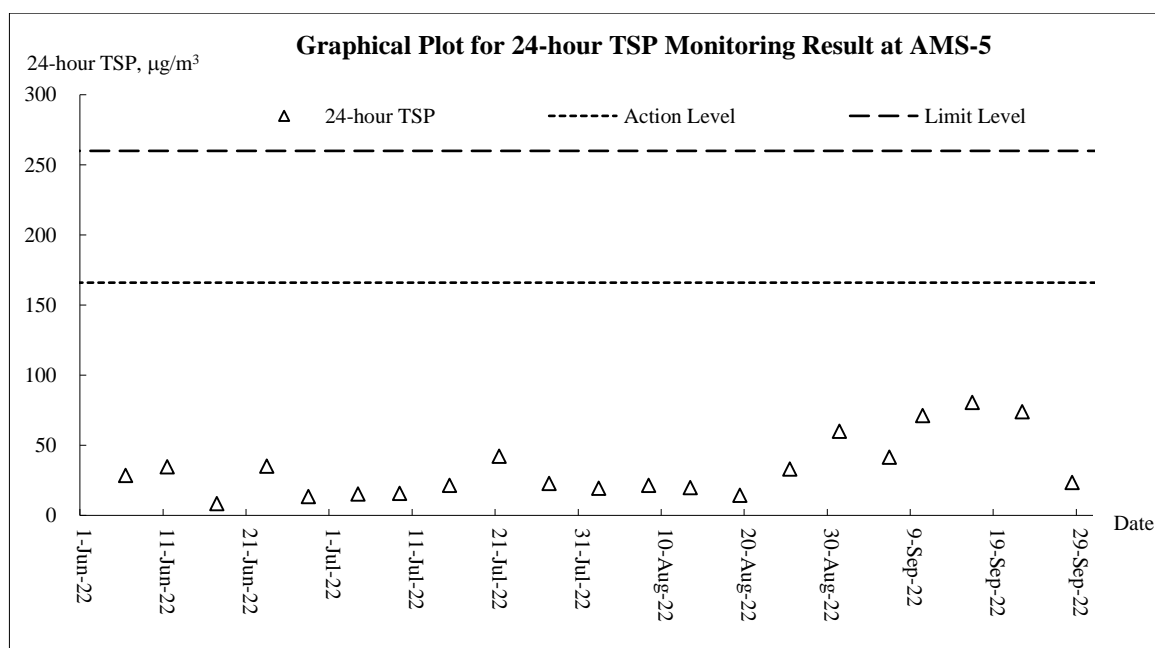
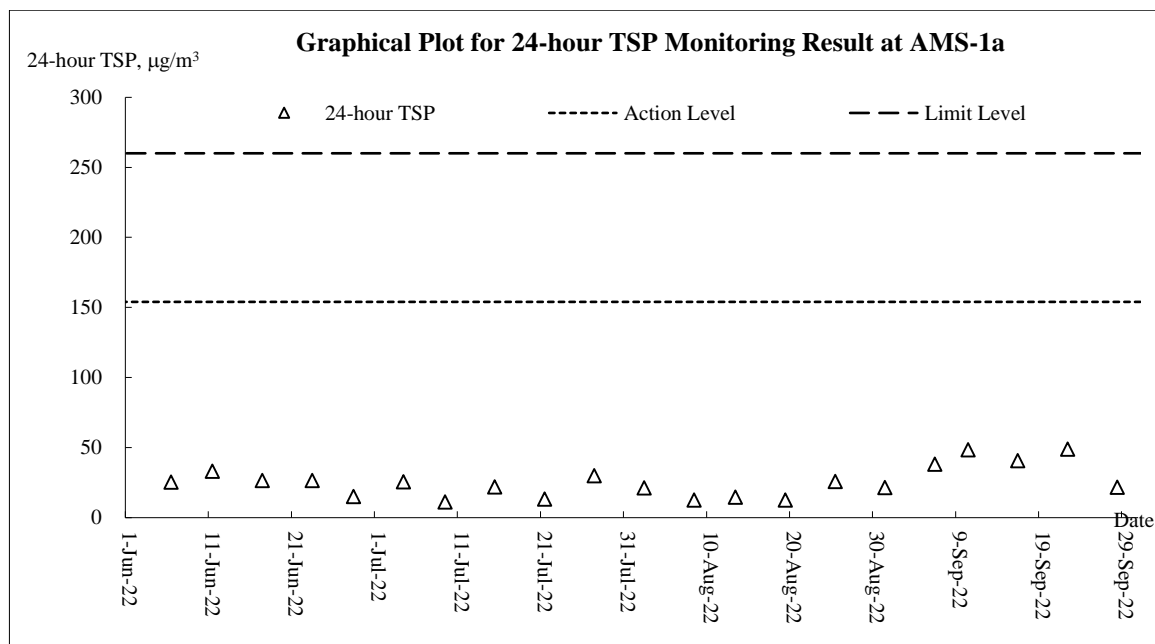
Air Quality – 24-hour TSP

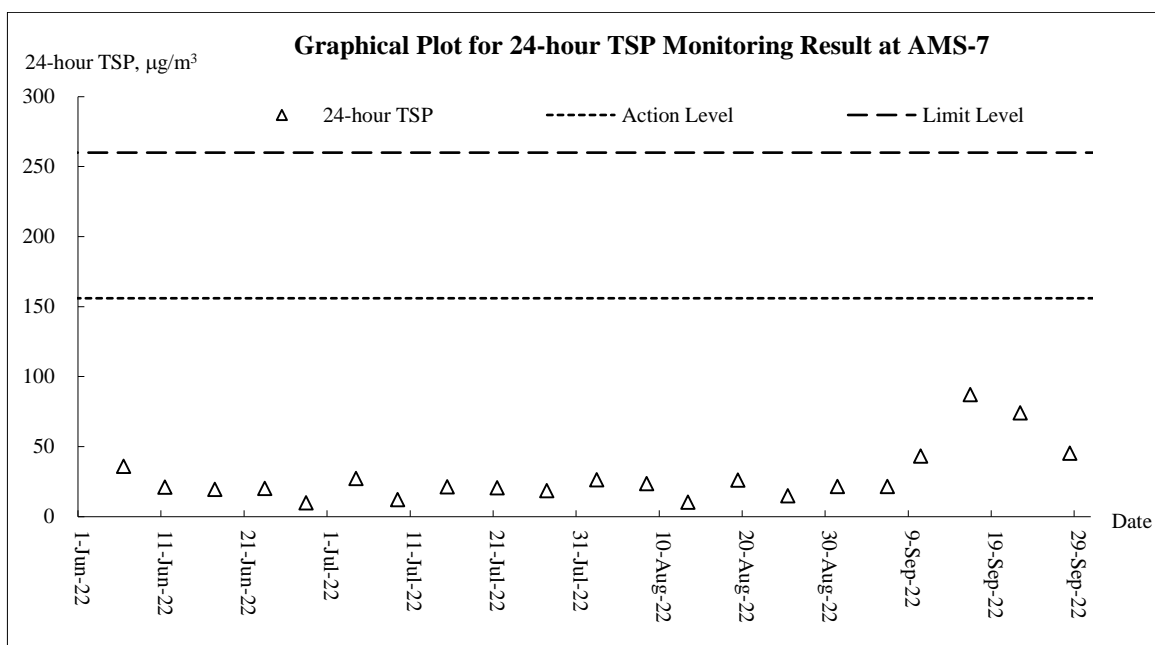
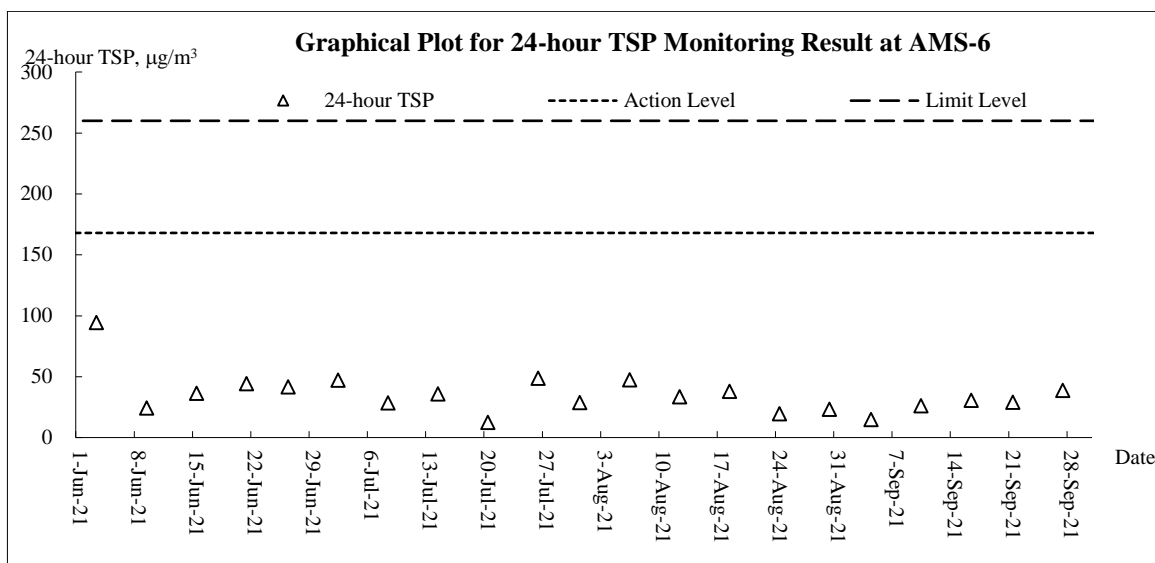


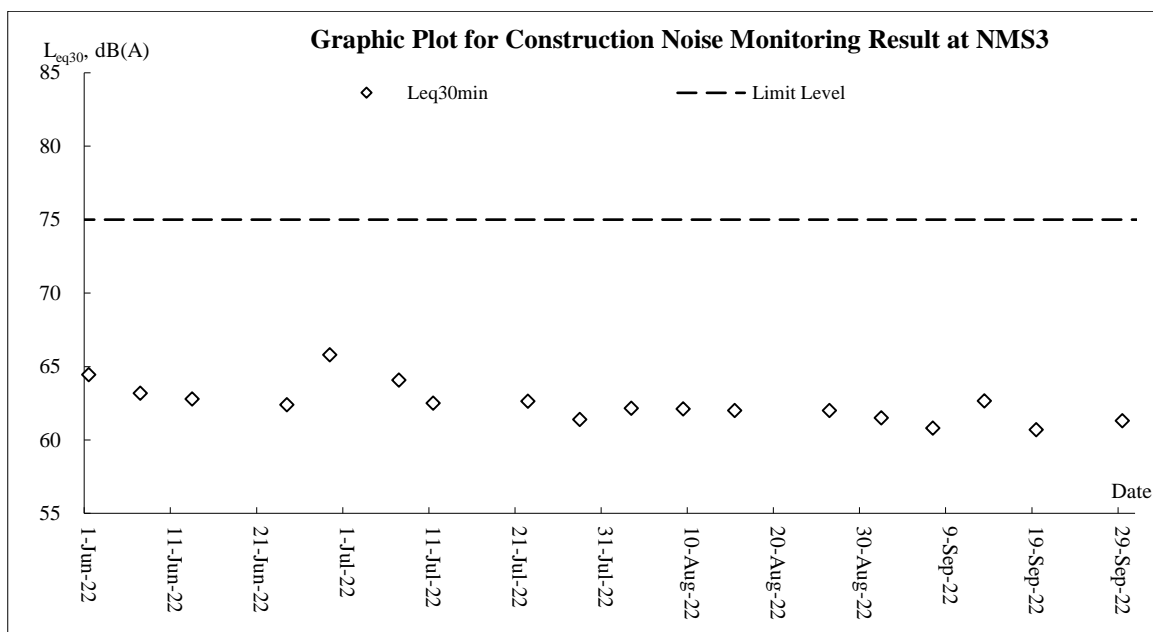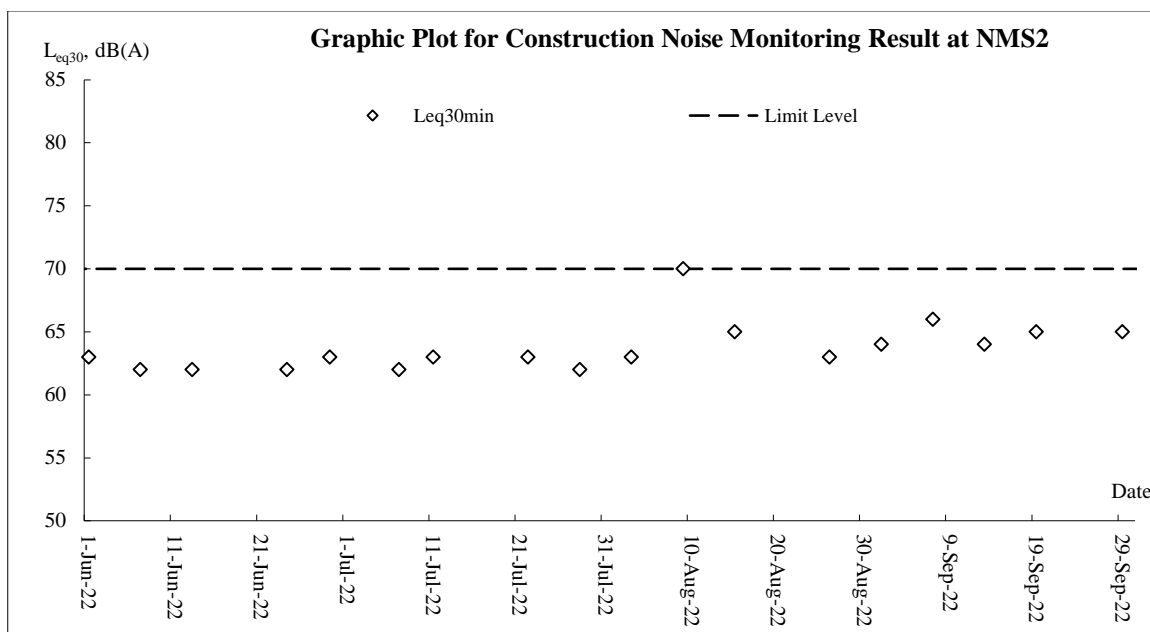Noise

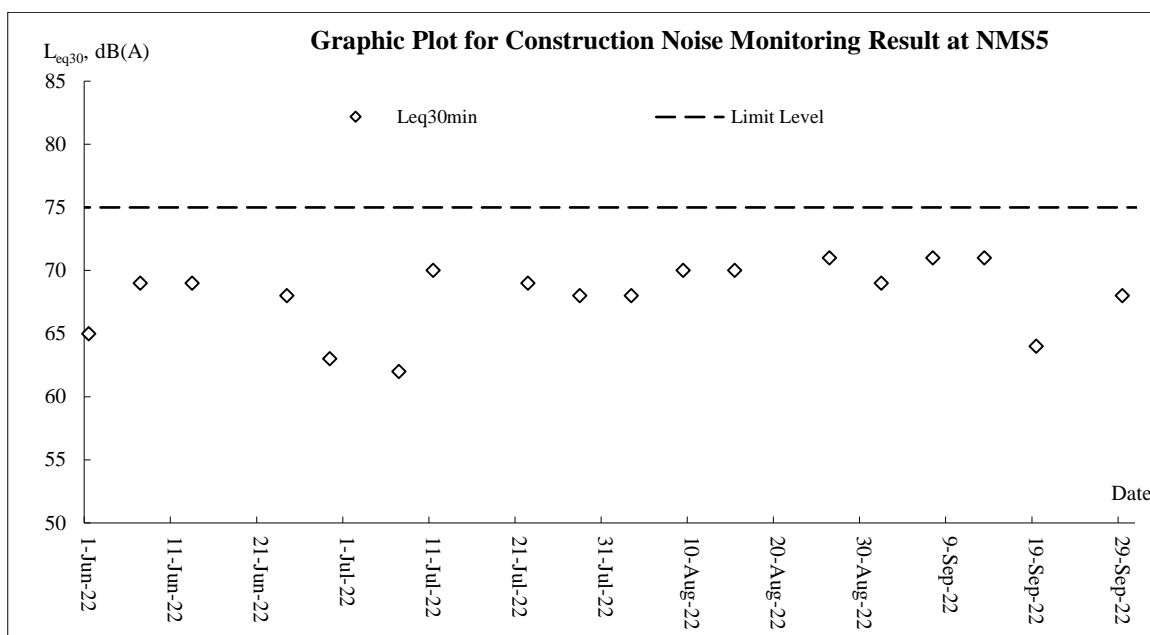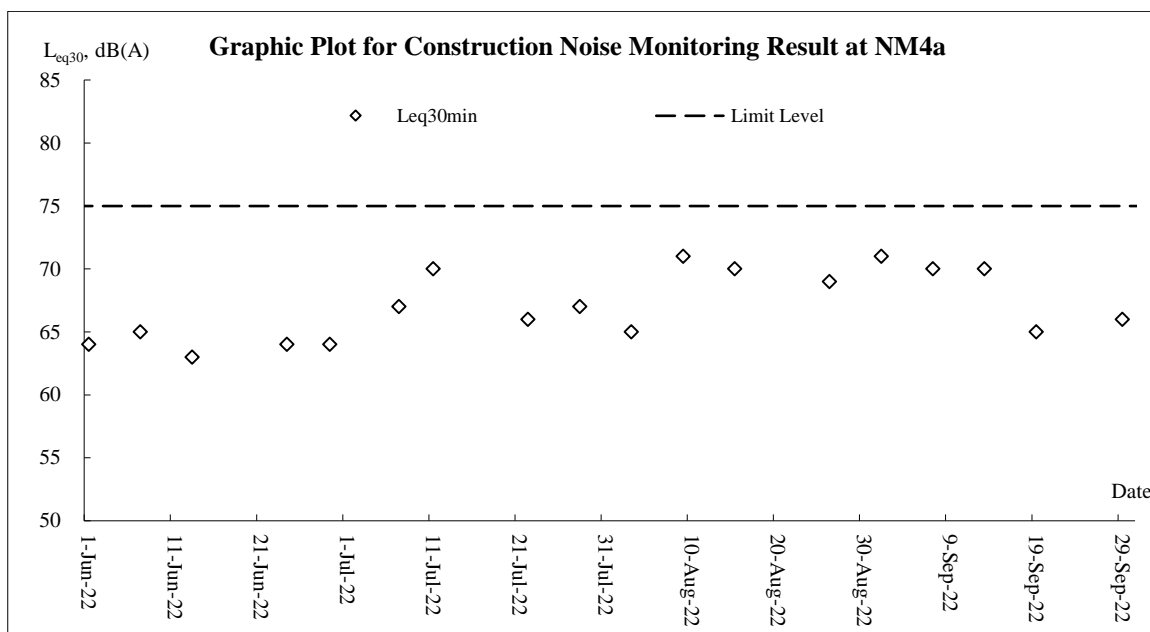

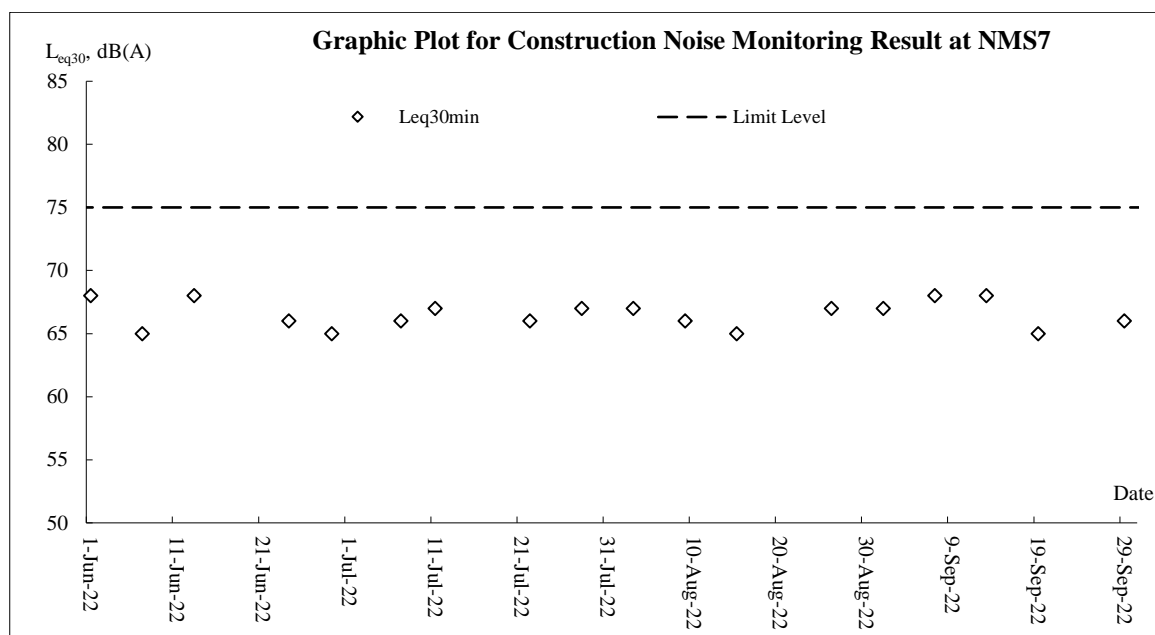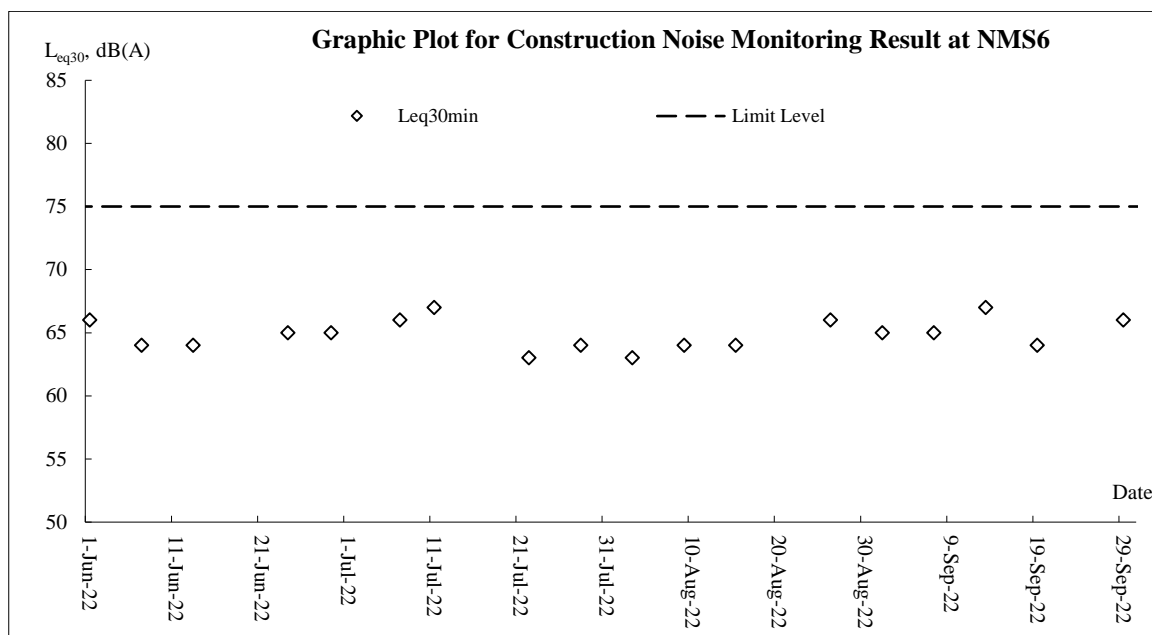

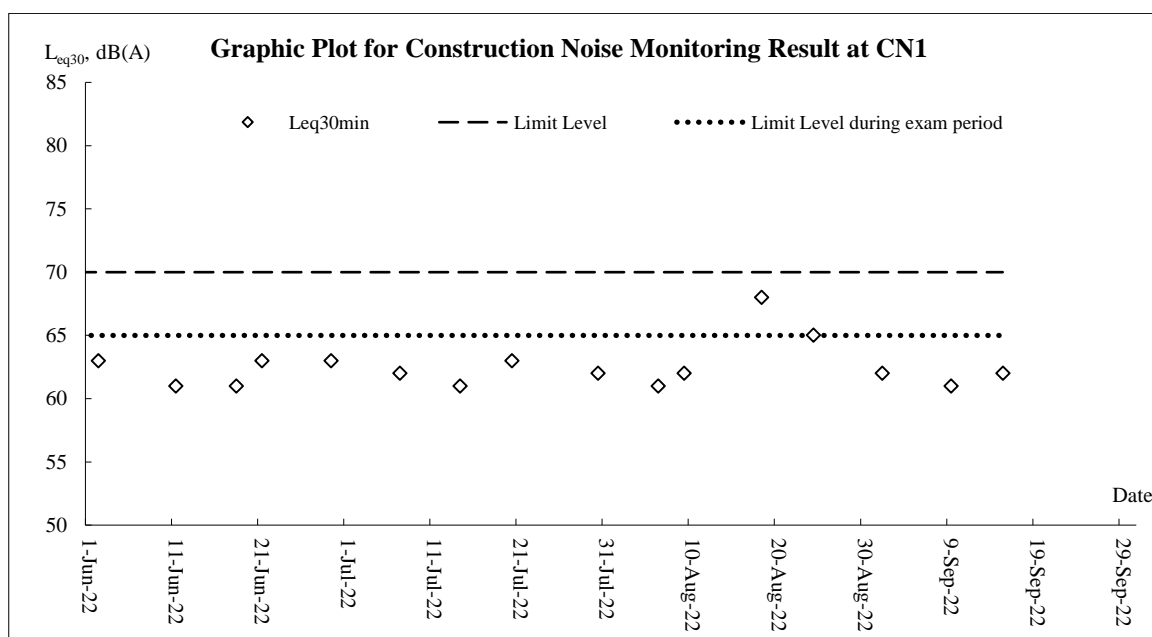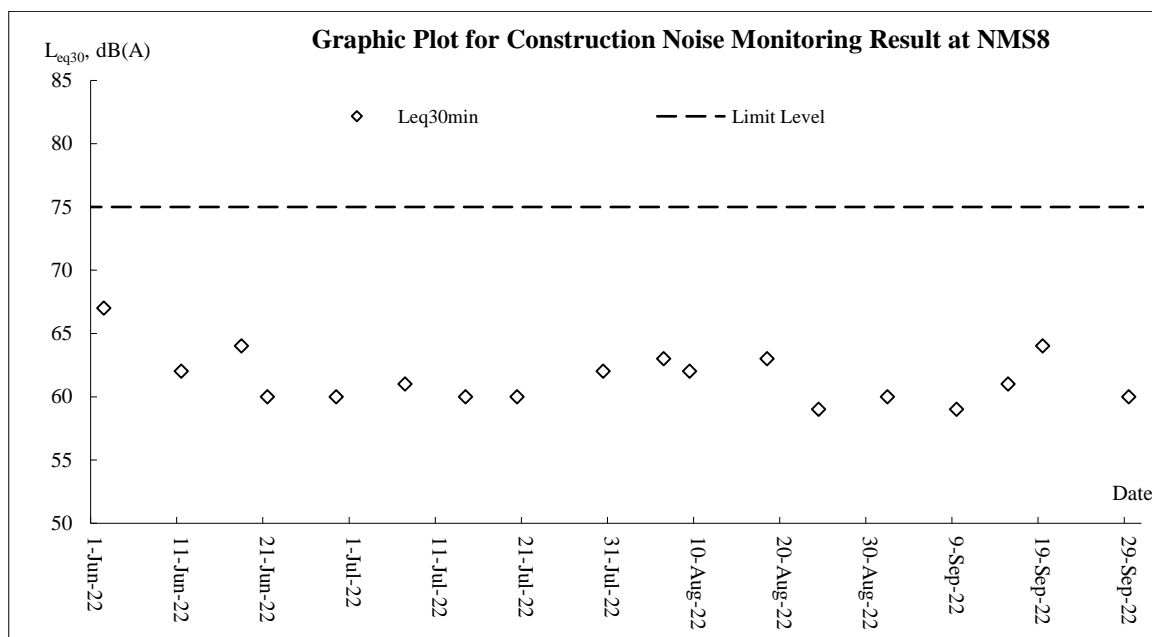

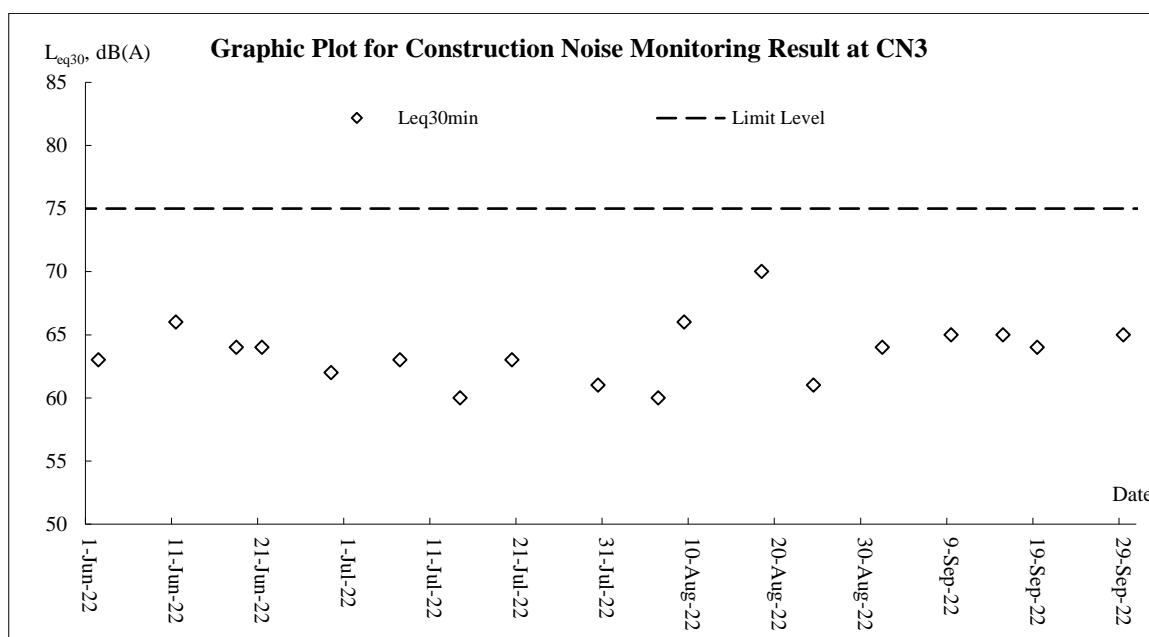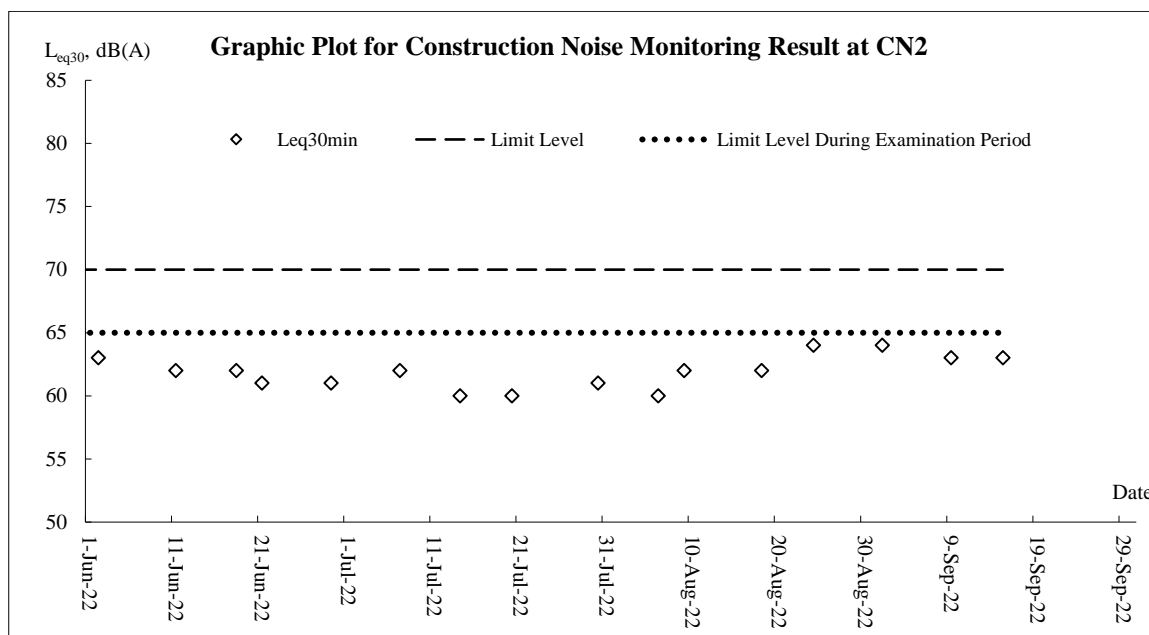

Appendix J

Meteorological Data

Date		Weather	Total Rainfall (mm)	Kwun Tong Station	Kai Tak Station		King's Park Station
				Mean Air Temp. (°C)	Wind Speed (km/h)	Wind Direction	Mean Relative Humidity (%)
1-Sep-22	Thu	Very hot with sunny periods, a few showers and thunderstorms	2.8	30.1	8.7	SE	77
2-Sep-22	Fri	Very hot and dry during the day.	0	29	11.7	W/NW	61.7
3-Sep-22	Sat	Mainly fine.	0	29.2	10.5	W/NW	60.2
4-Sep-22	Sun	Moderate northerly winds, fresh offshore at first.	0	29.9	11.7	W/NW	50
5-Sep-22	Mon	Fine and dry. Very hot during the day.	0	30.7	8.2	N/NW	47.7
6-Sep-22	Tue	Moderate northwesterly winds.	0	30.7	9.5	E	52.5
7-Sep-22	Wed	Fine, dry and very hot in the afternoon.	8.6	27.1	13.2	E	85
8-Sep-22	Thu	Light winds, becoming moderate easterlies.	Trace	29.1	12.5	E/SE	71.5
9-Sep-22	Fri	Sunny intervals and a few showers.	0	29.7	10.2	E	69.5
10-Sep-22	Sat	Moderate to fresh easterly winds	Trace	28.6	11.7	E	71
11-Sep-22	Sun	Occasionally strong offshore later.	0	30.3	9.8	E/SE	70.2
12-Sep-22	Mon	Dry with sunny periods in the afternoon.	0	31.3	10.5	W/SW	51
13-Sep-22	Tue	Mainly cloudy tonight. Moderate to fresh easterly winds	0	32.4	7	W/SW	48
14-Sep-22	Wed	Occasionally strong offshore at first.	0	32.6	10	W/SW	50
15-Sep-22	Thu	Mainly fine.	0	32.4	9.2	W/SW	61
16-Sep-22	Fri	Moderate easterly winds, fresh offshore at first.	Trace	31.3	8.2	W/NW	71
17-Sep-22	Sat	Moderate easterly winds, fresh offshore at first.	Trace	31	11.5	W/NW	75
18-Sep-22	Sun	Moderate to fresh easterly winds	20.3	30.2	13.7	W/SW	77
19-Sep-22	Mon	Moderate to fresh easterlies tonight.	3.3	29.7	13.7	W/NW	78.7
20-Sep-22	Tue	Light winds.	3.5	27.4	12.5	E	78.7
21-Sep-22	Wed	Sunny intervals and a few showers.	8.5	27.6	19.5	E	73.7
22-Sep-22	Thu	Mainly cloudy with one or two showers tonight.	0	26.5	12.5	E	72.7
23-Sep-22	Fri	Hot with sunny periods in the afternoon.	13.4	27.9	10	E/SE	75
24-Sep-22	Sat	Mainly fine. Hot and dry.	0	27.8	9.5	E/SE	71.2
25-Sep-22	Sun	Moderate to fresh east to northeasterly winds	0	28.3	10	SE	70
26-Sep-22	Mon	Mainly cloudy with one or two showers.	0	28.9	13.5	E/SE	66.2
27-Sep-22	Tue	Sunny periods in the afternoon.	Trace	28.6	18	E	70
28-Sep-22	Wed	Mainly cloudy. Sunny intervals during the day.	0	28.1	21.5	E	72.5
29-Sep-22	Thu	Mainly cloudy with showers and a few squally thunderstorms.	8.1	26.1	16.5	E	84.7
30-Sep-22	Fri	Mainly cloudy with a few showers.	102.7	25.7	15	E	88.7

Appendix K

Waste Flow Table

Monthly Summary Waste Flow Table for 2022 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract (see Note 6)	Reused in other Projects (see Note 8)	Disposed as Public Fill	Imported Fill	Metals (see Note 9)	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste (see Note 5)	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	2.871	0.000	2.517	0.000	0.354	0.000	0.000	0.000	0.015	0.000	0.082
Feb	1.372	0.000	1.187	0.000	0.185	0.000	0.000	0.000	0.000	0.000	0.102
Mar	2.226	0.000	1.128	0.000	1.099	0.000	0.000	0.000	0.000	0.000	0.075
Apr	8.798	0.000	3.728	4.288	0.782	0.000	0.000	0.791	0.000	0.000	0.160
May	3.665	0.000	0.000	3.081	0.584	0.000	0.000	0.813	0.000	0.000	0.123
Jun	12.282	13.582	0.000	11.784	0.498	0.000	0.004	0.000	0.007	0.000	0.081
Sub-total	31.214	13.582	8.560	19.153	3.501	0.000	0.004	1.604	0.022	0.000	0.623
Jul	9.504	0.000	0.000	9.473	0.031	0.000	0.004	0.000	0.007	0.000	0.107
Aug	11.236	0.107	0.000	10.294	0.941	0.000	0.003	0.000	0.009	0.000	0.133
Sep	15.716	0.000	0.000	14.996	0.720	0.000	0.003	0.000	0.009	0.000	0.192
Oct	0.000										
Nov	0.000										
Dec	0.000										
Total	67.670	13.689	8.560	53.917	5.193	0.000	0.014	1.604	0.046	0.000	1.056

Notes:

- (1) The performance targets are given in PS Clause 1.119 (14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and waste will be collected by recycler for recycling.
- (4) Use the conversion factor, density of general refuse (1 t/m³) and inert C&D materials (2 t/m³).
- (5) Use the conversion factor for chemical waste (0.88kg/L).
- (6) Assume a dump truck delivers 7.5 m³ material in 1 trip.
- (7) The cut-off date of this summary is 20th of each month.
- (8) The Inert C&D materials of reused in other Projects including glass materials.
- (9) The C&D waste generation of metal including rechargeable battery recycling.

Remarks: refer to Rock and AHM Record (Z:\04 SUPPORT WORK FOLDERS\F. ENVIRONMENTAL\4 - Implementation and Operation\4.4 - Documentation and its Control\11 - WFT, ULSD & Timber\Waste Flow Table\2017-07)

Name of Department : CEDDContract No. : NE/2016/05**Monthly Summary Waste Flow Table for 2022** (year)**[PS Clause 1.129]**

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 m ³)
Jan	0.02	0	0	0	0.02	0	0	0	0	0	0.05
Feb	0.01	0	0	0	0.01	0	0	0	0	0	0.05
Mar	0.02	0	0	0	0.02	0	0	0	0	0	0.01
Apr	0.02	0	0	0	0.02	0	0	0	0	0	0.01
May	0.04	0	0	0	0.04	0	0	0	0	0	0.03
June	0.13	0	0	0	0.13	0	0	00	0	0	0.02
Sub-total	0.24	0	0	0	0.24	0	0	0	0	0	0.17
July	0.15	0	0	0	0.15	0	0	0	0	0	0.02
Aug	0.04	0	0	0	0.04	0	0	0	0	0	0.02
Sept	0.06	0	0	0	0.06	0	0	0	0	0	0.06
Oct											
Nov											
Dec											
Total	0.49	0	0	0	0.49	0	0	0	0	0	0.27

- Notes:
- (1) The performance targets are given in PS Clause 6.14
 - (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
 - (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works. Together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³.

Contract No.: NE/2017/03

Development of Anderson Road Quarry Site – Road Improvement Works and Pedestrian Connectivity Facilities Works Phase 2A

Monthly Summary Waste Flow Table for 2022 (year)

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract (see Note 6)	Reused in other Projects (see Note 6)	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste (see Note 5)	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan	1.587	0.000	0.441	0.000	1.146	0.000	0.003	0.000	0.003	0.000	0.052
Feb	1.039	0.000	0.200	0.000	0.839	0.000	0.000	0.000	1.694	0.000	0.016
Mar	1.261	0.000	0.090	0.000	1.171	0.000	0.000	0.000	0.434	0.000	0.041
Apr	1.200	0.000	0.460	0.000	0.740	0.000	0.002	0.099	0.523	0.000	0.015
May	1.087	0.000	0.094	0.000	0.993	0.000	0.000	0.000	1.456	0.070	0.033
Jun	0.976	0.000	0.014	0.265	0.697	0.000	0.000	0.000	0.602	0.000	0.026
Sub-total	7.149	0.000	1.299	0.265	5.586	0.000	0.005	0.099	4.712	0.070	0.183
Jul	1.594	0.000	0.067	0.495	1.032	0.000	0.000	0.000	1.778	0.000	0.027
Aug	1.913	0.000	0.187	0.954	0.772	0.000	0.002	0.092	1.601	0.000	0.025
Sep	2.045	0.000	0.570	0.221	1.254	0.420	0.000	0.000	0.000	0.000	0.041
Oct											
Nov											
Dec											
Total	12.702	0.000	2.123	1.936	8.643	0.420	0.007	0.191	8.091	0.070	0.275

Notes:

- (1) The performance targets are given in PS Clause 1.129 (4).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material and waste will be collected by recycler for recycling.
- (4) Use the conversion factor, density of general refuse (1 t/m³) and inert C&D materials (2 t/m³).
- (5) Use the conversion factor for chemical waste (0.88kg/L).
- (6) Assume a dump truck delivers 7.5 m³ material in 1 trip.

Monthly Summary Waste Flow Table

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity of Materials Generated	Hard Rock, Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 m ³)*
2021 Total	608.254	394.831	0.000	0.000	213.423	0.000	0.000	0.000	0.000	0.000	0.044
2022											
Jan	25.019	0.000	0.000	0.000	25.019	0.000	0.000	0.000	0.000	0.000	0.019
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.015
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.031
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.014
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.002
June	0.795	0.000	0.000	0.795	0.000	0.000	0.000	0.000	0.000	0.000	0.000
July	0.000	0.000	0.000	0.000	478.700	0.000	0.000	0.000	0.000	0.000	0.000
Aug	175.620	0.000	0.000	0.000	175.620	0.000	0.000	0.000	0.000	0.000	10.340
Sep	389.520	0.000	0.000	0.000	389.520	0.000	0.000	0.000	0.000	0.000	0.000
Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Nov	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Dec	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Accumulated Total (2021-2022)	1199.208	394.831	0.000	0.795	1282.282	0.000	0.000	0.000	0.000	0.000	10.465

*Remarks: Conversion factor for general refuse, 1 tonne = 2m³

Wing Lee – Univic Joint Venture ED/2019/02 - Environmental Management Plan Appendices - Appendix 13	Rev. No.	18
	Issue Date	30-Sep-2022

Name of Department : CEDD

Contract No. : ED/2019/02

Monthly Summary Waste Flow Table for 2022 (year)

Month	Annual Quantities of Inert C&D Materials Generated Monthly						Annual Quantities of C&D Materials Generated Monthly				
	Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 2)	Chemicals Waste	Others, e.g. general refuse
	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 m ³)
Jan	0.18	0.18	0	0	0.18	0	0	0	0	0	0.02
Feb	0.02	0.02	0	0	0.02	0	0	0	0	0	0
Mar	0.31	0.31	0	0	0.31	0	0	0	0	0	0.01
Apr	0.162	0.162	0	0	0.162	0	0	0	0	0	0.009
May	0.279	0.279	0	0	0.279	0	0	0	0	0	0.008
June	0.039	0.039	0	0	0.039	0	0	0	0	0	0.006
Sub-total	0.990	0.990	0	0	0.990	0	0	0	0	0	0.053
July	0.028	0.028	0	0	0.028	0	0	0	0	0	0.003
Aug	0.152	0.152	0	0	0.152	0	0	0	0	0	0.016
Sept	0.665	0.665	0	0	0.665	0	0	0	0	0	0
Oct	---	---	---	---	---	---	---	---	---	---	---
Nov	---	---	---	---	---	---	---	---	---	---	---
Dec	---	---	---	---	---	---	---	---	---	---	---
Total	1.835	1.835	0	0	1.835	0	0	0	0	0	0.072

- Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.

Appendix L

Implementation Schedule for Environmental Mitigation Measures

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
Dust Impact (Contraction Phase)									
S4.7.2 to S4.7.5	Mitigation measures in form of regular watering under a good site practice should be adopted. Watering once per hour on exposed worksites and haul road is proposed to achieve dust removal efficiency of 91.7%. While the above watering frequencies are to be followed, the extent of watering may vary depending on actual site conditions but should be sufficient to maintain an equivalent intensity of no less than 1.75 L/m ² to achieve the respective dust removal efficiencies.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	V	V	V	V	V
S4.7.6	The Contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction ion Dust) Regulation.	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	V	V	V	V	V
S4.7.6	Following dust suppression measures should also be incorporated by the Contractor to control the dust nuisance throughout the construction phase: <ul style="list-style-type: none">Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading;Any dusty materials remaining after a stockpile is removed should be wet ted with water and cleared from the surface of roads;A stockpile of dusty material should not be extend beyond the pedestrian barriers, fencing or traffic cones;The load of dusty materials on a vehicle leaving a construction ion site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle;Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road sect ion between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;When there are open excavation and reinstatement	Minimize dust impact at the nearby sensitive receivers	Contractor	All construction sites	@	@	@	@	@

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<p>works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction ion period.</p> <ul style="list-style-type: none"> • The port ion of any road leading only to construction ion site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; • Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; • Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet ; • Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; • Any skip hoist for material transport should be totally enclosed by impervious sheeting; • Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides; • Cement or dry PFA delivered in bulk should be stored in a closed silo fit ted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed; and • Exposed earth should be properly treated by compact ion, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, 								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	shortcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.								
S4.7.7	Implement regular dust monitoring under EM&A programme during the Construction phase.	Control construction airborne noise	Selected Representative dust monitoring station	All construction sites where practicable	V	N/A	V	N/A	N/A
Noise Impact (Contraction Phase)									
S5.6.9	Implement the following good site management practices: <ul style="list-style-type: none"> only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction ion programme; machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; plant known to emit noise strongly in one direct ion, where possible, be orientated so that the noise is directed away from nearby NSRs; silencers or mufflers on construction ion equipment should be properly fit ted and maintained during the construction ion works; mobile plant should be sited as far away from NSRs as possible and practicable; and material stockpiles, mobile container site office and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. 	Control construction ion airborne noise	Contractor	All construction sites where practicable	@	V	V	@	@
S5.6.11 to S5.6.13	Use of “ Quiet ” Plant and Working Methods.	Reduce the noise levels of plant items	Contractor	All construction sites where practicable	V	N/A	N/A	N/A	N/A
S5.6.14	Install temporary site hoarding (approx 2.5m high) located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction ion noise levels at low-level zone of NSRs through partial screening.	Contractor	All construction sites where practicable	V	V	V	V	V
S5.6.15 to S5.6.18	Install movable noise barriers, full enclosure and acoustic mat, screen the noisy plants including air compressor and generator.	Screen the noisy plant items to be used at all construction sites	Contractor	All construction ion sites where practicable	V	V	N/A	V	N/A
S5.6.19	Sequencing operation of construction plants equipment.	Operate sequentially	Contractor	All construction	V	V	N/A	N/A	N/A

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
		within the same work site to reduce the construction airborne noise		ion sites where practicable					
S5.6.34	Implement temporary noise barrier along Road L4.	Further reduce the construction ion airborne noise	Contractor	Road L4 of ARQ	N/A	N/A	N/A	N/A	N/A
S5.6.35	Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected Representative Noise monitoring stations	V	N/A	V	N/A	N/A
B		Water Quality Impact (Contraction Phase)							
S6.6.3	<u>Construction Runoff</u> In accordance with the Practice Note for Professional Persons on Construction ion Site Drainage, Environmental Protection Department, 1994 (ProPECC PN 1/94), best management practices should be implemented as far as practicable as below: <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. Diversion of natural stormwater should be provided as far as possible. The design of temporary on-site drainage should prevent runoff going through site surface, construction machinery and equipment in order to avoid or minimize polluted runoff. Sediment at ion tanks with sufficient capacity, constructed from preformed individual cells of approximately 6 to 8 m³ capacities, are recommended as a general mitigation measure which can be used for setting surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped. 	Control construction runoff	Contractor	All construction sites	@	@	@	@	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<ul style="list-style-type: none"> The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a silt /sediment trap. The silt /sediment traps should be incorporated in the permanent drainage channels to enhance deposition rates. The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94. The detailed design of the sand/silt traps should be undertaken by the contractor prior to the commencement of construction. Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas. Measures should be taken to minimise the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, it should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. All open stockpiles of construction materials (for example, aggregates, sand and fill material) of should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to 								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<p>prevent the washing away of construction ion materials, soil, silt or debris into any drainage system.</p> <ul style="list-style-type: none"> Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction ion materials or debris being washed into the drainage system and storm runoff being directed into foul sewers. Precautions to be taken at any time of year when rainstorms are likely, act ions to be taken when a rainstorm is imminent or forecasted, and act ions to be taken during or after rainstorms are summarized in Appendix A2 of <i>ProPECC PN 1/94</i>. Particular attention should be paid to the control of silty surface runoff during storm events. All vehicles and plant should be cleaned before leaving a construction ion site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing facilities should be provided at every construction ion site exit where practicable. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The sect ion of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient back all toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and rains. Oil interceptors should be provided in the drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain. Construction ion solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts. 								

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<ul style="list-style-type: none"> All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby. Regular environmental audit on the construction site should be carried out in order to prevent any malpractices. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the rivers. 								
S6.6.6 and 6.6.7	<p><u>Sewage from Workforce</u></p> <ul style="list-style-type: none"> Portable chemical toilets should be provided for handling the construction sewage generated by the workforce. Assume that the capacity of the chemical toilets would be 0.4m³ and suck up twice a day under normal practices, around 45 chemical toilets would be required for the whole site at peak hour. And it should be noted that under normal construction periods, less chemical toilets would be needed. In addition, the total number of the chemical toilets would be subject to later detailed design, the capacity of the chemical toilets, and contractor's site practices. Nevertheless, a licensed contractor should be employed to provide appropriate and adequate portable toilets to cater around 37.5 m³/day sewage and be responsible for appropriate disposal and maintenance. Since portable chemical toilets will be provided, no adverse water quality impact from the workforce sewage is anticipated. Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the Project. Regular environmental audit on the construction site should be conducted in order to provide an effective control of any malpractices and achieve continual improvement of environmental performance on site. It is anticipated that sewage generation during the construction phase of the Project would not cause 	Handling of site sewage	Contractor	All construction sites	V	V	V	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	water quality impact after undertaking all required measure								
S6.6.8 and 6.6.9	<u>Accidental Spillage</u> To prevent accidental spillage of chemicals, proper storage and handling facilities should be provided. All the tanks, containers and storage area should be bunded and the locations should be locked as far as possible from the sensitive watercourse and storm drains. The Contractor is required to register as a chemical waste producer if chemical wastes would be generated from the construction ion activities. Storage of chemical waste arising from the construction ion activities should be well managed with suitable labels and warnings while disposal of those chemical wastes should be comply with the requirement states in Waste Disposal Ordinance (Cap 354) as well as Waste Disposal (Chemical Waste) (General) Regulations.	Prevention of accidental spillage	Contractor	All construction sites	@	V	V	V	V
S6.6.11- S6.6.14	<u>Groundwater from Contaminated Area</u> The Contractor should apply for a discharge licence under the WPCO through the Regional Office of EPD for groundwater discharge. Prior to the excavation works within these potentially contaminated areas, the groundwater quality should be reviewed during the process of discharge license application. The compliancy to the TM-DSS and the existence of prohibited substance should be confirmed after further SI. If the review results indicated that the groundwater to be generated from the excavation works would be contaminated, the contaminated groundwater should be either properly treated in compliance with TMDSS or properly recharged into the ground. If wastewater treatment is deployed, the wastewater treatment unit shall deploy suitable treatment process (e.g. oil interceptor / activated carbon) to reduce the pollution level to an acceptable standard and remove any prohibited substances (e.g. Petroleum Carbon Ranges (PCRs)). All treated effluent from wastewater treatment plant shall meet the requirements as stated in TM-DSS and should be	Minimize contaminated groundwater impacts	Contractor	All construction sites	N/A	N/A	N/A	N/A	N/A

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<p>discharged into the foul sewers.</p> <p>If groundwater recharging wells are deployed, recharging wells should be installed as appropriate for recharging the contaminated groundwater back into the ground. The recharging wells should be selected at places where the groundwater quality will not be affected by the recharge operation as indicated in the Section 2.3 of TM-DSS. The baseline groundwater quality shall be determined prior to the selection of the recharge wells, and submit a working plan (including the laboratory analytical results showing the quality of groundwater at the proposed recharge location(s) as well as the pollutant levels of groundwater to be recharged) to EPD for agreement. Pollution levels of groundwater to be recharged shall not be higher than pollutant levels of ambient groundwater at the recharge well. Prior to recharge, any prohibited substances such as PCRs should be removed as necessary by installing the petrol interceptor.</p>								
Waste Management (Contraction Phase)									
S8.5.2	<p><u>Good Site Practice</u></p> <p>The following good site practices are recommended throughout the construction activities:</p> <ul style="list-style-type: none"> • nomination of an approved personnel, such as a site manager, to be responsible for the implementation of good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in site cleanliness, appropriate waste management procedures and concepts of waste reduction, reuse and recycling; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; 	Minimize waste generation during construction	Contractor	All construction sites	V	@	V	@	V
S8.5.2 (6)	The contractor should submit a Waste Management Plan	Minimize waste	Contractor	All construction	V	V	V	女	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	(WMP) as part of the Environmental Management Plan (EMP) in accordance with the <i>ETWB TC(W) No. 19/2005</i> for construction ion phase. The EMP should be submit ted to the Engineer for approval. Mitigation measures proposed in the EIA Report and the EM&A Manual should be adopted.	generation during construction		sites					
S8.5.3	<u>Waste Reduction Measures</u> Waste reduction is best achieved at the planning and design phase, as well as by ensuring the implementation of good site practices. The following recommendations are proposed to achieve reduction: <ul style="list-style-type: none"> segregate and store different types of waste in different containers, skip or stockpiles to enhance reuse or recycling o materials and their proper disposal; proper storage and site practices to minimize the potential for damage and contamination of construction ion materials; plan and stock construction ion materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste; sort out demolition debris and excavated materials from demolition works to recover reusable/recyclable port ions (i.e. soil, broken concrete, metal etc.); provide training to workers on the importance of appropriate waste management procedures, including waste reduction, reuse and recycling. 	Reduce waste generation	Contractor	All construction sites where practicable	V	V	V	V	V
S8.5.5	<u>Storage of Waste</u> The following recommendation should be implemented to minimize the impacts: <ul style="list-style-type: none"> waste such as soil should be handled and stored well to ensure secure containment ; stockpiling area should be provided with covers and water spraying system to prevent materials from wind-blown or being washed away; different locations should be designated to stockpile each material to enhance reuse; 	Minimize waste impacts from storage	Contractor Contractor	All construction sites	V	V	V	V	V
S8.5.6	<u>Collection and Transportation of Waste</u> The following recommendation should be implemented to minimize the impacts:	Minimize waste impacts from storage	Contractor	All construction sites	V	@	V	@	@

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<ul style="list-style-type: none"> remove waste in timely manner; employ the trucks with cover or enclosed containers for waste transportation; obtain relevant waste disposal permits from the appropriate authorities; and disposal of waste should be done at licensed waste disposal facilities. 								
S8.5.8	<p><u>Excavated and C&D Material</u></p> <p>Wherever practicable, C&D materials should be segregated from other wastes to avoid contamination and ensure acceptability at public filling areas or reclamation sites. The following mitigation measures should be implemented in handling the excavated and C&D materials:</p> <ul style="list-style-type: none"> maintain temporary stockpiles and reuse excavated fill material for backfilling; carry out on-site sorting; make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; implement a recording system for the amount of waste generated, recycled and disposed of for checking; <p>The recommended C&D materials handling should include:</p> <ul style="list-style-type: none"> On-site sorting of C&D materials Reuse of C&D materials Use of Standard Formwork and Planning of Construction Materials purchasing Provision of wheel wash facilities 	Minimize waste impacts from excavated and C&D materials	Contractor	All construction sites	V	V	V	V	V
S8.5.15	<p><u>Contaminated Soil</u></p> <p>As a precaution, it is recommended that standard good site practice should be implemented during the construction phase to minimize any potential exposure to contaminated soils or groundwater. The details of mitigation measures to minimize the potential environmental implications arising from the handling of contaminated materials refer to Land Contamination Section.</p>	Remediate contaminated soil	Contractor	All construction sites where applicable	V	V	N/A	N/A	N/A
S8.5.17	<u>Chemical Waste</u>	Control the chemical	Contractor	All construction	V	V	V	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<ul style="list-style-type: none"> If chemical wastes are produced at the construction site, the Contractors should register with EPD as chemical waste producer. Chemical wastes should be stored in appropriate containers and collected by a licensed chemical waste Contractor. Chemical wastes (e.g. spent lubricant oil) should be recycled at an appropriate facility as far as possible, while the chemical waste that cannot be recycled should be disposed of at either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation. 	waste and ensure proper storage, handling and disposal.		sites					
S8.5.18	<u>General Waste</u> <ul style="list-style-type: none"> General refuse should be stored in enclosed bins separately from construction and chemical wastes. Recycling bins should also be placed to encourage recycling. Preferably enclosed and covered areas should be provided for general refuse collection and routine cleaning for these areas should also be implemented to keep areas clean. A reputable waste collector should be employed to remove general refuse on a daily basis. 	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	@	V	V	V	@
S8.5.19	<u>Sewage</u> <ul style="list-style-type: none"> The WMP should document the locations and number of portable chemical toilets depending on the number of workers, land availability, site condition and activities. Regularly collection by licensed collectors should be arranged to minimize potential environmental impacts. 	Minimize production of sewage impacts	Contractor	All construction sites	V	V	V	V	V
Ecology (Contraction Phase)									
S. 10.7.2 to 10.7.6	Re-provision of Wooded Area for ecological function at the future Quarry Park.	Compensate for the loss of three woodland patches of a total area of about 1.13ha.	Contractor/ Detailed Design Consultant (qualified botanist / horticulturist / Certified Arborist to supervise the planting).	Northern part of the proposed Quarry Park.	N/A	N/A	N/A	N/A	N/A

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
.10.7.10	<p>Construction phase in situ mitigation measures to minimize impacts on hydrological condition and water quality of hillside watercourses include:</p> <ul style="list-style-type: none"> • Temporary sewerage and drainage will be designed and installed to collect wastewater and prevent it from entering nearby watercourses; • Proper locations well away from nearby watercourses will be used for temporary storage of materials (i.e. equipment, fill materials, chemicals and fuel) and temporary stockpile of construction debris and spoil, and these will be identified before commencement of works; • To prevent muddy water entering nearby watercourses, work sites close to nearby watercourses will be isolated, using such items as sandbags or silt curtains with lead edge at bottom and properly supported props. Other protective measures will also be taken to ensure that no pollution or siltation occurs to the water gathering grounds of the works site; • Stockpiling of construction materials, if necessary, will be properly covered and located away from nearby watercourses; • Erection of temporary geotextile silt fences will be carried out around earth-moving works to trap any sediments and prevent them from entering watercourses; • Construction debris and spoil will be covered and/or properly disposed as soon as possible to avoid being washed into nearby watercourses; • Exposed soil will be covered as quickly as possible following formation works, followed, where appropriate, by covering with biodegradable geotextile blanket for erosion control purposes; • Where appropriate, earth-bundling will be carried out of areas where soils have been disturbed or where vegetation has been cleared, to ensure that surface runoff will not move soils off-site; • Construction ion effluent, site run-off and sewage will be probably collected and/or treated. Wastewater from any construction ion site will be 	Minimize impacts on Hydrological condition and water quality of hillside watercourses.	Contractor	All construction sites	V	N/A	V	V	N/A

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
	<p>minimised via the following in descending order: reuse, recycling and treatment ;</p> <ul style="list-style-type: none"> • Proper locations for discharge out lets of wastewater treatment facilities well away from sensitive receivers will be identified and used; • Silt traps will be installed at points where drainage from the site enters local watercourses; • Appropriate sanitary facilities for on-site workers will be provided; • The site boundary will be clearly marked and any works beyond the boundary strictly prohibited, and • Regular water monitoring and site audit will be carried out at suitable points. If the monitoring and audit results show that pollution occurs, adequate measures including temporary cessation of works will be considered. 								
S.10.7.11	<p>Implement an emergency contingency plan during the construction phase and the plan will include, but not be limited to, the following:</p> <ul style="list-style-type: none"> • Potential emergency situations; • Chemicals or hazardous materials used on-site (and their location); • Emergency response team; • Emergency response procedures; • List of emergency telephone hot lines; • Locations and types of emergency response equipment , and • Training plan and testing for effectiveness. 	Minimize impacts on Hydrological condition and water quality of hillside watercourses.	Contractor	All construction sites	N/A	N/A	N/A	N/A	N/A
Landscape and visual (Contraction Phase)									
S11.14.23, Table 11.9, CM1 [4]	All existing trees to be retained shall be carefully protected during construction.	Avoid disturbance and protection of the existing trees	Detailed Design Consultant /	The whole area where applicable	V	V	@	V	@
S11.14.23, Table 11.9, CM2 [3]	Tree Transplantation - Should removal of trees be unavoidable due to construction impacts, trees will be transplanted or felled. Detailed transplanting proposal will be submit ted to relevant government departments for approval in accordance with LAO GN No. 7/2007, ETWB TCW No. 29/2004 and 10/2013 . Final locations of transplanted trees shall be agreed prior to commencement of the work.	Minimize landscape impact and retention of landscape resources	Detailed Design Consultant /	Onsite where possible. Otherwise consider offsite locations	*	N/A	N/A	V	V

EM&A Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concern to Address	Who to implement the measures?	Location of the measure	Implementation Status				
					Contract 1	Contract 2	Contract 3	Contract 4	Contract 5
S11.14.23, Table 11.9, CM3 [4]	Control of operation night -time glare with well-planned lighting operation system to minimize potential glare impact to adjacent VSRs	Minimize glare impact to adjacent VSRs	Contractor/ CEDD	The whole project area where applicable	V	V	@	V	N/A
S11.14.23, Table 11.9, CM [4]	Erection of decorative screen hoarding.	Minimize visual impact	Contractor/ CEDD	The whole project area where applicable	N/A	N/A	N/A	N/A	N/A
S11.14.23, Table 11.9, CM5 [2]	Minimise disturbance and limitation of run-off – temporary structures and construction works should be planned with care to minimize disturbance to adjacent landscape, vegetation, natural stream habitats.	Minimize visual impact	Contractor/ CEDD	The whole project area where applicable	V	V	V	V	N/A

Legend: V = implemented; x = not implemented; @ = partially implemented; * = pending to be implemented; N/A = not applicable

Appendix M

Complaint Log

Appendix M1

Cumulative Complaint and Summons/ prosecution

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/ Prosecution in Reporting Month
March 2017	1	0
April 2017	0	0
May 2017	0	0
June 2017	2	0
July 2017	3	0
August 2017	3	0
September 2017	4	0
October 2017	2	0
November 2017	3	0
December 2017	3	0
January 2018	1	0
February 2018	4	0
March 2018	0	0
April 2018	2	0
May 2018	1	0
June 2018	1	0
July 2018	0	0
August 2018	1	0
September 2018	1	0
October 2018	1	0
November 2018	3	0
December 2018	2	0
January 2019	2	0
February 2019	3	0
March 2019	1	0
April 2019	0	0
May 2019	0	0
June 2019	1	0
July 2019	1	0
August 2019	1	0
September 2019	0	0
October 2019	1	0
November 2019	4	0
December 2019	0	0
January 2020	0	0
February 2020	0	0
March 2020	4	0
April 2020	1	0
May 2020	1	0
June 2020	1	0
July 2020	0	0
August 2020	0	0
September 2020	0	0
October 2020	0	0
November 2020	1	0
December 2020	2	0
January 2021	1	0
February 2021	0	0
March 2021	2	0

April 2021	1	0
May 2021	0	0
June 2021	1	0
July 2021	1	0
August 2021	0	0
September 2021	2	0
October 2021	0	0
November 2021	0	0
December 2021	0	0
January 2022	0	0
February 2022	0	0
March 2022	1	0
April 2022	1	0
May 2022	3	0
June 2022	2	0
July 2022	0	0
August 2022	2	0
September 2022	1	0
Overall Total	80	0

Appendix M2 Complaint Log

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
1	23-Mar-17	8-Jun-17	On Tat Estate	Resident of On Tat Estate	Construction noise	SPRO hotline	NA	A resident living in On Tat House reported that some night works with noise and flashing caused nuisance to nearby resident after 11:00 pm on 23 March 2017.	According the incident report conducted by the CWSTVJV, demobilization of crawler crane was undertaken on 23 March 2017 11pm and it is TD requirement to carry out demobilization of heavy machine at nighttime. It is considered this complaint was a single incident and would not be happened again in future.	no comment by IEC on 11 Oct 2017	TCS00864/16/300/F0087
2	28-Jul-17	28-Jul-17	38/F of Yin Tat House (賢達樓), On Tat Estate	Resident of On Tat Estate	Construction noise	SPRO hotline	NA	Mr. Hsu received a complaint from a resident living in the flat on 38/F of Yin Tat House (賢達樓), On Tat Estate. The resident complained about the noise level of our works during daytime.	Noise monitoring by Contractor was conducted in Yin Tat House, On Tat Estate, at around 2 pm on 28-Jul-2017. Another noise monitoring was carried out by ET (AUES) and representatives of AECOM and JV in the presence of the complainant in her flat at 10 am on 1-Aug-2017 and was witnessed by Mr. Hsu. No exceedance of noise was recorded. The complainant was satisfied about the monitoring results.	no comment by IEC on 9 Aug 2017	TCS00864/16/300/F0060
3	29-Aug-17	29-Aug-17	Shing Tat House 24/F	Resident of On Tat Estate	Construction noise	SPRO hotline	NA	Mr. Hsu Yau Wai (Tel no.9519 5663) reported that he received complaint from a resident (Ms Cheng) living at Shing Tat House 24/F Room 22 about the noise generated from our site	Noise monitoring was carried out by ET (AUES) and representatives of AECOM and JV in the presence of the complainant in her flat at 3pm on 30-Aug-2017. No exceedance of noise was recorded. The complainant was satisfied about the monitoring results.	no comment by IEC on 8 Sep 2017	TCS00864/16/300/F0081

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								this week. The noise heard was mainly rock breaking noise from our site.			
4	21-Jun-17	29-Aug-17	Tat Yan House, Po Tat Estate	Resident of Po Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/00019373-17)	day time construction noise of breakers (8am to 6pm)	Since these two complaints were forwarded by CEDD to ET on 31 August 2017 which way after the complaint dates. Investigation would be conducted based on the site information by the Contractor of Contract 1 - NE/2016/01 (CWSTVJV) as well as the observation during weekly site inspection carried out ET during June 2017. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident and the working hour 08:00 to 18:00 did not breach any legal requirement. To eliminate the inconvenience caused to the nearby resident CWSTVJV was advised to further enhance the noise mitigation measures as appropriately.	no comment by IEC on 3 Nov 2017	TCS00864/16/300/F0093
5	22-Jun-17	29-Aug-17	Tat Yan House, Po Tat Estate	Resident of Po Tat Estate	Dust & Construction noise	EPD	EPD (ref. N08/RE/00019428-17)	Day time construction noise of breakers (8AM to 6PM). Requested to delay the operating hour of breakers to 10AM or 11AM			TCS00864/16/300/F0093

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
6	15-Jul-17	29-Aug-17	Tat Yi House, Po Tat Estate	Resident of Po Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/000 22479-17)	Construction noise	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident and the working hour 08:00 to 18:00 did not breach any legal requirement. To eliminate the inconvenience caused to the nearby resident, CWSTVJV was advised to further enhance the noise mitigation measures as appropriately.	no comment by IEC on 3 Nov 2017	TCS00864/16/300/F0094
7	28-Jul-17	29-Aug-17	Anderson Road	unknown	Dust	EPD	EPD (ref.N08/RE/000 23986-17)	Poor control on dust emission at Anderson Road Construction Site	CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident and status of the implementation of dust mitigation measures was considered effective based on the site observation.	no comment by IEC on 15 Nov 2017	TCS00864/16/300/F0097
8	2-Aug-17	29-Aug-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/000 24557-17)	Day time construction noise of breakers (8AM to 6PM)	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in August 2017, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should further enhance the noise mitigation measures as appropriately. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 15 Nov 2017	TCS00864/16/300/F0098

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
9	19-Sep-17	19-Sep-17	Sau Mau Ping Estate Sau Nga House	Resident of Sau Mau Ping Estate	Construction noise	SPRO hotline	NA	The complainant is living at Sau Mau Ping Estate Sau Nga House (秀雅樓) 38/F. He complained about the noise nuisance recently from August to September especially during night time after 12:00 am, even in Saturdays and Sundays. The noise nuisance caused a great disturbance to him. He made a request to conduct investigation about the source of the noise during night time.	ET has conducted an ad-hoc noise measurement for Leq (30min) on the rooftop of 秀雅樓 and 秀義樓 in the afternoon of 22 September 2017. (Photo 1 & 2) During the course of noise measurement, construction activities such as excavation and breaking were conducted in the Quarry Site. The measurement results taken at both 秀雅樓 and 秀義樓 were 63dB(A) which below the Limit Level under the EM&A Programme.	no comment by IEC on 18 Oct 2017	TCS00864/16/300/F0088
10	21-Sep-17	13-Oct-17	Sau Mau Ping Estate Sau Nga House and Sau Yee House	Resident of Sau Mau Ping Estate	Construction noise	EPD	EPD (ref.N08/RE/00031074-17)	On 21 September 2017, the same complaint further reported that the noise can be heard at both Sau Yee House and Sau Nga House even in daytime and he strongly requested the Contractor to follow up the case immediately.	ET has conducted an ad-hoc noise measurement for Leq (30min) on the rooftop of 秀雅樓 and 秀義樓 in the afternoon of 22 September 2017. (Photo 1 & 2) During the course of noise measurement, construction activities such as excavation and breaking were conducted in the Quarry Site. The measurement results taken at both 秀雅樓 and 秀義樓 were 63dB(A) which below the Limit Level under the EM&A Programme.		TCS00864/16/300/F0088

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
11	27-Sep-17	13-Oct-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction noise	EPD	EPD (ref.N08/RE/00029489-17)	The complainant questioned why there were 6 to 7 breakers operating in the morning but only 1 operating in the afternoon. He requested to shift the operation of the breakers to afternoon.	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in September and October 2017, there		TCS00864/16/300/F0106
12	3-Oct-17	13-Oct-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction noise	EPD	EPD (ref. N08/RE/00032407-17)	Day time construction noise, the complainant requested using less breaker at one time, erecting taller noise barrier to cover the equipment. In addition, the complainant would like to know the construction schedule whether there will be more breaking activities in near future	were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 30 Nov 2017	TCS00864/16/300/F0106
13	25-Oct-17	26-Oct-17	Tat Kwai House, Po Tat Estate	Resident of Po Tat Estate	Dust	EPD	NA	投訴安達臣道地盤的泥車落泥，令他達貴樓的住所受到大塵影響，要求跟進及回覆	Investigation revealed that CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident. Nevertheless, based on the observation during site inspection on 31 October 2017, CWSTVJV was advised to enhance the dust mitigation measures particularly during dry	no comment by IEC on 15 Nov 2017	TCS00864/16/300/F0100

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									season.		
14	6-Nov-17	7-Nov-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Noise	EPD	NA	安達邨俊達樓居民投訴石礦場地盤又再於早上07:45 開始傳出機器不停掙石的噪音(幾乎每日在 08:00-19:00 進行工程), 已持續一年, 他全家人受到滋擾。	Ad-hoc noise measurement was conducted by ET at rooftop of Chun Tat House in the morning of 20 November 2017 and measurement result was below the Limit Level under the EM&A Programme. CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 30 Nov 2017	TCS00864/16/300/F0109
15	13-Nov-17	14-Nov-17	Chi Tai House, On Tai Estate	Mr. Lam Wai	light pollution and noise	SPRO hotline	NA	1. 智泰樓面向安達臣地盤方向, 有照射燈深夜時分仍然常開, 影響居民正常睡眠質素, 造成一定的精神壓力。 2. 隔音布未固定, 大風吹過發出極大的聲浪	To ease the concern by the complaint, CWSTVJV has adjusted the lights to the orientation pointing the ground and that to minimise the nuisance. For the maintenance of noise barrier, CWSTVJV has immediately fixed the noise barrier nearest to On Tai Estate and prolonged the cover area of the noise barrier to reduce the noise impact to the public.	no comment by IEC on 24 Nov 2017	TCS00864/16/300/F0104

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
16	1-Nov-17	14-Nov-17	Shing Tat House, On Tat Estate	Resident of Po Tat Estate	Noise	EPD	NA	居住於安達邨誠達樓高層的投訴人投訴由早上八時半至下午六時聽到搗鐵噪音。	As advised by the Contractor, the works that most likely induced the iron hammering noise to Shing Tat House shall be the rock breaking works to the hard rock of the Southeastern side of the Underground Stormwater Retention Tank. CWSTVJV had already deployed the acoustic mat as noise barrier at the site boundary near Shing Tat House. To enhance the noise mitigation measures, CWSTVJV deployed an acoustic mat as noise barrier for the breaking work in order to reduce construction noise affecting the upper floor of On Tat Estate. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 13 Dec 2017	TCS00864/16/300/F0110
17	25-Aug-17	26-Oct-17	Sau Yee House, Sau Ping Estate	Resident of Sau Mau Ping Estate	Construction Noise	EPD	EPD (ref.N08/RE/00027738-17)	Night time construction noise of hammering (around 12AM)	As advised by CWSTVJV, there was a CNP (GW-RE0763-17) in force for the subject site for operation of generator and electric submersible water pump for the wastewater treatment plant and it is considered that abovementioned PME should not generate significant noise. Moreover, it is confirmed by CWSTVJV and checked against the site diary that no construction activities were carried out after 19:00 at the	no comment by IEC on 14 Dec 2017	TCS00864/16/300/F0114

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									subject site. Therefore, the complaint about noise nuisance during night time should not be related to the Project.		
18	12-Sep-17	26-Oct-17	Chun Tat House, On Tat Estate	Resident of On Tat Estate	Construction Noise	EPD	EPD (ref. N08/RE/0002948 9-17)	Day time construction noise of breakers (8AM to 5PM)	Noise mitigation measures were implemented to reduce the noise impact to the nearby resident. According to the impact noise monitoring result in September 2017, there were no breaches of EM&A requirement. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 10 Jan 2018	TCS00864/16/300/F01 17
19	15-Dec-17	21-Dec-17	Sau Yee House	Resident of Sau Mau Ping Estate	Construction Noise	EPD	NA	Resident of Sau Yee House complained suspected construction noise from Anderson Construction Site at restricted hour (7pm to 7am).	It is confirmed by CWSTVJV and checked against the site diary that no construction activities were carried out after 19:00 at the subject site. Therefore, the complaint about noise nuisance during night time should not be related to the Project.	no comment by IEC on 10 Jan 2018	TCS00864/16/300/F01 18
20	20-Dec-17	21-Dec-17	On Tat Estate	Resident of On Tat Estate	Dust	EPD	NA	Resident of On Tat Estate complained that the traffic of construction vehicles generated dust problem and arouse air pollution to On Tat Estate. 投訴安達臣道信和地盤水車已經壞了十多天，一直無灑水，四周非常大	CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident. It is considered that the complaint was an isolated case due to malfunction of water tanker and CWSTVJV has promptly rectified the deficiency. As advised by CWSTVJV, another water tanker will be deployed in mid-January 2018 to enhance the	no comment by IEC on 25 Jan 2018	TCS00864/16/300/F01 21

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								塵。投訴人住於安達邨，投訴安達臣道石礦場有大地盤，地盤大車工作時間不停出入揚起沙塵，吹到安達邨，影響空氣環境，要求部門到場視察。	dust suppression measures throughout the construction site.		
21	28-Dec-17	10-Jan-18	Sau House	Yee Sau Mau Ping Estate	Construction Noise	CE's office	NA	日間及凌晨均聽到轟隆聲的噪音及震動，懷疑是由附近工程引起 * Thomas 先生表示居於秀茂坪邨秀義樓，指附近的安達臣道一個由土木工程拓展署管轄的石礦場不時於非允許時段(即晚上七時後至翌日早上)發出疑似打地基的轟轟聲巨響，最近一次就是今早(28/12)凌晨五時多再次聽到石礦場傳來聲響，將 Thomas 先生吵醒，懷疑有人刻意在無人監管下施工，更表示曾向環保署及土木工程署作出投訴，但環保署表示巡查後無發現在非允許時段有工程進行，而土木工程署則	ET has conducted an ad-hoc noise measurement for Leq (30min) in the complainant's flat in the monitoring of 17 January 2018. It was noted that the complainant's flat is not in direct line of sight to the Anderson Road Quarry Site. The measurement noise result was below the Limit Level under the EM&A Programme. Moreover, it is confirmed by CWSTVJV and checked against the site diary that no construction activities were carried out during restricted hour at the subject site. Therefore, the complaint about noise nuisance during restricted hour should not be related to the Project.	no comment by IEC on 8 Feb 2018	TCS00864/16/300/F0129

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								表示晚上七時後不會再進行工程。Thomas 指石礦場經常在晚上八至十二時，或凌晨時份發出巨響，對附近居民已造成很大的滋擾，要求相關部門儘快作出跟進及回覆。			
22	15-Jan-18	15-Jan-18	Chun Tat House	Resident of Chun Tat House of On Tat Estate, 40/F	Construction Noise	SPRO mobile	NA	She is irritated by the construction noise of breaking rock for a long time and strongly requested to know exactly when will be the completion date of the breaking rock part of works opposite to Chun Tat House. She said we should do more on the mitigation measures because our site is very close to the residents nearby.	CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in January 2018, there were no breaches of EM&A requirement. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 8 Feb 2018	TCS00864/16/300/F0130

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
23	1-Feb-18	2-Feb-18	Chi Tai House On Estate	Resident of On Tai Estate (referred by Mr. Lam Wai)	Construction Noise	SPRO hotline	NA	"智泰對出，白天噪音過大，可否加裝隔音板？高層受影響"	the Environmental Team has conducted an ad-hoc noise measurement for Leq(30min) at the corridor of 22/F of Chi Tai House on 2 February 2018 facing the construction site. The measurement noise result was 65dB(A) which below the Limit Level under the EM&A Programme. In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. According to the impact noise monitoring result obtained in January 2018, there were no breaches of EM&A requirement.	no comment by IEC on 22 Feb 2018	TCS00864/16/300/F0137
24	1-Feb-18	2-Feb-18	Shing Tat House On Estate	Resident of Shing Tat House (referred by Mr. Hsu Yau Wai)	Construction Noise	SPRO hotline	NA	Mr. Hsu reported that some disturbing noise was heard after 6:00 pm from the site near Shing Tat House of On Tat Estate.	AECOM has liaised with Mr. Hsu on 2 February 2018 for the complaint matter and he reported to AECOM that the noise was generated until 7:00 pm on 1 February 2018. 3. As advised by Contractor of Contract 1, breaking works at USRT area which opposite to Shing Tat House was only carried out from 8:00 to 18:00. However, rock breaking at System A was extended to 19:00 on 1 February 2018. As noise mitigation measures, noise barriers were erected for the works area. Further to the complaint case, CWSTVJV would seek for other quiet work method such as using drilling	no comment by IEC on 28 Feb 2018	TCS00864/16/300/F0140

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									machine to reduce noise level and speed up the rock breaking process, so that to reduce the noise intensity level and the duration of exposure.		
25	28-Feb-18	28-Feb-18	Shing House On Estate	Tat of Shing Tat House	Resident of Shing Tat House	Construction Noise	EPD	NA	<p>安達邨誠達樓居民, 投訴人是返夜班, 一年半以來長期受對出地盤日間採石仔噪音滋擾, 由於單位與地盤太近, 堅持環保署跟進及回覆如何處理及減低噪音, 他亦要求知道何日完工.</p> <p>Breaking works at Underground Stormwater Retention Tank area which opposite to Shing Tat House was carried out from 8:00 to 18:00. The Contractor has implemented noise mitigation measures to reduce the noise impact to the nearby resident. It was advised that the rock breaking works shall tentatively be completed by end of April and it is believed that the noise impact should be minimized. Since the works were carried out within the non-restricted hours and noise monitoring noise were within acceptable level, it is considered that the works under the project did not breach the Noise Control Ordinance.</p>	no comment by IEC on 19 Mar 2018	TCS00864/16/300/F0143
26	11-Apr-18	12-Apr-18	Him House On Estate	Tat of Him Tat House	Resident of Him Tat House	Construction Noise	SPRO mobile	NA	<p>Mr. Hui Yau Wai reported that the noise irritation was becoming more severe recently and asked about the completion date of the works close to Him Tat House. The resident suspected that the noise comes from piling works</p> <p>In our investigation, since construction noise was generating from other construction site next to Him Tat House, it is considered that the complaint is due to cumulative noise generated by both construction sites. However, CWSTVJV should properly provide the noise mitigation measures at works area in System B to minimize the noise impact to the resident nearby.</p>	no comment by IEC on 7 May 2018	TCS00864/16/300/F0160b

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								nearby.	As advised by CWSTVJV on 20 April 2018, noise barrier was being erected at works area in System B as noise mitigation measures. According to the site photo, it is considered that the coverage of noise barrier is not sufficient and CWSTVJV should enhance the measure as far as practicable. The implementation of noise mitigation measures will be kept in view in subsequent site inspection.		
27	25-Apr-18	7-May-18	Junction of Hiu Kwong Street and Hiu Ming Street	A school but name of school not disclosed	Construction Noise	EPD	NA	This case is considered as an enquiry and no investigation is required under the EM&A Programme.			
28	18-May-18	24-May-18	Anderson Road Quarry Site	Undisclosed	Construction Noise	EPD	NA	投訴人指安達臣道石礦場地盤(NE/2016/01)在入夜 19:00 後仍見到有長臂喉工程車在運作, 及持續產生大噪音及閃燈, 非常擾民。	As advised by CWSTVJV and confirmed by RE/AECOM, there were no construction activities carried out after 19:00 and concreting was completed before 19:00. It is concluded that the retracting process is not a general construction work using Powered Mechanical Equipment and complaint was an isolated case due to misunderstanding of the site operation. To prevent similar incidents in future,	no comment by IEC on 30 July 2018	TCS00864/16/300/F0174b

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									CWSTVJV has recommended several mitigation measures.		
29	25-Jun-18	19-Jul-18	Pedestrian Connectivity E8 under Contract 3	Kwun Tong DC member Ms. So Lai-chun	Waste Management	CEDD	NA	A public complaint was referred from CEDD on 4 July 2018 regarding accumulation of dead leaves and branches found at slope (GLA-TNK 2458) near Hiu Yuk Path on 25 June 2018. The complainant requested the relevant department to clear the leaves and branch asap	CW-CMGC-JV has immediately clear the dead leaves and maintain the site cleanliness. Since the construction work has not yet commenced and the dead leaves and overgrown branches were not related project works, it is considered that the complaint is not valid the project.	no comment by IEC on 24 Sep 2018	TCS00864/16/300/F0189b
30	22-Aug-18	29-Aug-18	Hong Wah Court	Resident of Hong Wah Court	Construction Noise	1823 Hotline	NA	吳先生於 2018 年 8 月 22 日致電 1823 熱線投訴，指馬游塘區堆填區往將軍澳方向行車入口因配合項目需要而進行移除山坡工程，但其鑽地鑿石的噪音嚴重影響藍田康雅苑*居民，要求有關部門跟進。*註：投訴人於 2018 年 8 月 27 日更正指受影響屋苑應為藍田康華苑。	to reduce the inconvenience caused to the nearby resident, Kwan On should properly maintain the noise mitigation measures as appropriate, such as maintain good site practice including intermittent use of machine and plant and Sequencing operation of construction plant equipment. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 7 Sep 2018	TCS00864/16/300/F0196a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
31	28-Aug-18	31-Jul-18	Anderson Road Quarry Site	Undisclosed	Construction Noise	EPD	NA	安達邨誠達樓後面地盤，2月26日晚，晚上7時後，還在落石屎，相片拍攝時間大概晚上9時半，一直至晚上十一時五十分還有工程車在地盤行駛。影響居民休息。	According to the site diary which countersigned by RE, there was no concreting work carried out after 18:00 and the construction activities conducted during restricted hours with valid CNP were completed at 23:00. It is considered that the complaint was not valid to the Project. Nevertheless, CWSTVJV was reminded that in case of any work activities need to be carried out during restricted hours, CWSTVJV should strictly follow the requirements specified in the valid CNP.	no comment by IEC on 10 Oct 2018	TCS00864/16/300/F0197a
32	6-Sep-18	7-Sep-18	Tsui Yeung House	Resident of Tsui Yeung House	Construction Noise	Verbal	NA	Mr. CHENG Keung-fung complained that the contractor has conducted the noisy works such as rock excavation beyond the normal hours.	Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. As advised by Kwan On, the rock breaking works shall tentatively be completed by end of December 2018 and the mitigation measures will be implemented continuously during slope construction work and the slope construction will be carried out within the working hours at Portion 2. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 22 Oct 2018	TCS00864/16/300/F0201

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
33	24-Oct-18	25-Oct-18	E3	Kwun Tong DC member Ms. So Lai-chun	Construction Noise	WhatsApp Message	NA	KTDC member, Ms. Ann So, complaining the noise of the breaker at E3	As advised by the Contractor, the acoustic material wrapped on the breaker was worn-out on 24 October 2018 and replacement of new acoustic materials has been installed on the breaker immediately on 25 October 2018. The rock breaking works shall tentatively be completed to the road level in the middle of November 2018 and the mitigation measures will be implemented continuously during slope construction work and the slope construction will be carried out within the working hours at Portion 2. It is considered the complaint was an isolate case.	no comment by IEC on 23 Nov 2018	TCS00864/16/300/F0209a
34	12-Nov-18	13-Nov-18	Anderson Road Quarry Site	Resident of Ching Tat House (referred by Mr. Hui Yau Wai)	Construction Noise	SPRO Hotline	NA	Mr. Hui reported that he received complaint from a resident living in Ching Tat House about noise nuisance recently. Mr. Hui asked if project team can arrange some noise monitoring to check the noise level at the concerned flat or the same level at Ching Tat House.	The SPRO contacted Mr. Hui and explained to him about the purpose and benefits of the tunnel to the residents nearby and the expected date of completion of the tunnel will be earlier than 2020. Moreover, the noise mitigation measures had implemented to reduce the noise level effectively and the work progress will be closely updated to nearby stakeholders to enhance communication. Mr. Hui satisfied with the reply from SPRO and he agreed that the proposed noise monitoring in Ching Tat House was not needed. Since the works were	no comment by IEC on 12 Dec 2018	TCS00864/16/300/F0222a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									conducted within approved normal hours with implementation of noise mitigation measures, there were no breaches of legislative requirement.		
35	14-Nov-18	14-Nov-18	Anderson Road Quarry Site	Undisclosed	Light and Noise	EPD	NA	凌晨 1 時，地盤仍有大光燈正射民居和機器移動聲音，影響附近居民睡眠及違反環保條例。	CWSTVJV immediately adjusted the angle and brightness of the lighting to minimize the nuisance to the resident nearby. In response to the complaint, CWSTVJV immediately carried out remedial action to minimize the nuisance to the public. It was considered that complaint for noise generated by machine moving was an isolated case. CWSTVJV was reminded to closely monitor the plant use and sequence of night work and do not to violate CNP conditions.	no comment by IEC on 3 Jan 2019	TCS00864/16/300/F0223a
36	13-Nov-18	14-Nov-18	Anderson Road Quarry Site	Undisclosed	Noise and dust	1823	NA	Complainant requested to postpone the starting time of construction work at project site and also to solve the problem of construction noise and dust.	In our investigation, acoustic barrier and site hoarding were in place along the works area. No noticeable noise and dust impact was observed during the site inspection. As advised by CWSTVJV, the normal working hour of the construction site is 8am to 6pm and there were no violation of the relevant regulations. The senior public relation officer contacted the complainant Ms. Ma on 26 November 2018 to explain the site situation and she was satisfied with the reply. Investigation Report has been	no comment by IEC on 18 Feb 2019	TCS00864/16/300/F0224

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									completed by ET without comment from IEC.		
37	9-Dec-18	12-Dec-18	Anderson Road Quarry Site	Undisclosed	Construction noise	1823	2-4927907305	1823 has referred a case to CEDD on 10 December 2018, which the complainant complained that construction noise was generated from project site on Sunday and was affecting the resident at Hau Tat House, On Tat Estate. The complainant requested follow up action from related department as soon as possible.	In our investigation based on the information provided by CWSTVJV, there was no site activities undertaken at site access road as concerned by the complainant. The construction work carried out on Sunday was fully compliance with the CNP requirement. In response to the complaint, CWSTVJV was reminded to closely monitor the plant use and sequence of night work and do not to violate CNP conditions.	no comment by IEC on 10 Jan 2019	TCS00864/16/300/F0230a
38	19-Dec-18	27-Dec-18	Anderson Road Quarry Site	Undisclosed	Construction noise	1823	2-4948074127	1823 has referred a case to CEDD on 27 December 2018, which the complainant complained that noise barriers near the round-about at On Sau Road were not enough, and construction noise generated from the project site was affecting the resident at Ming Tai House, On Tai Estate. The complainant	Joint site inspection was carried out on 3 January 2019 the status of implemented mitigation measures provided by CWSTVJV was inspected. It was observed that noise mitigation measures including temporary noise barrier, acoustic mat and wrapped by acoustic materials are implemented on site. However, CWSTVJV was advised to extend the coverage of noise barrier as far as practicable and fully enclose the concerned works area which has been completed on 15 January 2019. Since the works were	no comment by IEC on 31 Jan 2019	TCS00864/16/300/F0237a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								requested follow up actions from related department as soon as possible.	carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.		
39	24-Jan-19	29-Jan-19	Anderson Road Quarry Site	Undisclosed	wastewater	Referred from DSD	NA	DSD has referred a case to CEDD on 24 January 2019 regarding suspended illegal discharge of cementitious slurry from construction site of Development of ARQ Site to nearby Public Stormwater Drainage System.	In our investigation, the concerned catchpit and U-channel mainly received the runoff from Po Lam Road as well as the discharge from the Anderson Road Quarry Site. It is suspected that the mud and silt found on the downstream has been accumulated over time particularly by rainstorm as well as routine discharge from construction site. As remedial action, CWSTVJV immediately clean the affected area where accessible. Nevertheless, in order to protection the watercourse at downstream of the construction site, CWSTVJV has some enhancement measures.	no comment by IEC on 29 Mar 2019	TCS00864/16/300/F0248a
40	30-Jan-19	30-Jan-19	Anderson Road Quarry Site	Undisclosed	noise	SPRO hotline	NA	A public complaint was received by SPRO hotline on 30 January 2019 regarding the construction noise near Ma Yau Tong Village and requested to add noise barrier as soon as possible.	In our investigation, CWSTVJV had provided the noise mitigation measures to minimize the noise impact to the resident nearby. The impact monitoring result obtained at Ma Yau Tong Village revealed that the construction noise were within acceptable level. Since the works were conducted within approved normal hours with implementation of noise and dust mitigation measures,	no comment by IEC on 15 Mar 2019	TCS00864/16/300/F0249a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									there were no breaches of legislative requirement.		
41	15-Feb-19	25-Feb-19	Anderson Road Quarry Site	Undisclosed	noise	1823	2-4948074127	1823 has referred a case to CEDD on 15 February 2019, which the complainant complained about the construction noise generated from the CEDD site near 法源寺 (Ma Yau Tong Village). The complainant requested for the details of works and the completion date, the complainant also requested CEDD to use other construction methods in order to re	In response to the complainant, CWSTVJV has proposed alternative quiet work method to alleviate the noise impact to the public. They will schedule the noisy activities to be carried out after 10am as far as practicable to minimize the impact to resident nearby, given that not affecting the site progress. Moreover, the coverage of acoustic barriers will be extended in view of the works programme.	no comment by IEC on 29 Mar 2019	TCS00864/16/300/F0251a
42	21-Feb-19	25-Feb-19	Anderson Road Quarry Site	Undisclosed	noise	EPD	NA	The resident from Sau Hong House complained that the noise from the Anderson Road Quarry construction site has gotten worse. In addition, sometimes even after midnight there are noise coming from the site. With the echo produces from the environment, this is not	In our investigation, CWSTVJV has implemented noise mitigation measures to reduce the noise impact to the nearby resident. However, to eliminate the inconvenience caused to the nearby resident, CWSTVJV should properly maintain the noise mitigation measures as appropriate, such as maintain good site practices such as intermittent use of machine and plant and Sequencing operation of construction plant equipment. Since	no comment by IEC on 28 Mar 2019	TCS00864/16/300/F0250

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								helping at all. Really a big disturbance to the residence in the area. The complainant suspecting the sound proof measure has lessened as time goes. Follow action is requested.	the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.		
43	21-Feb-19	26-Feb-19	Anderson Road Quarry Site	Undisclosed	noise	received by DEVB and referred to CEDD	NA	A public complaint was received by DEVB and referred to CEDD on 25 February 2019 regarding on the noise generated from the construction works of the Anderson Road Quarry Site affecting a local resident residing at the Anderson Road Squatter Area	Additional acoustic mat has been erected in front of the Squatter Area to minimize the noise impact. Noise mitigation measures such as acoustic barriers erected along the works area and breaker head wrapped with acoustic material were implemented continually. Alternative quiet work method was adopted such as drilling the hard rock before the breaking work to reduce the breaking duration. In our investigation, CWSTVJV had enhanced the noise mitigation measures to ease the complainant's concerns. CWSTVJV will continually implement the noise mitigation measures to reduce to noise impact to the public.	no comment by IEC on 29 Mar 2019	TCS00864/16/300/F0252a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
44	1-Mar-19	26-Feb-19	E3 of Contract 2	Undisclosed	noise	CEDD	NA	A complaint is forwarded by CEDD which was received by KTDC member Mr CHENG Keung Fung from the residents of Tsui Yeung House(翠楊樓) about the noise nuisance generated and the working time up to 7:00 pm from the rock excavation of E3 lift tower. Follow up action is requested.	The representative of the engineering team explained to Mr. Cheng about the project's details and concerned site was being constructed for the future pedestrian connection facilities. The related stone drilling process is expected to be completed in mid-April to end of April 2019. Mr. Cheng was satisfied with the rapid response from CEDD and the engineering team. In our investigation, Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Since the works were carried out within the non-restricted hours, it is considered that the works under the project did not breach the Noise Control Ordinance.	no comment by IEC on 6 May 2019	TCS00864/16/300/F0264
45	16-Jun-19	18-Jun-19	Anderson Road Quarry Site	Undisclosed	noise	EPD	NA	EPD referred a case to CEDD on 17 June 2019 regarding the construction noise heard at On Tat Estate on Sunday.	The Contractor explained that general cleaning by water jet was carried out in the construction site on the concerned day. Since the work did not involve the use of Powered Mechanical Equipment (PME), it would not violate the noise control ordinance. The Investigation report is underway by ET.	no comment by IEC on 21 August 2019	TCS00864/16/300/F0301a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
46	12-Jul-19	15-Jul-19	Anderson Road Quarry Site	Undisclosed	dust	EPD	NA	On 12 July 2019, a complaint was received by EPD regarding the dust impact to the residents at Po Tat Estate and On Tat Estate due to the dust emission at Anderson Road Quarry site.	In our investigation, CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident and status of implementation of dust mitigation measures was considered effective based on the site observation. Moreover, there was mostly rainy day throughout June and July 2019 in typical rainy season in Hong Kong and the dust impact was considered not significant in addition to the dust mitigation measures implemented provided by the Contractor. Nevertheless, the ET will closely monitor the environmental performance and dust mitigation measures in subsequent site inspection. The IR is under reviewed by IEC.	no comment by IEC on 12 August 2019	TCS00864/16/300/F0292b
47	6-Aug-19	14-Aug-19	Work Area Portion 2 E3 (Slope of Hiu Ming Street opposite of Tsui Yeung House)	翠屏(北)邨物業服務辦事處	Noise	1823	NA	A public complaint was received by 1823 on 6 August 2019 relating to the noise generated from construction work at the lift tower site (Slope E3) at Hui Ming Street from the residents of Tsui Yeung House. The complainant expressed that the construction works has been	In our investigation, Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Nevertheless, since the construction site is close to the residential area, adequate noise mitigation measures shall be provided to reduce to noise nuisance to the public. It is concluded that the complaint was valid to the contract. As the works were carried out within the non-restricted hours, it is	no comment by IEC on 16 Sep 2019	TCS00864/16/300/F0310a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								undertaken for 2 years and generated construction noise from 8am every day, which causing serious nuisance to the nearby residents.	considered that the works under the contract did not breach the Noise Control Ordinance.		
48	15-Oct-19	18-Oct-19	Work Area Portion 6 (Tseung Kwan O Tunnel Bus-Bus Interchange Pedestrian Connectivity Facilities E12)	Mr. Ng	Noise	1823	NA	A public complaint was received by 1823 on 15 October 2019 relating to the noise generated from construction work at Tseung Kwan O Tunnel Bus to Bus Interchange Pedestrian Connectivity Facilities E12. The complainant expressed that the construction noise was generated from breaking work at 8:20 am without noise mitigation measure, which causing nuisance to the nearby residents.	In our investigation, Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Nevertheless, since the construction site is close to the residential area, adequate noise mitigation measures shall be provided to reduce to noise nuisance to the public. As the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Kwan On was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.	no comment by IEC on 13 Nov 2019	TCS00864/16/300/F0326a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
49	5-Nov-19	11-Nov-19	Work Area Portion 2&3 (lift tower construction work at Hiu Kwong Street)	NA	Noise	EPD	NA	A public complaint was received by EPD relating to the noise generated from breaking work of lift tower construction work at Hiu Kwong Street (Portion 2&3).	In our investigation, Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Nevertheless, since the construction site is close to the residential area, adequate noise mitigation measures shall be provided to reduce to noise nuisance to the public. As the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Kwan On was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.	no comment by IEC on 27 Dec 2019	TCS00864/16/300/F03 32a
50	7-Nov-19	11-Nov-19	Work Area Portion 6	Mr. Cheng	Noise	EPD	NA	寶達邨居民鄭先生，表示將軍澳隧道出口工程，日間噪音嚴重，8:30-17:00，幾部幾同時開動，而且無防音欄，之前是有，現要求環保署向對方反映改善	In our investigation, Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Nevertheless, since the construction site is close to the residential area, adequate noise mitigation measures shall be provided to reduce to noise nuisance to the public. As the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Kwan On was reminded to implement the mitigation	no comment by IEC on 27 Dec 2019	TCS00864/16/300/F03 33a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
									measures as far as practicable as recommended in the EM&A Programme.		
51	10-Nov-19	12-Nov-19	Underpass	Undisclosed	Noise	EPD	NA	<p>On 10 November 2019 投訴人為馬游塘村居民，自本年初寶林路開展掘隧道工程，每天噪音不斷，由 8 至 6，由於欠缺遮擋，聲音直向 4 至 22 號村屋，將來通車，相信噪音不只 8-6，現懇請環保署為本村居民正式評估，並向政府提出村民困擾，考慮盡快設置隔音屏。</p> <p>On 11 November 2019 寶琳路近馬游塘村開掘隧道的工程地盤每日 8am-6pm 發出噪音，欠缺遮擋，聲音影響馬游塘村 4-22 號村屋。希望政府部門</p> <p>1.調查地盤有否違規 2.實施減音措施以減低對附近居民的滋擾</p>	<p>In our investigation, CWSTVJV had implemented the noise mitigation measures to reduce to noise impact to the public. Since the works were conducted within approved normal hours with implementation of noise mitigation measures, there were no violation of legislative requirement. For the complainant's concern on the operation noise after commencement of the project, it is out of the scope of the EM&A programme and the relevant department will follow up the concern.</p>	no comment by IEC on 30 Dec 2019	TCS00864/16/300/F0337

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
52	11-Nov-19	20-Nov-19	Construction site near On Tai Estate Ancillary Facilities Building on On Sau Road	Mr. Wong (resident of Yung Tai House of On Tai Estate)	Noise	1823	ref. 2-59763 03183	黃先生投訴安秀道安泰邨服務設施大樓附近掘路工程已持續數年還未完成，並投訴其經常發出噪音滋擾，要求部門跟進。 On 22 November 2019, the project hotline received a call from the same complainant reported on the noise nuisance near On Sau Road and On Yan Street. He suggested to speed up the noise making works by intensely concentrate the excavation works during day time. No intermittence is suggested in order to speed up the works and to avoid waste of manpower.	In our investigation, CWSTVJV had implemented the noise mitigation measures to reduce to noise impact to the public. However, in response to the complaint, the Contractor was advised to enhance the performance of the temporary noise barriers such as increase the coverage of the noise barrier. Since the works were conducted within normal working hours with implementation of noise mitigation measures, there were no breaches of legislative requirement.	no comment by IEC on 27 Dec 2019	TCS00864/16/300/F0338a
53	5-Mar-20	6-Mar-20	Tunnel work of Anderson Road Quarry Site (the Underpass)	Resident of On Tat Estate	Noise	EPD	NA	本人是安達邨居民，隧道工程在安達臣的工程，施工至今嘈音間中改善，最近又有嘈音出現，仲係重低音，希望能加裝隔音設備，工程不知何時將嘈音減至最	In our investigation, CWSTVJV had implemented the noise mitigation measures to reduce to noise impact to the public. In response to the complaint, CWSTVJV had immediately installed a layer of acoustic mat at boundary of System A. Since the works were conducted within	no comment by IEC on 1 Apr 2020	TCS00864/16/300/F0357a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								低。1. A public complaint was received by EPD on 5 March 2020 regarding the construction noise generated from the tunnel work of the subject site. The complainant mentioned that the noise from construction was improved before but it became serious recently.	approved normal hours with implementation of noise mitigation measures, there were no violation of legislative requirement.		
54	4-Mar-20	17-Mar-20	Near Hiu Ming Street Playground (E8)	Undisclosed	Noise	1823	ref. 3-62832 37171	投訴人投訴有關秀茂坪邨秀安樓附近有兩個地盤，地盤由星期一至五，每天早上約9AM-5PM 持續不斷發出強烈的嘈音，投訴人表示地盤是在曉明街藍球場旁邊的位置(投訴人未能告知確實街號)，因此要求部門盡快回覆及告知有關情況。A public complaint was received by 1823 on 4 March 2020 regarding the construction noise. The complainant mentioned that there	In our investigation, CW-CMGCJV had implemented the noise mitigation measures for the works at upper section of E8 near Hiu Yuk Path and no noise impact was observed and anticipated in Hiu Ming Street based on the site activities and our inspection record. It is considered that the complaint is likely related to another construction site located near Hiu Ming Street Playground and not caused by the works under the Project. Since the works were conducted within approved normal hours with implementation of noise mitigation measures, there were no violation of legislative requirement.	no comment by IEC on 15 Apr 2020	TCS00864/16/300/F03 59a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								were two construction sites near Hiu Ming Street Playground generated construction noise continuously during 9AM to 5PM on weekdays.			
55	23-Mar-20	23-Mar-20	Near Lin Tak Road (E11)	Undisclosed	Water Quality	Project hotline	NA	<p>藍田居民梁先生反映在將軍澳道往連德道天橋的大彎位，其中有一個車輛出入口每日早上八時左右不時有泥水從地盤流出路面，估計泥水是清洗工程車輛所致，令梁先生的車輛每次駛經時被濺濕及弄污，請問有何措施改善問題？</p> <p>A public complaint was received by project hotline on 23 March 2020 regarding overflow of muddy water from the construction site. The complainant mentioned that muddy water came out from site entrance, which spotted on his car, at 8am every morning.</p>	<p>In our investigation, the wheel washing facilities at site exit of E11 is one of the dust quality mitigation measures conducted by CW-CMGCJV and corresponding measure was implemented to prevent overflow of wastewater out of the site. In our recent site inspection, no outflow of muddy water from the site was observed and the condition of concerned Lin Tak Road was satisfactory. It is considered that the complaint was unlikely due to the project.</p>	no comment by IEC on 15 Apr 2020	TCS00864/16/300/F0360a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
56	17-Mar-20	19-Mar-20	Anderson Road Quarry Site	Resident of Yan Tat House	Noise	Project hotline	NA	許有為區議員接獲安達邨仁達樓 2613 室居民反映，安達臣道石礦場發展用地工程噪音持續兩年，要求工程團隊下周派員到有關單位視察，並採取可行的噪音緩解措施。許有為區議員要求陪同視察。 A public complaint was received by hotline on 17 March 2020 regarding the construction noise generated from the Anderson Road Quarry Site. The complainant mentioned that the construction noise generated from the Anderson Road Quarry Site had been continued for two years.	In our investigation, CW-CMGCJV has implemented noise mitigation measures to reduce the noise impact and nuisance to the public. However, to eliminate the inconvenience caused to the nearby residents, CW-CMGCJV was advised to further adopt good practices on mitigating construction noise to reduce the noise impact to the nearby residents. 5. Since the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Nevertheless, as the construction site is close to the residential area, CW-CMGCJV was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.	no comment by IEC on 11 May 2020	TCS00864/16/300/F0361a
57	1-Apr-20	20-Apr-20	Work Area Portion 2	Undisclosed	Noise	1823	NA	觀塘秀茂坪紀念公園傍及曉明街的地盤，共兩個地盤，是地政總署管轄的。投訴人表示已被工程噪音滋擾了兩年多；另外投訴人得知完	In our investigation, Kwan On has implemented noise mitigation measures to reduce the noise impact to the nearby resident. Nevertheless, since the construction site is close to the residential area, adequate noise mitigation measures shall be provided	no comment by IEC on 7 May 2020	TCS00864/16/300/F0366a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								<p>工時間要到 2021 年，投訴人不明白為何工程頭尾要 3 年多時間。要求地政總署直接以電郵回覆工程長的原因及有沒有措施解決地盤發出的噪音。 A public complaint was received by 1823 on 1 April 2020 and subsequently transmitted to Environmental Team (ET) on 20 April 2020, regarding the noise nuisance generated from the construction site in Hui Ming Street. The complainant concerned about the slow progress and implementation of noise mitigation measures to alleviate the noise impact arising from the construction work.</p>	<p>to reduce to noise nuisance to the public. It is concluded that the complaint was valid to the contract. However, as the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Kwan On was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.</p>		

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
58	11-May-20	12-May-20	Work Area Portion 2	Undisclosed	Noise	Project hotline	NA	陳先生住於翠楊樓 17 樓，投訴對面鑽石工程產生噪音對母親健康構成影響，現查詢完工日期、噪音監控標準及措施。 A public complaint was received by Project Hotline on 11 May 2020 regarding the noise generated from rock breaking work from a construction site opposite to Tsui Yeung House, which affecting his mother's health. The complainant enquired about the completion date of construction work, construction noise level standard and implementation of noise mitigation measures on site.	In our investigation, Kwan On has enhanced the noise mitigation measures to reduce the noise impact to the nearby resident. Based on the noise measurement result, the construction noise was reduced to acceptable level after the additional noise mitigation measures in place. Nevertheless, Kwan On was reminded to continually implement the noise mitigation measures as far as practicable in the remaining work. The performance of noise mitigation measures will keep in view by ET in subsequent site inspection	no comment by IEC on 28 May 2020	TCS00864/16/300/F0370a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
59	18-Jun-20	23-Jun-20	Anderson Road Quarry Site, System B	Undisclosed	Noise	EPD	NA	A public complaint was received by EPD on 18 June 2020 regarding the noise generated from rock breaking by machinery before 7pm from construction site near Hau Tat House. The complainant understood that the Contractor could carry out construction works, other than percussive piling, before 7pm under the CNP and hoped that the Contractor could arrange the noisy construction works to be carried out before 6pm. According to the information provided by the complainant, it is suspected complaint location would be Anderson Road Quarry Site, System B.	In our investigation, the Contractor has implemented noise mitigation measures to reduce the noise impact and nuisance to the public. Since the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Nevertheless, as the construction site is close to the residential area, the Contractor was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme	no comment by IEC on 17 July 2020	TCS00864/16/300/F0391a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
59#	23-Jul-20	24-Jul-20	Anderson Road Quarry Site near On Tat Estate	Undisclosed	Noise	EPD	NA	A public complaint was received by EPD on 23 July 2020 regarding the construction noise generated from the use of PME at Anderson Road Quarry Site near On Tat Estate at 6:30am (restricted hours). He/she requested relevant department to follow up.	In our investigation, CWSTVJV had restricted the use of PME before 7am. There was no construction work and use of PME during the restricted hours. Since the works were conducted within approved normal hours with implementation of noise mitigation measures, there were no violation of legislative requirement. Nevertheless, as the construction site is close to the residential area, CWSTVJV was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme	no comment by IEC on 25 August 2020	TCS00864/16/300/F0401
60	14-Nov-20	18-Nov-20	Near Hiu Ming Street Playground (E8)	Undisclosed	Noise	1823	NA	A public complaint was received by 1823 on 14 November 2020 regarding the construction noise. The complainant mentioned that there was piling works at Hiu Ming Street Playground, generating huge noise during 9AM to 10AM on 14 November 2020. He/she requested relevant department to follow up	In our investigation, there was no noise impact was observed and anticipated in Hiu Ming Street based on the site activities and our inspection record. Since the works were conducted within approved normal hours with implementation of noise mitigation measures, there were no violation of legislative requirement	no comment by IEC on 4 January 2021	TCS00864/16/300/F0424

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
61	4-Dec-20	7-Dec-20	Opposite to On Tai Estate – lower portion of Road L4	Undisclosed	Dust	EPD	NA	A public complaint was received by EPD on 4 December 2020 regarding the dust impact. The complainant mentioned that the construction site opposite to On Tai Estate had dust emission problem due to lack of water spraying. He/she requested relevant department to follow up	In our investigation, CWSTVJV has implemented dust mitigation measures to eliminate the inconvenience caused to the nearby resident. In view of the potential traffic dust impact and implementation of dust mitigation measures, it is considered that the complaint was not valid to the Project	no comment by IEC on 4 January 2021	TCS00864/16/300/F0434
62	3-Dec-20	7-Dec-20	Ma Yau Tong Village (East Portal)	Undisclosed	Noise and dust	1823 & EPD	3-6574141017	A public complaint was received by 1823 and EPD on 14 November 2020 regarding the construction dust and noise impact arising from the project. There were acoustic mats erected on the slope of East Portal, however, the complainant enquired about effectiveness of the noise barriers with dozens of 15 cm "X"-shaped cuts. Moreover, there was lack of water sprinkling on the site and fugitive	In our investigation, CWSTVJV had provided the dust and noise mitigation measures to minimize the dust and noise impact to the resident nearby. To response the concern from the complainant, as enhancement noise measure, the Contractor extended the noise barrier to encircle noisy activity. Since the works were conducted within approved normal hours with implementation of noise and dust mitigation measures, there were no breaches of legislative requirement	no comment by IEC on 4 January 2021	TCS00864/16/300/F0435

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								dust was blowing to the village			
63	7-Jan-21	7-Jan-21	System B	Resident of Yan Tat House	Noise	Project hotline	NA	A public complaint was referred by district Councillor Mr. HSU Yau-wai and received by project hotline on 7 January 2021 regarding the construction noise. The complainant mentioned that the construction site next to SKH St. John's Tsang Shiu Tim Primary School generated noise problem and she requested relevant department to follow up.	In our investigation, the Contractor has implemented noise mitigation measures to reduce the noise impact and nuisance to the public.6. Since the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Nevertheless, as the construction site is close to the residential area, the Contractor was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme.	no comment by IEC on 19 July 2021	TCS00864/16/300/F0441
64	18-Mar-21	18-Mar-21	Anderson Road Quarry Site (between On Tat Estate and On Tai Estate)	Undisclosed	Noise	1823 & EPD	NA	A public complaint was received by 1823 and referred by EPD on 18 March 2021 regarding the construction noise generated from construction works at Anderson Road Quarry Site between On Tat Estate and On Tai Estate. The complainant expressed that construction works	In our investigation, CWSTVJV had restricted the use of PME before 7am. There was no construction work and use of PME during the restricted hours and there should not be any non-compliance of Noise Control Ordinance. Nevertheless, as the construction site is close to the residential area, CWSTVJV was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme	no comment by IEC on 1 April 2021	TCS00864/16/300/F0454

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								of the site started from 6:45am everyday which causing noise disturbance to the nearby resident and he/she requested relevant department to follow up			
65	1-Apr-21	1-Apr-21	Construction site near SKH St. John's Tsang Shiu Tim Primary School (System B under Contract 3)	Undisclosed	Noise	EPD	NA	A complaint was received by EPD and referred to CEDD on 1 April 2021 regarding the construction noise. The complainant mentioned that piling work was conducted at construction site near SKH St. John's Tsang Shiu Tim Primary School in recent week which generated noise problem. Moreover, there were no noise mitigation measures provided in the construction site	In our investigation, the Contractor has implemented noise mitigation measures to reduce the noise impact and nuisance to the public. Since the works were carried out within the non-restricted hours, it is considered that the works under the contract did not breach the Noise Control Ordinance. Moreover, the Contractor has adopted noise mitigation measures to minimise noise impact to the public. Since the construction site is close to the residential area, the Contractor was reminded to implement the mitigation measures as far as practicable as recommended in the EM&A Programme	no comment by IEC on 19 July 2021	TCS00864/16/300/F0458a
66	28-Mar-21	30-Mar-21	Anderson Road Quarry Site (between On Tat Estate and	Resident of Tai Fung House of On	Noise	EPD	K13/RE/00007086-21	A public complaint was received by EPD on 28 March 2021 regarding the construction noise generated from construction works at	In our investigation, CWSTVJV had followed that CNP for work during restricted hour and there should not be any non-compliance of Noise Control Ordinance. Nevertheless, some site areas had been handed over to other	no comment by IEC on 22 April 2021	TCS00864/16/300/F0459

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
			On Tai Estate)	Tai Estate				Anderson Road Quarry Site until 9pm on Monday to Saturday. Moreover, the complainant concerned about the construction noise heard on 28 March 2021 which was a Sunday.	contract and construction noise generated from others is not controlled by the project. As a reminder, CWSTVJV should implement the mitigation measures as far as practicable as recommended in the EM&A Programme.		
67	11-Jun-21	11-Jun-21	Anderson Road Quarry Site	Resident of Chi Tat House, On Tai Estate	Noise	EPD	EPD Ref.: 13208-21	A public complaint was received by EPD on 11 June 2021 and complained about noise nuisance from multiple construction sites on Anderson Road Quarry Site. The complainant stated that there were noise nuisances from different construction sites from 0800 am to 1800 pm from Monday to Saturday without adequate noise mitigation measures. On 17 June 2021, the complainant added that the noise was generated from rock breaking works in front of Chi Tai House (not from the housing sites near the	6. In our investigation, CWSTVJV had implemented the noise mitigation measures to reduce to noise impact to the public. In response to the complaint, CWSTVJV had immediately installed a layer of acoustic barrier at boundary of concern works area. Since the works were conducted within approved normal hours with implementation of noise mitigation measures, there were no violation of legislative requirement.	no comment by IEC on 19 July 2021	TCS00864/16/300/F0478a

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								Tai Sheung Tok slope) and no mitigation measure was implemented for the rock breaking works.			
68	20&21/June/21	23-Jul-21	Anderson Road Quarry Site	DSD	Water Quality	EPD	EPD Ref.: 13208-21	EPD received complaints from DSD on 20 and 21 July 2021 concerning about discharge of muddy water as found on Po Lam Road and at the drainage facility near Tin Hau temple.	In our investigation, CWSTVJV had implemented the water quality mitigation measures to minimise the impact arising from the construction site. In view of the site condition and inclement weather condition on the complaint days, it is considered that the complaints raised by DSD were unlikely due to the C1 Project. Nevertheless, CWSTVJV was advised to closely monitor the discharge quality to avoid non-compliance of water quality happened in the construction site. Moreover, to cope with the adverse weather condition in wet season, CWSTVJV should regularly review the drainage plan as needed.	no comment by IEC on 6 August 2021	TCS00864/16/300/F0485b
69	14&16/Sep/21	15-Sep-21	Anderson Road Quarry Site	DSD	Water Quality	EPD	NA	EPD received complaints from DSD on 14 Sep 2021 and 16 Sep 2021 concerning about discharge of muddy water as found at the catchpit SCH4003250 near Po	In our investigation, CWSTVJV had implemented the water quality mitigation measures to minimise the impact arising from the construction site. However, there were incidents of seepage of silty water at Q2 and Q3 and rectified actions were undertaken immediately. Having investigated, the incidents were considered very short	no comment by IEC on 6 October 2021	

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								Lam Road and catchpit SSH4001400 near Po Tat Tin Hau Temple.	term and would not generate large amount of muddy water. In view of the inclement weather condition and there were other major sources, it is considered that the complaints raised by DSD were not fully contributed by C1 Project. Nevertheless, CWSTVJV was advised to closely monitor the discharge quality to avoid non-compliance of water quality happened in the construction site. Moreover, to cope with the adverse weather condition in wet season, CWSTVJV should regularly review the drainage plan as needed.		
70	23/Sep/21	29-Sep-21	Anderson Road Quarry Site	CEDD & EPD	Noise	CEDD & EPD		A public complaint was referred by 1823 to both CEDD and EPD on 23 September 2021. The complainant stated that the construction works at Anderson Road Quarry Site started before 7am, which generated construction noise and affecting the upper floor resident of On Tat Estate. EPD have contacted the	Our investigation revealed that there was no construction works under the Project undertaken during the concerned period by the complainant, and there were other concurrent contracts on Anderson Road Quarry Site and the contribution noise may be related to others. Therefore, it is considered that the noise complaint was unlikely to be related to the works under the Project. Nevertheless, CWSTVJV was reminded to properly maintain the noise mitigation measures as far as	No comment by IEC on 15 November 2021	

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								complainant and clarify that the concerned about construction dust and daytime construction noise after 7am.	practicable considering the construction site is relatively close to residential area.		
71	30/Mar/22	12/Apr/22	Anderson Road Quarry Site	DSD	Water Quality	DSD		EPD received complaint from DSD on 28 March 2022 concerning about siltation and discharge of muddy water observed at the public drainage system at catchpit SSH4001400 near Tin Hau Temple and the site discharge points at Po Lam Road on 28 March 2022	In our investigation, the Contractor had implemented the water quality mitigation measures to minimise the impact arising from the construction site. Based on the investigation findings, it is considered that the complaint was likely caused by the interfacing contractors under rainy days and not due to the works under the Project.	No comment by IEC on 19 April 2022	TCS00864/16/300/F0540
72	14/Apr/22	25/Apr/22	Anderson Road Quarry Site	DSD	Water Quality	DSD		DSD carried out site inspection at site discharge point at Po Lam Road on 12 April 2022 and observed discharge of muddy water at public drainage system. The case was then referred to CEDD and EPD to investigate the source of the muddy water discharge.	In our investigation, the Contractor had implemented the water quality mitigation measures to minimise the impact arising from the construction site. Based on the investigation findings, it is considered that the complaint was likely caused by the interfacing contractors and not due to the works under the Project.	No comment by IEC on 16 May 2022	TCS00864/16/300/F0541
73	11/May/22	25/May/22	Anderson	DSD	Water	DSD		EPD received complaint	Based on the above findings and	No	TCS00864/

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
	2022	2022	Road Quarry Site		Quality			from DSD on 11 May 2022 concerning about muddy water observed entering Tsui Ping River, with similar situation observed at Tin Hau Temple and Po Lam Road.	successive heavy rainstorm on 11 to 13 May 2022, it is considered the muddy water found in the concerned catchpit SSH4001400 near Tin Hau Temple and Po Lam Road on 11 to 13 May 2022 were likely caused by impact of rainstorm and partially contributed by the interfacing contractors at Sites R2-9 & R2-10.	comment by IEC on 13 June 2022	16/300/F559
74	17/May/2022	30/May/2022	Anderson Road Quarry Site	DSD	Water Quality	DSD		EPD received complaint from DSD on 14 and 16 May 2022 concerning about muddy water observed entering Tsui Ping River.	Heavy rain led to large amount of storm runoff from roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. Besides, there were several construction sites at upstream of Tsui Ping River. It is considered that complaint mainly related to the interfacing contractor(s) and unlikely to have been caused by the project.	No comment by IEC on 13 June 2022	TCS00864/16/300/F562a
75	27/May/2022	9/Jun/2022	Anderson Road Quarry Site	DSD	Water Quality	DSD		EPD received complaint from DSD on 27 May 2022 concerning about muddy water observed entering Tsui Ping River, with similar situation observed at Tin Hau Temple and Po Lam Road.	Heavy rain led to large amount of storm runoff from roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. Besides, there were several construction sites at upstream of Tsui Ping River. It is considered that complaint mainly related to the interfacing contractor(s) and unlikely to have been caused by the project.	No comment by IEC on 13 June 2022	TCS00864/16/300/F563
76	6, 7, 8/ Jun/2022	7, 8, 9/ Jun/2022	Anderson Road	DSD	Water Quality	DSD		On 6 June 2022, DSD	As a matter of fact, heavy rain led to large amount of storm runoff from roads	Sent to EPD on	TCS00864/16/300/F56

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
	2	2	Quarry Site					informed that dirty water with bad odour was observed entering Tsui Ping River this morning at the upstream near junction of Kai Lim Road and Tsui Ping Road. The situation has persisted over 50 mins. Furthermore, muddy water was observed entering Tsui Ping River, with similar situation at Tin Hau Temple and Po Lam Road (山渠) on 6, 7 and 8 June 2022.	and landscape into the public drainage system, which deteriorated the water quality in the drainage system. Besides, there were several construction sites at upstream of Tsui Ping River. It is considered that complaint mainly related to the interfacing contractor(s) and unlikely to have been caused by the project.	21 June 2022	5
77	14/Jun/2022	15/Jun/2022	Anderson Road Quarry Site	DSD	Water Quality	DSD		DSD concerning muddy water discharge found at Tin Hau Temple and Po Lam Road on 14 June pm.	As a matter of fact, heavy rain led to large amount of storm runoff from roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. Besides, there were several construction sites at upstream of Tsui Ping River. It is considered that complaint mainly related to the interfacing contractor(s) and unlikely to have been caused by the project.	Sent to EPD on 29 June 2022	TCS00864/16/300/F566
78	8/Aug/2022	8/Aug/2022	Anderson Road	DSD	Water Quality	DSD		DSD advised EPD that muddy water was	As a matter of fact, heavy rain led to large amount of storm runoff from	No comment	TCS00864/16/300/F58

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
			Quarry Site					observed entering Tsui Ping River in the morning of 8 August 2022, with similar situation at Tin Hau Temple and Po Lam Road	roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. No muddy water discharge was evident in the morning or afternoon of 8 August 2022. It is therefore considered that the muddy water discharge observed by DSD in the morning of 8 August 2022 was unlikely to have been caused by the ARQ contracts of C1 or C4.	by IEC on 19 September 2022	0
79	12/Aug/2022	12/Aug/2022	Anderson Road Quarry Site	DSD	Water Quality	DSD		DSD advised EPD that muddy water was observed entering Tsui Ping River in the morning of 12 August 2022, with similar situation at Tin Hau Temple and Po Lam Road (山渠).	As a matter of fact, heavy rain led to large amount of storm runoff from roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. No muddy water discharge was evident in the morning of 12 August 2022. It is therefore considered that the muddy water discharge observed by DSD in the morning of 12 August 2022 was unlikely to have been caused by the ARQ contracts of C1 or C4.	No comment by IEC on 19 September 2022	TCS00864/16/300/F581
80	29&30/Sep/2022	29/Sep/2022&3 Oct 2022	Anderson Road Quarry (ARQ) Site	DSD	Water Quality	DSD		DSD's complaint was made to EPD who requested CEDD in the same respective mornings to handle and investigate in accordance with the	As a matter of fact, heavy rain led to large amount of storm runoff from roads and landscape into the public drainage system, which deteriorated the water quality in the drainage system. No muddy water discharge from ARQ	Sent to EPD on 18 October 2022	TCS00864/16/300/F593

Log ref.	Date of Complaint	Date of Received by ET	Complaint Location	Complainant	Complaint nature	Channel	Ref. no.	Complaint details	Follow up action	Log ref.	Date of Complaint
								procedure in EM&A Manual.	<p>Site was evident in the morning of 29 and 30 September 2022. It is therefore considered that the muddy water discharge observed by DSD in the morning of 29 and 30 September was unlikely to have been caused by the ARQ contracts of C1 or C4.</p> <p>During wet season, the Contractor was strongly reminded to implement adequate water quality mitigation measures to minimise the impact arising from the construction site. The Contractor should closely monitor the discharge quality from the Site to avoid non-compliance. The ET will pay special attention on water quality mitigation measures implementation on site through regular site inspection, and give advice on remedial action when necessary.</p> <p>Incidentally, it is noted that Site R2-9 has kept discharging muddy water to downstream manhole D310. Record photos of the manhole dated 6, 7 and 8 October 2022 are enclosed for reference.</p>		

Appendix N

Implementation Status for Water Quality Mitigation Measures

Water Quality Mitigation Measure



Paving for exposed slope to reduce dust dispersion & mitigate the silty runoff generation at Q1.



Impermeable cover for slope at System A.



Q1. Wastewater treatment facility 30 cu.m Sedimentation Tank + AquaSed of 15 cu.m per hour + WETSEP



Q4. Wastewater treatment facility Temporary Water Reservoir 150 cu.m + AquaSed of 60 cu.m per hour



Q6: Wastewater treatment facility 24 cu. m.



Q7. Wastewater treatment facility 30 cu.m Sedimentation Tank + AquaSed of 60 cu.m per hour



Q9. Two nos. of 30 cu.m Sedimentation Tank + AquaSed of 60 cu.m per hour
